



## Internal Monitoring Report (IMR)

Document stage: Final

Date: 10 August, 2017

---

# National Highway Authority (NHA)

Government of Pakistan

## National Highway Network Development in Balochistan Project

### Internal Monitoring Report (IMR) on Resettlement Plan (RP) Implementation for N-50 Zhob - Mughal Kot Section

#### Prepared by

National Highway Authority; Environment, Afforestation, Land and Social Wing  
(EALS)

#### Reviewed by

Jointly reviewed and finalized by Mr. Azeem Resettlement Specialist (Consultant)  
ADB and NHA Project team

#### Notes

This IMR is a document of the borrower. The views expressed herein do not necessarily represent those of ADB's Board of Directors, Management, or staff, and may be preliminary in nature.

Asian Development Bank

# NATIONAL HIGHWAY AUTHORITY



(N-50)

Zhob – Mughal Kot (81 km)

Road Project

## **Internal Monitoring Report**

Of RP Implementation

**10<sup>th</sup> August 2017**

**1<sup>st</sup> Quarterly Report (May – July, 2017)**

## Contents

<b>1. Introduction.....</b>	<b>1</b>
<b>1.1. Objectives of the IMR .....</b>	<b>1</b>
<b>1.2. Monitoring Methodology .....</b>	<b>1</b>
<b>2. Updated Resettlement Plan and RP implementation set-up. ....</b>	<b>2</b>
<b>2.1. Project Description .....</b>	<b>2</b>
<b>2.2. Updated Resettlement Plan.....</b>	<b>2</b>
<b>2.4. LAR institutional Set-up and RP implementation process.....</b>	<b>3</b>
<b>3.1. Compensation Payment Progress achieved.....</b>	<b>4</b>
<b>3.2. Sections where Compensation is fully Paid or impacts are avoided .....</b>	<b>4</b>
<b>3.3. Sections where Compensation Payment is under process .....</b>	<b>5</b>
<b>4. RP disclosure, Consultations, and Grievance Redress. ....</b>	<b>7</b>
<b>4.1. Public Consultations/Meetings .....</b>	<b>7</b>
<b>4.2. Grievance Recording and Redress.....</b>	<b>7</b>
<b>5. Conclusion and Recommendations .....</b>	<b>9</b>

## **Quarterly Internal Monitoring Report of Zhob – Mughal Kot Road Project (N-50)**

### **1. Introduction**

1. Through ADB financial support, National Highway Authority (NHA), Pakistan is upgrading Zhob – Mughal Kot Section of N-50 road as two lanes 7.3 meter wide carriageway with 2.5 meter shoulders on each side. As per design the total pavement width of the road will be 13.3 meters (44 ft). The designated NHA owned ROW of project road section is 110 feet in urban areas and 220 feet in rural areas and project did not entail acquisition of land. However, to address the resettlement issues in sections wherever ROW was encroached near settlements and agricultural land along the project road, NHA endorsed updated resettlement plan was cleared by ADB in May 2017. Immediate after clearance of updated resettlement plan, implementation activities were started for compensating impacted before clearing the encroached sections of ROW and to ensure implementation of project is consistent with ADB's IR requirements. The RP implementation require day to day monitoring of implementation progress and compile quarterly monitoring reports for ADB's review and acceptance. Accordingly this 1<sup>st</sup> Internal Monitoring Report is prepared that covers the implementation progress achieved between May to July 2017.

#### **1.1. Objectives of the IMR**

2. The objective of this internal monitoring report is to:

- Review and assess the process of ongoing progress on payment of compensation for assets and entitled allowances to the DPs;
- Review implemented coordination progress and payment activities performed to project affected families and facilitate them in compensation processing and payment.
- Consultations, recording, tracking and handling of grievances at local and GRC levels.
- Recommend actions for improved RP implementation and execution of project works.

#### **1.2. Monitoring Methodology**

3. Methodolgy for this monitoring report includes a continued review of LARP implementation progress data and consultations with key informants and the displaced persons. The monitoring instruments included review of progress on the a) institutional set-up placed for RP implementation, b) RP disclosure and community outreach efforts implemented, c) compensation payment progress achieved for impacted assets, d) consultations progress and meeting proceedings by DPC and project GRC etc. Based on the review the results are summarized in the sections below explaining the achieved progress and actions required to improve the progress,

## 2. Updated Resettlement Plan and RP implementation set-up.

### 2.1. Project Description

4. The project road section is 81 km long single carriageway that starts outside the city premises of Zhob District in Baluchistan and terminates at the Mughalkot in Khyber Pakhtoonkhawa. For rehabilitation and improvement works the project road has been divided into two contract packages: Contract package Lot-1 is from RD 0+000 to RD 49+000, and second contract package Lot-2 is from RD 49+000 to RD 81+300. The project works include rehabilitation and upgrading of existing single lane Zhob – Mughal Kot Section of N-50 road into 7.3 meter wide carriageway with 2.5 meter shoulders on each side. As per design the total pavement width of the road is 13.3 meters (44 ft.).

### 2.2. Updated Resettlement Plan

5. Identified resettlement impacts are scattered in small portions of the road, hence to facilitate implementation of project works in parallel with LARP updating work, ADB allowed the construction in LAR free areas based on due diligence reports cleared in October 2016 and the identified LAR section were kept on hold to update the RP after completing design review in LAR sections. Accordingly, after completing design review, NHA updated the draft RP into final implementation ready RP. NHA, endorsed updated RP was reviewed and cleared by ADB in May 2017. As per updated RP total 46 DPs are entitled for compensation for their lost assets including structures, trees and other assets located in the ROW. A summary of DPs entitled for compensation by category of impact due to clearance of COI is presented in table 2.1 below.

Table 2.1 Impact type with number of displaced households

S#	Impact Type	Displaced Persons
1	Agricultural Infrastructure (farm boundary walls, well, Hand Pump, Rooms Check Posts etc)	10
2	Shops and Veranda	13
3	Other miscellaneous structures (kiosks, Huts, Cabins, sign board requiring shifting	17
4	Community Rooms (Non Residential)	1
5	Rental Business Operators	4
6	Privately owned Trees	10
7	Community Structures/Mosques	2
8	Public / Government Structures	2
9	Households facing loss of rented in commercial structures	2
10	Impacted Communal Trees <sup>1</sup>	1

### 2.3. RP costs and availability of Funds

6. As per updated RP total RP cost is Rs. **20.035** million released from NHA HQ, which include Rs **16.031** million for delivery of compensation costs against affected assets and entitled allowances and Rs.**4.003** million as RP implementation support cost. Initially, based on draft RP, Rs 9.44 million was released to facilitate the RP updating work and start its implementation of updated RP. Immediate after clearance of final RP remaining RP cost amounting to Rs10.594 million was released and deposited in the project account in June 2017 for ensuring its early implementation.

<sup>1</sup> During updating of RP impacted wild olive trees grown within ROW near Hasuband mouza (RD 28+800 to 37+550) were claimed as communal asset of Marhail (Shirani) tribe which was confirmed by the forest department and local administration and is included in the updated impact inventory.

#### **2.4. LAR institutional Set-up and RP implementation process.**

7. The LAR unit including Resettlement Specialist mobilized by the DCSC is established and project grievance redress committee already operationalized during the monitoring period. Besides, a team of two social mobilizers (one male and one female) is engaged through RP implementation support costs to assist the Resettlement Specialist and LARU in community coordination and consultations. The project grievance redress committee is established and operational. The DPs have been explained on the GRM system available to them. For improved coordination, consultations and DPs participation in the GRM, 3 (2 male & 1 female) Displaced Persons Committees are constituted and functional at village level. Through DPC meetings, the DPs representatives and local notables are being coordinate and engaged in the grievance redress process.

### 3. RP Implementation Progress

8. Immediate after clearance of updated RP by ADB in May 2017, it disclosure was started and the DPs were informed about their impacted assets, entitlements and the process for submission of claim and payment of compensation. Compensation processing and payment scheduled was designed and accordingly compensation cases were processed in three batches to ensure full implementation of RP in a speedy manner and keep a track of implementation progress and make adjustments if required.

#### 3.1. Compensation Payment Progress achieved

9. In total 40 DPs had been paid their entitled compensation during monitoring period in three batches. In Batch -1, compensation cases for **23** DPs were processed and entitled compensation amount of **Rs. 4,519,810/-** was paid in May 2017. This followed payment of compensation for 11 DPs in June and 6 DPs in July 2017 in batch-2 and batch-3 and compensation amount Rs. 8,180,864 was disbursed. Thus out of total payable compensation amount Rs. 16,031,894 for 46 DPs, compensation amount **Rs. 12,700,674/-** (79%) has been paid to **40** DPs (87%). The efforts are in progress to ensure the DPs having administrative issues or those went out of project area are paid as and when they are available to receive compensation. On payment of compensation paid DPs were advised to clear the ROW by removing their assets to facilitate execution of project works. The lists of DPs compensated as Batches – 1, 2 and 3 including signatures/thumb impressions of DPs and Pictures presenting disbursement process are attached as **Annex I**. The breakup of payment disbursement detail is shown in table 3.1 below.

Table 3.1 Compensation Payment Status during the reporting Period

S#	Date	Total DPs	Paid DPs	Remainin g DPs	Total unpaid Amount	Amount Disbursed	Balance Amount
1	22.05.2017	46	23	23	16,031,894	4,519,810	11,512,084
2	09.06.2017	23	11	12	11,512,084	2,856,196	8,655,888
3	26.07.2017	12	6	6	8,655,888	5,324,668	3,331,220

10. Achieved progress on compensation payment by close of monitoring report reflect that out of total payable compensation amount Rs. 16,031,894 for 46 DPs, compensation amount Rs. 12,700,674/- (79%) has been paid to 40 DPs (87%). The payment process for remaining 6 DPs (13%) including 3 DPs facing loss of their private assets and 3 government/community owned assets ( one mosque which is avoided and 2 security check posts) is ongoing and compensation amount Rs. 3,331,220 (21%) is available in project account. The table below updated payment status as of 31 July 2017. Table 3.1.2 Compensation Payment Current Status

S#	No of Total DPs	Paid DPs	Remaining DPs	Govt / community assets	Total Amount	Paid Amount	Remaining Amount
1	46	40	3	2	20,035,083	12,700,674	3,331,220

#### 3.2. Sections where Compensation is fully Paid or impacts are avoided

11. During the reporting months the LARP implementation process was continued and the payable 40 DPs were paid their entitled compensation. After payment of compensation the DPs were advised to remove their assets for clearing the construction limits. In cases where DPs requested for uprooting of trees by use of machinery, they were facilitated in removing trees through machinery provided by the contractor and salvage material was

allowed to the DPs. The handing over of salvage material to DPs was properly documented by the project team.

12. Meanwhile, one mosque (community structure) located in Sangar Bazar (RD 54+850) moza Norask has been avoided through making design adjustment at site. The community have been informed and clarified about the design adjustments made to avoid impacts on the mosque and assured about compensation under LARP provisions in case if any part of avoided asset is affected during execution of construction works. Consensus statements duly signed by the DPs confirming their no objection to the construction activities at site have been recorded **Annex-III**. The LAR sections cleared through full payment of compensation and by avoiding impact to one community structure (mosque) in Sangar Bazar are reported in table 3.3 below.

Table. 3.2: Shows below the Area Cleared by Cheques.

LOT - 1			LOT - 2		
S#	Compensation paid LAR sections	Km	S#	Compensation paid LAR sections	Km
1	5+800 – 5+900	0.1	1	51+500-51+800	0.3
2	7+600 – 7+750	0.150	2	54+800 – 55+100	0.3
3	9+400 – 13+550	4.15			
4	22+200 – 22+300	0.1 Graveyard			
5	29+600 – 29+675	0.075			
6	37+100 – 37+850	0.75			
7	45+000 – 45+500	0.5			
	Total	<b>5.825Km</b>		Total	<b>0.6 Km</b>
Area of Graveyard has been cleared in design review by squeezing construction limit					

13. The table above represent that the RP has been implemented in **5.825 Km** out of 5.95 Km of withheld LAR sections in Lot-1 and **0.6 Km** of withheld LAR area is cleared in Lot-2 in the reporting months. Based on achieved progress a linear plan is attached as Annex-II showing sections where LAR implementation is completed (green), the sections where RP implementation is still ongoing (red) and LAR free sections (white). Thus upon acceptance of the IMR by ADB, the reported clear areas can be allowed and handed over to contractor for construction. .

### 3.3. Sections where Compensation Payment is under process

14. Although after payment of compensation most of the withheld areas are cleared in lot-1 and lot-2, but the payment for 6 DPs including 3 private assets owners, 2 government departments (affected security check posts) and a mosques (impacts avoided) is still pending. The main reason for pending payments to 3 DPs include assets owner ship dispute for one DP and other 2 DPs were not available in project corridor. The efforts to resolve the dispute and locate DPs are in progress with the assistance of the DPCs and it is expected that the DPs could be approached and paid by October 2017. For government owned security check posts, the security agencies (FC and Levis) are being coordinated for shifting of check posts out of the construction limits. Efforts will be ensured to convince the security agencies to relocate their posts out of COI at their own and if required by them the compensation will be provided as per RP provisions by October 2017. Due to unpaid assets in Lot-01 total **0.125 Km** area is not cleared yet. Table 3.3 below shows the remaining LAR area that are shown as red in the liner plan attached as annexure –II.



Table. 3.4: Shows the Area under LARP.

<b>Over All Status Un Paid LAR Sections</b>							
<b>Un Paid Private and Government Owned Structures</b>							
<b>LOT - 1</b>				<b>LOT - 2</b>			
<b>S#</b>	<b>LAR sections</b>		<b>Kms</b>	<b>S#</b>	<b>LAR sections</b>		<b>Km</b>
1	13+550	13+600	0.050		-	-	-
2	29+675	29+700	0.025		-	-	-
3	37+850	37+900	0.05		-	-	-
		<b>Total</b>	<b>0.125 Km</b>		-	-	-

#### **4. RP disclosure, Consultations, and Grievance Redress.**

15. Immediate after clearance of RP by ADB, the DPs were coordinated to disclose RP provisions and compensation claim notices were delivered at their door steps. Meanwhile, the DPs were clarified on compensation payment mechanism, grievance redress system available to them and were mobilized and supported to submit their compensation claims. The DPs lacking bank accounts were informed payment through their nominated special attorneys having bank accounts and were facilitated to provide the requisite documents including power of attorney in the name of their relative for processing of their claims. For effective coordination the DPs were guided and supported to constitute the displaced persons committee by nominating their representatives. Accordingly the 3 DPCs (2 male and 1 female) constituted by the DPs and were notified by the PMU during the monitoring period. The Sections below explain community consultations and grievance redress progress achieved through participation of the DPCs.

##### **4.1. Public Consultations/Meetings**

16. Besides approaching DPs individually to deliver notices for claiming compensation, structured public consultations were arranged through the DPCs at different locations of the project to ensure the involvement and participation of project DPs and local community. During the consultation process, resettlement specialist and his team discussed the issues with DPs and community, explained project design and provided information to the DPs regarding resettlement impacts, compensation payment process and mechanism for recording and redress of grievances. The DPs concerns on payment of compensation through bank accounts were responded and they were explained that the compensation will be paid through cross cheques and were advised to open and share their bank accounts for processing of their claims. For DPs lacking bank accounts or those unwilling to open accounts due to small compensation amounts, delivery of compensation through DP's nominated special attorney was also explained during consultation meetings. During reported period, 2 consultation meetings of male DPCs has been conducted (1 in Lot-I and 1 in Lot-II) and 1 meeting of female DPCs were conducted in Lot-1. Minutes of DPC meetings (male and female) were recorded and are attached as **Annex IV**.

##### **4.2. Grievance Recording and Redress**

17. Immediate after start of RP implementation, the DPs started approaching the project GRM for raising their concerns about impacts assessment, compensation payment and construction related issues. During the reporting months, 15 applications were received to GRC regarding assessment of trees, structures and land etc. All applications have been properly registered in Grievance register. Out of total 15 applications, 7 were related to land compensation, while the remaining 8 were about compensation of trees and structures. After reviewing 7 complaints about land compensation, the project LAR team informed DPs that the NHA owned ROW as per decision of Government of Balochistan is 110 ft in urban sections and 220 ft in rural areas. The same is confirmed by commissioner Zhob division and SMBR. It was also explained that project impacts will be limited to the construction limits only and the assets located within construction limits will be compensated as per RP prepared for the project and ADB's safeguards policy.

18. Meanwhile, GRC reviewed the 8 complaints/applications and advised resettlement team to verify and assess the claimed loss of trees and structures and conduct consultations with the complainants and the local notables to address the concerns raised by the aggrieved DPs. In this regards, the resettlement specialist assisted by social mobilizers is coordinating with the DPs and the DPC members in the area to verify and assess the impacts if any. The Assessment work will be completed in August and accordingly the GRC will convene its meetings in the project area to resolve the issues pending 8 complaints during next monitoring period. Tables below shows the overall status of grievances recorded and redressed during the reporting months.

Table. 6.1: GRC Complaints Recorded

Over All Status										
S.N	District	Type of Grievance			Total Complaints	Resolved	Out Standin g/ Bogus	Status of Complaints		Remarks
		May 2017	June 2017	July 2017						
1	Zhob and Sherani	5	3	7	15	Payment Regarding Land, Trees, and Structure etc.	7+8= 15	7 Resolved	8 pending	7 DPs claiming land compensation informed on ROW limits.  8 complaints about impact assessment are being verified.

## 5. Conclusion and Recommendations

19. The RP implementation progress achieved during this monitoring period (May-July 2017) illustrate that out of 46 unpaid DPs in withheld LAR sections 40 DP (87%) have been fully paid and an amount Rs 12.701/- million (79%) is disbursed on account of payable compensation. The remaining balance compensation amount Rs. 3.331 million (21%) is due for unpaid 6 DPs (13%). Out of withheld 5.95 KM LAR section in Lot-01, 5.825 Km LAR sections are cleared either through payment of compensation or by avoiding the impacts on one grave yard. While in Lot 02 0.6 Km withheld LAR sections are cleared through payment of compensation and by avoiding impacts to one mosque in Sangar urban section (RD 54+850).

20. The left over unpaid 6 DPs include 2 government security agencies, 3 DPs having legal and administrative impediments (i.e asset ownership dispute for one DP and 2 are not available in project area) and one mosque that are avoided through design adjustment. Total unpaid compensation amount Rs. 3.331 million (10.6%) is available in project account to compensate unpaid assets. Due to unpaid compensation to 6 DPs with impediments and unpaid government assets 0.125 Km area in Lot-1 is still under LAR impacts.

21. Institutional set-up for delivery of unpaid compensation, management of emerging LAR issues and redress of grievances is in place and operational. However, for delivery of pending compensation, improved consultation and early resolution of grievances following actions will be ensured during next monitoring period:









- Three unpaid DPs will be followed and facilitated to resolve their issues to ensure delivery of compensation as and when they come up after resolving their disputes. Meanwhile the mechanism for relocation of government assets (security check posts) will be sorted out with the two security agencies in September 2017 and if required they will be compensated under RP provisions by October 2017.
- The site verification and assessments of unanticipated impacts and other emerging LAR issues will be completed and presented in next GRC meetings to be scheduled in September 2017 for decision and resolving grievances on construction related emerging LAR issues.
- The community consultation, participation and information disclosure at village level will be improved through increased frequency of DPC meetings. The project based GRM, its roles and responsibilities will be clarified to the communities. The project GRC will convene its meetings regularly to review and redress grievance in a timely manner. All consultation and GRC meetings will be recoded and meeting records will be maintained.

22. Based on achieved progress it can be safely concluded that the RP implementation is substantially completed in most of the LAR sections in Lot-01 and is fully completed in withheld LAR section in Lot- 02 as presented in table 3.3. In Lot-01, only unpaid 0.125 Km section scattered at three locations as presented in table 3.4 is due to non-availability of DPs and pending payment for security check posts of government agencies. Therefore it is recommended that ADB may be requested to consider allowing construction works in all withheld LAR section of Lot-01 and Lot-02, meanwhile the efforts will be ensured to deliver compensation to unpaid.







**Batch - I**

Zhob - Mughal Kot Road Project N-50

**Detailed Summary of Compensation Disbursement to Project Affectees**

S#	Moza	Name & F/Name of AF	ZM S. No	Amount	Name of Attorney	Amount Received	Cheque No	Date	Sign/Thumb
1	Hassanzai	Gulab Khan s/o Lal Baig	1	131,868	Gulab Khan s/o Lal Baig	131,868	2809/338	22.05.2017	
2	Hassanzai	Sher Hassan, Malik Khalid Hassan s/o Malik Gul Hassan	2,2/1	50,000	Malik Khalid Hassan s/o Malik Gul Hassan	50,000	2809/339	22.05.2017	
3	Takkai	M Hashim s/o Murad Khan	4	287,744	M Hashim s/o Murad Khan	287,744	2809/340	22.05.2017	 
4	Takkai	M. Nawaz s/o Baz Khan	6	18,594	M. Nawaz s/o Baz Khan	18,594	2809/341	22.05.2017	 
5	Takkai	H. Khudaiddad Babar s/o Sudaman Shah (Harnoor) Hayat Shah, M. Shah, M. Sadeeq s/o Khudaiddad	11	261,360	Hayat Shah s/o Khudaiddad Babar	261,360	2809/342	22.05.2017	 

6	Killi Kamal	Mehmood Khan s/o Ibrahim Khan (Forest)	12	106,920	Mehmood Khan s/o Ibrahim Khan (Forest)	106,920	2809/344	22.05.2017	
	Parvezaan	Wali. M s/o Sultan Shah	15	47,520	Wali. M s/o Sultan Shah	47,520	2809/345	22.05.2017	
7	Parvezaan	Khaliqdad s/o Zabto Khan	17	71,874	Khaliqdad s/o Zabto Khan	71,874	2809/346	22.05.2017	
8	Parvezaan	Darya Khan s/o Zabto Khan	16	123,716	Darya Khan s/o Zabto Khan	123,716	2809/347	22.05.2017	
9	Parvezaan	Karimdad s/o Zabto Khan	18	19,800	Karimdad s/o Zabto Khan	19,800	2809/348	22.05.2017	
10	Asoband	Allauddin s/o Umar Daraz	22	18,594	<del>LODIN</del> Allauddin s/o Umar Daraz	18,594	<del>2809/349</del> 2809/350	22.05.2017 9-6-17	
11	Asoband	Noor. M s/o Jalal Alias Baran	27	18,594	Noor. M s/o Jalal Alias Baran	18,594	2809/350	22.05.2017	

12	Asoband	Kashmeer s/o Rab Nawaz	28	18,594	Kashmeer s/o Rab Nawaz	18,594	28304651	22.05.2017	
13	Sar-e-Toi	M. Amin s/o Sardar Khan	31	61,114	M. Amin s/o Sardar Khan	61,114	28304652	22.05.2017	
14	Sar-e-Toi	Nemat Khan s/o Jalal Khan (Hotel)	33	33,594	Nemat Khan s/o Jalal Khan (Hotel)	33,594	28304653	22.05.2017	
15	Khaorina	Abdul Rauf s/o Sanzar	30	228,096	Atta, M s/o Abdul Rauf	636,768	28304654	22.05.2017	
		M. Hanif s/o Sanzar	35	171,072					
		Zardad s/o Allahdad	39	237,600					
16	L'Wara	Abdul Qaim s/o Abdullah Khan	40	104,940	Abdul Qaim s/o Abdullah Khan	104,940	28304655	22.05.2017	
17	Narosak	M. Din s/o Khairuddin	42	213,840	M. Din s/o Khairuddin	213,840	28304656	22.05.2017	

*Handwritten signatures and marks are present below the table, including a large signature on the left and a circular stamp on the right.*





18	Narosak	Bakht. M s/o Tarakai	43	18,594	Bakht. M s/o Tarakai	18,594	28304657	22.05.2017	1st
19	Narosak	Bahramdin (Alias) Madi s/o Kabir	44	18,594	Bahramdin (Alias) Madi s/o Kabir	18,594	28304658	22.05.2017	
20	Narosak	Din. M s/o Faiz. M	46	18,594	Din. M s/o Faiz. M	18,594	28304659	22.05.2017	
21	Narosak	Nasibullah (Alias) Sargai s/o Habibullah Khan	46/1	18,594	Nasibullah (Alias) Sargai s/o Habibullah Khan	18,594	28304660	22.05.2017	
22	Asoband	Mushtarika (Asoband)	19/2	2,220,000	Ameer Shah s/o Malik Sanak	2,220,000	28304661	22.05.2017	
23				4,519,810	<b>Total</b>	4,519,810			






**Batch - 2**

Zhob - Mughal Kot Road Project N-50


**Detailed Summary of Compensation Disbursement to Project Affectees**

S#	Moza	Name & F/Name of AF	ZM S. No	Amount	Name of Attorney	Amount Received	Cheque No	Date	Sign/Thumb
1	Sangar	Umar Hayat s/o Khan Meer	45	154,688	Umar Hayat s/o Khan Meer	154,688			
2	Manikha	Muhammad (Khan) Marak s/o Tameez Khan (Hawak) Ayub Khan, Gazar Khan, Akmal Mahal, Spinar Khan, Narmadakh s/o Mumraiz Khan	34	331,056	Spinzar Khan s/o Mumraiz Khan	331,056			 <i>Signature</i>
3	Hassanzai	Ajmal (Juvenile) s/o M. Ayub (via Brother) Moladad	7	23,594	Moladad s/o M. Ayub	23,594			 <i>Signature</i>
4	Sangar	Paing s/o Gul Baran	36	187,440	Sardar Khan s/o Juma Khan	187,440			



5	Sangar	Abdul Rasheed s/o Khudai Nazar	37 ✓	117,096	Mir Qalam s/o Khudai Nazar	117,096			
6	Hassanzai	Abdul Nasir s/o Abdul Rehman	3 ✓	515,860	Abdul Nasir s/o Abdul Rehman	515,860			
7	Asoband	Nazar. M s/o Abdul	29 ✓	18,594	Kashmir s/o Rab Nawaz	186,462			
8	Asoband	Khaj. M s/o Dad. M	25 ✓	18,594					
9	Asoband	Dunya Khan s/o Painda	21 ✓	18,594					
10	Asoband	Ahsan. M s/o Jalal Khan	24 ✓	130,680					
11	Asoband	Mushtarka	19 ✓	1,340,000	Ameer Shah s/o Sanak	1,340,000			
10				<b>Total</b>	8	2,856,196			

11 total



**Batch - 3**


Zheh - Mughal Kot Road Project N-50


**Detailed Summary of Compensation Disbursement to Project Affectees**

S#	Moza	Name & F/Name of AF	ZM S. No	Amount	Name of Attorney	Amount Received	Cheque No	Date	Sign/Thumb
1	Takai	Saleh Muhammad S/O Baz Khan	5	242,848	Saleh Muhammad S/O Baz Khan	242,848			
2	Takai	Muhammad Ayaz S/O Masho	8	19,810	Muhammad Ayaz S/O Masho	19,810			
3	Takkai	Ibrahim Khalil, Muhammad Bahim S/O Ameer Khan (Yahya Khan)	9, 944	110,880	Ibrahim Khalil S/O Ameer Khan (Yahya Khan)	110,880			
4	Takkai	Muhammad Ali S/O Hyder Khan	10	44,674	Muhammad Ali S/O Hyder Khan	44,674			
5	Asoband	Manjid Ada Asoband Core (Taker Hefia Kashmir S/O Rab Nawaz)	23	389,000	Kashmeer s/o Rab Nawaz (Chairman Committee)	389,000			

6	Sar-e-Toi	H Ameer Muhammad S/O Muhammad Raman	32	327,456	Aziz Ur Rehman S/O Ameer Muhammad	327,456			
7	Asoband	Mushtarika (Asoband)	19(1)	2,290,000	Ameer Shah s/o Malik Sanak (Chairman Committee)	2,290,000			
8	Sar-e-Toi	Mushtarika (Sari e-Toi Kamazai)	19(3)	1,550,000	Ameer Shah s/o Malik Sanak (Chairman Committee)	1,550,000			
9	Var Ghari	Mushtarika (VarGhari)	19(4)	350,000	Ameer Shah s/o Malik Sanak (Chairman Committee)	350,000			
6				5,324,668	<b>Total</b>	5,324,668			



LINEAR PLAN		N - 50 Road, Zhob - Mughal Kot Section (81 Km)		(0 + 000 to 49 + 000)		LOT - 1		End Point Sec - 1	
								49 + 000	
		45+500 - 49+000				3.5 KM			
		45+000 - 45+500				0.5 KM			
		37+900 - 45+000				7.1 KM			
		<del>37+850 - 37+900</del>				<del>0.05 KM</del>			
		37+100 - 37+850				0.75 KM			
		29+700 - 37+100				7.4 KM			
		29+675 - 29+700				0.025 KM			
		29+600 - 29+675				0.075			
		22+300 - 29+600				7.3 KM			
		22+200 - 22+300				0.1			
		13+600 - 22+200				8.6 KM			
		<del>13+550 - 13+600</del>				<del>0.05 KM</del>			
		9+400 - 13+550				4.15 KM			
		7+750 - 9+400				1.65 KM			
		7+600 - 7+750				0.150 KM			
		5+900 - 7+600				1.7 KM			
		5+800 - 5+900				0.1 KM			
		2+400 - 5+800				3.4 KM			
		0+000 - 2+400				2.4 KM Deleted			
				Start Point					
				0 + 000					

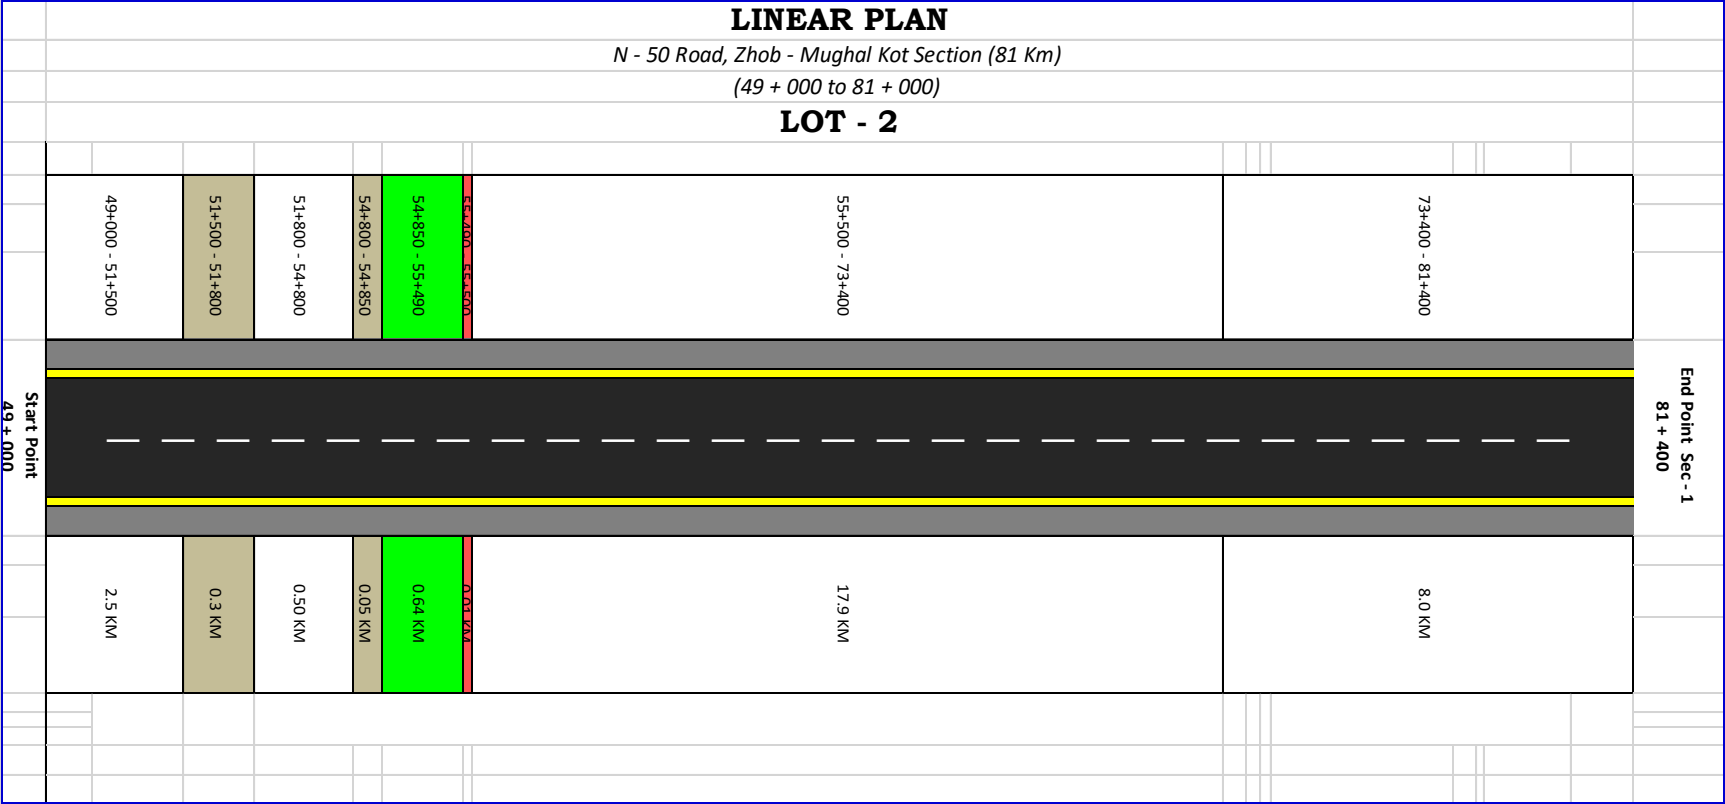

## Statement by the local community on avoiding impacts to Mosques RD 54+850.

اقوام  
مخدومین و اہل خانہ مولوی محمد صوف ولد خان، محمد علی خان، محمد علی خان، وزیر خان ولد ترلائی، میر حسن ولد امیر خان، سکھان  
اڈا ناروگہ، ملکہ اہل جائے کے رہائشی ہیں۔  
اڈا ناروگہ پر روڈ کی رائٹ سائیز پر جانے والے اڈا کی ایک کچھ مسجد شریف موجود ہے۔ جو کہ روڈ  
کے ساتھ جو کہ روڈ پر ایک مسجد شریف کے نام سے منسوب ہے۔ اس کے جتنی ہے۔  
مولوی محمد صوف مذکورہ مسجد شریف کے پیش احرام ہیں۔ اور دیگر حجم مذکورہ ان محمدین، وزیر خان  
میر حسن اس مسجد کے نگران و منتظم ہیں۔  
نوبت کوٹ روڈ پر ایک مسجد کے نام سے منسوب مسجد شریف فیروز آباد، قلاب، محمد علی  
HA کے جانے والے اڈا ناروگہ کے۔ اور روڈ کی تعمیر و توسیع سے متعلق بات چیت  
میں۔ کڑاں لہو بنایا کہ اڈا ناروگہ کی مسجد شریف جو کہ مذکورہ وزیر خان روڈ سے ملتی ہے۔  
جہاں کو شہر سے ملتی ہے۔ اس کے مذکورہ روڈ کی تعمیر سے مذکورہ مسجد شریف کو نقصان پہونے  
سے بچایا جائے۔ اور یہ موقع روڈ کی حدود کی نشاندہی کروانے کے لیے لیا ہے۔ اور  
بنایا ہے کہ مسجد شریف فی روڈ کی تعمیر سے روڈ سے باہر ہے۔ اور تاکہ اگر دوران تعمیر  
مسجد شریف کو کوئی نقصان پہونے تو جبکہ HA کے حقائق کے مطابق مسجد شریف کی آداسی کر گیا۔  
ابرت دیگر حجم اہل خانہ مولوی محمد صوف ولد خان، محمد علی خان، محمد علی خان، وزیر خان ولد ترلائی، میر حسن ولد امیر خان، سکھان  
نے یہ بیان باقی رضا خیری اور رجبیت سے دیا ہے۔ کہ وہ حجم اہل خانہ مولوی محمد صوف ولد خان، محمد علی خان، محمد علی خان، وزیر خان ولد ترلائی، میر حسن ولد امیر خان، سکھان  
دیتے ہیں۔ تاکہ سند رہے۔

میر حسن ولد امیر خان  
وزیر خان ولد ترلائی  
میر حسن ولد امیر خان  
وزیر خان ولد ترلائی  
میر حسن ولد امیر خان  
وزیر خان ولد ترلائی



21-06-2017 مؤرخ

آج مورخہ 10/06/2017 کو ٹروپ جیل کوٹ روڈ پر ویکٹ 50-51 میں ٹروپ میں زنی ٹروپ  
تلی میں مختلف مقامات پر OPC میٹنگ منعقد کی گئی۔ جس میں تجربہ دہل مسائل پر  
متاثرین سے بات چیت ہوئی۔ ان کے مسائل کو غور سے سنا گیا۔ اور مذکورہ بیانے  
نئے مسائل سے متعلق ان کی رہنمائی کی گئی۔ اور ناجائز خطابات سے متعلق ان  
کو سنجھا گیا۔ جس سے وہ مطمئن ہوئے۔

نہایت زبرداری و حیا میں روڈ کی قعر و تہیہ میں تاثرِ حیا کی حیاتہ اراچی کے معاوضہ سے متعلق معمولات گئے۔

نیز۔ معاشرہ و مہندرانے روڈ کی تعمیر و سہرائی روڈ سے اپنی آمد و  
معاوضہ کے ساتھ ہی متعلق سوالات ہیں۔

نہ جیو، مینا شرن نے روڈ کی پھیرائی کی صہرت میں اپنی اپنی کلی ہائے کو  
 جگے والے راستوں سے متعلق اپنے تحفظات، مآخذ، سارے سارے  
 بڑے۔ مینا شرن نے معاوضہ درخت کے دیوار پائے و دیگر جگہ کی وھوٹی سے  
 حقیقی بھی راتھائی طلب کی۔

سبر فضیلت = زمہ داران کے معاوضہ اراچی سے متعلق ان کو بتایا  
 نیکی کے رخصت NHA اپنے روڈ کی حدود میں رہ کر

of Luther

مذکورہ روڈ کی اب گٹر مشن کر رہا ہے۔ مگر خیر نہ رہیں بنائے گئے ہیں۔  
اس کو گٹر نے عمارت روڈ کی حدود میں تجاوز کر کے درخت و پل لگائے اور  
بنائے ہوئے ہیں۔ مگر وہ روڈ کے تصادم کی نشاندہی کر کے بنائے گئے ہیں  
جس سے وہ خطرہ نہ ہے۔

نمبر ۲: روڈ کی پھرائی سے متعلق بنائے گئے ہیں۔ مگر وہ مذکورہ ایریا  
پہاڑی ہے۔ یہ سائیڈ میز بنانے سے روڈ کو نقصان پہنچ  
سکتا ہے۔ اس میں دہریہ پھرائی ضروری ہے۔ ویسے بھی ایسا  
مذکورہ روڈ پر ایسے۔ اس صورت میں آپ اپنی اس حد تک حل  
روڈ کو روڈ سے دور کر کے تعمیر کریں۔ تو کوئی نقصان نہیں ہے  
نمبر ۳: روڈ کی پھرائی سے متعلق راستوں کی بحالی سے N-50 PD  
سے ملاقات / رابطہ اور حل سے متعلق رائے بنائی گئی

میرے خیر و صحت کے معاوضہ سے متعلق بھی اس کی رائے بنائی  
گئی تھی۔ اور بنائے گئے ہیں۔ اس کو معاوضہ کا کمر اس حد تک دیا  
جائے گا۔ جو متاثرین ہزارت خود معاوضہ لیتا جاسکے۔ تو اس کے  
بے۔ انیا ذاتی سنگ کاٹاؤنگ یونٹ ضروری ہے اگر نہیں ہے تو نوپے  
یا کوئی اپنے کسی بھی یاد مگر شہر دار / دوست کے اکاؤنٹ میں اپنا  
معاوضہ وصول کرنا چاہئے۔ تو وہ اس کو اختیار بنا کر حاصل دے۔  
بھارتی سنگ / شیشیام ہڈی مری ہوئی اور سنگ شہر کا مطلق ہوئے

طالعہ

### Attendance Sheet of DPC Meeting

Date: 21-06-2017 Moza: حسن زئی - تکی LOT: 1

Signature/Thumb

Name & F/Name

[Signature]

نمبر 1 فہر اللہ (RS)

Wadood

نمبر 2 عبدالودود (SM)

[Signature]

نمبر 3 صالح محمد ولد یاز خان

[Thumbprint]

نمبر 4 محمد علی ولد حیدر خان

[Signature]

نمبر 5 عبدالنافع ولد عبدالرحمن

سید اباز

نمبر 6 محمد اباز ولد مشہو

[Thumbprint]

نمبر 7 حوالا دار وید اللوب خانی

راشم خان

نمبر 8 ماہشم خان ولد مراد خان

# APC میٹنگ ٹوب محل کوٹ پر ویکٹ N-50

موضع پرویز الہی - جسوئہ

روز 12-07-2017

آج کا دن 12/07/2017 کو موضع جسوئہ و موضع پرویز الہی محلہ ٹوب محل کوٹ N-50 میں APC میٹنگ منعقد کی گئی۔ وہاں پر موجود زمینداران و کمیٹی شرکا و نمبران نے روڈ کی تعمیر تو میم جوڈ (ADB) کے مالی تعاون سے تعمیر ہو رہی ہے۔ اس تعمیراتی کام کی صورت میں ملحقہ علاقوں کے نقصانات امداد اور روڈ کے فوائد سے متعلق کئی عام بات چیت کی گئی۔

شرکا میٹنگ میں روڈ کی تعمیر میں تاخیر ہونے والی امداد سے متعلق اپنے خیالات کا اظہار کیا۔ تاخیر روڈ کی تعمیر میں مختلف جگہوں پر خطرناک صورتحال کو سامنے ختم کر کے سیدھا کرنے کی دستبرداری۔ تاخیر سے روڈ کی تعمیر کی صورت میں حادثات سے بچا جائے۔

تاخیر متاثرہ اراچی اور دیوڑ پور جی۔ ایس۔ اور روڈ سے ملحق اپنے کاموں کے متاثر ہونے سے متعلق سوانح کے ہیں۔

ان کے خیالات اور امور غور سے سنئے گئے۔ اور رہنمائی دیا کہ وہ عوامی سطح پر سہولت کیا گیا اور وہ مطمئن رہے۔

میں اس غور کی تعمیل میں ہے۔

نائبہ کمیٹی زمینداران کو بتایا کہ ان کے علاقے

میں مذکور روڈ 5-5-50 کی نمبر الٹائی ترقیاتی بنک (ADB) کے حالی  
تعاون سے چل رہی ہے۔

اگرچہ اس سے متعلق خوف و ہراس بھی نہیں بتایا گیا ہے مگر مذکورہ روڈ حکم 2014 کے  
مقام کے اندر بنا رہا ہے۔ یعنی اسے روڈ کی حدود میں اپ گریڈیشن کر رہا  
ہے۔ اس میں کسی بھی زمیندار کی اراضی کو کوئی نقصان نہیں ہوگا۔  
مزید مذکورہ کی تعمیر سے علاقے کی ترقی جو در تجارت، صحت اور  
آمدورفت سے متعلق بھی بہت زیادہ ہے۔

مزید روڈ کی حدود میں فائنل تصویر جھلی پائے، کیس یا دکان و دیوار وغیرہ  
کے معاوضہ مناسب حکم 2014 کے تحت اس کی ترقیاتی بنک دے سے متعلق بتایا  
گیا ہے۔ اور معاوضہ وصول کرنے کی صورت میں روڈ کی حدود چھانی کرنے  
کے لیے خواہ روڈ صواب کیا جائے۔ اس مذکورہ اصول کے جو روڈ کی حدود میں  
یو جی ٹی تمام چھوٹی اس کے معاوضہ کی وصولی سے متعلق صحیح رہا ہے  
مذرت خود یا مزید اس کا زنی سمجھا گیا ہے۔

دوران شنگ زمیندار شنگ کا لکھی نے سرائی فاول اور اپنی اراضی  
کی میرا لی کی صورت سے متعلق روڈ کوٹ 1 بھی خط لکھا ہے۔ خواہش  
اس بابت 2014 کے 5-5-50 سے مددگار کے لیے کیا گیا ہے۔  
مجاہد الزمینگ اختتام ہزار پوٹی، اور شنگ کا دھنڑا ہے۔


۶-۵-۵۰

**Attendance Sheet of DPC Meeting**

N-70 Q1 : Saifullah - Loralai - Wagum Road Section (120 km)

Date: \_\_\_\_\_ Moza: \_\_\_\_\_ LOT: \_\_\_\_\_

**Signature/Thumb****Name & F/Name**

- |   |                             |
|---|-----------------------------|
|  | فiaz احمد .8                |
| Wadood  | عبد الوود .9                |
| درب خان   | دری خان ولد عبد طوفان .10   |
| کریم داد  | کریم داد ولد عبد طوفان .11  |
| 33  | حالی محمد ولد سلطان خان .12 |
| حافظ شير  | حافظ اکبر ولد رب نواز .13   |
| MAHMOOD KHAN  | محمد خان ولد ابراهيم .14    |
| خواجہ محمد  | خواجہ محمد ولد داد محمد .15 |

# bpc میٹنگ ٹروپ چل کوٹ روڈ پروجیکٹ N-50

خواجہ 2017-06-06-21

خواجہ حسن زئی - تلمی

آپ کو 2017/06/06 کو ٹروپ چل کوٹ روڈ پروجیکٹ N-50 سے ملتی خواجہ حسن زئی خواجہ حسن تلمی میں دو مختلف مقامات پر خواتین سے میٹنگ منعقد کی گئی ہے جس میں دوران میٹنگ خواتین کو انتہائی ترقیاتی بنک کے تعاون سے بنائے جانے والے روڈ N-50 ٹروپ چل کوٹ کی افادیت بارے میں بتایا گیا ہے جسٹس میں شریک کے مہر سہاوردت کے بھی جواب دیئے گئے ہیں۔ میٹنگ کی تفصیل ذیل ہے۔

1۔ مذکورہ زیر التعمیر روڈ سے ملتی خواجہ حسن زئی خواجہ حسن تلمی کے دو مکمل شدہ علاقہ دیہات / کھلی پائے موجود ہیں۔ مذکورہ دیہات اکثر کچی آبادی یعنی پتھر اور مٹی گارے سے بھیجی ہوئی ہے۔ مذکورہ دیہات پائے میں انتہائی ترقی کے پائے پر آگئی اور محلہ تک درختے اور لڑکیوں کے مکانات موجود ہیں۔ وہیں کے عہدہ انتہائی طبی عہدہ 50 سالہ کے لیے خواجہ حسن زئی کھلی میں ڈ سپری موجود ہے۔ دلچسپ طور پر مذکورہ گاؤں میں روڈ N-50 سے لڑکیاں سے 1/2 کلومیٹر کے فاصلے پر واقع ہیں

2۔ مذکورہ باہر عزین کے تحت خواتین سے میٹنگ کے دوران خواتین کو زیر التعمیر روڈ کی افادیت بارے میں بتایا گیا ہے کہ مذکورہ روڈ کی تعمیر سے عہدہ میں ترقی ہوئی گاؤں بار کے وسائل بہاؤں کے۔ شہدہ دکان داری، پتھر و لیمب، سپری اور فروٹ پائے کی بروقت مہارت میں رسائی وغیرہ۔



میں نے صحت کے معاملہ میں بھی بروقت علاج حاصل کے لیے نزدیکی برائے سیکر میں  
رہائی۔ خیر، ایسے بچے جو اتھروئی تعلیم تکمیل تک پہنچتے ہیں۔ ان کے لیے نزدیکی  
برائے سیکر میں تعلیم کا حصول ضرورہ شامل ہیں۔

③۔ مذکورہ نوڈ کی تعمیر میں متاثر ہونے والے درخت ہائے بلبلہ (دلواریہ)۔ دھان۔ برہم و غیرہ  
الغیر جن چیزوں کے متاثر ہونے کی صورت میں معاوضہ ازارہ نقصان دیکاروباری نقصان  
دیکر انہیں متاثرین کو دیے جانے سے متعلق بھی بتایا گیا ہے۔ جس سے وہ خوش ہوئی  
اور بتایا کہ عدالت کی ترقی کے ساتھ ساتھ جو نوڈ کی تعمیر کے حوالے سے ہوئی۔ وہی نوڈ  
جو متاثرین کو معاوضہ کی ادائیگی کی جا رہی ہے۔ یہ بھی ایک قسم کی ریس فریب اور سیمانہ  
عدالت کی آمد آمد بھی ہے۔ خیر معاوضہ کی ادائیگی کی صورت بہت سارے لوگ رہے  
یہ بہترین نوڈ مار بھرا کر سکتے ہیں۔

4۔ خیر حشر میں متاثرین خواہش سے تعلیم۔ ملازمت اور گھرداری سے متعلق سواہت کے لئے  
توجہ دینے بتایا ہے کہ ہمارا علاقہ جو قبائلی ہے۔ یہاں پر وہ کی بہت حرکت پانہری ہے  
ہزاروں بنا ہر نوڈوں خواہش کو دستی تعلیم اور اتھروئی دنیاوی تعلیم دی جاتی ہے۔ جس  
آئے تعلیم نہیں دی جاتی۔ عدالت کے خیر فائدے جن کے وسائل ضبط ہیں۔ وہ اپنے بچوں کی  
تعلیم کے لیے کچھ مختلف نزدیکی برائے شہر میں ملے جاتے ہیں۔ خیر بتایا کہ ریس عدالت میں  
لوگوں کے سکول اکی تعلیم ٹول تک پہنچتی ہے۔

زیادہ خواہش گھرداری کرتی ہیں۔ ریس خیر ایک خواہش حکم بہبود رباری میں بھی عارضی طور  
پر کرتی ہیں۔

⑤۔ خیر متاثرین خواہش میں سے خیر نے شہر سوال معاوضہ کی ادائیگی اور متاثرہ اشیاء سے  
متعلق کیا۔ تو انہیں ریس سے متعلق بھی بتایا گیا ہے جس سے وہ مطمئن ہو گئے ہیں۔ بلکہ ازارہ  
میں 2:45 پر اختتام پذیر ہوئی ہے۔

شرکا OPE میٹنگ شہر بھفل کوٹ روڈ 50-N

موصوفہ حسن زئی۔ موصوفہ تکی

خوش 9/1/06  
لوٹ بھرا



