



Malawi Floods Emergency Recovery (P154803)

AFRICA | Malawi | Social, Urban, Rural and Resilience Global Practice Global Practice | IBRD/IDA | Investment Project Financing | FY 2015 | Seq No: 3 | ARCHIVED on 14-Jun-2016 | ISR23428 |

Implementing Agencies: Government of Malawi

Key Dates

Key Project Dates

Bank Approval Date:07-May-2015 Planned Mid Term Review Date:31-Jul-2017 Original Closing Date:31-Dec-2019 Effectiveness Date:20-Aug-2015 Actual Mid-Term Review Date:--Revised Closing Date:31-Dec-2019

Project Development Objectives

Project Development Objective (from Project Appraisal Document) The Project Development Objective is to "sustainably restore agricultural livelihoods, reconstruct critical public infrastructure to improved standards in the flood-affected districts, and improve the Government of Malawi's disaster response and recovery capacities".

Has the Project Development Objective been changed since Board Approval of the Project Objective? No

Components

 Name

 Livelihoods Restoration and Food Security:(Cost \$29.00 M)

 Infrastructure Rehabilitation and Reconstruction:(Cost \$43.00 M)

 Promoting Disaster Resilience:(Cost \$4.00 M)

 Program Management:(Cost \$4.00 M)

Overall Ratings

Name	Previous Rating	Current Rating
Progress towards achievement of PDO	Satisfactory	Satisfactory
Overall Implementation Progress (IP)	Satisfactory	Satisfactory
Overall Risk Rating	Substantial	Substantial



Implementation Status and Key Decisions

A second Implementation Support Mission for the Malawi Floods Emergency Recovery Project (MFERP) took place in Lilongwe from April 9-19, 2016. The mission observed that the project is beginning to achieve its intended developmental impact and is making significant progress towards meeting its financial and physical targets. Feedback provided and key next steps agreed during the December 2015 mission are being implemented across the various project components. Significant progress was also achieved to complete PIU staffing.

Risks

Systematic Operations Risk-rating Tool

Risk Category	Rating at Approval	Previous Rating	Current Rating
Political and Governance	 Substantial 	 Substantial 	Substantial
Macroeconomic	Substantial	Substantial	 Substantial
Sector Strategies and Policies	Moderate	Moderate	Moderate
Technical Design of Project or Program	Moderate	Moderate	Moderate
Institutional Capacity for Implementation and Sustainability	 Substantial 	 Substantial 	Substantial
Fiduciary	Substantial	Substantial	Substantial
Environment and Social	Moderate	Moderate	Moderate
Stakeholders	Moderate	Moderate	Moderate
Other			
Overall	 Substantial 	 Substantial 	 Substantial

Results

Project Development Objective Indicators

▶ Number of people with sustainably restored agricultural livelihoods under the IFA program (Number, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00		35794.00	180000.00
Date			19-Apr-2016	15-Jun-2019



Number of schools with services fully restored (Number, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	82.00
Date			19-Apr-2016	15-Jun-2019

▶ Number of health facilities reconstructed with services fully restored (Number, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	2.00
Date			19-Apr-2016	15-Jun-2019

▶ Number of kilometers of roads reconstructed to improved standards and with services restored (Kilometers, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	15.00	90.00
Date			23-May-2016	15-Jun-2019

► Institutionalization/adoption of PDNA methodology, and institutional and financing framework for recovery (Yes/No, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	Ν	Ν	Ν	Y
Date		21-Dec-2015	19-Apr-2016	15-Jun-2019

▶ Institutionalization/adoption of disaster resilient designs for schools, health facilities and roads (Yes/No, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	Ν	Ν	Ν	Y



Date	 21-Dec-2015	19-Apr-2016	15-Jun-2019

Direct project beneficiaries (Number, Core)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	35794.00	500000.00
Date			19-Apr-2016	15-Jun-2019

▲ Female beneficiaries (Percentage, Core Supplement)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	53.00	50.00

Overall Comments

Intermediate Results Indicators

▶ Number of individuals receiving IFA vouchers (Number, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	35794.00	180000.00
Date			19-Apr-2016	15-Jun-2019



► Quantity of maize purchased (Metric ton, Custom)						
	Baseline	Actual (Previous)	Actual (Current)	End Target		
Value	0.00		36942.00	50000.00		
Date			19-Apr-2016	15-Jun-2019		

Quantity of maize released (Metric ton, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	30408.66	36942.00	50000.00
Date		21-Dec-2015	19-Apr-2016	15-Jun-2018

► Number of SGR beneficiaries (Number, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00		329000.00	500000.00
Date			21-Dec-2015	15-Jun-2019

► Roads rehabilitated, Rural (Kilometers, Core)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	15.00	90.00
Date			23-May-2016	15-Jun-2019



Date

15-Jun-2019

19-Apr-2016

Number of additional classrooms built or rehabilitated at the primary level resulting from project interventions. (Number, Core) Baseline Actual (Previous) Actual (Current) End Target Value 0.00 0.00 0.00 82.00

► Health facilities constructed, renovated, and/or equipped (number) (Number, Core)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	2.00
Date			19-Apr-2016	15-Jun-2019

▶ Improved Damage Assessment Guidelines, Templates and SOPs for Damage Assessment (Yes/No, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	Ν	Ν	Ν	Υ
Date			19-Apr-2016	15-Jun-2019

► DoDMA and Civil Protection Committees trained in Emergency Response (Number, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	3.00	15.00
Date			19-Apr-2016	15-Jun-2019



Disaster resilient designs for the education, health and roads sectors (Yes/No, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	Ν	Ν	Ν	Y
Date			19-Apr-2016	15-Jun-2019

Overall Comments

PIU awaits updated figures from WFP on "Number of SGR beneficiaries." In the meantime, the Dec. 2015 figure remains.

Data on Financial Performance

Disbursements (by loan)


Project	Loan/Credit/TF	Status	Currency	Original	Revised	Cancelled	Disbursed	Undisbursed	Disbursed
P154803	IDA-56360	Effective	XDR	29.00	29.00	0.00	0.00	29.00	0%
P154803	IDA-D0580	Effective	XDR	29.00	29.00	0.00	18.62	10.38	64%

Key Dates (by loan)

Project	Loan/Credit/TF	Status	Approval Date	Signing Date	Effectiveness Date	Orig. Closing Date	Rev. Closing Date
P154803	IDA-56360	Effective	07-May-2015	03-Jun-2015	20-Aug-2015	31-Dec-2019	31-Dec-2019
P154803	IDA-D0580	Effective	07-May-2015	03-Jun-2015	20-Aug-2015	31-Dec-2019	31-Dec-2019

Cumulative Disbursements

The World Bank Malawi Floods Emergency Recovery (P154803)

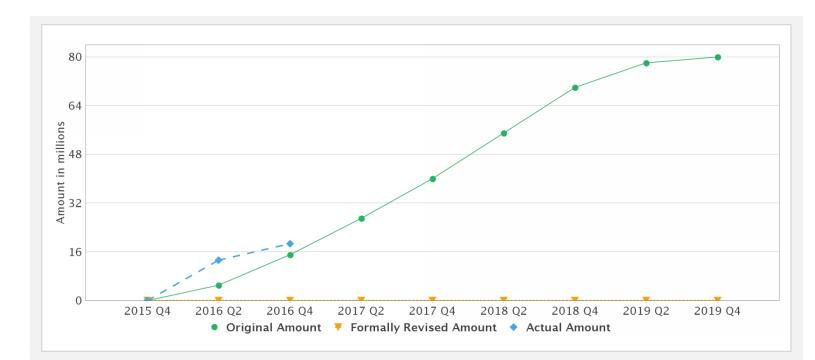

Restructuring History

There has been no restructuring to date.

Related Project(s)

There are no related projects.
