



Water Management Improvement Project (P040712)

SOUTH ASIA | Bangladesh | Agriculture and Rural Development Global Practice |
IBRD/IDA | Specific Investment Loan | FY 2008 | Seq No: 16 | ARCHIVED on 16-Jun-2015 | ISR19707 |

Implementing Agencies:

Key Dates

Key Project Dates

Board Approval date:18-Sep-2007

Effectiveness Date:26-Nov-2007

Planned Mid Term Review Date:--

Actual Mid-Term Review Date:02-May-2011

Original Closing Date:30-Jun-2015

Revised Closing Date:30-Jun-2016

Project Development Objectives

Project Development Objective (from Project Appraisal Document)

The primary Project Development Objective (PDO) is to improve national water resources management by involving the local communities to play an expanded role in all stages of the participatory scheme cycle management. The secondary objective is to enhance institutional performance of the Country's principal water institutions, particularly BWDB and WARPO. This is expected to result in reduced vulnerability and enhanced livelihood opportunities for the beneficiaries, and will also create a favorable environment for improved water resources management.

Has the Project Development Objective been changed since Board Approval of the Project Objective?

Yes

Board Approved Revised Project Development Objective (If project is formally restructured)

The Project Development Objective (PDO) is to improve water resources management by improving infrastructure and institutions through rehabilitating damaged water infrastructure, piloting the role of local communities and enhancing the institutional performance of the Country's principal water institutions, particularly BWDB and WARPO.

Components

Name

System Improvement and Management Transfer (SIMT):(Cost \$10.70 M)

O&M Performance Improvement (OMPI):(Cost \$5.00 M)

Institutional Improvement

(a) BWDB; (b) WARPO; and (c) PCU:(Cost \$10.30 M)

Flood Damage Rehabilitation (FDR) Works:(Cost \$59.00 M)

Overall Ratings

Name	Previous Rating	Current Rating
------	-----------------	----------------



Progress towards achievement of PDO	● Satisfactory	● Satisfactory
Overall Implementation Progress (IP)	● Satisfactory	● Satisfactory
Overall Risk Rating	--	● Moderate

Implementation Status and Key Decisions

The implementation progress remains good since last mission. All agreed actions are completed and additional progress has been achieved under various components. The overall scope of the project is spread in 39 districts of the country and to date the project has achieved the following results:

- 685 km of embankments rehabilitated
- 329 water control structures reconstructed
- 29 km of protective works repaired
- 500,000 households are directly benefitting
- 12 million person-days of employment generated
- 785 Water Management Organizations (WMOs) formed
- 377 WMOs registered under the Chief Water Management (CWM) cell
- 785 WMOs have been provided with training

The rehabilitation of irrigation, drainage and river bank protection infrastructure has improved an area of 800,579 ha, reaching a population of 9.5 million. The Sirajganj Hardpoint (SHP) works are completed. The Flood Damage Rehabilitation (FDR) works are nearly completed.

The irrigation sector reforms initiated under this project are progressing with the devolved O&M of completed schemes through Water Management Organizations (WMOs). To date a total of 785 WMGs and 72 WMAs have been formed in the 67 schemes financed under WMIP. The BWDB is keen to initiate dialogue on future support for strengthening and sustaining the newly formed Water Management Organizations (WMOs) that were supported through the WMIP. By the closure of the current project, the legal registration, training, and joint operations and maintenance (O&M) trial management activities will be completed. However, to ensure WMOs remain functional and engage in visible role of participatory irrigation management, these new structures would require additional support.

The overall disbursements are at 93%. The FM performance of the Water Resources Planning Organization (WARPO) has improved. WARPO has hired a consultant to provide dedicated FM reporting support. The reconciled IUFs are prepared and sent to Bank for review. The overall FM performance rating is maintained as Moderately Satisfactory in this ISR and a review for upgrading this rating will be done at next mission. Overall, the project implementation is on track and the PDO and IP ratings are maintained at Satisfactory.

Risks

Systematic Operations Risk-rating Tool

Risk Category	Rating at Approval	Previous Rating	Current Rating
Political and Governance	--	--	● Low
Macroeconomic	--	--	● Moderate
Sector Strategies and Policies	--	--	● Low
Technical Design of Project or Program	--	--	● Low



Institutional Capacity for Implementation and Sustainability	--	--	● Moderate
Fiduciary	--	--	● Substantial
Environment and Social	--	--	● Moderate
Stakeholders	--	--	● Moderate
Other	--	--	--
Overall	--	--	● Moderate

Results

Project Development Objective Indicators

► A reduction in the level of damage to property and assets that is to the satisfaction of the communities in 60% of completed project schemes (Text, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	BDT 79.9 Billion in total damage, 2007 BDT 4.9 Billion in damages to all embankments and water control structures, 2007 BDT 5559.2 Million in damages in 475 BWDB schemes, 2007 BDT 322.8 Million in damages in 39 WMIP sample project schemes, 2007	60% of completed project schemes	60% of completed project schemes	Less than baseline in 60% of completed project schemes
Date	01-Jul-2011	19-Nov-2014	06-Jun-2015	30-Jun-2016

► About 60% reduction in crop area damaged by floods/cyclones in 60% of project schemes starting 2014-15 (Text, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	Total of 186,883 ha fully damaged and 498,645 ha partially damaged, 2007 27,100 ha damaged in 23 WMIP sample project schemes, 2007	60% of completed project schemes	60% of completed project schemes	60% lesser than baseline in crop area in 60% of completed project schemes
Date	01-Jul-2011	19-Nov-2014	06-Jun-2015	30-Jun-2016



► About 60% of completed project schemes have WMOs functioning in accordance with their roles and responsibilities agreed upon in the management plan (Text, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	22% of WMIP sample project schemes with WMOs	857 WMOs formed in 50% of completed schemes	785 WMOs formed in 100% of completed schemes	WMOs in 60% of completed project schemes
Date	01-Jul-2011	19-Nov-2014	06-Jun-2015	30-Jun-2016

Overall Comments

Intermediate Results Indicators

► Operational water user associations created and/or strengthened (number) (Number, Core)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	857.00	785.00	--
Date	--	19-Nov-2014	06-Jun-2015	30-Jun-2016

► Successful completion of rehabilitation and improvements in 100% of targeted project schemes (Text, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	Not applicable	97% of targeted project schemes completed	100% of targeted project schemes completed	100% of targeted project schemes completed
Date	01-Jul-2011	19-Nov-2014	06-Jun-2015	30-Jun-2016

► Signed agreement between BWDB and WMOs completed in 100% of project schemes (Text, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	NA	50% schemes have WMOs	100% schemes have WMOs	100% of completed project schemes
Date	01-Jul-2011	19-Nov-2014	06-Jun-2015	30-Jun-2016



► Timely completion of need-based O&M assessment and allocation of BWDB's O&M budget for 100% of completed project schemes (Text, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	Compliance to need-based O&M assessment and allocation of BWDB's O&M budget	Need based O&M assessment is yet to be completed	Need based O&M assessment completed	100% of project schemes completed
Date	01-Jul-2011	19-Nov-2014	06-Jun-2015	30-Jun-2016

► Compliance to participatory monitoring system in 100% of completed project schemes (Text, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	WMO compliance to participatory monitoring system	80% of WMOs in completed project schemes	100% of WMOs in completed project schemes	80% of WMOs in completed project schemes
Date	01-Jul-2011	19-Nov-2014	06-Jun-2015	30-Jun-2016

► BWDB's institutional reform plan completed by June 2011 and approved by December 2011 (Text, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	Not applicable	Institutional reform plan completed and approved	Institutional reform plan completed and approved	BWDB's institutional reform plan completed by June 2011 and approved by December 2011
Date	01-Jul-2011	19-Nov-2014	06-Jun-2015	30-Jun-2016

► Following BWDB's approved institutional reform plan, new staffing plan completed and approved by June 2012 (Text, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	Not applicable	New staffing plan completed and approved	New staffing plan completed and approved	HRD plan completed by December 2012
Date	01-Jul-2011	19-Nov-2014	06-Jun-2015	30-Jun-2016



► Following Intermediate Indicator (5) and (6), HRD plan completed by December 2011 (Text, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	NA	HRD plan completed and under implementation	HRD plan completed and under implementation	100% of target
Date	01-Jul-2011	19-Nov-2014	06-Jun-2015	30-Jun-2016

► Updated NWRD database with enhanced data layers completed and disseminated (Text, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	NWRD prepared in 2001 with 421 data layers and currently it consists of 824 data layers.	50% progress reported	50% progress reported	100% completion
Date	31-Mar-2008	19-Nov-2014	06-Jun-2015	30-Jun-2016

► WARPO's institutional reform plan completed by June 2011 and approved by December 2011 (Text, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	Not applicable	Completed	Completed	Completion by December 2011
Date	01-Jul-2011	19-Nov-2014	06-Jun-2015	30-Jun-2016

► Successful completion of rehabilitation and improvement in 100% of target (Text, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	NA	80% of targeted works	98% of targeted works	100% of targeted project schemes completed
Date	01-Jul-2011	19-Nov-2014	06-Jun-2015	30-Jun-2016

Overall Comments

Data on Financial Performance




Disbursements (by loan)

Project	Loan/Credit/TF	Status	Currency	Original	Revised	Cancelled	Disbursed	Undisbursed	Disbursed
P040712	IDA-43590	Effective	USD	102.26	93.77	8.49	86.84	7.37	<div style="width: 93%; background-color: #4CAF50;"></div> 93%
P040712	TF-94800	Closed	USD	20.00	2.65	17.35	2.65	0.00	<div style="width: 100%; background-color: #4CAF50;"></div> 100%

Key Dates (by loan)

Project	Loan/Credit/TF	Status	Approval Date	Signing Date	Effectiveness Date	Orig. Closing Date	Rev. Closing Date
P040712	IDA-43590	Effective	18-Sep-2007	08-Oct-2007	26-Nov-2007	30-Jun-2015	30-Jun-2016
P040712	TF-94800	Closed	08-Oct-2007	08-Oct-2007	26-Nov-2007	30-Jun-2015	06-Aug-2014

Cumulative Disbursements

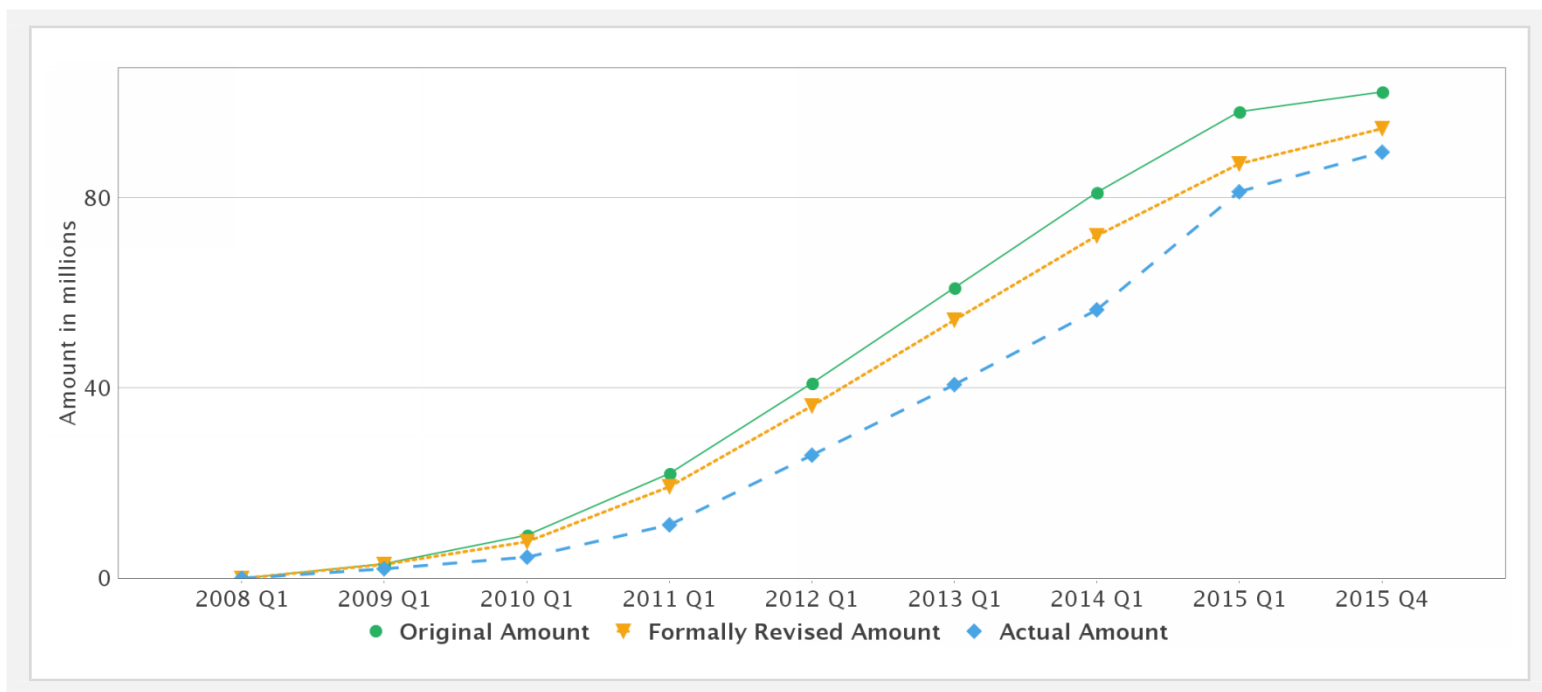

Restructuring History

Level Approved on 15-Jul-2011 ,Level 2 Approved on 05-Mar-2015

Related Project(s)



There are no related projects.
