

# Social Monitoring Report

---

Semiannual Report  
June 2017

## IND: Railway Sector Investment Program

Prepared by the Ministry of Railways, Government of India for the Asian Development Bank.

This social monitoring report is a document of the borrower. The views expressed herein do not necessarily represent those of ADB's Board of Directors, Management, or staff, and may be preliminary in nature.

In preparing any country program or strategy, financing any project, or by making any designation of or reference to a particular territory or geographic area in this document, the Asian Development Bank does not intend to make any judgments as to the legal or other status of any territory or area."

# **Indian Government Ministry of Railways Asian Development Bank**

**Multitranche Financing Facility No. 0060-IND  
Loans No. 2793-IND, 3108-IND  
Railway Sector Investment Program  
Track Doubling and Electrification on Critical Routes**


**Resettlement and Rehabilitation Implementation Status  
Semi Annual Report October 2016 - March 2017**





**Document Identification**


Project Name :	Railway Sector Investment Program
	ADB MFF no. 0060-IND
	ADB Loans no. 2793-IND, 3108-IND
	Track Doubling and Electrification on Critical Routes
Report Name :	General Consultant Half yearly R&R Report No. 8, March 2017
Reference	R&R_March 2017

**Preparation, Review and Authorisation**

Prepared by :	Dr. Sudesh Kaul	Signature :	
Organisation :	General Consultant		
Position :	Resettlement Expert	Date :	19-05-2017

Checked by :	Prem Narayan Shukla	Signature :	
Organisation :	General Consultant		
Position :	Dy. Team Leader	Date :	22/5/17

Reviewed by :	Ramashray Pandey	Signature :	
Organisation :	RVNL		
Position :	General Manager/Corporate Coordination	Date :	23.5.2017

Approved by :	Vijay Anand	Signature :	
Organisation :	RVNL		
Position :	Director Projects	Date :	26.5.2017

**Revision, Preparation, Review Issue**

Revision	Date	Subject	Prepared by	Reviewed by



## Contents

<b>Executive Summary</b> .....	1
Major events.....	1
<b>1. Background</b> .....	3
<b>2. Current issues</b> .....	5
<b>3. Status</b> .....	7
4.1 Sambalpur–Titlagarh project.....	7
4.2 Raipur–Titlagarh project .....	10
4.3 Daund-Gulbarga project.....	12
4.4 Hospet-Tinaighat project .....	12
4.5 Electrification of Pune-Guntakal project .....	17
4.6 Summary table .....	18
<b>Annexure I: R&amp;R Closuer letter of Agreement for Sambalpur-Titlagarh project</b> .....	29
<b>Annexure II: Compensation of NTH 1st &amp; 2nd Installment for Sambalpur-Titlagarh project</b> .....	30

## Table

Table 1: Project Covenants and Compliance.....	2
Table 2: Detail of Projects .....	3
Table 3: Final summary of subproject impacts Chhattisgarh and Odisha Section .....	11
Table 4: Reasons for additional requirements in HT .....	14
Table 5: Status of land acquisition in HT .....	15
Table 6: Financial status of compensation in HT .....	16
Table 7: Status of land compensation in HT .....	17
Table 8: Status of land Acquisition and Resettlement .....	24
Table 9: Details regarding Rehabilitation and Resettlement.....	28

## Figure

Figure 1: Map of India showing track doubling and electrification projects .....	3
--	---

## Abbreviation

ADB	Asian Development Bank
BPL	Below Poverty Line
CPM	Chief Project Manager
DG	Daund – Gulbarga
DGPS	Differential Global Position System
DM	District Magistrate
DPs	Displaced Persons
EA	Executing Agency
FHH	Female Headed Household
GAD	General Arrangement Drawing
GC	General Consultant
GCC	General Conditions of Contract
GRC	Grievance Redressal Cell
HT	Hospet – Tinaighat
HHs	House Holders
IA	Implementing Agency
India	Indian Government
INR	Indian Rupees
IP	Indigenous People
IPP	Indigenous Peoples Plan
IPPF	Indigenous Peoples Planning Framework
IR	Inception Report
LAO	Land Acquisition Officer
MOR	Ministry of Railways
NEFT	National Electronic Funds Transfer
NGO	Non-Governmental Organisation
NTH	Non-Title Holder
OSRC	Orissa Space Applications Centre
PAP/Aps	Project Affected Persons
PIU	Project Implementation Unit
PG	Pune – Guntakal
PMC	Project Management Consultant
PWD	Public Works Department
RAP	Resettlement Action Plan
RFCTLARR	Right to Fair Compensation and Transparency in Land Acquisition, Rehabilitation and Resettlement Act
R&R	Resettlement and Rehabilitation
RO	Resettlement Officer
RP	Resettlement Plan
RT	Raipur – Titlagarh
RTGS	Real Time Gross Settlement
RVNL	Rail Vikas Nigam Limited

SC	Scheduled Caste
SIA	Social Impact Assessment
SLAO	Special Land Acquisition Officer
ST	Scheduled Tribe
ST	Sambalpur – Titlagarh
TH	Title Holder
USD	United States Dollars

## Executive Summary

The current report is the quarterly Social Safeguard Monitoring Report prepared to comply with the loan covenants covering the period from October to March 2017. As usual, this report covers resettlement and social safeguard monitoring results to comply with the spirit of ADB policy.

Increasingly, social safeguards are being codified in all operations of development agencies, international financial institutions, and national and international decision makers. ADB clarified its safeguard policy in 2009 with the Safeguard Policy Statement (SPS). The development of all project proposals considered for ADB loan funding must be consistent with the SPS and, after approval, must follow through on implementation in a manner that can be verified by regular monitoring.

## Major events

### *Project Covenants and Compliance*

S.N.	Grant Covenants	Status of Compliance
1.	Policy grant covenants and compliance	Complied with
2.	Financial loan covenants and compliance	Complied with
3.	<b>Other project specific covenants:</b>	
3.1	Social Safeguards	<ul style="list-style-type: none"> <li>All social safeguard issues including resettlement etc, have been closely monitored by the RVNL and has been reported by the GC that no further resettlement is needed were compensation to the affected PAPs have been reimbursed.</li> <li>Resettlement has been done with the requirements of the project document.</li> <li>Due Diligence Report to record and ensure compliance with social safeguard measures is being done.</li> </ul>
3.2	Implementation arrangements	<ul style="list-style-type: none"> <li>All required institutions have been duly established and staffed except NGO staff (NGO contract not extended beyond 31/08/2016).</li> <li>Requisites for implementation are largely met.</li> </ul>
3.3	Project selection	Complied with

3.4	Others	<ul style="list-style-type: none"> <li>Most of the covenants mentioned here have been complied with or are in the process of being complied.</li> <li>Preparation of consolidated progress reports quarterly and by annually is being submitted regularly to RVNL.</li> </ul>
-----	--------	---

Table 1: Project Covenants and Compliance

*Status of Critical Actions during this quarter*

Issues	Actions	Responsibility	Status
NGO not mobilized since August 2016	Completion of all pending works immediately and Disbursement of Compensation for the remaning NTH at Raipur	NGO /RVNL	Delayed
Land Acquisition activities by the Revenue Department	Finalization of disbursement of compensation	RVNL/SLAO	In process

**Global progress:**

The calculated global progress of implementation of R&R activities across the various projects at the end of March 2017 is as under:

S. No	Name of Project	Global progress
1.	Doubling of Daund-Gulbarga	100%
2.	Doubling of Hospet-Tinaighat	60%
3.	Doubling of Sambalpur-Titlagarh	50%
4.	Doubling of Raipur-Titlagarh	95%
5.	Electrification of Pune-Guntakal	N/A



## 1. Background

Five Railway projects are financed by the present ADB loans.

S. No	Project Name	Length (in Km.)	Location (State)	Project components
1	Daund-Gulbarga	225	Maharashtra and Karnataka	Doubling
2	Sambalpur-Titlagarh	182	Odisha	Doubling
3	Raipur-Titlagarh	203	Chhattisgarh and Odisha	Doubling
4	Hospet-Tinaighat	229	Karnataka	Doubling
5	Pune-Guntakal	641	Maharashtra, Karnataka, and Andhra Pradesh	Electrification

Table 2: Detail of Projects

The location of the projects is shown as red and blue in the map (Figure 1) here under:

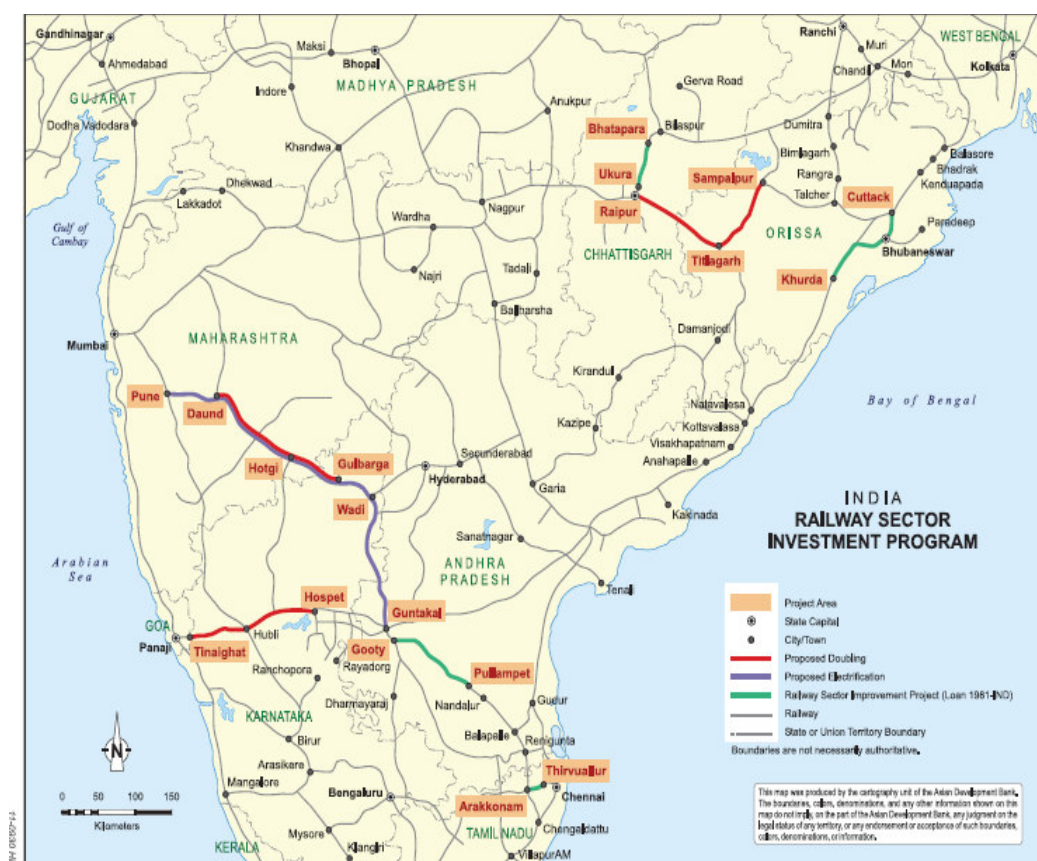


Figure 1: Map of India showing track doubling and electrification projects

In general, the resettlement planning documents related to above projects were disclosed in September 2011. Out of five projects only two, namely Sambalpur-Titlagarh and Hospet-Tinaighat doubling projects require land acquisition. The other two doubling projects (Daund-Gulbarga and Raipur-Titlagarh) involve resettlement of non-titleholders only. In Pune-Guntakal electrification project there is no land acquisition or resettlement of TH & NTH.

The current Semi Annual Report is the Social Safeguard Monitoring Report prepared to comply with the loan covenants covering the period from October 2016 to March 2017. As usual, this report covers resettlement and social safeguard monitoring results to comply with the spirit of ADB policy.

## 2. Current issues

### **Implementation of the new land acquisition Bill 2015:**

The new bill “The Right to Fair Compensation and Transparency in Land Acquisition, Rehabilitation and Resettlement (Amendment) Bill 2015”, also known as Land Bill 2015 introduced by the new government in March 2015 could not get approval in Parliament and was referred to a Joint Committee in May 2015 comprising Member of Parliament from both houses to make out a bill acceptable to all parties. Meanwhile, after lapse of ordinances over land acquisition on 31 August 2015 the Central Government has not re-promulgated the ordinance and instead allowed the state Governments to formulate their own laws or amend central law in this regard to expedite developments. Now, a ninth extension has been given by parliament to extend the time for presentation of the report of the Joint Committee up to the last day of first week of the winter session, December 2017. Further, the parliamentary joint panel reviewing the legislation will meet on May 22, 2017 to debate its social impact assessment regarding the land acquisition amendment bill 2015.

Since new Land Acquisition Amendment Bill 2015 has not come in force with the act of parliament, Ministry of Railways has streamlined rules through circular (refer our last semi annual report) for the acquisition of land through any existing law of State/Central Government, direct negotiation with landholders and Railways (Amendment) Act 2008.

### **Non-Government Organization (NGO), Assistance to RVNL:**

#### **NGO contract for Raipur-Titlagarh and Sambalpur-Titlagarh projects:**

The extension of time to NGO M/s Sugam International Sansthan (SIS) expired on 31/08/16 and no extension has been granted for Sambalpur-Titlagarh project (See Annexure-I).

NGO has still to complete the pending tasks of NTH at Raipur. No payment has been verified by them for compensation in Raipur for Parwati Nagar (2 PAPs) and Chandi Nagar area (all PAPs) in Chattisgarh state during March end quarter.

General consultant Social expert visited RVNL Raipur from 14/03/2017 to 16/03/2017 and had a thorough discussion with Nodal Social Officer of RVNL regarding the status of R&R till March 2017 and site clearance at Chandi Nagar for release of 2<sup>nd</sup> installment to PAPs.

#### **Assistance for Hospet-Tinaighat project:**

CPM has approved the extension of services of R&R personnel for further six months engaged for implementation of balance Resettlement Plan (RP). It was agreed to place the work order to M/s Manjunath Enterprises with same terms and conditions of earlier agreement for further period of 6 month (17/12/2016 to 16/06/2017) for total amount of 2,58,750 INR.

**Direct Purchase of land through Revenue Department:**

In the starting months of year 2015, South Western Railway, zonal Railway for Hospet-Tinaighat section had received proposals from districts Land Acquisition offices for direct purchase of land through Revenue Department.

In this connection, Railway Board, Ministry of Railways has communicated its approval to RVNL on 20/5/16 for direct purchase of land from landowners through Revenue Department of Government of Karnataka for Hospet-Tinaighat doubling project with condition that compensation amount should not be less than specified in Land Acquisition and Rehabilitation Act (LARRA) 2013.

Disbursement of compensation for acquisition of land and assets will be done through Land Acquisition Officer of Revenue Department of District and project authorities will disburse R&R benefits to Project Affected Persons (PAPs) and communities. For this purpose, Collector of each District will convene a meeting in which each and every component of Resettlement Action Plan (RAP) implementation and land acquisition will be finalized.

Several direct purchase meetings have been conducted with land owners at Hospet-Tinaighat project during this period, compensation have been finalized for TH located at villages of Hasalli, Kampasagar (Koppal Dist), Koppal station and Betagiri (Gadag Dist). Negotiation for compensation through direct purchase are in progress for TH of other villages also.

The land acquisition is proposed in 4 districts namely Belgaum, Darward, Koppal and Gadag. The Joint Measurement Survey (JMS) with Revenue department is in progress in the remaning villages and the valuation is also in progress by the concerned Public Works Department (PWD).

### 3. Status

The current status of field work of land acquisition and resettlement plan implementation of different projects is provided in table 3.

The status per project is as follows:

#### 4.1 Sambalpur–Titlagarh project


This project passes through four districts namely Sambalpur district (SambalpurTahasil), Baragarh district (3 Tahasils i.e. Attabira, Baragarh and Barapalli), Sonepur (Rampur Tahasil) and Bolangir district (8 Tahasils i.e. Agalpur, Loisingha, Bolangir, Puintala, Deogaon, Siantala, Titlagarh ad Muribahal).

The NGO Contract Agreement for Implementation of Resettlement Plan for project affected persons of Raipur-Titlagarh and Sambalpur-Titlagarh sections was signed on 23 January 2012. The contract was extended up to 31<sup>st</sup> August 2016 to complete all the pending works at Raipur and Sambalpur.

Since the resettlement work of TH is being done directly by the Revenue department so the NGO has been asked to not to work for them in Sambalpur- Titlagarh section by the RVNL.

For NTH affected persons of Khetajpur, Guhratikra and Balangir first and second installment have been transferred in their respective accounts in the month of April 2016 and August 2016 respectively. The land is totally free from any encumbrances (see in Annexure II).

Progress of compensation up to March 2017 for NTH is depicted below:

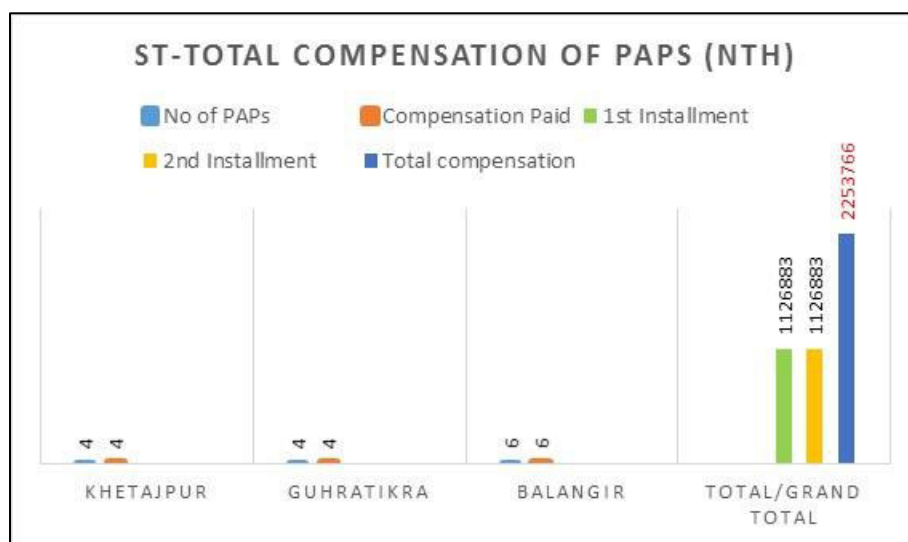

Income restoration and skill upgradation training programme for the affected persons of Khetajpur, Guhratikra and Balangir was held from 27th August to 29th August, 2016.

Total requirement of Land to be acquired acres is currently estimated as: (1) Private land: 76.678-(2) Govt. Land: 46.746 (3) Forest Land: 15.340.

There may be some additional requirements due to design changes in layout of station yards and approaches of the major bridge at 423A between Saintala and Deogaon in ST. The additional requirements of land in Sambalpur-Titlagarh section has not been officialized yet.

The survey details of the Title holders for 26 villages along with public hearing has been submitted to Revenue Department by State SIA Unit, Nabakrushna Choudhury Centre for Development Studies (NCDS), Bhubaneswar.

During March 2017, Social Impact Assessment of Land Acquisition for Construction of Sambalpur-Titlagarh Doubling Railway Link Project, in Bargarh District has been submitted to the Revenue Department. Public Hearing has also been carried out and the final report is under preparation.

The status of acquisition of private land, Government land and forest land received from PIU, Sambalpur is as under:

Name of the District	Private Land
<b>Sambalpur</b>	<p>(a) 4.62 acres (1.870 Ha) Pvt. land acquisition required in 5 villages. Possession taken for acres 4.45 in 3 villages.</p> <p>(b) U/s 19(1) declaration issued for village Sambalpur unit-9 (acre 0.130) and Barapalli (acre 0.040) in total acre 0.170 in 2 villages on 03/10/2016 by Revenue and DM. department, government of Odisha. As reported by SLAO/SBP the remaining 2 villages Sambalpur unit-9 (acre 0.130) and Barapalli (acre 0.040) payment are being done. Urgent possession is required.</p> <p>(c) As per demand of State government fund of 2,73,37,735 INR towards land cost has been deposited with Spl.LAO/SBP on 05/11/2016 by Railway (cheque No. 944785 and dated 02/11/2016).</p>
<b>Baragarh</b>	<p>(a) 21.425 acres (8.670 Ha) Pvt. Land acquisition required in 26 villages.</p> <p>(b) SIA report received by Collector/Bargarh from NCDS/BBS. Spl.LAO/SBP has written to Collector/BRGA for formation of expert group on 28/09/2016 and 17/11/2016. SLAO has confirmed that expert group approved by collector/Bargarh.</p> <p>(c) Public hearing in all 26 villages completed on 17/12/2016. The final report after public hearing has been submitted to Collector /BRGA by SLAO/SBP on: 22/02/2017. Date has been fixed on: 27/04/2017 by Collector/BRGA for examination of final SIA report by the expert committee.</p>
<b>Bolangir</b>	<p>(a) 41.448 acres (16.774Ha) Pvt. Land acquisition required in 32 villages. Required fund towards SIA Study has been deposited with NCDS/BBS on 26/02/2016.</p> <p>(b) Public Hearing on SIA in all 32 villages of Bolangir district have been completed commencing from 27/03/2017 to 03/04/2017.</p>
<b>Sonepur</b>	<p>(a) 9.185 acres (3.717 Ha) Pvt. land acquisition required in 8 villages.</p> <p>(b) U/s 19(1) declaration issued for acres 9.185 in 8 villages on 03/10/2016 by revenue and DM department, government of Odisha.</p> <p>(c) Out of 8 villages, payment for one village i.e Paphatamunda has been paid. Notice was served on 09/03/2017 and 10/03/2017 for payment of 07 villages. But land owners of one villager's i.e Sannuapali are unwilling to</p>



	<p>receive payment on 09/03/2017 due to lower valuation. They have represented to Collector/Sonepur through SLAO/SBP for enhancement of valuation who is the competent authority to settle this issue. Collector/Sonepur has been pleased to decide on: 28/03/2017 regarding enhancement of compensation as per the New LA Act-2013. Others 4 villages namely Patharkhandi, Cherupali, Kusuamal and Sahala have been partially paid. The full Payment of remaining land owners of Villages Patharkhandi, Cherupali, Kusuamal and Sahala are being done. Steps are being taken for payment of other two villages namely Khuntpali and Dunguripali.</p> <p>(d) As per demand of state government fund of 13,88,35,510 INR vide Cheque no. 908268 dated 24/06/2016 and 79,04,475 INR vide cheque no. 944785 dated 02/11/2016 towards land cost has been deposited with Spl.LAO/SBP on 24/06/2016 and 05/11/2016 by Railway.</p>
--	--

#### Government Land

- (a) Total government land required: 46.746 acres (64 villages).
- (b) 46.746 acres of government land required for the project in Sambalpur, Baragarh, Sonepur and Bolangir District. Alienation has been sanctioned for 1.921 acres in 15 villages of Baragarh district and 4.380 acres in 23 villages of Bolangir district, 2.310 acres in 1 village in Sambalpur district and 1.057 acres in 7 villages in Sonepur district.
- (c) Lease deed executed for acres 9.668 with concerned Sub-Registrar office against sanctioned acres 9.668.
- (d) Balance 37.078 acres of government land is yet to be alienated by State government pending with Water Resources Department and HUD Department government of Odisha.
- (e) In SBP district, for alienation of acres 1.102, fund of 1,18,60,275 INR demand received. Apprehending the amount to be exorbitant reconfirmation was sought from revenue authorities. They have confirmed the demand to be correct and hence payment is paid on 14/03/2017.
- (f) In SBP district acres 12.059 and acres 5.885 has to be sanctioned in favour of Railway as DOWR has relinquished the same in favour of Revenue and D.M. Department vide their letter no. 24717/WR dated 24/10/2016 for acres 12.059 and No.12125/WR dated 02/06/2015 for acres 5.885. Pending with Tahasildar/Sambalpur.

#### Forest Land

- (a) 15.340 acres (6.208 Ha) of forest land diversion is required in 5 villages for the entire Sambalpur – Titlagarh doubling rail project.
- (b) In compliance to observations made by Nodal/Officer of PCCF office, hard copies are submitted with concerned DFOs and district Collectors on 04/05/2016.
- (c) Compliance to Observations of DFO/BLGR submitted on: 28/09/2016 through Dy. CE/Con/SBP.
- (d) DFO/BLGR has jointly site inspected with RVNL officials on 03/11/2016 and 04/11/2016. Site inspection report (part-II) made and sent RCCF/Bhawanipatnam on 21/11/2016.
- (e) RCCF/Bhawanipatnam raised some observations and sent for compliance to DFO/BLGR on 16/12/2016.
- (f) Re submitted to RCCF/ Bhawanipatnam on 11/01/2017 with due compliance by DFO/BLGR and pending with RCCF/Bhawanipatnam.

- (g) Observations dated 24/05/2016 given by DFO/Bargarh complied and submitted on 22/11/2016 to DFO/Bargarh.
- (h) DFO/Bargarh made field verification on 06/12/2016 and given some observation.
- (i) Observations of DFO/BRGA complied and resubmitted on 04/01/2017.
- (j) DFO/BRGA submitted the file with recommendation to RCCF/SBP on 07/01/2017 and pending with RCCF/SBP.
- (k) Observations dated 05/07/2016 given by DFO/SBP complied and submitted on 25/11/2016 to DFO/Samablpur.
- (l) DFO/SBP vide his letter no. 6667 dated 02/12/2016 again raised some observation.
- (m) To comply SI.No.9 of DFO/SBP a letter has been submitted to Collector/SBP on: 09/01/2017.
- (n) Compliance to others Observations of DFO/SBP submitted on: 27/01/2017 through Dy. CE/Con/SBP and after that sites inspection of DFO/SBP Completed on 08/02/2017 and pending with DFO/SBP for onwards transmission to RCCF/SBP.
- (o) DFO/SBP vide his letter no. 870 dated 25/02/2017 again raised some observation. Observation Under Compliance. Tree enumeration is in process.

## 4.2 Raipur-Titlagarh project

The General Consultant expert visited Raipur from 14/03/2017 to 16/03/2017 and had a meeting with DGM-RVNL, Raipur Nodal Social Officer to discuss the status the R&R till March 2017. Also discussed the possibility of extension of NGO for completing the pending task at Raipur.

RVNL Raipur has approved the micro plan for 1,74,40,503 INR and the total compensation disbursed till March is 1,63,89,296 INR to rehabilitate 261 PAPs.

For Kantabaji area of Odisha state, the total no of PAPs is 23, 2nd and final disbursement for the 23 PAPs has been completed and the land is totally free from encumbrances.

For Mahasamund area of Chhattisgarh state, the total no. of PAPs is 45. 2nd and final disbursement for those 45 PAPs has been completed and land is totally free from encumbrances.

For Parvati Nagar at Raipur of Chhattisgarh state, the total no. of PAPs is 143. First installment for 143 PAPs was completed in the month of February 2016. The second installment for 141 PAPs has been transferred in their respective accounts in March 2017. Now the land is free from squatters as all them have removed their existing structures from the Corridor of Impact (COI). Release of 2<sup>nd</sup> installment for remaining 2 nos PAP has been recommended by RVNL.


For Ekta Nagar at Raipur of Chhattisgarh state, all the affected PAPs have vacated their structures as they have been provided alternative shelter in the nearby area by the District Administration. The land is totally free from any encumbrances.


For Chandinagar at Raipur of Chhattisgarh state, the total no. of PAPS is 50. Identity cards have been distributed for 49 PAPs. During previous period the first installment for 49 PAPs has been transferred in their respective accounts. 1 PAP is not traceable and this will be checked. 2<sup>nd</sup> instalment is pending as NTH in Chandinagar have not removed their structures from COI.

S. No	Impacted project area	Total number of affected persons	Compensation paid
1	Kantabaji	23	Fully paid
2	Mahasamund	45	Fully paid
3	Parvati Nagar	143	141 fully paid
4	Ekta Nagar	0	Vacated by District Administration
5	Chandinagar	50	49 PAPs paid 1st installment.

**Table 3: Final summary of subproject impacts Chhattisgarh and Odisha Section**

Progress of compensation up to March 2017 as depicted below:

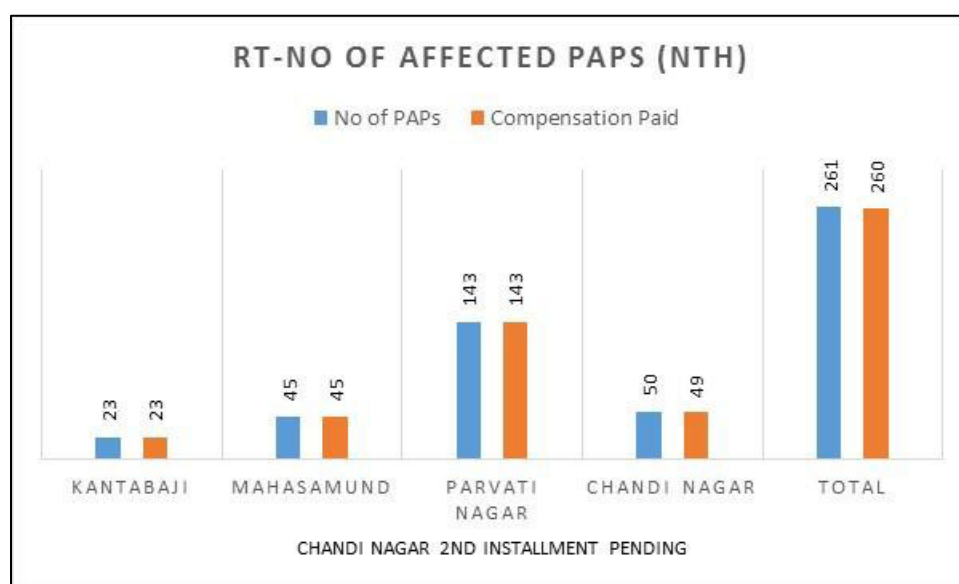


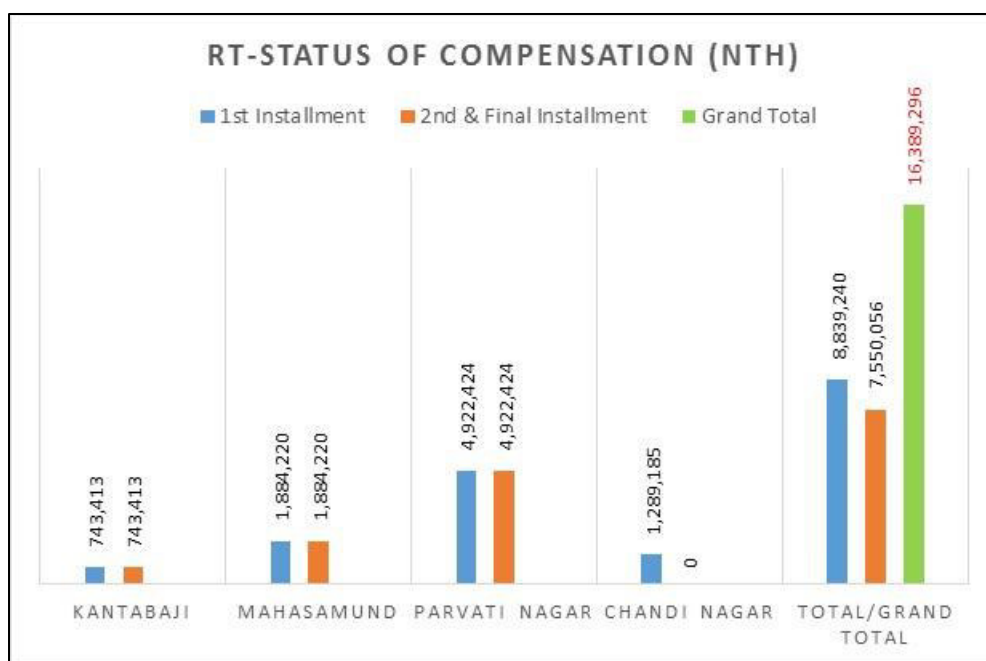

### 4.3 Daund-Gulbarga project

No land acquisition and all NTH have been compensated.

Progress of compensation up to March 2017 as depicted below:

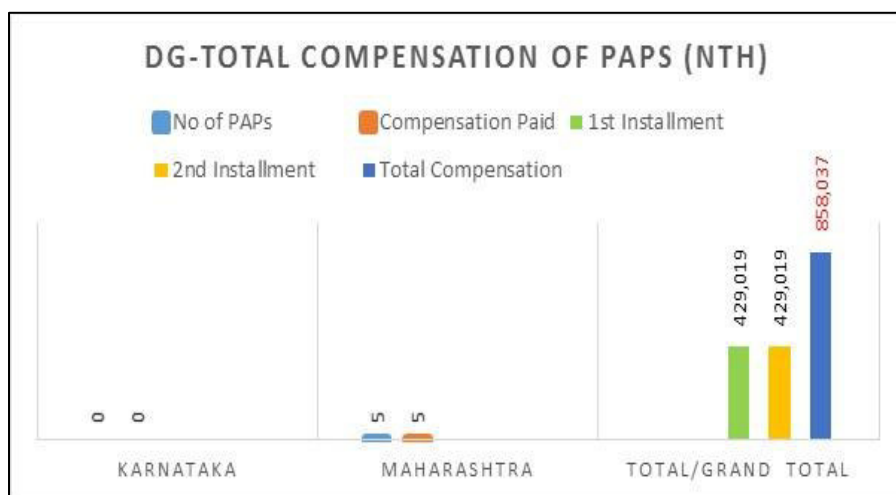

### 4.4 Hospet-Tinaighat project

This project is situated in the state of Karnataka. The total scope of land acquisition has now been revised to 30 acres 9 gunta. 19.00 acres had been notified under clause 6(1) of Land Acquisition Act and 11.9 acres is proposed to be acquired through direct purchase.

No NTH were found in this project. The Micro plan for resettlement allowance has been approved for 25 out of total 43 PAPs. An amount of 3,70,000 INR of entitlements has been disbursed in three stages to 25 PAPs/House Holders (HHs).

### **Assistance for resettlement/NGO**

On termination of the NGO contract, RVNL corporate office advised the PIU to appoint a local agency or local experts in consultation with GC to carry out the balance R&R activities of the project. Contract for resettlement monitoring was initially given to M/s Shree Manjunatha Enterprises for six months starting from 16/06/2016. The contract period was expired on 15/12/2016. Now, the Extension for the local experts for implementation of balance resettlement plan has been granted for further period of six months (17/12/2016 to 16/06/2017).

### **Land acquisition - requirements**

The revised total land acquisition requirement under this project is now 30 acres 9 gunta in districts of Koppal, Gadag and Dharwad. So far, 19.00 acres had been notified under clause 6(1) of Land Acquisition Act and 11.9 acres is proposed to be acquired through direct purchase.

The project comprised major land acquisition in Koppal district for four Railway Stations. To minimize land acquisition, the scope of yard construction in Munirabad has been restricted to Railway land only. Similarly, in Munirabad-Bhanpur section construction of extension of minor bridges has been restricted to Railway land by constructing retaining walls.

There are some savings in land acquisition but also some additional requirements in station yards due to design changes.

NAME OF THE VILLAGE	Package No	Revised Land after Joint Measurement Survey (JMS) with RVNL & Revenue Dept Proposed for Direct Purchase			Impact on Social Safeguards	Remarks
		Acre	Gunta	Anna		
Betagari ,Gadag (Gadag DT)	HT-2	0	27	0	Two Buildings are effected and the valuation is completed submitted to DC office by PWD department . General Consultant Social expert field Visited in November 2016	For public and bullock carts movement extra taken 27 Gunta.
Alnawar new proposal (Darwad DT )	HT-3	1	1	0	At present no Social Impact found only agriculture land is affected .General Consultant Social expert field Visited in November 2016.JMS Completed.	Loop line increasing from 500 m to 750 m
Devarai new proposal (Belgaum DT)	HT-3	0	28	0	At present no Social Impact found only agriculture land is affected .General Consultant Social expert field Visited in November 2016.JMS Completed.	Due to high bank and extension of Yard.
Khurdagosh Village new proposal(Belgaum DT)	HT-3	0	12	0	At present no Social Impact found only agriculture land is affected .General Consultant Social expert field Visited in November 2016.JMS Completed.	This is a Major bridge, initially track centre was designed with 11 mts. Due to technical reasons of the closing bridge features track centre is increased to
Londa Village new proposal (Belgaum DT)	HT-3	0	12	0	At present no Social Impact found only agriculture land is affected .General Consultant Social expert field Visited in November 2016.JMS Completed.	Curve improvement Grade improvement along with yard remodeling.
Akrali Village new proposal (Belgaum DT )	HT-3	0	12	0	At present no Social Impact found only agriculture land is affected .General Consultant Social expert field Visited in November 2016.JMS not Completed.	L.C gate No 3 has been eliminated duly construction of location was not having adequate land to build side road.
<b>Grand Total</b>		<b>3</b>	<b>12</b>	<b>0</b>		

Table 4: Reasons for additional requirements in HT



## Land acquisition - progress

The present status of land acquisition in Hospet-Tinaighat project after Joint Measurement Survey (JMS) is as follows:

As on 31-03-2017											
NAME OF THE VILLAGE	Package no	Total land acquisition scope	Notification issued for (Till date notification 6(1))	Notification 6(1) issued for Land acquisition	Land yet to be taken over	Revised Land proposed for direct purchase	Revised /Balance Land after JMS proposed for direct purchase as on March 2017	After Revised Grand Total as on March 2017	Remarks as on March- 2017	Direct purchase Amount Finalised as on March 2017 by DC But Railways not released amount .	
1	2	3	4	5	6=3-4 or 3-5	7	8	9=8+5 or 4	11	12	
		A G a A G a A G a A G a A G a A G a									
ANNIGERI (Darwad)	HT-2	1 22 0 1 22 0 1 22 0 1 22 0 1 22 0									
ANNIGERI (Darwad Govt. Agriculture University)	HT-2	1 1 0 1 1 0 1 1 0 1 1 0 1 1 0									
SOMAPUR (Koppal)	HT-1	8 6 0 4 16 0 4 16 0 3 30 0 0 31 0							Land Owner not given acceptance / Consent letter		
BHANAPUR (Koppal)	HT-1	3 32 0 1 31 0 1 31 0 2 1 0 1 2 0							Land Owner not given acceptance / Consent letter		
HOSALLI (Munirabad) (Koppal)	HT-1	2 26 0 1 25 0 1 25 0 1 1 0 0 23 0							Land Owner given acceptance / Consent letter	₹ 760,000	
KOPPAL (Koppal)	HT-1	13 3 0 6 14 0 6 14 0 6 29 0 4 12 0							Land Owner given acceptance / Consent letter	₹ 83,684,930	
TALABALA (Bhanapur) (Koppal)	HT-1	2 11 0 2 11 0 2 11 0 0 0 0 0 0 0									
KAMPASAGAR (Munirabad) (Koppal)	HT-1	2 19 0 0 0 0 0 0 0 2 19 0 0 28 0							Land Owner given acceptance / Consent letter	₹ 1,859,000	
Munirabad Additional (Koppal)	HT-1	0 22 0 0 0 0 0 0 0 0 22 0 0 22 0							DC negotiations		
1.Total as per March 201		35 22 0 19 0 0 19 0 0 16 22 0 7 38 0						26 37 0			
New proposals											
Gadag (Gadag)	HT-2	0 0 0 0 0 0 0 0 0 0 0 0 0 0 0							Land Owner given acceptance / Consent letter	₹ 57,765,212	
Alnavar new proposal (Darwad DT)	HT-3	0 0 0 0 0 0 0 0 0 0 0 0 1 1 0							DC negotiations		
Devrai new proposal (Belgaum DT)	HT-3	0 0 0 0 0 0 0 0 0 0 0 0 3 30 0							DC negotiations		
Khurdagosh Village new proposal (Belgaum DT)	HT-3	0 0 0 0 0 0 0 0 0 0 0 0 0 12 0							DC negotiations		
Londa Village new proposal (Belgaum DT)	HT-3	0 0 0 0 0 0 0 0 0 0 0 0 0 12 0							DC negotiations		
Akrai Village new proposal (Belgaum DT)	HT-3	0 0 0 0 0 0 0 0 0 0 0 0 0 12 0							DC negotiations		
2.Total as per new proposals as on March 2017		0 0 0 0 0 0 0 0 0 0 0 0 6 14 0						3 12 0			

Details

Acre

Gunta

Anna

1 Acre = 40 Gunta

1 Gunta = 16 anna

Total Notification 4(1) Issued

19

0

0

Remaining Land with New proposals

11

9

0

Grand Total Land

30

9

0

in this Old 7 Acre 37 Gunta and New proposals 3 Acre 12 Gunta

Details		Acre	Gunta	anna
Total Notification 6(1) Issued		19	0	0
Remaining Land with New proposals		11	9	0
Grand Total Land		30	9	0

1 Acre = 40 Gunta  
1 Gunta = 16 anna  
a = anna


In this Old 7 Acre 37 Gunta and New proposals 3 Acre 12 Gunta


Table 5: Status of land acquisition in HT

Financial status of compensation against land acquisition and resettlement as on 31/03/2017												
S No	Name of district	name of village/station	Total nos of PAPS	Total Nos of NTH	Total nos of TH	Total compensation paid against land purchase to THs upto March 2017			Total Resettlement Allowance paid upto March 2017		Total resettlement pending	
						No. of TH	Amount	Land acquired in acres	No of PAPS	Amount	No of PAP	Amount
1	Koppal	Koppal/Koppal	6	0	6	0	₹ 0	6.350	1	₹ 8,000	5	₹ 60,000
2	Koppal	HOSSALLI/Munirabad	4	0	4	4	₹ 1,328,453	1.625	4	₹ 62,000	0	₹ 0
3	Koppal	SOMPUR/Sompur	7	0	7	0	₹ 0	4.400	4	₹ 62,000	3	₹ 24,000
4	Darwad	ANNIGERI/Annigeri	11	0	11	3	₹ 368,750	2.575	11	₹ 178,000	0	₹ 0
5	Koppal	TALABALA/Bhanapur	3	0	3	3	₹ 1,182,099	2.275	2	₹ 26,000	1	₹ 8,000
6	Koppal	BHANAPUR/Bhanapur	12	0	12	1	₹ 191,029	1.775	3	₹ 34,000	9	₹ 102,000
7	Koppal	Kampasagar /Munirabad										
8	Gadag	Bettageri/Gadag										
9	Koppal	HOSSALLI/Munirabad										
10	Darwad	Alnawar new proposal										
11	Belgaum	Devarai new proposal										
12	Belgaum	Khurdagosh new proposal										
13	Belgaum	Londa new proposal										
14	Belgaum	Akrali new proposal										
Total			43	0	43	11	₹ 3,070,331	19.000	25	₹ 370,000	18	₹ 194,000

Table 6: Financial status of compensation in HT

Progress of compensation up to March 2017 as depicted below:

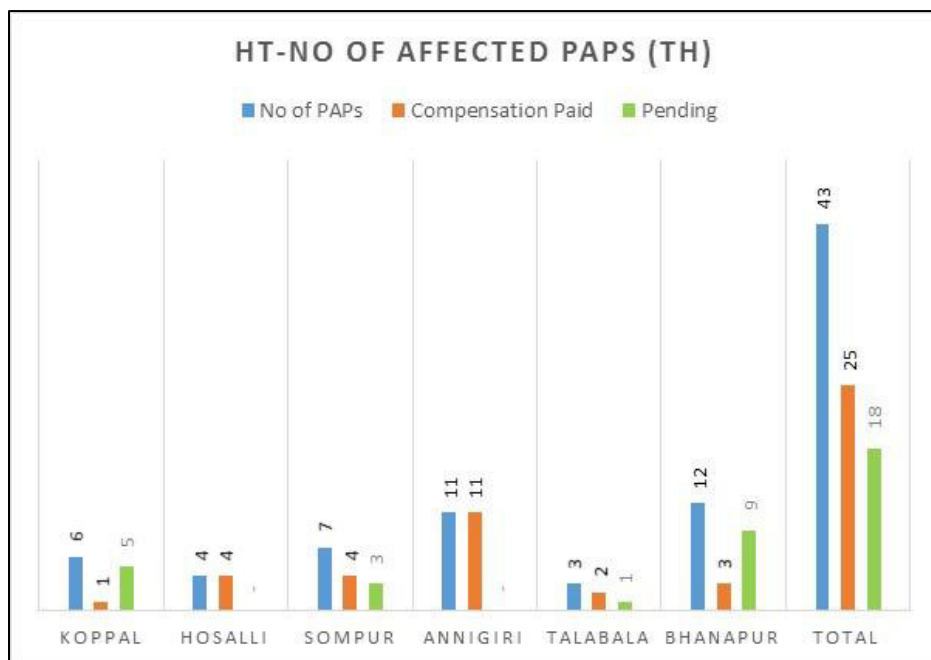

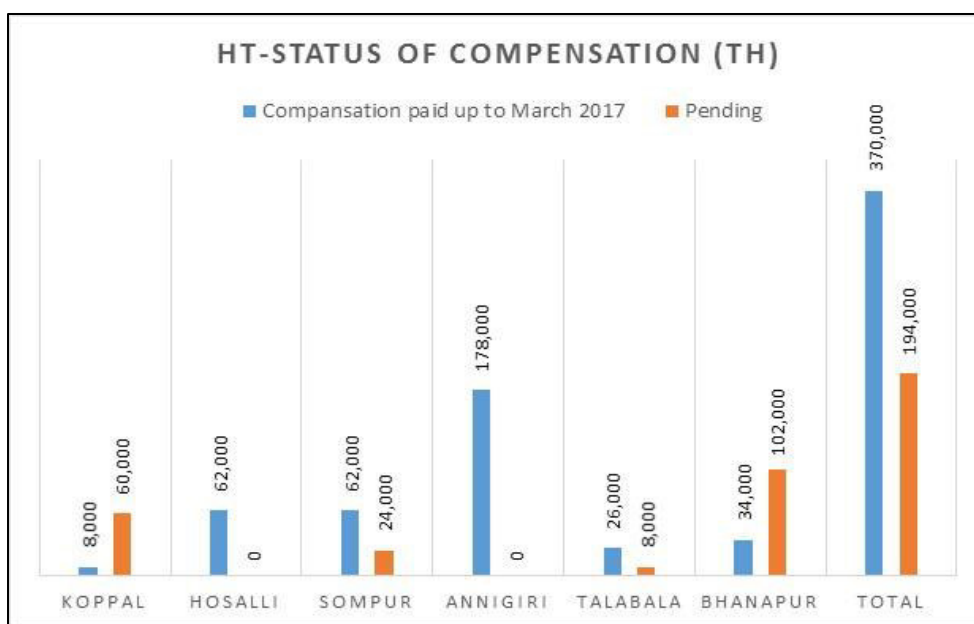

Statement Of Land Compensation received by Land Owners against partial land notified under 6 (1) notification							
Sl. No.	Name of the Land owner	Village	Yard	District	Survey No.	Amount Received in Rs.	Date of Receipt of Amount
1	Mohammad Rafic Thasildar	Annigiri	Annigiri	Dharwad	1340	₹ 131,697.00	4/15/2015
2	Rangannavar	Annigiri	Annigiri	Dharwad	1340	₹ 85,602.00	4/15/2015
3	Thulsa	Annigiri	Annigiri	Dharwad	1361/16	₹ 151,451.00	4/15/2015
A).Total Amount in Rs						₹ 368,750.00	
4	Mahesh	Talabala	Bhanapur	Koppal	212	₹ 70,191.00	9/1/2015
5	Ling Bassamma	Talabala	Bhanapur	Koppal	213/3	₹ 774,998.00	7/23/2015
6	Rajashekar	Talabala	Bhanapur	Koppal	213/4	₹ 336,910.00	7/23/2015
B).Total Amount in Rs						₹ 1,182,099.00	
7	Satyanarayana Yamanappa Kalal	Hosahalli	Munirabad	Koppal	54	₹ 185,365.00	5/10/2016
8	Satyanarayana Yamanappa Kalal	Hosahalli	Munirabad	Koppal	55	₹ 710,568.00	5/10/2016
9	Ishappa S/O Bharmappa	Hosahalli	Munirabad	Koppal	59/a	₹ 278,048.00	7/23/2016
10	Bharmappa W/O Prabhuraj	Hosahalli	Munirabad	Koppal	60	₹ 154,472.00	7/23/2016
11	Rudragouda Bhavi	Bhanapur	Bhanapur	Koppal	7	₹ 191,029.00	6/29/2016
C).Total Amount in Rs						₹ 1,519,482.00	
A+B+C Grand Total						₹ 3,070,331.00	

Table 7: Status of land compensation in HT

## 4.5 Electrification of Pune-Guntakal project

No land acquisition and no TH & NTH in this project.

#### 4.6 Summary table

Status of Land Acquisition with resettlement plan implementation of different projects is as follows:

Item No	Indicators	Section					
		Raipur-Titlagarh project (Odisha Section)	Raipur-Titlagarh project (Chhattisgarh Section)	Sambalpur-Titlagarh project*	Hospet-Tinaighat project *	Daund-Gulbarga project (Karnataka Section)	Daund-Gulbarga project (Maharashtra Section)
1	Appointment of the RP implementation NGO	Sugam International Sansthan.	Sugam International Sansthan.	Sugam International Sansthan. Closur of agreement of R&R implementati on work for Sambalpur-Titlagarh project from 31/08/2016 as per letter no. RVNL/WAT/D GM(P)/BLGR/ R&R/SBP-TIG/SBP-TIG/2017/02 dated 13/02/2017	To complete the balance work of implementation of resettlement plan, two persons from Sree Manjunatha Enterprises providing support from 16/06/16. Contract extended for further six months from 17/12/2016 to 16/06/2017.	Sugam International Sansthan end of contract on 4/1/2016	Sugam International Sansthan end of contract on 4/1/2016
2	No. of displaced households	23	238	666 (14 NTH)	43	NIL	5

		Section					
Item No	Indicators	Raipur-Titlagarh project (Odisha Section)	Raipur-Titlagarh project (Chhattisgarh Section)	Sambalpur-Titlagarh project*	Hospet-Tinaighat project *	Daund-Gulbarga project (Karnataka Section)	Daund-Gulbarga project (Maharashtra Section)
3	No. of displaced persons	76	621	2343 (14 NTH) (number of TH Displaced Persons under verification)	173	NIL	20
4	No. of physically displaced households	23	238	14 NTH	NA	NIL	NIL
5	No. of physically displaced persons	76	621	14 NTH	NA	NIL	NIL
6	No. of economically displaced households	23	136	644 TH	43	NIL	NIL
7	No. of economically displaced persons	23	238	2251 TH	173	NIL	NIL
8	Total number of titleholders being displaced	NIL	NIL	644	43	NIL	NIL

		Section					
Item No	Indicators	Raipur-Titlagarh project (Odisha Section)	Raipur-Titlagarh project (Chhattisgarh Section)	Sambalpur-Titlagarh project*	Hospet-Tinaighat project *	Daund-Gulbarga project (Karnataka Section)	Daund-Gulbarga project (Maharashtra Section)
9	Total number of non titleholders being displaced	23	238	14	NIL	NIL	5
10	Entitlement matrix disclosed	Yes	Yes	Yes	Yes	Yes	Yes
11	Number of identity cards issued to the displaced persons	Identity cards released to 23 PAPs in Kantabanji area	Identity cards distributed to all PAPs	Identity cards distributed to all PAPs	Identity cards distributed to PAPs of 5 villages (25 PAPs)	NA	5
12	Micro plans prepared for titleholders	Not required	Not required	After award by Deputy Land Acquisition Officer (DLAO)	Revised corrected micro plan has been approved in May 2015	Not required	Not required
13	Micro plans prepared for non- titleholders	Completed and submitted (23 NTH)	Completed and submitted (238 NTH)	Completed and submitted (14 NTH)	NA	NA	Yes
14	Micro plans prepared for CPRs	NA	NA	NA	NA	NA	NA



		Section					
Item No	Indicators	Raipur-Titlagarh project (Odisha Section)	Raipur-Titlagarh project (Chhattisgarh Section)	Sambalpur-Titlagarh project*	Hospet-Tinaighat project *	Daund-Gulbarga project (Karnataka Section)	Daund-Gulbarga project (Maharashtra Section)
15	Micro plans approved for TH	NA	NA	Not yet	Approved	NA	NA
16	Micro plans approved for NTH	Approved	Approved	Approved	NA	Approved	Approved
17	Micro plans approved for CPRs	NA	NA	NA	NA	NA	NA
18	Quantum of private land to be acquired	NIL	NIL	76.678 acres	now revised from 35.22 to 30.09 acres	NIL	NIL
19	Progress on LA	NA	NA	Requisition for LA submitted and completed for Government, forest and private land for Sambalpur, Sonapur, Baragarh and Balangir districts.	Out of revised 30.9 acres, 19 acres was already notified under 6(1). Balance 11.9 acres to be acquired under direct purchase	NIL	NIL

Item No	Indicators	Section					
		Raipur-Titlagarh project (Odisha Section)	Raipur-Titlagarh project (Chhattisgarh Section)	Sambalpur-Titlagarh project*	Hospet-Tinaighat project *	Daund-Gulbarga project (Karnataka Section)	Daund-Gulbarga project (Maharashtra Section)
20	Whether compensation distributed to DPs	2 <sup>nd</sup> /final installment of compensation has been distributed to all 23 nos DPs of Kantabaji area	2 <sup>nd</sup> and final installment has been distributed to all 45 DPs of Mahasumund area whereas 2 <sup>nd</sup> installment of compensation paid for 141 DPs of Parwati Nagar out of proposed 143. 1 <sup>st</sup> installment of Chandi Nagar for 49 PAPs paid. 2 <sup>nd</sup> installment under process.	1 <sup>st</sup> and 2 <sup>nd</sup> instalment of compensation paid to 14 nos NTH in April/August 2016	Distributed to 12 PAPs under Phase-I in December 2013.  Distributed to 8 PAPs under Phase II in April 2014.  Distributed to 5 PAPs under Phase-III in Sep 2015	NA	1st installment of assistance has been distributed on 24/12/12. 2nd/final installment has been distributed on 24/08/2013. Total 5 PAPs identified as Squatters has been compensated in two installment for 858,037 INR
21	Whether assistance distributed to DPs	Yes	Yes	Yes	Not yet	NA	All the PAPs are working in nearby Cement factory-Hotagi and are getting 10,000 INR to 15,000 INR per month, and they have given in

		Section					
Item No	Indicators	Raipur-Titlagarh project (Odisha Section)	Raipur-Titlagarh project (Chhattisgarh Section)	Sambalpur-Titlagarh project*	Hospet-Tinaighat project *	Daund-Gulbarga project (Karnataka Section)	Daund-Gulbarga project (Maharashtra Section)
							writing that they don't need any training as they are already employed
22	Whether GRC formed	GRC formed at 1 district (Balangir)	GRC formed at 2 district (Mahasumund and Raipur)	GRC formed in all 4 districts	Special Land acquisition Officer cum Assistant Commissioner has been nominated as a Chairman of GRC and DGM/RVNL as member of GRC from PIU	NA	Yes
23	Complaints to GRC received/ resolved	NIL	NIL	NIL	NIL	NIL	NIL
24	Consultations held with DPs	3 places	4 places	5 places	13 places	NA	Yes
25	Relocation	Kantabaji completed	Completed at Mahasamund, Ekta Nagar, partly Parwati	Completed	NA	NA	Completed

		Section					
Item No	Indicators	Raipur-Titlagarh project (Odisha Section)	Raipur-Titlagarh project (Chhattisgarh Section)	Sambalpur-Titlagarh project*	Hospet-Tinaighat project *	Daund-Gulbarga project (Karnataka Section)	Daund-Gulbarga project (Maharashtra Section)
			Nagar and Chandi Nagar in process				
26	Inventory of losses of Displaced Persons (DPs)	Completed	Completed	Completed	Completed	Completed	Completed
27	Impact on Indigenous People/STs with kind of impact	Completed (STs not found)	Completed (STs not found)	Completed (STs not found)	Completed (STs not found)	Completed (STs not found)	Completed (STs not found)

Table 8: Status of land Acquisition and Resettlement

*\*Impact reported by NGO/RVNL after verification may change after conducting social impact assessment study by Revenue Department or Joint Measurement Survey findings*

Details regarding status of R&R implementation as on 31 March 2017

S. No	Name of Project	Length of line (in kms)	Length of section free from R&R	Area of land to be acquired	No. of HHs/PAPs	Status of R&R implementation
1.	Raipur-Titlagarh doubling project (Odisha section)	99.94	98.85 kms	Nil	261/261	Identification and verification of PAPs has been revised and completed and submitted. Joint Measure Survey (JMS) has also been completed. GRC formed. Valuation of structures have also been completed, micro plan prepared and submitted on 09/09/2013 by NGO at total rehabilitation cost of 87,386,088 INR for 681 HHs. However, R&R expert of GC advised to minimize the Right of Way (ROW) and was agreed by PMC and RVNL. Actual COI (Corridor of Impact) was worked out by NGO, RVNL and Revenue Officer. Accordingly, Micro plan was revised and completed on 12/11/2013 at total R&R cost of 19,714,627 INR for 265 HHs based on actual COI. Micro plan has been approved and Identity cards distribution was started in Odisha section. Further, Revised micro plans was approved in August 2015 for Mahasamund and Kantabanji areas bringing the new total to 261 HHs. Identity card distributed to 45 PAPs in Mahasamund District in Chhattisgarh section. Bond paper of PAPs completed. Assistance distributed through RTGS.

S. No	Name of Project	Length of line (in kms)	Length of section free from R&R	Area of land to be acquired	No. of HHs/PAPs	Status of R&R implementation
2.	Raipur-Titlagarh doubling project (Chhattisgarh section)	98.01	96.60 kms	Nil	261/261	Paid in December 2015. For Parwati Nagar of Raipur area, revised (Micro Plan) was submitted by NGO in December 2015 short listing 143 PAPs for amount of 9,844,847 INR was finalized for disbursement. Micro plan for Chandi Nagar for 50 PAPs has been approved in February 2016 for disbursement. 1 <sup>st</sup> installment disbursement for 49 PAPs of Chandinagar and 2 <sup>nd</sup> installment for 123 PAPs of Parwati Nagar have been paid in July/August 2016. For Parwati Nagar, NGO has verified the conditions for second installment to 18 PAPs (NTH) in addition to 123 PAPs already approved and the amounts have been transferred in their respective accounts on 19 <sup>th</sup> March 2017.

S. No	Name of Project	Length of line (in kms)	Length of section free from R&R	Area of land to be acquired	No. of HHs/PAPs	Status of R&R implementation
3.	Sambalpur–Titlagarh doubling project	182.00	125.00 kms	76.678 acres	TH 644/2251 NTH 14/14	<p><b>TH:</b> Requisition for LA submitted for government and private land for Sambapalur, Sonepur Bargargh and Balangir Districts</p> <p><b>NTH:</b> Identification and verification and Joint measurement report completed on 02/07/2013. Micro Plan prepared on 27/09/2013 at total rehabilitation cost of 6,657,962 INR for 65 HHs. However, Revenue officer (RO) provided actual corridor of Impact (COI) and track plan which was reviewed by RVNL representative ,NGO and GC. Micro plan was revised accordingly and completed and submitted on 28/10/2013 for a total R&amp;R cost of 4,419,511 INR for 38 NTH. Micro plan was reviewed on behalf of PIU Sambalpur. Rehabilitation cost of 4,419,511 INR for 38 NTH reduced to 33,40,643 INR for 14 NTH</p> <p>1<sup>st</sup> instalment of compensation has been released to all 14 NTH in April 2016. 2<sup>nd</sup> and final installment has been paid in August 2016.</p>
4.	Hospet–Tinaighat doubling project	201.31	195.31 kms	31.37 acres revised to 35.22 acres	43/173	<p>Identification and verification of PAPs has been completed and data updation work has also been completed and submitted</p> <p>Micro plan is finalized and Identity cards have been issued to PAPs of Koppal, Hosalli, Sompur and Annigeri villages</p> <p>Disbursement of allowances to PAPs (12 Nos.) under phase - I was conducted during 3rd week of</p>



S. No	Name of Project	Length of line (in kms)	Length of section free from R&R	Area of land to be acquired	No. of HHs/PAPs	Status of R&R implementation
						December 2013 and (08 Nos) under Phase – II during the first week of April 2014 19.0 acres of land notified 6(1) for acquisition. 11.9 acres of land to be acquired through direct purchase. Compensation in village Hosahalli yard Munirabad district Koppal 2 PAPs have collected the cheque from the Revenue Department for 432,520 INR in July 2016.
5.	Daund–Gulbarga doubling project (Karnataka section)	46	46 kms	0	0	NA
6.	Daund–Gulbarga doubling project (Maharashtra section)	179	176 kms	0	5/20	Total 5 PAPs identified as Squatters has been compensated in two installment of 858,037 INR. All the PAPs are found working in a nearby Cement factory-Hotagi and are getting INR 10,000 to 15,000 per month and they have given in writing that they don't need any training. The GC social has collected all the relevant papers for final completion of this section. GC Social Expert recommends to close this project.

Table 9: Details regarding Rehabilitation and Resettlement

**Annexure I: R&R Closures letter of Agreement for Sambalpur-Titlagarh project**

Rail Vikas Nigam Limited  
(A Government of India Enterprise)  
Office of the CPM/RVNL/Waltair  
(SBP-TIG Project)  
RLY BLDG. NO.T-34,MSM COLONY  
GNANAPURAM SIDE Rly Station entry  
road,Visakhapatnam-530004 (AP)  
PIN:530017

No. RVNL/WAT/DGM(P)/BLGR/R&amp;R/SBP-TIG/SBP-TIG/2017/02

Dt: 13.02.2017

To  
M/S Sugam International Sansthan,  
B-109, Vibhuti Khand,  
Gomti Nagagar,  
Lucknow - 226010 (UP).

Sub: Memorandum of intimation regarding Closure of Agreement of R&R implementation work for SBP-TIG doubling.

Name of work: Implementation of resettlement Plan in Raipur-Titlagarh Doubling Rail Line in the State of Chhattisgarh and Sambalpur - Titlagarh Doubling Project in the state of Orissa.

Ref: LOA No. RVNL/PP&D/R&R/Tender/SBP-TIG-R/2011, dtd. 02.11.2011.

Dear Sir,

With the approval of Competent Authority, it has been decided to close down the above agreement w.e.f. last date of Time Extension (i.e. 31.08.2016) without any liability on either side. As the work of R&R implementation for Title Holders is being done by the State Authorities under Land Acquisition process, no such repeated work has to be carried by your Agency and hence the same work of Title Holders is kept out of scope of the above agreement.

Hence, it is to inform you that the above agreement is closed without any liability on either side with effective date being 31.08.2016.

  
DGM/RVNL/BLGR

Copy to:

- 1) CPM-I/RVNL/WAT for information please.
- 2) DGM/Fin/RVNL/BBS for information please
- 3) GM/PP&D/Corporate Office/NDLS for information please.


**Annexure II: Compensation of NTH 1st & 2nd Installment for Sambalpur-Titlagarh project****JOINT SURVEY REPORT OF VECATION STATUS OF NTHs****OF SBP - TIG DOUBLING**


Joint verification of Vacated house holds of NTHs, for whom 1st instalment R&R Compensation has been paid, is attended by Sri Anil Kumar (SIS), Sri W. P. Rayalu (Sr.Executive/Civil/RVNL/SBP) and Sri P. Kishore Ramana (DGM/EGIS - Gen. Consultant) on dt. 29.07.2016.

The NTH occupants as listed below have vacated and cleared the Railway land under their occupation and shifted their dwelling to other places out of Railway premises. The PAPs (NTHs) have already received the 1st instalment R&R Compensation and now they are eligible to get the 2nd instalment of the Compensation.

Sl. No.	Name of NTH	F/H name	A/C No.	Bank Name	Compensation Received ₹ in 1st instl.	Compensation to be paid in 2nd instl.
1.	Rambrij Bhagat	s/o Ram Pratap Bhagat	30074487186	SBI/Khetrajpur IFSC: SBIN0001966	46,188	46,188
2.	Brijbhasani Tiwari	Lt. Shabhaati Tiwari	3448059114	CBI/Khetrajpur IFSC: CBIN0283249	92,347	92,347
3.	Prafulla Suna	Beeru Suna	10754946669	SBI/Burla IFSC: SBIN0002034	1,09,159	1,09,159
4.	Beeru Sona	Bidya Sona	30088628791	SBI/Burla IFSC: SBIN0002034	55,875	55,875
5.	Gulbari Newar	Lt. Raj Kumar Newar	005510011007535	AB/Burla IFSC: ANDB0000055	1,81,741	1,81,741
6.	Santosh Suna	s/o Beeru Suna	20136145499	SBI/Burla IFSC: SBIN0002034	50,177	50,177
7.	Kumbharu Rohidas	s/o Vishnu	0747104000080486 /82472036	IDBI/Bolangir IFSC: IBKL0000747	61,817	61,817
8.	Koushalya Chhatra	Ghasi Chhatra	005610100077249	AB/Bolangir IFSC: ANDB0000056	81,951	81,951
9.	Subidha Chhatra	Lt. Valsi Chhatra	005610100077258	AB/Bolangir IFSC: ANDB0000056	48,630	48,630
10.	Duryodhan Chhatra	Bansi Chhatra	005610100077373	AB/Bolangir IFSC: ANDB0000056	73,050	73,050
11.	Kunti Tandi	Sankar Tandi	30980100004432	BOB/Bolangir IFSC: BARB0BOLANG	85,064	85,064
12.	Sudhir Kumbhar	s/o Dasaru Kumbhar	005610100077364	Andhra Bank/BLGR IFSC: ANDB0000056	76,306	76,306
13.	Gariba Chhatra	Ramesh Chhatra	33679010911	SBI/Bolangir IFSC: SBIN0000046	45,781	45,781
14.	Basant Kumbhar	Bishnu	4798000100022432	PNB/Bolangir IFSC: PUNB0479800	1,18,797	1,18,797
				<b>Total to be paid =</b>		<b>11,26,883</b>

  
(Sri Anil Kumar)  
Project Co. (SIS)

  
(Sir W.P. Rayalu)  
Sr.Executive(Civil)/RVNL/SBP

  
(Sri P. Kishore Ramana)  
DGM/EGIS - Gen. Cons.
