

# Social Monitoring Report

---

Bi-annual Social Monitoring Report  
February 2017

## PAK: MFF – Power Distribution Enhancement Investment Program (Tranche 3)

Prepared by Gujranwala Electric Power Company, Punjab for the Asian Development Bank.

## NOTES

- (i) The fiscal year (FY) of the Government of the Islamic Republic of Pakistan and its agencies ends on 30 June.
- (ii) In this report “\$” refer to US dollars.

This social monitoring report is a document of the Borrower. The views expressed herein do not necessarily represent those of ADB's Board of Directors, Management, or staff, and may be preliminary in nature.

In preparing any country program or strategy, financing any project, or by making any designation of or reference to a particular territory or geographic area in this document, the Asian Development Bank does not intend to make any judgments as to the legal or other status of any territory or area.

**Re: Loans 2727-PAK/2972-PAK/3096-PAK: PDEIP, Tranches 2, 3 and 4 -  
Bi-Annual Social Monitoring Reports July-Dec 2016 (GEPCO)**

Jose Tiburcio Nicolas for Liaqat Ali

13/02/2017 04:01 PM

Cc: Ehtesham Z. Khattak, Zhang Lei, Ashfaq Khokhar, Muhammad  
Zeeshan

Dear Liaqat sb,

The revised SMRs have addressed my comments. I endorse acceptance of these by ADB and uploading for disclosure. Please advise us when these have been disclosed so we can reflect in our records.

Regards,

Tito S. Nicolas

Senior Social Development Specialist (Safeguards)  
Pakistan Resident Mission  
North Wing Level 8, Serena Office Complex  
Khayaban-e-Suhrawardy, G-5, Islamabad, Pakistan  
email: jnicolas@adb.org  
+92 51 2600351-69/ 208 7300 ext 219  
+92 305 9419662 (mobile)



From: Liaqat Ali/PRM/ADB  
To: Jose Tiburcio Nicolas/CWRD/ADB@ADB  
Cc: Ehtesham Z. Khattak/PRM/ADB@ADB, Zhang Lei/CWRD/ADB@ADB  
Date: 13/02/2017 11:24 AM  
Subject: Fw: Loans 2727-PAK/2972-PAK/3096-PAK: PDEIP, Tranches 2, 3 and 4 - Submission of Bi-Annual Social Monitoring Reports and Bi-Annual Environment Monitoring Reports

Dear Tito:

Attached below, please find revised SMRs submitted by GEPCO after incorporation of your comments. Please review, comments and/or clear the SMRs for disclosure.

Regards,

Liaqat Ali, Project Analyst, Pakistan Resident Mission  
Level 8, North, Serena Office Complex, G-5, Islamabad/Pakistan  
Tele: (92-51) 2600351-69/2087210 Fax: (92-51) 2600365-66/2087397-98  
email: lali@adb.org.



Bi-annual Social Monitoring Report Tr. 2 July-Dec 2016.doc



Bi-annual Social Monitrg. Report Tr.3 July-Dec 2016.docx



## Bi-annual Social Monitoring Report

---

**Project Number:** 2972-PAK

***Pakistan (Power Distribution Enhancement Investment Program-Multi-Tranche Financing Facility-Tranche-3)***

***For period:*** July–December 2016

(Financed by the Asian Development Bank)

***Gujranwala Electric Power Company (GEPCO)***

PMU Section 565-A Model Town G.T Road Gujranwala, Pakistan.

Executing Agency (EA) Pakistan Electric Power Company (PEPCO)

Implementing Agency (IA) GEPCO

**Asian Development Bank**

*This report does not necessarily reflect the views of ADB or the Government concerned. The ADB and the Government cannot be held liable for its contents.*

## DEFINITION OF TERMS


Affected Persons (AP'S)	People (households) affected by project-related (or household) changes in use of land, water or other natural resources Compensation Money or payment in kind to which the people affected are entitled in order to replace the lost asset, resource or income.
Displaced persons.	In the context of involuntary resettlement, displaced persons are those who are physically displaced (relocation, loss of residential land, or loss of shelter) and/or economically displaced (loss of land, assets, access to assets, income sources, or means of livelihood) as a result of (i) involuntary acquisition of land, or (ii) involuntary restrictions on land use or on access to legally designated parks and protected areas.
Compensation	Payment in cash or in kind for an asset or a resource that is acquired or affected by a project at the time the asset needs to be replaced.
Cut-off Date	The completion date of the census of project-displaced persons is usually considered the cut-off date. A cut-off date is normally established by the borrower government procedure that establishes the eligibility for receiving compensation and resettlement assistance by the project displaced persons. In the absence of such procedures, the borrower/client will establish a cut-off date for eligibility.
Due diligence Report	Projects which do not have any significant social impacts hence do not involve/ require any land acquisition therefore; a brief due diligence report (DDR) is prepared for the documentary requirements.
Encroachers	Those people who move into project area after the cut-off date and are therefore not eligible for compensation or other rehabilitation measures provided by the project.
Entitlement	Range of measures comprising compensation, income restoration, transfer assistance, income substitution, and relocation which are due to affected people, depending on the nature of their losses, to restore their economic and social base
Economic displacement.	Loss of land, assets, access to assets, income sources, or means of livelihood as a result of (i) involuntary acquisition of land, or (ii)

	involuntary restrictions on land use or on access to legally designated parks and protected areas.
Resettlement effect	Loss of physical and non-physical assets, including homes, communities, productive land, income-earning assets and sources, subsistence, resources, cultural sites, social structures, networks and ties, cultural identity, and mutual help mechanisms.
Resettlement Field Survey	The detailed inventory of losses that is completed after detailed design and marking of project boundaries on the ground, socioeconomic data on the affected households/families, and stakeholder consultations.
Social Impact assessment	Social Impact Assessment is analyzing, monitoring, and management of social consequence of development interventions project infrastructure.
Vulnerable Group	Distinct groups of people who might suffer disproportionately from resettlement effects
Resettlement Field Survey	The detailed inventory of losses that is completed after detailed design and marking of project boundaries on the ground, socioeconomic data on the affected households /families, and stakeholder consultations.

# 1 INTRODUCTION

## 1.1- **GEPCO**

Gujranwala Electric Power Company Ltd. GEPCO is a Public Limited Utility Company, established in 1998 under Companies Ordinance 1984 and is responsible for distribution of Electric Power within its territorial jurisdiction and presently serving approximately 2.5 Million Customers (Domestic, Commercial, Agricultural, Industrial and others) in the six districts of Province Punjab (Gujranwala, Narowal, Gujrat, Hafizabad, Sialkot and Mandi-Bahawal-din).

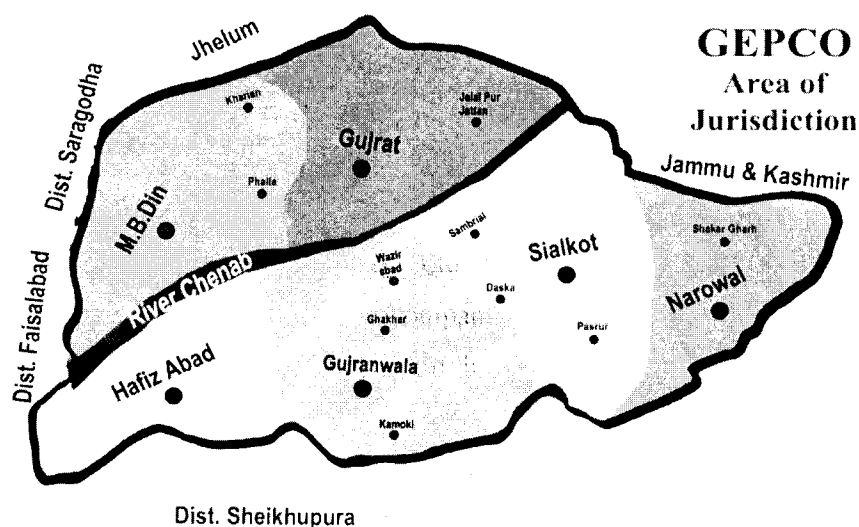

## **Project Management Unit (PMU)**

- 1.2 To effectively plan, execute and monitor the Power Distribution Enhancement Investment Program (Tranche-3), a Project Management Unit (PMU) has been established under Chief Engineer (Development) comprising of four sections i.e. Planning, Scheduling & Coordination, Procurement, Finance, Environmental and Social Safeguard along with Project Director (GSC). Organogram of PMU/ Development Directorate is placed at *Annexure-A*.

## 2 Project Overview

- 2.1 GEPCO through GOP has undergone a loan, project and financing agreement with the Asian Development Bank under Power Distribution Enhancement Investment Project Tranche-III in order to strengthen its existing distribution, transmission infrastructure and institutional capacity. The detail regarding project is summarized below:

<b>Loan Number</b>	ADB-2972 PAK
<b>Project Title</b>	Power Distribution Enhancement Investment Program_Multi-tranche financing facility (PDEIP_MFF_Tranche_3 (STG))
<b>Borrower</b>	Islamic Republic of Pakistan
<b>Executing Agency</b>	Pakistan Electric Power Company (PEPCO)
<b>Implementing Agency</b>	Gujranwala Electric Power Company (GEPCO)
<b>Loan Approval Date</b>	14-12-2012
<b>Loan Signing Date</b>	09-09-2013
<b>Effectiveness Date</b>	10-12-2013
<b>Loan Closing Date</b>	31-12-2016 (Original)
<b>Amount of Loan</b>	9.100 Million US\$

## 3 Scope of Work

- 3.1 There are 04 No. of GEPCO proposed projects under ADB Tranche-3. Its detail is here as under:
1. Conversion of 04 No. existing 66kV Grid Stations (Daska, Head-Marala, Siranwali & Malikwal) to 132kV along with 132kV Tr./Lines as an allied component.
  2. Associated transmission line component will be executed by GEPCO own sources (*Table: 3.1*).

Overall the proposed MFF has been designed to address both investment and institutional aspects in electric power sector. Development Objectives/ Project Purpose will be fully achieved after completion of the proposed sub-projects.



**Table: 3.1a**

Grid Stations Under Tranche-III						
Sr. No	Grid Stations		Feeding Line			Total Cost (Rs. Million)
	Name	Cost (Rs. Million)	Name	Length (Km)	Cost (Rs. Million)	
1	Daska	250	In & Out of New Daska-Sahowala T/Line at Daska 132 kV G/S	2.706	35	285
2	Siranwali	207	Kot Agha- Siranwali (Feed for 132kV Siranwali G/S)	14.874	112	319
3	Head Marala	207	Kotli Loharan-Head Marala (Feed for 132 kV Head Marala G/S)	6.443	45.5	252.5
4	Malikwal	207	In & Out of Bhalwal-Kuthiala Shiekhan at Malikwal G/S	29.025	171	378
Total						1234.5

**Table: 3.1b**

GEPCO Tranche 3 Projects						
Project Number	Associated Project	Project Name	Type of Project	Quantity of Projects	DISCO Estimated Cost (Millions PKR)	SMEC Estimated Costs Excluding Administrative Costs
G1	132 kV Kothiala Shaikan - Malikwal Transmission Line	Malikwal	Conversion from 66kV to 132kV	1	250	207
G2	132 kV Kotli Loharan - Head Marala Transmission Line	Head Marala	Conversion from 66kV to 132kV	1	250	207
G3	132 kV Kot Agha - Siranwali Transmission Line	Siranwali	Conversion from 66kV to 132kV	1	250	207
G4	132 kV New Daska - Daska Transmission Line	Daska	Conversion from 66kV to 132kV	1	325	287
			Total Conversion from 66kV to 132kV	4	1,075	908
			Total Projects	4	1,075 PKR Million	908 PKR Million

#### 4 Project Construction/ Civil Works Activities

- 4.1 There is 01 Contractor M/s Sinosteel Equipment & Engg. Manufacturing Co. engaged by GEPCO to execute civil work activities at sub-project sites (Photographs of civil works attached at Annexure-B).
- 4.2 Construction activities and project progress during previous 6 months: The control house building works at Daska & Siranwali grid station have been completed and at other two project sites (Malikwal & Head Marala) is under progress. The structuring works in yard area has been completed and leveling, land filling & civil works of tranches and approach paths is under progress at four project sites (Daska, Head Marala, Siranwali and Malikwal).

**Table 4.1: Progress of Conversions of Grid Stations Under ADB Funded Tranche # 3**

Project No.	Name of G/S	Loan No.	Name of Contractor/ Sub-Contractor	Civil & Electrical Work	Target Date
G1	Conversion of Old Daska GS from 66KV to 132 KV	ADB-2972-PAK-PDEIP-MFF-Tr.# 3	SINOSTEEL/ZEC	91 % of Civil works and 25 % of electrical works has been completed at all projects sites.	Expected Completion date for all four Sub-projects is 31 <sup>st</sup> March, 2017.
G2	Conversion of Siranwali GS from 66KV to 132 KV	-do-			
G3	Conversion of Malakwal GS from 66KV to 132 KV	-do-	SINOSTEEL/CME		
G4	Conversion of Head Marala GS from 66KV to 132 KV	-do-			

\*ZEC Zain Engineering Company

\*CME Chaudhry Meraj Engineering

- 4.3 The civil works of associated transmission line component has been started at 132kV feeding transmission lines for Siranwali, Daska and Head Marala grid stations.
- The Foundation & Erection works of 132kV Kotli Loharan- Head Marala & 132kV Kot Agha-Siranwali transmission line have been completed and Stringing works is in progress. Whereas the pile Foundation works of 132 kV feeding transmission line Daska have been started. The Foundation works of six no. of locations have been completed so far. The works order for tower foundation of Kuthiala Sheikhan\_Malikwal T/line is under progress.
  - The civil works progress status of all four transmission lines is as under;

**Progress of 132 kV T/Lines under GEPCO Own Resources, Allied Component under ADB Funded Tranche # 3**

<b>Table 4.2: Progress of 132 kV T/Lines Under GEPCO Own Resources, Allied Component Under ADB Funded Tranche # 3</b>									
<b>Project No.</b>	<b>Name of Tr./Lines</b>	<b>Funding Head</b>	<b>Length (Km)</b>	<b>No. of Towers/Poles</b>	<b>No. of Foundations Completed</b>	<b>No. of Erected Towers</b>	<b>Length of Stringing completed (Km)</b>	<b>Progress Status (%)</b>	
<b>G1</b>	132 kV New Daska - Daska Transmission Line	GEPCO Own Resources	2.706	19	06	-	-		
<b>G2</b>	132 kV Kot Agha - Siranwali Transmission Line		14.874	52	48	48	4.2 Km	65%	
<b>G3</b>	132 kV Kothiala Shaikhani - Malikwal Transmission Line		29.025	106	-	-	-		
<b>G4</b>	132 kV Kotli Loharan - Head Marala transmission Line		6.443	29	28	28	1.2 Km	60%	

## 5 Social Monitoring & Management

- 5.1 Clauses regarding Social safeguards have been provided to the procurement section to include in the bidding documents and EMMP & RP is the part of Bidding Document of STG Projects on turnkey basis.
- 5.2 04 No. Draft Land Acquisition and Resettlement Plans LARPs of Malikwal, Head Marala, Siranwali and Daska has been approved by ADB. PMU GEPCO to ensure that all 04 No. LARPs be updated/ revised as per current & approved 132kV profile/ route map T/line. (Details attached at **Annex- C**)
- 5.3 Proper implementation of the land acquisition plan and expropriation, including considerations concerning vulnerable groups among land-owners, farmers, and farm workers and minimization of adverse impacts due to the property acquisition and resettlement are mitigated according to the LARP.
- 5.4 The land for all grid stations is in the possession of GEPCO. No involuntary resettlement is involved as land for Malikwal, Head Marala, Siranwali and Daska is already in GEPCO possession. No compensation is involved in conversion of all four sub-projects, as the land is already in GEPCO possession. However, the allied component 132kV feeding transmission lines for all the four sub-projects is under GEPCO own sources. Compensation for Foundation stage works have already been paid, while for the Erection works is under progress.

**Table 5.1: GEPCO LARP'S IMPLEMENTATION STATUS TRANCHE # III**

Project No.	Name of G/S	Effective Date	Crop Compensation	Resettlement
<b>G1</b>	Conversion of Old Daska GS from 66KV to 132 KV	10/12/2013	Grid Stations Lands are already in GEPCO's possession, for T/Line compensation is under progress.	Not Required
<b>G2</b>	Conversion of Siranwali GS from 66KV to 132 KV	10/12/2013		-do-
<b>G3</b>	Conversion of Malakwal GS from 66KV to 132 KV	10/12/2013		-do-
<b>G4</b>	Conversion of Head Marala GS from 66KV to 132 KV	10/12/2013		-do-

- 5.5 Approved draft LARPs (Land Acquisition and Resettlement Plans), Public Notice in Urdu and English, Complaints Register of Malikwal, H/Marala, Siranwali and Daska has been placed / disclosed at sub-project site. (Details attached at **Annex-D**). All the

required documents (LARPs, Public Notice and Complaint register) have been handed over to the project site in-charge at under construction grid stations. The project site/ camps site/ grid station have been designated as grievance focal points. All the complaints/ grievances received being resolved on site in coordination with GEPCO GRC members.

- 5.6 Pak. Rs. 509,165.00/- have been disbursed/ compensated within 37 No.of AHs till 30<sup>th</sup> December, 2016 for all the allied transmission lines of tranche #3 . Table 5.2 shows the detail of LARP implementation cost against each sub-projects and the actual disbursed amount against the no. of affectees of Tr. # 3 Sub-Projects.

**Table 5.2 (a): Total Disbursed Amount of Tr. # III Sub-projects**

Sr.No.	Sub-Project Names	LARPs Implementation Cost (In PAK Rs.)	Disbursed Amount till Dec. 2016 (In PAK Rs.)	Remarks
1	Conversion of Head Marala Gr. Station from 66kV to 132kV and associated Double Circuit 132kV Transmission Line	5,644,455.30	203,125.00	Compensation under progress
2	Conversion of Daska Gr. Station from 66kV to 132kV and Associated 132kV Double Circuit Transmission Line	5,894,198.00		
3	Conversion of Malikwal Gr. Station from 66kV to 132kV and associated Double Circuit Transmission Line	5,717,888.00		
4	Conversion of Siranwali Gr. Station from 66kV to 132kV and associated 132kV Double Circuit Transmission Line	5,928,655.00	306,040.00	
		23,185,196.30	509,165.00	

**Table 5.2 (b) : LARP(s) Status      TRANCHE-III Allied Component      as on December, 2016**

Sr.#	Sub Project Name	Revised LARP/DDR approved by ABD	Compensation Status (Total No. of Compensated APs/AHHs)			Compensated Amount	Remarks
			Foundation Stage	Erection Stage	Stringing Stage		
1	132 kV New Daska - Daska Transmission Line	13/11/2012	-	-	-		Compensation under progress
2	132 kV Kot Agha - Siranwali Transmission Line	13/11/2012	22	-	-	306,040	
3	132 kV Kothiala Shaikhan - Malikwal Transmission Line	13/11/2012	-	-	-	-	
4	132 kV Kotli Loharan - Head Marala transmission Line	13/11/2012	15		-	203,125	
	<b>Total</b>		37	-	-	509,165	

**Table 5.3: Total no. of Cheques distributed in Tranche # 3 Allied Component**

Sub Project Name	Total No of DP's as per Revised LARP	Compensated AHs/ Total no. of cheques Disbursed	Remaining no. of AHs to be compensated	Total Amount Paid
132 kV New Daska - Daska Transmission Line	225	-	225	-
132 kV Kot Agha - Siranwali Transmission Line	205	22	183	306,040
132 kV Kothiala Shaikhan - Malikwal Transmission Line	195	-	195	-
132 kV Kotli Loharan - Head Marala transmission Line	215	15	200	203,125
<b>Total</b>	<b>840</b>	<b>37</b>	<b>803</b>	<b>509,165</b>

- 5.7 Environment and Social training/ workshop conducted at different sites (Siranwali, Head Marala, Daska and Malikwal) grid stations and transmission lines. The capacity building of contractor/ labors/ workers on social issues; workers health, communicable disease, grievance redressal procedure, Compensation process

according to civil works activities, social norms & values of the area, hiring of local CNIC holder labor to avoid child labor, safety issues, use of PPEs, availability of properly equipped first aid boxes, site aesthetic value (segregation of waste materials, water sprinkling, oil leakages and spillages etc.) being carried out twice a year at each project site for smooth working. (detail provided at Annexure-E)

- 5.8 Permission/consent from the formers (APs) were taken for civil works activities.
- 5.9 Contractor/workers were instructed to take into the account of local norms & values and hiring of local labor to increase the employment opportunities of the area and avoidance of child labor at project site by keeping the CNIC record of all workers/ labor.
- 5.10 Public Consultation were conducted at different location of allied transmission line component, in which people were informed about the Crops/trees/building damages and their compensation payment and process and finally they were paid compensation for the Foundation stage works. (detail provided at Annexure-F)
- 5.11 Verification of kharaba (compensation) payments carried out through random sampling by verifying the actual affectees' name, CNIC, damaged crop/ tree.
- 5.12 GSC staff and on site briefing to the contractor has also be given for effective implementation of LARPs during site visits. The GSC staff which involves in the construction of grid station and transmission line activities has been apprised regarding social aspects of the subprojects. A monthly progress review meeting is carried out in the office of C. E. Dev. (PMU) GEPCO. In which the GSC staff briefed about the LARP implementation and the compensation status. The concerned GSC staff for LARP implementation is as under:
  - Project Director (GSC)
  - XEN Transmission Line Construction
  - SDO Transmission Line Construction
  - Assistant Land Acquisition Officer (ALAO)
  - Qanoongo/ Patwari GEPCO
  - Transmission line Surveyor
- 5.13 GSC (T&G) Division is making assessment payment to the affected persons of feeding transmission line of Malikwal, Head Marala, Siranwali and Daska. Compensation will be paid on actual basis to each affected persons in three stages (construction of foundation and Erection of tower and stringing of conductor).

- 5.14 Assessment for payments for the feeding lines of Siranwali and Head Marala for Erection Stringing works was carried out in the month of November and December 2016. Whereas, the compensation for Foundation stage works has already been disbursed. After that a noting initiated by the GSC division having affectee's data (Name, CNIC, document of ownership and amount to be paid) for further verification/ audit and approval for disbursement of amount to affectees. Compensation cheques will be disbursed through committee formulated by P.D GSC.
- 5.15 Internal monitoring of the projects carried out by Environmental and Social Safeguard (E&SS) section PMU, GEPCO on fortnightly basis during the execution phase for the smooth working at projects sites.
- 5.16 Environment and Social training/ workshop conducted at different sites (Siranwali, Head Marala, Daska and Malikwal) grid stations and transmission lines considering the following points; (date & location of workshop snaps)
- Proper office for sitting arrangements, computer, racks to keep office record.
  - Environmental & social safeguard record (environmental, social reports, Urdu notice etc)
  - Accidents/ incident log book/ register.
  - Copy of Land Acquisition and Resettlement Plan (LARP)
  - Social complaint register
  - Provision of PPEs (helmets, safety shoes, masks, overall)
  - First aid training with first aid box facility (with all medicines)
  - Firefighting drill record and fire cylinders (01 DCP, 01 carbon dioxide)
  - Scrap yard (for collection, segregation of waste)
  - Proper housekeeping (use of tool box kit) no slip, trip & fall hazard.
  - Provision of soil investigation, laboratory test records of air, noise & water at work site.
  - Water sprinkling activity record.
  - Provision of earth leakage circuit breakers (ELCB) and No expose wiring
  - Safety policy in Urdu/ English.
  - Notice in Urdu to affectees in local language.
  - MSDS (material safety data sheets) of used chemicals, oil etc.
  - Observe oil leakage/ spillage from concrete mixing machines.
  - Marking of Smoking & Assembly areas.
  - Provision of attendance, weekly rest & leave record



- No child labor (temporary/permanent labor without holding CNIC)
- Local labor shall be given preference.
- Cutting of over grown herbs & shrubs.
- Keep good relations with local community NO NUISANCE
- Observe traffic speed of 10 KMs at work site.
- Provision of 01 weekly rest/ holiday, good living facility washrooms etc.
- Provision of hygienic food for local labor.
- Proper drainage for accumulated water in rainy season to avoid waterborne diseases and insects.


## **7 Grievance Redressal**

- 7.1 Environmental & Social Complaint Register (SCR) in English and Urdu version has been prepared and placed at active site in order to register the grievances and complaints of the stakeholders and GEPCO will also ensure for same at the other project sites but no significant complain have been received yet. The site incharge is responsible for maintaining the complaints record.
- 7.2 Grievance Redressal Committee (GRC) has been notified for Tranche III in order to comply with the Grievance Redressal Mechanism (GRM) described in LARPs. The Organogram of GRC is given below:

- |  |                   |
|--|-------------------|
| • Manager (P.S&C)                      | Convener          |
| • P.D (GSC)                            | Member/ Secretary |
| • Dy. Manager TLC                      | Member            |
| • A.M (Social Safeguard / Environment) | Member            |
| • ALAO/ LAO (GSC)                      | Member            |




**Annexure- A**

**Organogram**

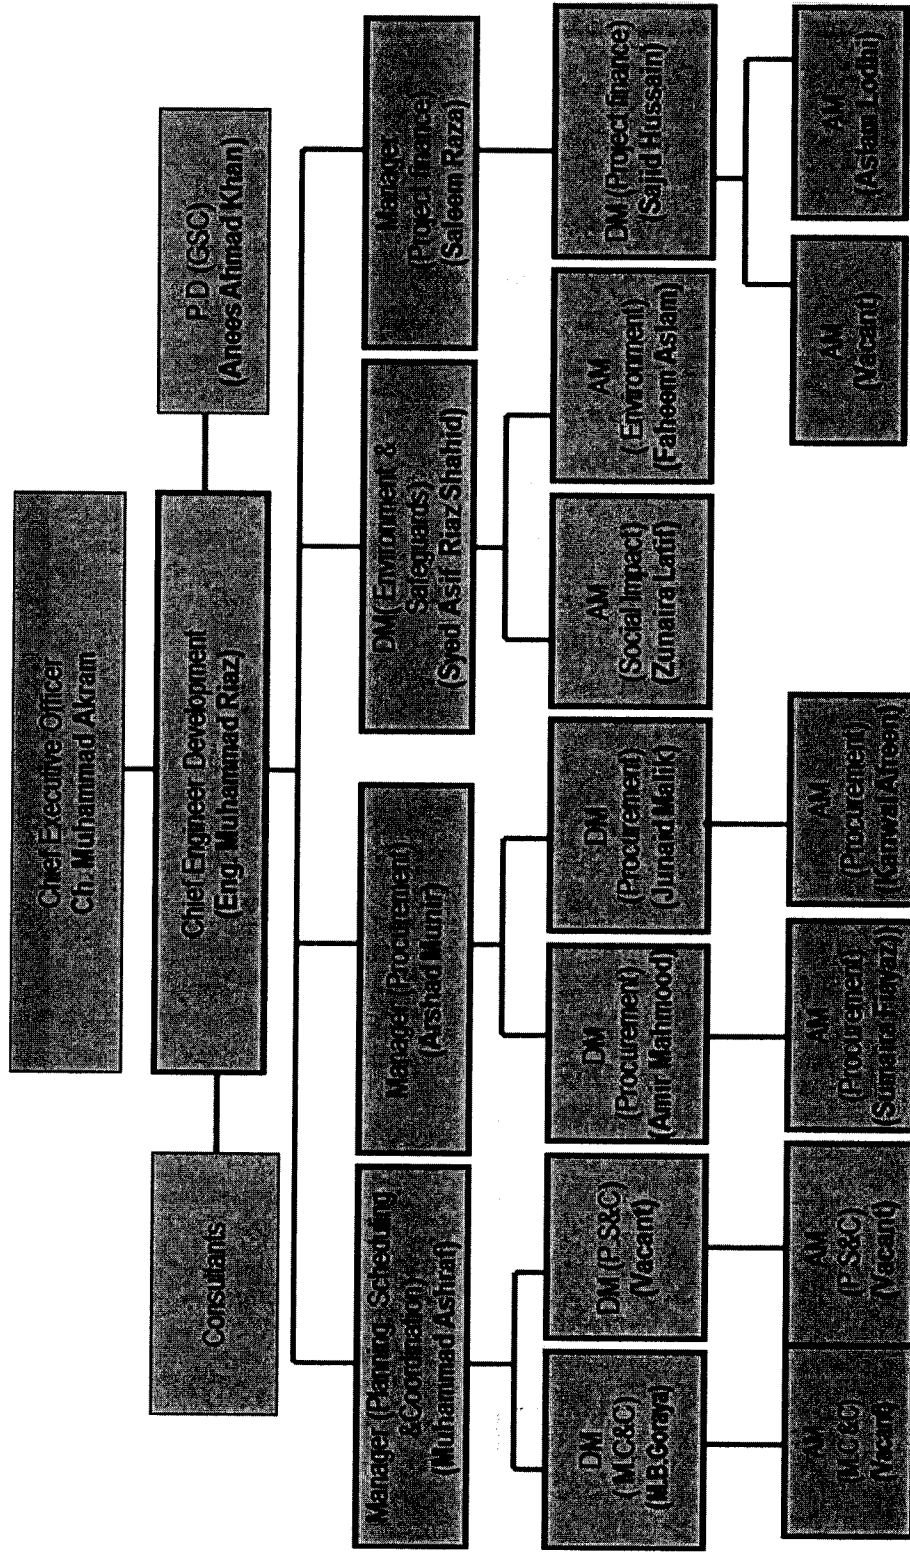

**Annexure- B**

**Civil Works at Tr. # 3 Substations (Malikwal, Daska, Siranwali  
and Head Marala)**

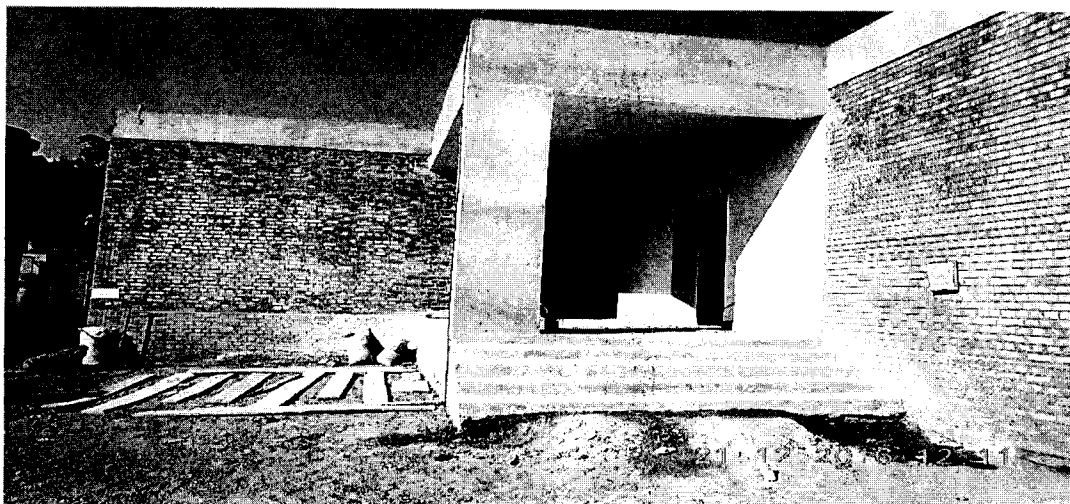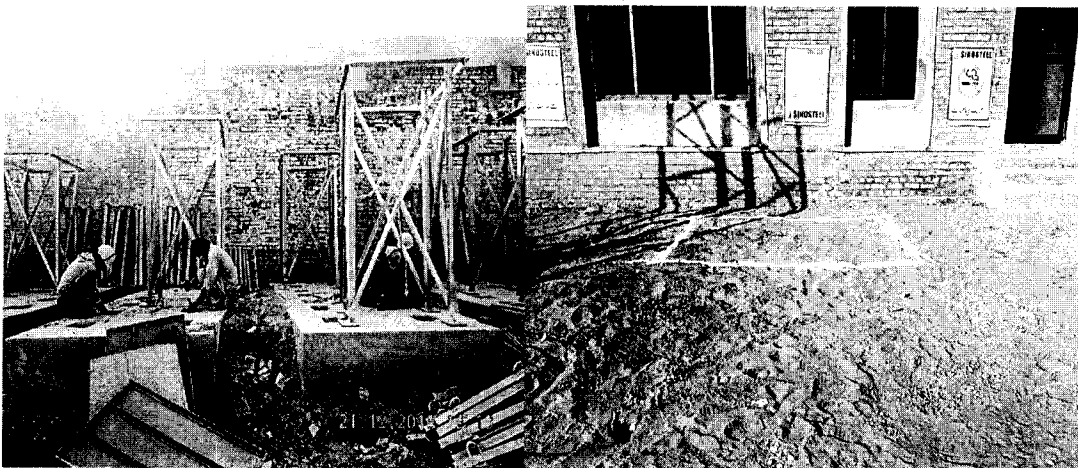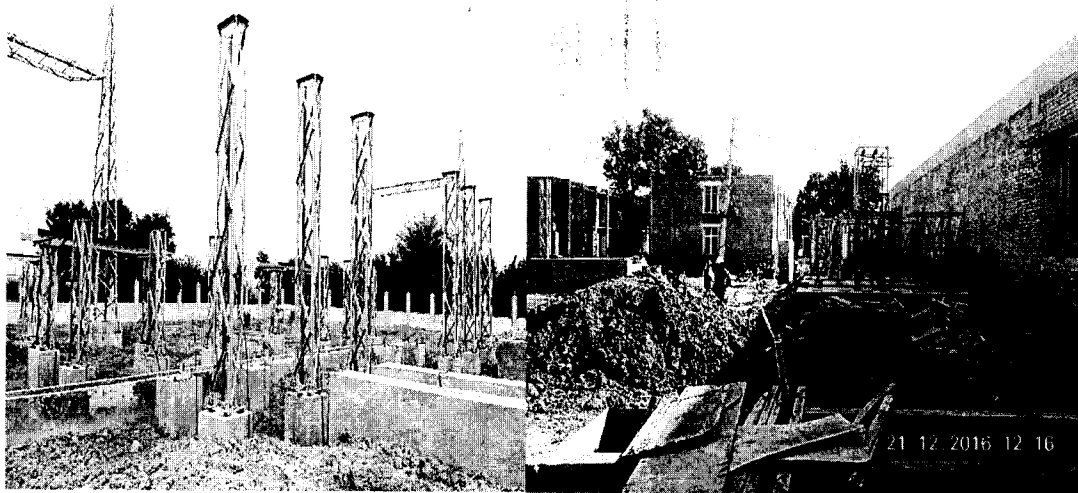

## Annexure- C

### *Revised Rates of Trees (FY-2016)*

10/01/2016  
DIVISIONAL FOREST OFFICER, SIALKOT FOREST DIVISION, SIALKOT  
Phone & Fax No. 052-4296016.

To,

The Manager (PS&C),  
PMU GEPCO H.Q. Gujranwala,  
565-Model Town G.T Road Gujranwala.

No. 354 /LC Dated Sialkot, the 01/02/2016.

Subject: - **REVISED RATE OF TREES AND CROPS (FY 2014-15) REQUIRED FOR ASIAN DEVELOPMENT BANK (ADB) FUNDED PDEIP-TRANCHE-3 SUB-PROJECTS.**

Reference: - Your office letter No. 187-90/PMU dated 29-01-2016.

As desired in your letter cited under reference the required rate of the trees are given as under.

Sr No.	Species	Girth in Inches	Rates	
1.	Shisham	0 to 23"	2000/-	
2.	do	24 to 36"	3000/-	
3.	do	37 to 49"	7200/-	
4.	do	50 to 62"	16000/-	
5.	do	63 to 75"	26000/-	
6.	do	76 to 88"	43000/-	
7.	do	89 to 101"	51000/-	
8.	do	102 to 114"	71000/-	
9.	do	115" to above	93000/-	
10.	Eucalyptus - Popular	0 to 23"	1260/-	
11.	Bakri	do	24 to 36"	1420/-
12.	do	37 to 49"	2200/-	
13.	do	50 to 62"	5700/-	
14.	do	63 to 75"	9100/-	
15.	do	76 to 88"	11800/-	
16.	do	89 to 101"	15200/-	
17.	do	102 to 114"	18550/-	
18.	do	115" to above	22600/-	

AD (Env.)  
Pir  
D. Singh  
27/01/2016  
DIVISIONAL FOREST OFFICER,  
SIALKOT FOREST DIVISION,  
SIALKOT.

١٩٥٥

۲۵۶  
نفس در پادشاه و در هر یک از شخص و از آن کثیر حساب فی بن تمیز و مع فی مادی و ادبیت

*[Handwritten signature]*

سدری کباد ارمین

نائب قیما اراض

سورۃ مجادہ انور سے

عبدالله بن محمد

نائب صدر قانون

شہزادہ ادریس

## Annexure- D

### *PUBLIC NOTICE IN LOCAL LANGUAGE*

## معلومات عامہ

گیپکو (گوجرانوالہ الیکٹرک پاور کمپنی) اپنے اختیاراتی اضلاع (سیالکوٹ اور منڈی بہاؤ الدین) میں بجلی کی ترسیل، تقسیم اور پھیلاؤ کے لیے ایس۔ ٹی۔ جی منصوبے مرحلہ سوم کے تحت ترقیاتی کاموں کا آغاز کر رہی ہے۔ اس منصوبے کے تحت ضلع سیالکوٹ اور منڈی بہاؤ الدین میں 132KV کے چار موجودہ گریڈ اسٹیشنز (سراوالی، ڈسکہ، حیدرآلہ اور ملکوال)، ضلع سیالکوٹ میں تین اور ضلع منڈی بہاؤ الدین میں ایک 66KV سے 132KV گریڈ اسٹیشنز کی منتقلی کا کام مکمل کیا جائیگا۔ اس طرح 4 نئی ٹرانسمیشن لائنوں کی تعمیر کا کام (ضلع سیالکوٹ میں تین اور ضلع منڈی بہاؤ الدین میں ایک) کیا جائیگا۔ مذکورہ بالا ذیلی منصوبوں کی تعمیر کا کام ایشیائی ترقیاتی بینک کی مالی معاونت سے مکمل کیا جائے گا۔ ایشیائی ترقیاتی بینک کی پالیسی کے مطابق گریڈ اسٹیشنز اور اسکی فیڈنگ ٹرانسمیشن لائنز کی ماحولیاتی و سماجی تخمینہ سازی کی گئی ہے اور حصول اراضی و بجائی متاثرین کا مختصر منصوبہ تیار کیا گیا ہے۔ جسے عوامی رابطہ پالیسی کے تحت گیپکو نے دفتر ہذا میں متعلقہ متاثرہ لوگوں کی معلومات کے لئے رکھا ہے۔

مزید معلومات کے لئے مندرجہ ذیل افراد سے رابطہ کیا جاسکتا ہے۔

رابطہ نمبر: 0092-55-9200593

چیف انجینئر ڈویلمنٹ گیپکو:

پتہ:- GEPCO H/Q, 565-A, Model Town, G.T. Road Gujranwala.

رابطہ نمبر: 0092-55-9239071

پراجیکٹ ڈائریکٹر (جی۔ ایس۔ سی) گیپکو

پتہ:- Project Director (GSC) GEPCO, 132KV Grid Station Awan Chowk, Gujranwala.

### **PUBLIC NOTICE (ENGLISH LANGUAGE)**

Gujranwala Electric Power Company (GEPCO) has started the Construction of its Secondary Transmission Grid (STG) sub-projects under Asian Development Bank (ADB) funded Power Distribution Enhancement & Investment Program (PDEIP\_MFF\_Tranche-3) Sub-projects of electricity transmission & distribution in its existing region. Under this ADB funded Tranche-3 sub-projects, there are 04 No. Conversions of existing 66kV Siranwali, Daska, H/Marala & Malikwal Grid Stations. Out of 04, 03 No. of Siranwali, Daska, H/Marala 66kV Grid Stations are located in district Sialkot while 01 No. 66kV Malikwal Grid Station is located in M.B.Din district. Similarly, the construction of new 04 No. 132kV T/lines (03 in district Sialkot and 01 in district M.B.Din) has started. These sub-projects are going to be executed with the financial assistance of Asian Development Bank. The Environmental & Social Impact Assessment (E&SIA) of aforesaid sub-projects has been carried out in compliance to the Asian Development Bank (ADB) Safeguard Policy Statement-2009; these reports have been disclosed for proper disclosure at GEPCO sub-project sites, office of P.D (GSC) and GEPCO official website.

In case of any query, further information or concern, Following GEPCO offices can be contacted:-

**1. O/O Chief Engineer Development**

PMU Section, GEPCO H.Q 565-A Model Town G.T Road Gujranwala

Phone No. 0092-055-9200593

**2. O/O P.D (GSC) GEPCO Gujranwala**

132kV Awan Chowk Grid Station, GEPCO Gujranwala

Phone No. 0092-055-9239071


**3. Mr. Sagheer Ahmad (Project Manager Construction)**

M/s Sinosteel Equipment & Engg. Manufacturing Co.

MobileNo. +92-0300-8640973

## Annexure-E

### Capacity building sessions on Environmental & Social safeguard



**GUJRANWALA ELECTRIC POWER COMPANY LIMITED**

565-A MODEL TOWN G.T. ROAD GUJRANWALA

Office of the Chief Engineer Development PMU

Phone # 9200538

Fax # 9200594

Memo No: 3216-12/PMU

Dated: 15/11/2016

The

✓ **Project Chief (Construction)**

**M/s Sinosteel Equipment & Engineering Manufacturing Co. China**


**Sub: CAPACITY BUILDING/ TRAINING PROGRAME ON ENV. & SOCIAL SAFEGUARD AT DASKA & MALIKWAL ADB FUNDED TR. III PROJECTS**

**Ref:** Meeting held with Project Manager Construction (M/s Sinosteel) in O/Q Manager (P.S&C) GEPCO H/Q on 10.11.2016.

With ref. to above, PMU GEPCO Environment and Social officers will conduct an internal/in-house capacity building sessions on Environmental & Social Safeguard on *17.11.16 (Thursday) at Malikwal Grid Station* and *18.11.16 (Friday) at Daska Grid Station* work sites. The main objective of this capacity building program is to enhance the skills of site construction staff, labor to implement the environmental, social, health and safety component of the power distribution expansion.

It is therefore requested to make sure the presence of all site construction staff, labor, civil & safety supervisor and labor on 17-11-2016 at Malikwal GS and on 18-11-16 at Daska GS work sites.

**Matter most urgent**

  
**Muhammad Ashraf**  
**Manager (P.S&C) PMU**  
**GEPCO H/Q Gujranwala**

**CC:**

1. The Chief Engineer (Development) PMU GEPCO, for his kind information please
2. Environmental Specialist ADB, for her kind information please





### Training Attendance Record

Training Course Title/Topic	ENVIRONMENT MANAGEMENT PLAN
Venue	CONVERSION OF KERV DASICA (LOCKSETS)
Duration	1 - HOUR
Date(s) of Delivery	23-11-2016
Training Company/ Organisation	GEPIA/WAPDA (GUJRANWALA H/O)
Trainer (Name)	FAHEEM ASLAM (A.D ENVIRONMENT) ZUNARA LATIF (A.D SOCIAL WELFARE)

No.	Attendee Name	Designation	Department	Signature
1	M. Rehan Shafiq	Supervisor	Civil	R. Shafiq
2	M. Shabbaz	Labour		Shabbaz
3	Imam ul Munir	Labour		Imam ul Munir
4	M. Yasin	Labour		M. Yasin
5	M. Asim	Labour		M. Asim
6	M. Ijaz	CARPENTER		M. Ijaz
7	M. Ijaz	CARPENTER		M. Ijaz
8	Zulfiqar	Driver		Zulfiqar



### Training Attendance Record

Topics Covered During Training Course	Site waste management, Occupational health & safety, Environment management, Social impacts & remedial measures during civil works, Local labour laws & communicable diseases
Venue	NATIONAL 66KV GS, M.R. DIN
Duration	1 HOUR
Date(s) of Delivery	17-11-2018 (THURSDAY)
Training Company/ Organisation	PMU Section GEPCO H.Q. Gujranwala
Trainer(s) Name	Faheem Aslam, Zunaira Latif

No.	Attendees Name	Designation	Department	Signature
1.	SHAHID SARAN	Civil Engineer	CME	<i>[Signature]</i>
2.	Adil Rehman	HSE officer	HSE	<i>[Signature]</i>
3.	DIORAN AKRAM	Electrical	CME	<i>[Signature]</i>
4.	Nazim Sikander	Worker	Civil	<i>[Signature]</i>
5.	Jabir Khan	Helper	Civil	<i>[Signature]</i>
6.	Hasan Ali	Helper	Electrical	<i>[Signature]</i>
7.	Sagheer Ahmad	Construction Manager	Civil	<i>[Signature]</i>

Py. No. 01 of 02.

Snap taken during Capacity Building Sessions

