

Implementation Status & Results
China
Shaanxi Small Towns Infrastructure Project (P133069)

Operation Name: Shaanxi Small Towns Infrastructure Project (P133069)	Project Stage: Implementation	Seq.No: 1	Status: ARCHIVED	Archive Date: 23-Nov-2014
Country: China	Approval FY: 2015			
Product Line: IBRD/IDA	Region: EAST ASIA AND PACIFIC	Lending Instrument: Investment Project Financing		
Implementing Agency(ies): Foreign Debt Management Office, Shaanxi Provincial Development and Reform Commission				

Key Dates

Board Approval Date	25-Sep-2014	Original Closing Date	31-Dec-2020	Planned Mid Term Review Date	Last Archived ISR Date
Effectiveness Date		Revised Closing Date	31-Dec-2020	Actual Mid Term Review Date	

Project Development Objectives

Project Development Objective (from Project Appraisal Document)

To improve the infrastructure and service delivery in selected small and medium towns in Shaanxi Province

Has the Project Development Objective been changed since Board Approval of the Project?

Yes No

Component(s)

Component Name	Component Cost
Infrastructure and Service Upgrading	253.90
Town Management Improvement and Project Implementation Support	3.00

Overall Ratings

	Previous Rating	Current Rating
Progress towards achievement of PDO		Satisfactory
Overall Implementation Progress (IP)		Satisfactory
Overall Risk Rating		Substantial

Implementation Status Overview

The project is in the early stages of implementation.

Locations

Country	First Administrative Division	Location	Planned	Actual
China	Shaanxi	Shaanxi		✓

Results

Project Development Objective Indicators

Public Disclosure Copy

Indicator Name	Core	Unit of Measure		Baseline	Current	End Target
Number of people in urban areas provided with access to Improved Water Sources under the project	<input checked="" type="checkbox"/>	Number	Value	0.00	0.00	151000.00
			Date	01-Jan-2014	07-Nov-2014	31-Dec-2020
			Comments			
Number of women in urban areas provided with access to Improved Water Sources under the project	<input type="checkbox"/>	Number Sub Type Breakdown	Value	0.00	0.00	72200.00
			Date	01-Jan-2014	07-Nov-2014	31-Dec-2020
			Comments			
People provided with access to "improved sanitation facilities" under the proj.	<input checked="" type="checkbox"/>	Number	Value	0.00	0.00	194500.00
			Date	01-Jan-2014	07-Nov-2014	31-Dec-2020
			Comments			
People provided with access to "improved sanitation facilities" - urban	<input checked="" type="checkbox"/>	Number Sub Type Breakdown	Value	0.00	0.00	194500.00
			Date	01-Jan-2014	07-Nov-2014	31-Dec-2020
			Comments			
Number of women provided with access to "improved sanitation facilities" under the project	<input type="checkbox"/>	Number Sub Type Breakdown	Value	0.00	0.00	94000.00
			Date	01-Jan-2014	07-Nov-2014	31-Dec-2020
			Comments			
Increase in area with access to newly built or rehabilitated roads	<input type="checkbox"/>	Square kilometer (km2)	Value	0.00	0.00	21.70
			Date	01-Jan-2014	07-Nov-2014	31-Dec-2020
			Comments			

Intermediate Results Indicators

Public Disclosure Copy

Indicator Name	Core	Unit of Measure		Baseline	Current	End Target
Roads constructed, non-rural	<input checked="" type="checkbox"/>	Kilometers	Value	0.00	0.00	40.00
			Date	01-Jan-2014	07-Nov-2014	31-Dec-2020
			Comments			
Roads rehabilitated, Non-rural	<input checked="" type="checkbox"/>	Kilometers	Value	0.00	0.00	34.00
			Date	01-Jan-2014	07-Nov-2014	31-Dec-2020
			Comments			
Wastewater sewers and storm drains constructed / rehabilitated	<input type="checkbox"/>	Kilometers	Value	0.00	0.00	168.00
			Date	01-Jan-2014	07-Nov-2014	31-Dec-2020
			Comments			

Length of water supply pipes laid	<input type="checkbox"/>	Kilometers	Value	0.00	0.00	45.50
			Date	01-Jan-2014	07-Nov-2014	31-Dec-2020
			Comments			
Counties/Districts implementing improved O&M plans with recommended budget allocations	<input type="checkbox"/>	Number	Value	0.00	0.00	9.00
			Date	01-Jan-2014	07-Nov-2014	31-Dec-2020
			Comments			
Counties/Districts completed infrastructure mapping	<input type="checkbox"/>	Number	Value	0.00	0.00	9.00
			Date	01-Jan-2014	07-Nov-2014	31-Dec-2020
			Comments			
Counties/Districts prepared asset registers	<input type="checkbox"/>	Number	Value	0.00	0.00	9.00
			Date	01-Jan-2014	07-Nov-2014	31-Dec-2020
			Comments			

Data on Financial Performance (as of 26-Sep-2014)


Financial Agreement(s) Key Dates

Project	Ln/Cr/Tf	Status	Approval Date	Signing Date	Effectiveness Date	Original Closing Date	Revised Closing Date
P133069	IBRD-84250	Not Effective	25-Sep-2014			31-Dec-2020	31-Dec-2020

Disbursements (in Millions)

Project	Ln/Cr/Tf	Status	Currency	Original	Revised	Cancelled	Disbursed	Undisbursed	% Disbursed
P133069	IBRD-84250	Not Effective	USD	150.00	150.00	0.00	0.00	150.00	0.00

Disbursement Graph

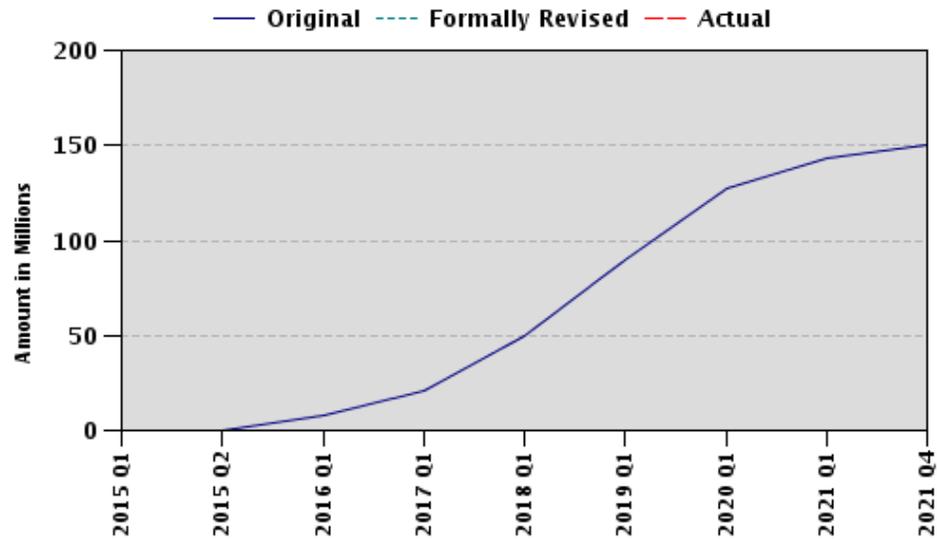

Key Decisions Regarding Implementation

The client should make Loan and Project Agreements effective by February 2,2015. The Bank and client should together plan and hold the project launch workshop.

Restructuring History

There has been no restructuring to date.

Related Projects

There are no related projects.
