



China: Gansu Rural-Urban Integration Project (P132775)

EAST ASIA AND PACIFIC | China | Transport Global Practice |
IBRD/IDA | Investment Project Financing | FY 2015 | Seq No: 1 | ARCHIVED on 16-Jun-2015 | ISR19783 |

Implementing Agencies: GansuProvincial Project Team

Key Dates

Key Project Dates

Board Approval date:31-Mar-2015

Effectiveness Date:--

Planned Mid Term Review Date:22-Oct-2018

Actual Mid-Term Review Date:--

Original Closing Date:30-Jun-2021

Revised Closing Date:30-Jun-2021

Project Development Objectives

Project Development Objective (from Project Appraisal Document)

The project development objective is to provide residents in Wuwei Municipality and Linxia Prefecture with improved connectivity between rural and urban areas.

Has the Project Development Objective been changed since Board Approval of the Project Objective?

No

Components

Name

Component A: Wuwei Road Network Improvement:(Cost \$138.56 M)

Component B: Linxia Road Network Improvement:(Cost \$73.30 M)

Component C: Technical Assistance:(Cost \$4.07 M)

Overall Ratings

Name	Previous Rating	Current Rating
Progress towards achievement of PDO	--	● Satisfactory
Overall Implementation Progress (IP)	--	● Satisfactory
Overall Risk Rating	--	● Substantial



Implementation Status and Key Decisions

The project is currently on track to be effective by September 30, 2015.

To date, four civil works contracts under the Linxia component have been signed, which will be supported through retroactive financing.

Risks

Systematic Operations Risk-rating Tool

Risk Category	Rating at Approval	Previous Rating	Current Rating
Political and Governance	--	--	● Moderate
Macroeconomic	--	--	● Low
Sector Strategies and Policies	--	--	● Low
Technical Design of Project or Program	--	--	● Substantial
Institutional Capacity for Implementation and Sustainability	--	--	● Substantial
Fiduciary	--	--	● Moderate
Environment and Social	--	--	● Moderate
Stakeholders	--	--	● Moderate
Other	--	--	--
Overall	--	--	● Substantial

Results

Project Development Objective Indicators



► Share of rural population with access to an all-season road (Percentage, Core)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	65.00	--	65.00	78.00
Date	23-Sep-2014	--	12-Jun-2015	30-Jun-2021

▲ Number of rural people with access to an all-season road (Number, Core Supplement)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	978000.00	--	978000.00	1166000.00

► Share of Rural women with Access to an All-Season Road (Percentage, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	65.00	--	65.00	78.00
Date	23-Sep-2014	--	12-Jun-2015	30-Jun-2021

► Travel time savings on rehabilitated roads (Text, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0%	--	0%	39%
Date	23-Sep-2014	--	12-Jun-2015	30-Jun-2021

► Travel time savings between select O-D pairs connected partially by newly constructed or rehabilitated roads (Text, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0%	--	0%	8%



Date	23-Sep-2014	--	12-Jun-2015	30-Jun-2021
------	-------------	----	-------------	-------------

Overall Comments

Intermediate Results Indicators

► Roads rehabilitated, Rural (Kilometers, Core)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	--	0.00	53.50
Date	23-Sep-2014	--	12-Jun-2015	30-Jun-2021

► Roads constructed, non-rural (Kilometers, Core)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	--	0.00	55.40
Date	23-Sep-2014	--	12-Jun-2015	30-Jun-2020

► Preparation of long term maintenance strategies (Text, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0%	--	0%	100%
Date	23-Sep-2014	--	12-Jun-2015	30-Jun-2021



▶ Number of counterparts who attended training and study tours (Text, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0	--	0	345
Date	23-Sep-2014	--	12-Jun-2015	30-Jun-2021

▶ Number of project villages with new streetlight and/or traffic calming measures (Text, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0	--	0	150
Date	23-Sep-2014	--	12-Jun-2015	30-Jun-2021

Overall Comments


Data on Financial Performance**Disbursements (by loan)**

Project	Loan/Credit/TF	Status	Currency	Original	Revised	Cancelled	Disbursed	Undisbursed	Disbursed
P132775	IBRD-84800	Not Effective	USD	150.00	150.00	0.00	0.00	150.00	0%

Key Dates (by loan)

Project	Loan/Credit/TF	Status	Approval Date	Signing Date	Effectiveness Date	Orig. Closing Date	Rev. Closing Date
P132775	IBRD-84800	Not Effective	31-Mar-2015	25-May-2015	--	30-Jun-2021	30-Jun-2021

Cumulative Disbursements

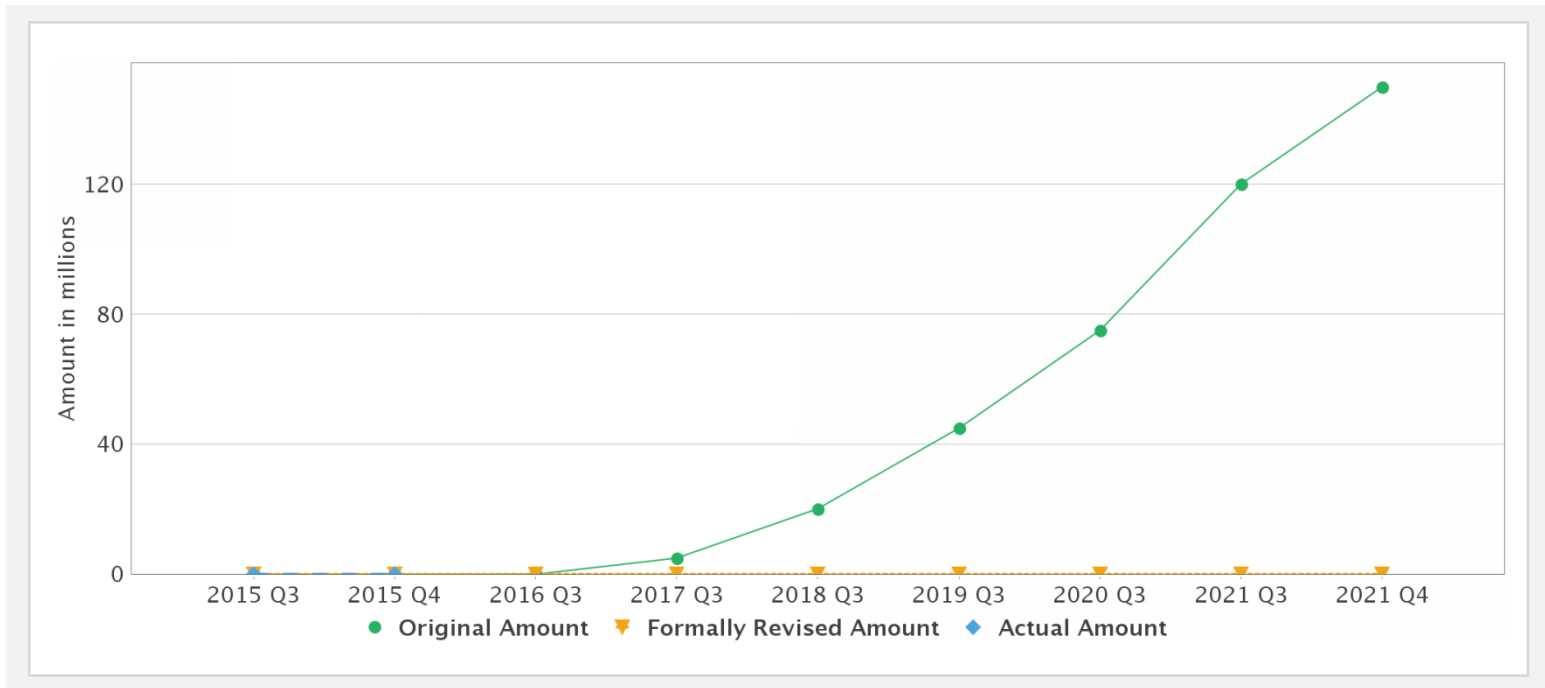

Restructuring History

There has been no restructuring to date.

Related Project(s)

There are no related projects.
