Implementation Status & Results Honduras

HN Water and Sanitation Sector Modernization Project (P103881)

	Vater and Sanitat 3881)	ion Sector Modernization Project	Project Stage:	Implementation	Seq.No: 15	Status: ARCHIVED	Archive Date	e: 06-Mar-20
		Country: Honduras		Approval FY	2007			
Product Line: IBRD/IDA		Region: LATIN AMERICA A	ND CARIBBEAN	Lending Inst	rument: Specific	c Investment Loan		
Implementing Agency(ie	es):							
Key Dates								
Board Approval Date	21-Jun-2007	Original Closing Date 31-Dec-201	3 Planne	d Mid Term Review Dat	e 31-May-20	11 Last Archiv	ed ISR Date 1	9-Aug-2013
Effectiveness Date	22-Feb-2008	Revised Closing Date 31-Dec-201	6 Actual	Mid Term Review Date	05-May-20	11		

Project Development Objectives

Project Development Objective (from Project Appraisal Document)

Revised project development objective: to support the Recipient to improve: (a) the sustainability, efficiency, and reliability of its WSS services in Eligible Municipalities; (b) the performance of its national WSS sector institutions in the exercise of their respective roles in accordance with the WSS Sector Framework Law; and (c) its capacity to respond promptly and effectively to an Eligible Emergency.

Has the Project Development Objective been changed since Board Approval of the Project?

● Yes ○ No

Component(s)

Component Name	Component Cost	
Component 1: Support to medium-size municipalities to create autonomous service providers and invest in efficiency, rehabilitation,	21.20	
Component 2: Tegucigalpa Non-Revenue Water Reduction	4.50	
Component 3: Institutional strengthening of national and regional sector institutions	7.20	
Component 4: Project management	1.60	
Component 5: IRM Contingent Component	0.00	


Overall Ratings

_	-	Previous Rating	Current Rating
F	Progress towards achievement of PDO	Moderately Satisfactory	Moderately Satisfactory
(Overall Implementation Progress (IP)	Moderately Satisfactory	Moderately Satisfactory
(Overall Risk Rating		

Implementation Status Overview

Public Disclosure Authorized

Public Disclosure Copy



This ISR presents the project situation as of February 12, 2014 and reports on the main activities and project related events occurred from August 2013 to January 2014.

The Project's progress towards the achievement of its Development Objectives and the implementation pace continue to be moderately satisfactory. The Financing Agreement relative to the US\$10 million Additional Financing Credit (AF) approved for the Project became effective on October 9, 2013. To date, all original Project funds have been allocated/ committed and US\$18.3M (92.5% of Project funds) has been disbursed. Regarding the AF, to date US\$1M have been allocated/committed and US\$ 1M (9.71% of AF Project funds) has been disbursed.

From October 7 to October 11, 2013 a World Bank mission was carried with the objective to support the implementation of the project and follow up the progress of its activities.

Component 1: The project has continued to strengthen the capacities of the six municipal service providers and the regional water utility (Mancomunidad) to improve service guality and financial viability. As a result of implementation and follow some of the recommendations from the Technical Assistance Service Provider the majority of the municipalities have laid the necessary foundations to achieve improvements in performance indicators. Overall the beneficiary utilities remain engaged at the technical and managerial level to improve their operational and commercial processes with the aim to recover their costs and supply safe water during longer periods to their customers. Given that the expected improvements depend on the execution of the works and on the implementation of the recommendations of the hydraulic modeling indicators show at present only marginal improvements; the completion works planned over the coming months will enable improved service continuity and reduced operating costs.

Following consultations with local authorities and national water sector institutions the Government of Honduras selected the two new beneficiary municipalities of PROMOSAS. Both municipalities are among the country's poorest and less developed (Categories C and D).

Component 2: Physical contract works are completed 96% and 94% business. This phase was extended by 3 months and ends on October 31. It is contemplated that all activities are completed within planned. Following the completion of the micrometers installation and replacement campaign the NRW indicators have shown clear improvements and the goal of continuity under the contract seems within reach. For the purpose of determining the performance bonuses SANAA and the contractor agreed two periods (February 3 to September 2, 2013 and September 3, 2013 to April 2, 2014) to calculate the result on the basis of the weighted average of metered flows for the registered users in the given period.

Component 3: Under the Institutional Strengthening component (Component 3) the main national water sector institutions (ERSAPS, CONASA and SANAA) reached an agreement on the scope and activities that will be financed with resources from the AF. ERSAPS benchmarking activities will be supported through capacity building facilitated by WSP with the objective to facilitate the publication of indicators of PROMOSAS utilities on IBNet. A final draft Sector Financing Policy for the WSS sector was completed by CONASA however the likelihood of its adoption remains unclear. Under the TA for the transfer/decentralization in Tegucigalpa the completion of the last consultancy is ongoing, although the date, modality and financing of an actual transfer are still unclear.

Locations

Country	First Administrative Division	Location	Planned	Actual
Honduras	Departmento de Francisco Morazan	Tegucigalpa		

[>]ublic Disclosure Copy D - - - lt -

Results											
Project Development Objective Indicators											
Indicator Name	Core	Unit of Measure		Baseline	Current	End Target					
7 of the WSS utilities reach cost recovery (ratio		Number	Value	4.00	5.00	7.00					
total revenue / total operative cost equal to			Date	31-Dec-2006	12-Feb-2014	31-Dec-2016					
one).			Comments	Baseline's date ranges from 2008 to 2009.							

At least 5 of the WSS utilities increase their		Number	Value	0.00	0.00	5.00
service continuity rating by one category			Date	31-Dec-2009	12-Feb-2014	31-Dec-2016
lefined by ERSAP#s performance indicators note: definition on the Category A, B, C, and D			Comments			
on service continuit					· · · · · · · · · · · · · · · · · · ·	
At least 50% of the SANAA systems financed		Percentage	Value	0.00	100.00	50.00
under the Project are transferred to the			Date	18-May-2007	12-Feb-2014	31-Dec-2016
municipalities.			Comments			
At least 50% of municipal service providers		Percentage	Value	0.00	67.00	50.00
(non-SANAA WSS systems that are operated directly by municipalities) supported by the			Date	31-Jul-2013	12-Feb-2014	31-Dec-2016
Project are converted into autonomous			Comments			
municipal service providers.				·		
CONASA issues the new financial policy of the		Text	Value	No	No	Yes
sector.			Date	18-May-2007	12-Feb-2014	31-Dec-2016
			Comments		The Financing Policy is under review by CONASA	
Number of other water service providers that	\times	Number	Value	0.00	7.00	9.00
the project is supporting			Date	18-May-2007	12-Feb-2014	31-Dec-2016
			Comments			
Time taken to disburse funds requested by		Weeks	Value	0.00	0.00	4.00
Government for an eligible emergency			Date	31-Jul-2013	12-Feb-2014	31-Dec-2016
			Comments			

Indicator Name	Core	Unit of Measure		Baseline	Current	End Target
Number of people in urban areas (covering		Number	Value	0.00	3786.00	3700.00
semi-urban or small urban areas) provided with			Date	18-May-2007	12-Feb-2014	31-Dec-2016
access to improved sanitation under the project.			Comments			
Piped household water connections that are	X	Number	Value	0.00	1907.00	2000.00
benefiting from rehabilitation works undertaken			Date	18-May-2007	12-Feb-2014	31-Dec-2016
by the project			Comments			
At least 6 design proposals of autonomous		Number	Value	0.00	7.00	9.00
service providers approved by ERSAPS.			Date	18-May-2007	12-Feb-2014	31-Dec-2016
			Comments			

5 of the WSS utilities increase by 20% the ratio		Number	Value	0.00	5.00	6.00
of revenues per volumetric unit of water produced.			Date	18-May-2007	12-Feb-2014	31-Dec-2016
			Comments			
People trained to improve hygiene behavior/	\times	Number	Value	0.00	600.00	5000.00
sanitation practices under the proj			Date	31-Jul-2013	12-Feb-2014	31-Dec-2016
			Comments			
People trained to improve hygiene behavior/	X	Number	Value	0.00	200.00	3000.00
sanitation practices - female		Sub Type	Date	31-Jul-2013	12-Feb-2014	31-Dec-2016
		Breakdown	Comments			
Percentage of grievances redressed		Percentage	Value	0.00	0.00	75.00
satisfactorily by utilities per year			Date	31-Jul-2013	12-Feb-2014	31-Dec-2016
			Comments			
At least 6 of the WSS utilities share indicators		Number	Value	0.00	0.00	6.00
in the regional benchmarking database of			Date	31-Jul-2013	12-Feb-2014	31-Dec-2016
BNET according to their protocols			Comments			
Urban areas covered by the contract increase		Text	Value		С	В
service continuity by one category			Date	31-Jul-2013	12-Feb-2014	31-Dec-2016
			Comments			
Percentage increase of collection per cubic		Percentage	Value	0.00	18.00	20.00
meter of supplied water to the project area.			Date	18-May-2007	12-Feb-2014	31-Dec-2016
			Comments			
SANAA has at least one regional unit operating		Text	Value	No	No	Yes
under the new model.			Date	18-May-2007	12-Feb-2014	31-Dec-2016
			Comments			
ndicators regarding utilities' performance are		Text	Value	No	Yes	Yes
oublished by ERSAPS			Date	18-May-2007	12-Feb-2014	31-Dec-2016
			Comments			
At leat 5 utilities have published their financial		Number	Value		7.00	9.00
statements in a Website.			Date	18-May-2007	12-Feb-2014	31-Dec-2016
			Comments	Not available.		
SANAA / Tegucigalpa has complied with legal		Text	Value	No	No	Yes
requirements for transfer to municipality.			Date	18-May-2007	12-Feb-2014	31-Dec-2016
			Comments			

Cumulative percentage of disbursement	Percentage	Value	0.00	92.00	100.00
targeted according to disbursement plan is met.		Date	18-May-2007	12-Feb-2014	31-Dec-2016
		Comments			
IRM established and ready to provide access	Number	Value		0.00	
to financial resources to Honduras in case of	Date	Date		12-Feb-2014	
an eligible emergency		Comments			

Data on Financial Performance (as of 23-Dec-2013)


Financial Agreement(s) Key Dates

Project	Ln/Cr/Tf	Status	Approval Date	Signing Date	Effectiveness Date	Original Closing Date	Revised Closing Date
P103881	IDA-43350	Effective	21-Jun-2007	16-Nov-2007	22-Feb-2008	31-Dec-2013	31-Dec-2016
P103881	IDA-52700	Effective	19-Jun-2013	12-Jul-2013	09-Oct-2013	31-Dec-2016	31-Dec-2016

Disbursements (in Millions)

Project	Ln/Cr/Tf	Status	Currency	Original	Revised Cancelled		Disbursed	Undisbursed	% Disbursed
P103881	IDA-43350	Effective	XDR	19.80	19.80	0.00	18.31	1.49	92.00
P103881	IDA-52700	Effective	XDR	6.70	6.70	0.00	0.65	6.05	10.00

Disbursement Graph

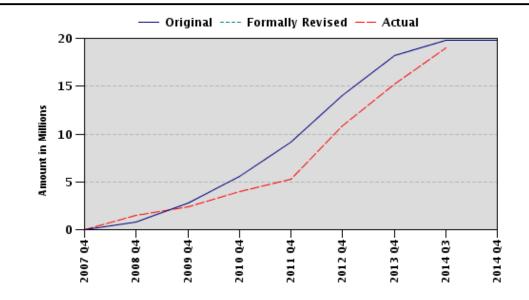

Public Disclosure Copy

Key Decisions Regarding Implementation

None

Restructuring History

There has been no restructuring to date.

Related Projects

P144357-HN AF WSS Modernization
