

Ayeyarwady Integrated River Basin Management Project (P146482)

EAST ASIA AND PACIFIC | Myanmar | Water Global Practice | IBRD/IDA | Investment Project Financing | FY 2015 | Seq No: 1 | ARCHIVED on 07-Apr-2015 | ISR18123 |

Implementing Agencies: Directorate of Water Resources and Improvement of River Systems, Ministy of Transport

Key Dates

Key Project Dates

Board Approval date:09-Dec-2014 Planned Mid Term Review Date:01-Jun-2017 Original Closing Date:30-Sep-2020 Effectiveness Date:--Actual Mid-Term Review Date:--Revised Closing Date:**30-Sep-2020**

Project Development Objectives

Project Development Objective (from Project Appraisal Document)

The program development objective for the Series of Projects (of which the AIRBM will be the first) is to strengthen integrated, climate resilient management and development of the Ayeyarwady River Basin and national water resources. The project development objective of the AIRBM is to contribute to the development of integrated river basin management on the Ayeyarwady river.

Has the Project Development Objective been changed since Board Approval of the Project Objective? No


Components

Name

Component 1: Water Resource Management Institutions, Decision Support Systems & Capacity Building:(Cost \$32.00 M) Component 2. Hydro-meteorological Observation and Information Systems Modernization:(Cost \$30.15 M) Component 3. Navigation Enhancement on the Ayeyarwady River:(Cost \$37.85 M) Component 4. Contingent Emergency Response

Overall Ratings

Name	Previous Rating	Current Rating
Progress towards achievement of PDO		Moderately Satisfactory
Overall Implementation Progress (IP)		Moderately Satisfactory
Overall Risk Rating		High



Implementation Status and Key Decisions

The Project was approved by the World Board on Dec. 9, 2014. The Finanicng Agreement was signed on April 3, 2015 with effectiveness expected to be declared in May. There have been two mission since Board approval: i) a Project Launch Workshop in January 2015; and ii) a Navigation Component mission in March 2015. A Hydro-Met mission is planned for April 27-May 1, and a Water Resources mission is planned for May 11-15.

Risks

Systematic Operations Risk-rating Tool

Risk Category	Rating at Approval	Previous Rating	Current Rating
Political and Governance			High
Macroeconomic			Moderate
Sector Strategies and Policies			Moderate
Technical Design of Project or Program			Substantial



The World Bank Ayeyarwady Integrated River Basin Management Project (P146482)

Institutional Capacity for Implementation and Sustainability	 	• High
Fiduciary	 	High
Environment and Social	 	High
Stakeholders	 	Substantial
Other	 	
Overall	 	 High

Results

Project Development Objective Indicators

► Component 1: River Basin Master Plan (Yes/No, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	Ν		Ν	Υ
Date	09-Dec-2014		27-Mar-2015	31-Mar-2020

► Component 1: Preparation of Feasibility Studies (Number, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00		0.00	2.00
Date	09-Dec-2014		27-Mar-2015	31-Mar-2020

► Component 2: Hydro-Met Stations Functioning per SOP (Percentage, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00		0.00	90.00
Date	09-Dec-2014		27-Mar-2015	31-Mar-2020

Component 2: Hydro-Met Products (Number, Custom)

4/7/2015 Baseline Actual (Previous) Actual (Current) End Targage 3 of 7 Public Disclosure Copy



The World Bank

Ayeyarwady Integrated River Basin Management Project (P146482)

Value	0.00	 0.00	3.00
Date	09-Dec-2014	 27-Mar-2015	31-Mar-2020

► Component 3: Navigation Improvements (Percentage, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00		0.00	90.00
Date	09-Dec-2014		27-Mar-2015	31-Mar-2020

Overall Comments

Intermediate Results Indicators

Component 1: River Basin Master Plan - Phase 1 Report (Yes/No, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	Ν			Υ
Date	09-Dec-2014		09-Mar-2015	31-Dec-2017

► Component 2: Hydromet System Design (Yes/No, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	Ν		Ν	Υ
Date	09-Dec-2014		27-Mar-2015	31-Dec-2017



Component 3: Navigation Detailer Design (Yes/No, Custom)BaselineActual (Previous)Actual (Current)End TargetValueN---NYDate09-Dec-2014--27-Mar-201531-Dec-2017

► Component 1: Decision Support System (Yes/No, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	Ν		Ν	Υ
Date	09-Dec-2014		27-Mar-2015	31-Mar-2020

► Component 2: Hydromet Stations Upgraded (Percentage, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00		0.00	100.00
Date	09-Dec-2014		27-Mar-2015	31-Mar-2020

▶ Component 2: Hydromet System Financial Sustainability (Percentage, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00		0.00	90.00
Date	09-Dec-2014		27-Mar-2015	31-Mar-2020



► Component 3: River works construction (Percentage, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00		0.00	100.00
Date	09-Dec-2014		31-Mar-2015	31-Mar-2020

Capacity building and gender (Number, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00		0.00	500.00
Date	09-Dec-2014		27-Mar-2015	31-Mar-2020

▲ Capacity building - percentage of participants female (Percentage, Custom Supplement)


	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00		0.00	40.00
Date	09-Dec-2014		27-Mar-2015	31-Mar-2020

Overall Comments

Data on Financial Performance

Disbursements (by loan)

Project	Loan/Credit/TF	Status	Currency	Original	Revised	Cancelled	Disbursed	Undisbursed	Disbursed
P146482	IDA-55590	Not Effective	XDR	67.50	67.50	0.00	0.00	67.50	0%
Key Dates (by Ioan)									
Project	Loan/Credit/TF	Status	Approval Date	e Signir	ng Date	Effectiveness D	Date Orig. (Closing Date	Rev. Closing Date






The World Bank

Ayeyarwady Integrated River Basin Management Project (P146482)

P146482	IDA-55590	Not Effective	09-Dec-2014	 	30-Sep-2020	30-Sep-2020

Cumulative Disbursements

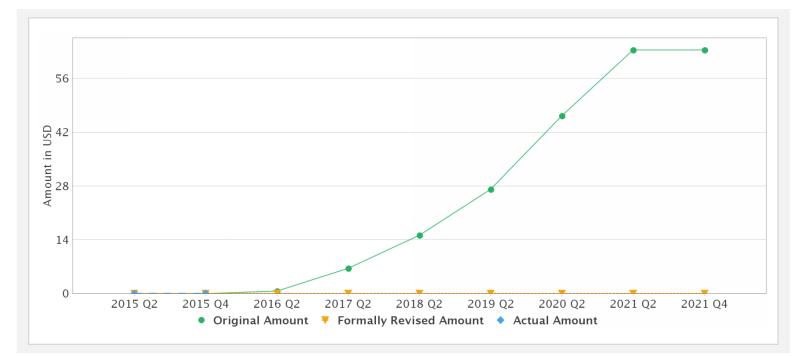

Restructuring History

There has been no restructuring to date.

Related Project(s)

There are no related projects.
