

Environmental and Social Monitoring Report

Sixth Quarterly Report
October 2016

India: Jaipur Metro Rail Line 1-Phase B Project

Prepared by Jaipur Metro Rail Corporation Limited for the Asian Development Bank.

CURRENCY EQUIVALENTS

(as of 30th June 2016)

Currency unit	-	Indian Rupee (INR)
INR 1.00	=	\$ 0.0148
\$1.00	=	INR 67.467

ABBREVIATIONS

ADB	-	Asian Development Bank
ADF	-	Asian Development Fund
CEC	-	Continental Engineering Corporation
CSC	-	Construction Supervision Consultant
ES	-	Environmental Specialist
DMRC	-	Delhi Metro Rail Corporation
EMP	-	Environmental Management Plan
EA	-	Execution Agency
EIA	-	Environmental impact Assessment
EARF	-	Environmental assessment and review framework
ESMS	-	Environmental and social management system
EMR	-	Environmental Monitoring Report
GPR	-	Ground penetrating radar
HSO	-	Health and Safety Officer
IEE	-	Initial environmental examination
IPP	-	Indigenous People Plan
JMRC	-	Jaipur Metro Rail Corporation
PAM	-	Project Administration Manual
PCAG	-	Public Consultation and Addressing of Grievances
RP	-	Resettlement Plan
SHE	-	Safety Health & Environment Management Plan
SPS	-	Safeguard Policy Statement
VMR	-	Vibration Monitoring Results

WEIGHTS AND MEASURES

km	-	Kilometer
m	-	Meter

NOTES

In this report, "\$" refers to US dollars

This environmental and social monitoring report is a document of the borrower. The views expressed herein do not necessarily represent those of ADB's Board of Directors, Management, or staff, and may be preliminary in nature. Your attention is directed to the "terms of use" section of this website.

In preparing any country program or strategy, financing any project, or by making any designation of or reference to a particular territory or geographic area in this document, the Asian Development Bank does not intend to make any judgments as to the legal or other status of any territory or area.

CONTENTS

EXECUTIVE SUMMARY	I
I. INTRODUCTION	1
A. Purpose of the Report	1
B. Project Description	1
C. Project Implementation Arrangement	2
D. Project Implementation Progress	3
II. COMPLIANCE TO SAFEGUARDS PROVISIONS IN AGREEMENTS UNDER THE PROJECT	12
A. Compliance to Loan Agreement	12
B. Compliance to Project Administration Manual	18
C. Compliance to the Civil Works Contract Agreement	28
III. COMPLIANCE TO THE ENVIRONMENTAL MANAGEMENT PLAN	34
IV. ACTIVITIES UNDERTAKEN FOR PROTECTION AND MONITORING OF HERITAGE STRUCTURES	45
A. Findings in Badi Chaupar and Chhoti Chaupar	45
B. D-Wall Construction	45
C. Chandpole Gate Tunnel Underpass Scheme/ Isarlat Side Pass Scheme	46
D. Results of the Ground Penetrating Radar	47
V. SUMMARY OF ENVIRONMENTAL MONITORING	48
A. Summary of Inspection Activities	48
B. Monitoring of Cracks, Settlements of Structures	49
C. Vibration Monitoring:	51
D. Noise Monitoring	53
E. Air Quality	55
F. Water Quality	56
VI. SOCIAL AND RESETTLEMENT IMPACTS	56
A. Impacts on Structures	56
B. Land Acquisition and Resettlement	59
VII. PUBLIC CONSULTATIONS AND ADDRESSING OF GRIEVANCES	60
A. Public Consultations carried out	60
B. Complaints and Requests Received	61
VIII. UNANTICIPATED SAFEGUARD ISSUES	61
IX. CONCLUSION	61
A. Summarize the overall Progress of Implementation of safeguard Measures	61
B. Problems Identified and Actions Recommended	61
APPENDICES	
Appendix 1: Photolog of Progress	65
Appendix 2: Record of SHE Trainings	68
Appendix 3: Sample format of Monthly SHE report	74
Appendix 4: Environment Quality Monitoring Report	76
Appendix 5: Monthly Report of Heritage Consultant	90
Appendix 6: Consent to establish letter from Rajasthan State Pollution Control Board.....	94
Appendix 7: Muck disposal details	99
Appendix 8: Tree transplantation details	104
Appendix 9: Photographs of tilt, crack and other instruments in working	114

EXECUTIVE SUMMARY

1. This report is the 6th quarterly report on environmental and social safeguards compliance of the Jaipur Metro Rail Line -1 Phase B Project. It covers the period from April 2016 to June 2016. Line 1 - Phase B of the project includes construction of 2.4 km underground portion from Chandpole to Badi Chaupar, with two stations. Line 1 – Phase B is being financed by ADB and expected to be completed by March 2018 at a cost of INR 1126 crore.
2. Jaipur Metro Rail Corporation (JMRC) is the Executing Agency for the Project. The sole civil works contract package under the project was awarded to Continental Engineering Corporation (CEC) in September 2013. The General Consultant overseeing the design and supervision of physical works is Delhi Metro Rail Corporation Limited (DMRC).
3. Progress in construction works as of June 2016 are: i) TBM 1 has completed tunnelling of 1457 rings and is 7 rings away from Badi Chaupar station ii) TBM 2 has reached the center of Chhoti Chaupar station and has completed tunnelling of 941 rings. iii) Chhoti Chaupar station work using cut & cover method has progressed as scheduled iv) For construction work of D Wall at Badi Chaupar, traffic has been blocked from Hawa Mahal side with one way still open for movement of general traffic, this is with permission of Traffic Police, Jaipur and as per consensus with Business community. As of June 2016, total physical and financial accomplishments are about 40.74% and 48.46% respectively. The contract has achieved physical 4.98% and financial 8.00% progress during this reporting quarter ending June 2016. So far no damage has been reported during the tunneling work. Extra precautions had been taken to ensure no mishap happens during the tunneling process. 12 prisms have been installed on both sides of the gate to keep a check on the vibrations with monitoring the reading every hour. Additionally, 10 crack meter and six strips of glass have also been put on the gate to receive any information if the cracks widen. Moreover, eight Multi Point Borehole Extensometer (MPBX) have been installed at the depth of 2.5 meter and 5 meter. The status of all the relevant structures have been regularly monitored. Sites are being regularly visited by JMRC Heritage/structural experts i.e., M/s Abha Narain Lambah Associates and M/s Shashank Mehendale & Associates.
4. The project is running 18 months behind the initially planned schedule. This is mainly due to the design changes and discovery of two ancient tanks which were buried right in the path of the alignment. These tanks once brought water to the city centre from the surrounding Aravalli hills. To preserve the tanks, the Jaipur Metro Rail Corporation has altered the design. The tunnel has been lowered by about one meter and made incidental design changes to accommodate the tanks above the metro stations at Chhoti and Badi Chaupar. Another design change that resulted in delay is the decision to tunnel through Chhoti Chaupar station instead of retrieving and re-launching the TBMs at Chhoti Chaupar. This was done to avoid disturbance to general public and business community. Also at Badi Chaupar, the station was lowered to accommodate proposed subway and retrieving shaft location was changed to minimize the period of road blockage. In addition to above, in order to make better utilization of the space above reversal line between Badi Chaupar and Ramganj, which otherwise was to be filled with earth, now the same will be developed for property development and parking area.
5. The environmental and social safeguards of the project are being implemented in compliance with the loan covenants, project agreement and contractor is complying with the proposed mitigation measures described in the Environmental Management Plan (EMP); Safety, Health and Environment (SHE) Manual and the contract specifications. The implementation of environmental and social safeguards are being monitored at Project

Management and General Consultant (GC) level. With exception of few issues the project is being implemented in compliance with project requirements.

6. With regards to the baseline study carried out on heritage structures located in the project area before the start of work of Phase 1B, during the reporting period of report i.e. up to June 2016 no major changes in the condition of structures have been reported.

7. The list of structures requiring immediate action was submitted to Jaipur Nagar Nigam, so that to ensure no damage during the tunneling work. Preventive measures like propping of the verandahs and the repair of shops along the above length have been taken up during the tunneling work and beyond.

8. For structures located around the Chaupars (station sites) where construction works are ongoing, proactive measures of providing propping support to unstable structures is already in place and are taken care by by the contractor under instructions of the 'engineer' (General Consultants). In addition regular monitoring of weak structures through installation of crack, tilt and vibration meters and building settlement markers is also being done on regular basis.

9. The minor social and resettlement impacts such as the acquisition of a strip of private land (10 by 10 meters) outside Chandpole station and at the tunnel construction start point, as the shops (3 Shopkeepers) on that strip are blocking traffic. JMRC has already rehabilitated the shop owners across the Chandpole Metro Station near Church land. 6 Temples at Chhoti Chaupar, which were infringing the station box area have all been rehabilitated and given built up structures as per their satisfaction at Old Atish market land. 7 temples at Badi Chaupar have been identified which are infringing the station box area, out of these 7, as on date none of them has been relocated.

10. Civil Administration and JMRC has ensured round the clock availability of Rescue team consisting of Ambulance, Civil defence, Earth moving Machines & Crane, staff from Jaipur Discom and PHED. This is to ensure quick response to any problem which may arise during construction.

11. After complete and detailed documentation of Badi Chaupar and handing over of Gaumukh to A&M Department, Government of Rajasthan, the old water tank has been refilled and the station work will begin soon after completion of D Wall/ top slab work.

12. The construction works are proceeding in accordance with the provisions of the EMP such as review of monitoring reports, regulatory compliance action plan and approval by the GC. The environmental monitoring plan is successfully being implemented by the JMRC through an instrumentation company M/s AMIL engaged by executing agency with the approval of 'Engineer'.

13. JMRC and DMRC officials have regularly been meeting with the local people and business associations in the project area to inform them about the construction works. Measures have been taken to address concerns of the local businesses such as stopping of work and providing proper pathways for customers during festivals. All reports and information on the project is disclosed on the JMRC website. In addition JMRC has a full-time Public Relation Officer dealing with media/press issues and also maintains a facebook page and twitter account for disclosing project information and responding to queries and concerns from the general public.

14. Various proactive measures are being taken to implement project in compliance with requirements, prevent damages to heritage structures, coordination with relevant agencies,

communicate with the public and address grievances of the local public. Areas such as public communications, documentation and reporting need further enhancement.

15. There were no significant environmental impacts observed during the reporting period. All environment related observations are regularly recorded and monitored and in case of any short-comings necessary corrective measures are taken up.

I. INTRODUCTION

A. Purpose of the Report

16. The objective of environmental monitoring is to allow ADB and the Jaipur Metro Rail Corporation (JMRC) gather information to: i) evaluate the environmental management plan (EMP) progress by establishing compliance status, ii) detect and correct non-conformances, iii) identify unanticipated impacts and implement necessary mitigation measures, and iv) provide evidence to support enforcement of penalty provisions of the civil works contract to deter non-compliance.

17. Environmental monitoring and disclosure of quarterly or semi-annual monitoring reports is an ADB requirement for environmental category-A projects like Jaipur Metro Rail Line-1 Phase B. Environmental monitoring is part of project implementation process to be complied by both ADB and JMRC. The preparation and submission of the quarterly or semi-annual monitoring reports is the responsibility of JMRC while supervision to provide guidance is the role of ADB.

18. As many sensitive heritage structures of the Pink City exist above the metro underground alignment, it was agreed during project preparation that quarterly environmental monitoring reports will be prepared and disclosed for this project. Since the significant physical construction works started in July 2015, the first environmental and social semi-annual monitoring report for the period July 2014 – December 2014 has been submitted to ADB and disclosed on ADB and JMRC websites. Thereafter quarterly monitoring reports are being regularly submitted to ADB and disclosed on ADB and JMRC websites. This is the sixth quarterly environment and social monitoring report for reporting period April 2016 to June 2016.

B. Project Description

19. Jaipur, the capital of the Indian state of Rajasthan, is one of the fastest growing cities in India. The fast paced industrial and commercial development has resulted in a steep rise in travel demand, but the city's existing public transport infrastructure is inadequate in terms of capacity and service. With the growing economy, passengers are shifting to private modes of transport, as evident in the rise in vehicle ownership, aggravating congestion and pollution. The modal share for public transport was 19% in 2009—one of the lowest in cities with more than 3 million inhabitants in India¹.

20. In 2009, Jaipur Development Authority developed a comprehensive mobility plan, seeking to provide an overall transport plan, up to 2031, that emphasizes the preeminence of public transport for the movement of people, not just vehicles, and integrating land use with transport networks. The plan recommended, among others, the development of high capacity metro lines along the east–west corridor of 12 km from Mansarovar to Badi Chaupar, and the north–south corridor of 23 km from Ambabadi to Sitapura. In January 2010, the government of Rajasthan established the Jaipur Metro Rail Corporation (JMRC) to implement the metro rail lines. Line 1- Phase A (9.6 km elevated portion from Mansarovar to Chandpole) and Line 1- Phase B (2.4 km underground portion from Chandpole to Badi Chaupar, with two stations).

21. Line 1 – Phase B is being financed by ADB and expected to be completed by March 2018 at a cost of Rs. 1126 Crore². Figure 1 show the system map of the Project.

¹<http://www.adb.org/sites/default/files/project-document/79730/46417-001-rrp.pdf>

²<https://www.jaipurmetrorail.in/Present%20Status>

Figure 1. JMRC Project System Map

C. Project Implementation Arrangement

22. The Government of Rajasthan acting through the Urban Development and Housing Department and Jaipur Metro Rail Corporation (JMRC) is the executing agency of the Project.

JMRC has established an environment safeguard cell to look after implementation and monitoring of the safeguards measures associated with the Project. It constitute six officials of JMRC. Organization structure of Safeguards Cell is show in Figure 2.

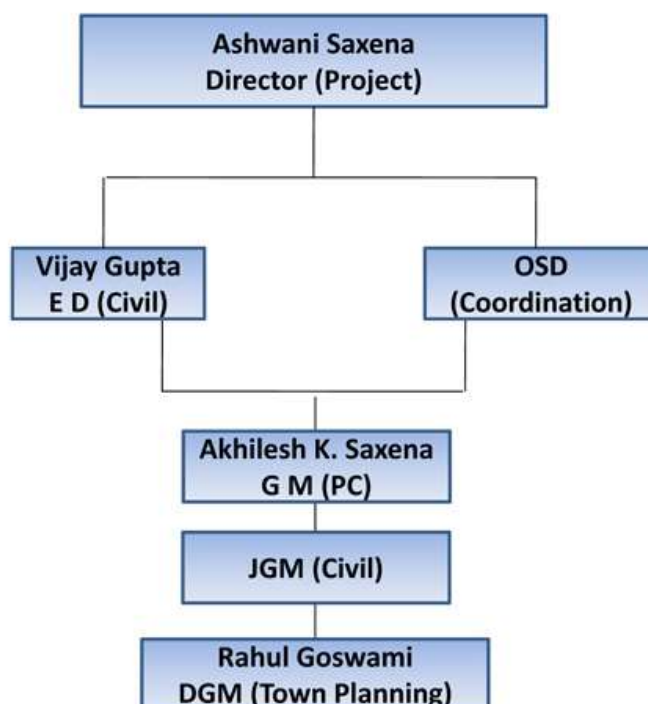




Figure 2: Organization Structure of Safeguards Cell of JMRC

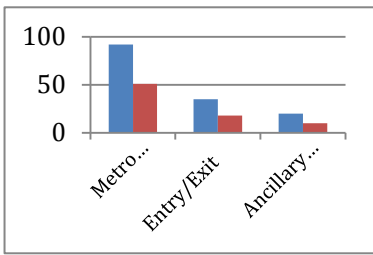
D. Project Implementation Progress

23. As of June 2016, total physical and financial accomplishment are about 40.74% and 48.46%, respectively. The status of various construction activities is provided in the Table 1. Photolog demonstrating the progress of works is provided in Appendix 1.

Table 1: Status of Construction Works as of June 2016



S.N.	Activities	Location		Status	
1	Earthworks: Earthwork is to be done for construction of Launching shaft at Chandpole, construction of underground stations at Chhoti Chaupar and Badi Chaupar by cut & cover method. During the tunneling earth will be excavated with Tunnel Boring Machine (TBM-I & II).	Location	Estimated quantity (in cum)	Location	% Completion
		Chandpole	8000	Chandpole	100%
		Chhoti Chaupar	162000	Chhoti Chaupar	26.61%
		Badi Chaupar	174000	Badi Chaupar	3.76%
		Tunneling Work	180000	Tunneling Work	67.0%
		Cut & cover	70000	Cut & cover	0%



S.N.	Activities	Location	Status																						
																									
2	Spoil Disposal: <table border="1" data-bbox="282 522 623 837"><thead><tr><th>Location</th><th>Estimated quantity *(in cum)</th></tr></thead><tbody><tr><td>Chandpole</td><td>8000</td></tr><tr><td>Chhoti Chaupar</td><td>145800</td></tr><tr><td>Badi Chaupar</td><td>156600</td></tr><tr><td>Tunneling Work</td><td>180000</td></tr><tr><td>Cut & cover</td><td>70000</td></tr></tbody></table> <p><i>*Estimated quantity of soil which will be disposed during complete project duration</i></p>	Location	Estimated quantity *(in cum)	Chandpole	8000	Chhoti Chaupar	145800	Badi Chaupar	156600	Tunneling Work	180000	Cut & cover	70000	<div>1. Sumel</div> <div>2. Govindpura/Ropada</div> <div>3. Mathuradaspura</div> <div>4. Langariyawas</div>	<div>➤ Jaipur Development Authority has allotted following soil disposal sites vide letter dated 01.09.2014</div> <div><div>1. Sumel</div><div>2. Govindpura/Ropada</div><div>3. Mathuradaspura</div></div> <div>➤ Jaipur Nagar Nigam has allotted following soil disposal sites vide letter dated 08.09.2014:</div> <div><div>1. Langariyawas</div></div> <div>➤ Spoil disposed at different disposal sites during the reporting period is as under:</div> <table border="1" data-bbox="1029 1142 1403 1394"><thead><tr><th>Location</th><th>Estimated quantity (in cum)</th></tr></thead><tbody><tr><td>Sumel</td><td>0</td></tr><tr><td>Govindpura/Ropada</td><td>0</td></tr><tr><td>Mathuradaspura</td><td>48005</td></tr><tr><td>Langariyawas</td><td>0</td></tr></tbody></table> <div data-bbox="1029 1425 1403 1782"><div>Muck Disposal</div><div><div>■ Sumel</div><div>■ Govindpura</div><div>■ Mathuradaspura</div><div>■ Langariyawas</div></div><div></div></div> <div>On an average 534 cubic meter of muck is transported daily to the dumping ground. Muck is</div>	Location	Estimated quantity (in cum)	Sumel	0	Govindpura/Ropada	0	Mathuradaspura	48005	Langariyawas	0
Location	Estimated quantity *(in cum)																								
Chandpole	8000																								
Chhoti Chaupar	145800																								
Badi Chaupar	156600																								
Tunneling Work	180000																								
Cut & cover	70000																								
Location	Estimated quantity (in cum)																								
Sumel	0																								
Govindpura/Ropada	0																								
Mathuradaspura	48005																								
Langariyawas	0																								


S.N.	Activities	Location	Status																
			transported only during night time to avoid nuisance to general public. Wheels of every truck leaving the site with muck are washed/cleaned before entering public carriage to avoid deposition and spillage. Also the truck is covered with tarpaulin sheet to avoid dust pollution enroute to dumping ground. The dumping ground will be compacted to avoid generation of dust. The route map and photographs of dumping site are annexed as Appendix-7 .																
3	Vegetation and Plant Clearing: Some trees are coming in the metro route in launching shaft at Chandpole, station box and in entry exit at Chhoti Chaupar and Badi Chaupar. These trees are to be cut or relocated with the prior approval of District Collector.	<ul style="list-style-type: none">Location of the trees as per survey which are to be cut or located as under:<table><tr><th>Location</th><th>Trees</th></tr><tr><td>Metro route</td><td>92</td></tr><tr><td>Entry/Exit at Chhoti Chaupar & Badi Chaupar</td><td>35</td></tr><tr><td>Ancillary Building area at Chhoti Chaupar</td><td>20</td></tr></table>The tree species include Gulmohar, Banyan tree & Pipal tree.The trees have been transplanted at Ghat ki Guni, Sylvan Bio diversity forest Agra road Jaipur & Ram Niwas Bagh, JDA Jaipur.	Location	Trees	Metro route	92	Entry/Exit at Chhoti Chaupar & Badi Chaupar	35	Ancillary Building area at Chhoti Chaupar	20	<p>Permission for cutting/transplantation of 20 trees has been obtained from ADM, Jaipur vide their letter dated 24.04.2015.</p> <p>Details of trees cut or transplanted is as under:</p> <table><tr><th>Location</th><th>Trees transplanted</th></tr><tr><td>Metro route</td><td>51</td></tr><tr><td>Entry/Exit at Chhoti Chaupar & Badi Chaupar</td><td>18</td></tr><tr><td>Ancillary Building area at Chhoti Chaupar</td><td>10</td></tr></table> <div></div> <p>In total 79 trees have been transplanted to three locations viz. Ghat Ki Ghuni, Ramniwas Garden and Sylvan Bio-diversity forest. The survival</p>	Location	Trees transplanted	Metro route	51	Entry/Exit at Chhoti Chaupar & Badi Chaupar	18	Ancillary Building area at Chhoti Chaupar	10
Location	Trees																		
Metro route	92																		
Entry/Exit at Chhoti Chaupar & Badi Chaupar	35																		
Ancillary Building area at Chhoti Chaupar	20																		
Location	Trees transplanted																		
Metro route	51																		
Entry/Exit at Chhoti Chaupar & Badi Chaupar	18																		
Ancillary Building area at Chhoti Chaupar	10																		


S.N.	Activities	Location	Status																																				
			<p>rate as on June 2016 is 27%. All efforts are being made for the survival of the transplanted trees.</p> <p>In addition transplantation the contractor has carried out multiple tree plantation drive at casting yard and office area. Till June 2016, 133 samplings have been planted at these locations. Photographs and additional details on tree plantation is annexed as Appendix-8.</p>																																				
4	<p>Utility Shifting:</p> <p>Utility shifting is an important activity for underground station work.</p> <p>Underground electric cables, water supply lines and telecom lines are to be realigned at Chandpole for launching shaft and underground station at Chhoti Chaupar and Badi Chaupar.</p>	<table><tr><td>Chandpole – Launching shaft</td></tr><tr><td>Electric cables</td></tr><tr><td>Water supply lines</td></tr><tr><td>Telecom lines</td></tr><tr><td>Chhoti Chaupar</td></tr><tr><td>Electric cables</td></tr><tr><td>Water supply lines</td></tr><tr><td>Telecom lines</td></tr><tr><td>Badi Chaupar</td></tr><tr><td>Electric cables</td></tr><tr><td>Water supply lines</td></tr><tr><td>Telecom lines</td></tr></table>	Chandpole – Launching shaft	Electric cables	Water supply lines	Telecom lines	Chhoti Chaupar	Electric cables	Water supply lines	Telecom lines	Badi Chaupar	Electric cables	Water supply lines	Telecom lines	<p>Status during reporting period is as under:</p> <table><tr><td colspan="2">Chandpole – Launching shaft</td></tr><tr><td>Electric cables</td><td>100%</td></tr><tr><td>Water supply lines</td><td>100%</td></tr><tr><td>Telecom lines</td><td>100%</td></tr><tr><td colspan="2">Chhoti Chaupar</td></tr><tr><td>Electric cables</td><td>100%</td></tr><tr><td>Water supply lines</td><td>100%</td></tr><tr><td>Telecom lines</td><td>100%</td></tr><tr><td colspan="2">Badi Chaupar</td></tr><tr><td>Electric cables</td><td>100%</td></tr><tr><td>Water supply lines</td><td>Work in Progress</td></tr><tr><td>Telecom lines</td><td>100%</td></tr></table>	Chandpole – Launching shaft		Electric cables	100%	Water supply lines	100%	Telecom lines	100%	Chhoti Chaupar		Electric cables	100%	Water supply lines	100%	Telecom lines	100%	Badi Chaupar		Electric cables	100%	Water supply lines	Work in Progress	Telecom lines	100%
Chandpole – Launching shaft																																							
Electric cables																																							
Water supply lines																																							
Telecom lines																																							
Chhoti Chaupar																																							
Electric cables																																							
Water supply lines																																							
Telecom lines																																							
Badi Chaupar																																							
Electric cables																																							
Water supply lines																																							
Telecom lines																																							
Chandpole – Launching shaft																																							
Electric cables	100%																																						
Water supply lines	100%																																						
Telecom lines	100%																																						
Chhoti Chaupar																																							
Electric cables	100%																																						
Water supply lines	100%																																						
Telecom lines	100%																																						
Badi Chaupar																																							
Electric cables	100%																																						
Water supply lines	Work in Progress																																						
Telecom lines	100%																																						
5	<p>Traffic Management and Diversion:</p> <p>For the construction of launching shaft at Chandpole, underground stations at Chhoti Chaupar and Badi Chaupar, traffic is to be diverted.</p> <p>Project specific traffic management plan has been developed and the same has been approved by Jaipur Traffic Authority.</p>	<p>Chandpole Launching Shaft</p> <p>Traffic from Station Road to Jhotwara Road has been diverted via Pareek College Road.</p> <p>Chhoti Chaupar</p> <p>Direct access from Chandpole Bazar to Tripolia Bazar. Traffic is diverted via Nahargarh Road – Gangauri Bazar – Cheeni Ki Burj.</p>	<p>Chandpole Launching Shaft</p> <p>Traffic Management & diversion is continuing.</p> <p>Chhoti Chaupar</p> <p>Road is open for traffic from all directions.</p>																																				

S.N.	Activities	Location	Status																																
		Badi Chaupar Traffic Diversion Plan is under preparation	Badi Chaupar Road has been partially closed for diaphragm wall construction. One-way traffic is allowed from Hawa Mahal road to Badi Chaupar - Chhoti Chaupar, tripoliya Via Adarsh High school.																																
6	Launching shaft: Launching shaft is to be constructed for tunnel boring machine. A launching shaft has diaphragm wall/concrete wall and it is built to be permanent. Once the access shaft is completed, Tunnel Boring Machine will be lowered to the bottom and excavation will start. Launching shaft is the main entrance & exit of the tunnel until project is complete. Launching shaft is rectangular in shape and constructed with reinforce cement concrete M50 grade. Walls of launching shaft are 800 mm thick. Dimension of launching shaft at Chandpole is 24m X 20m and a depth of 14m.	Chandpole	Launching shaft work has been completed.																																
7	Tunnel Boring Machine Tunnel boring machine will be used in excavating and advancing tunnels through any type of ground strata for the complete tunnelling work. The underlying principle of the EPB method is that the excavated soil or muck itself is used to provide continuous support to the tunnel face by balancing earth pressure against the forward pressure of the machine. As the shield advances at the	The main activities of these TBMs are as under: <table><tr><th colspan="2">TBM 1</th></tr><tr><td>Refurbishment</td><td></td></tr><tr><td>Lowering in launching shaft</td><td></td></tr><tr><td>Tunneling work</td><td>1875 meter</td></tr><tr><th colspan="2">TBM 2</th></tr><tr><td>Refurbishment</td><td></td></tr><tr><td>Lowering in launching shaft</td><td></td></tr><tr><td>Tunneling work</td><td>1875 meter</td></tr></table>	TBM 1		Refurbishment		Lowering in launching shaft		Tunneling work	1875 meter	TBM 2		Refurbishment		Lowering in launching shaft		Tunneling work	1875 meter	<table><tr><th colspan="2">TBM 1</th></tr><tr><td>Refurbishment</td><td>100%</td></tr><tr><td>Lowering in launching shaft</td><td>100%</td></tr><tr><td>Tunneling work</td><td>93.24% (1748.4 m) tunneling completed.</td></tr><tr><th colspan="2">TBM 2</th></tr><tr><td>Refurbishment</td><td>100%</td></tr><tr><td>Lowering in launching shaft</td><td>100%</td></tr><tr><td>Tunneling work</td><td>60.28%(1130.4 m) tunneling completed.</td></tr></table>	TBM 1		Refurbishment	100%	Lowering in launching shaft	100%	Tunneling work	93.24% (1748.4 m) tunneling completed.	TBM 2		Refurbishment	100%	Lowering in launching shaft	100%	Tunneling work	60.28%(1130.4 m) tunneling completed.
TBM 1																																			
Refurbishment																																			
Lowering in launching shaft																																			
Tunneling work	1875 meter																																		
TBM 2																																			
Refurbishment																																			
Lowering in launching shaft																																			
Tunneling work	1875 meter																																		
TBM 1																																			
Refurbishment	100%																																		
Lowering in launching shaft	100%																																		
Tunneling work	93.24% (1748.4 m) tunneling completed.																																		
TBM 2																																			
Refurbishment	100%																																		
Lowering in launching shaft	100%																																		
Tunneling work	60.28%(1130.4 m) tunneling completed.																																		

S.N.	Activities	Location	Status												
	<p>face, the cutter head on the TBM rotates through the earth. The excavated soil is then mixed together with a special foam material that actually alters its viscosity or thickness and transforms it into flowing material. The use of a foaming agent to break down muck into a liquefied form provides some obvious benefits. The muck is then stored and controlled in a pressurized chamber located inside the cutter head, and is used to apply support and balance pressure to the tunnel face during the excavation process. The foam acts as a lubricant that conditions the soil to a suitable fluidity, in effect reducing the risk of clogging in the pressurized chamber head or muck storage area.</p> <p>A screw conveyor then removes excess fluidized muck in controlled volumes from behind the cutter head and in front of the "Pressure bulkhead", synchronizing the screw conveyor with the actual speed of the tunnel boring machine, and equalizing the actual volume of soil travelling into and out of the machine and establishes earth pressure balance during excavation, thereby also reducing the risk of surface or ground settlement. The performance of the EPBV machine, however, largely depends on the actual properties of the excavated muck. The soil may be coarse sands, gravel or stiff clays.</p> <p>The EPB TBM also has the unique capability of placing a continuous ring of segment liners from within the tail shield of the machine inside</p>		<div>TBM-1</div> <div><table><caption>TBM-1 Tunneling Work</caption><tr><th>Category</th><th>Value</th></tr><tr><td>Blue Bar</td><td>~1800</td></tr><tr><td>Red Bar</td><td>~1600</td></tr></table></div> <div>TBM-2</div> <div><table><caption>TBM-2 Tunneling work</caption><tr><th>Category</th><th>Value</th></tr><tr><td>Blue Bar</td><td>~1800</td></tr><tr><td>Red Bar</td><td>~1100</td></tr></table></div>	Category	Value	Blue Bar	~1800	Red Bar	~1600	Category	Value	Blue Bar	~1800	Red Bar	~1100
Category	Value														
Blue Bar	~1800														
Red Bar	~1600														
Category	Value														
Blue Bar	~1800														
Red Bar	~1100														

S.N.	Activities	Location	Status																												
	<p>the tunnel as it advances. These concrete segments provide critical additional reinforcement and support and accomplish all tunnel construction in one pass.</p> <p>Tunneling works from Chandpole to Badi Chaupar will be done by the two TBMs.</p> <p>Diameter of the cutting head of TBM is 6.55 meter. The tunnel size is of 5.60 meter internal diameter.</p>																														
8	<p>Segment casting:</p> <p>Internal lining of the tunnel will be done by precast reinforced cement concrete segments. The segments are to be constructed with M 50 concrete having outer diameter of 6.35 meter. One ring comprises 6 segments.</p>	<p>Segment casting will be done at casting yard in Bhankarota.</p> <table><tr><td>Rings</td><td>3200 (19200 segments)</td></tr></table>	Rings	3200 (19200 segments)	<p>Rings casted are as under:</p> <table><tr><td>Rings</td><td>96.25% (3080)</td></tr></table>  <p>Rings</p>	Rings	96.25% (3080)																								
Rings	3200 (19200 segments)																														
Rings	96.25% (3080)																														
9	<p>Guide wall and D wall at Chhoti Chaupar & Badi Chaupar stations:</p> <p>For the construction of D-Wall initially guide walls are constructed so as to keep the D-Wall in proper alignment.</p> <p>Guide walls are constructed with reinforce cement concrete of M20 grade. The thickness of guide wall is about 600 mm and depth is 1.5 m.</p> <p>Diaphragms walls are constructed with reinforce cement concrete of M35 grade. The thickness of diaphragms wall is about 800 mm and depth is about 26 m.</p>	<table><tr><th>Location</th><th>Length (m)</th></tr><tr><td colspan="2">Chhoti Chaupar</td></tr><tr><td>Guide Wall</td><td>590</td></tr><tr><td>D-Wall</td><td>590</td></tr><tr><td colspan="2">Badi Chaupar</td></tr><tr><td>Guide Wall</td><td>590</td></tr><tr><td>D-Wall</td><td>590</td></tr></table>	Location	Length (m)	Chhoti Chaupar		Guide Wall	590	D-Wall	590	Badi Chaupar		Guide Wall	590	D-Wall	590	<table><tr><th>Location</th><th>% Completion</th></tr><tr><td colspan="2">Chhoti Chaupar</td></tr><tr><td>Guide Wall</td><td>100%(590)</td></tr><tr><td>D-Wall</td><td>100%(590)</td></tr><tr><td colspan="2">Badi Chaupar</td></tr><tr><td>Guide Wall</td><td>67.11%(396)</td></tr><tr><td>D-Wall</td><td>52.54%(310)</td></tr></table> <p><u>Chhoti Chaupar</u></p>  <p>Guide Wall D Wall</p>	Location	% Completion	Chhoti Chaupar		Guide Wall	100%(590)	D-Wall	100%(590)	Badi Chaupar		Guide Wall	67.11%(396)	D-Wall	52.54%(310)
Location	Length (m)																														
Chhoti Chaupar																															
Guide Wall	590																														
D-Wall	590																														
Badi Chaupar																															
Guide Wall	590																														
D-Wall	590																														
Location	% Completion																														
Chhoti Chaupar																															
Guide Wall	100%(590)																														
D-Wall	100%(590)																														
Badi Chaupar																															
Guide Wall	67.11%(396)																														
D-Wall	52.54%(310)																														

S.N.	Activities	Location	Status																																												
			<div>Badi Chaupar</div> <div></div>																																												
10	<p>Roof Slabs at Chhoti Chaupar & Badi Chaupar Station</p> <p>Stations are to be constructed with top down method. Top slab, roof slab, concourse slab & base slab are to be constructed.</p>	<table><tr><th>Location</th><th>Area (sqm)</th></tr><tr><td colspan="2">Chhoti Chaupar</td></tr><tr><td>Top slab</td><td>7000</td></tr><tr><td>Roof slab</td><td>7000</td></tr><tr><td>Concourse</td><td>7000</td></tr><tr><td>Base slab</td><td>7000</td></tr><tr><td colspan="2">Badi Chaupar</td></tr><tr><td>Top slab</td><td>7000</td></tr><tr><td>Roof slab</td><td>7000</td></tr><tr><td>Concourse</td><td>7000</td></tr><tr><td>Base slab</td><td>7000</td></tr></table>	Location	Area (sqm)	Chhoti Chaupar		Top slab	7000	Roof slab	7000	Concourse	7000	Base slab	7000	Badi Chaupar		Top slab	7000	Roof slab	7000	Concourse	7000	Base slab	7000	<table><tr><th>Location</th><th>Area (sqm)</th></tr><tr><td colspan="2">Chhoti Chaupar</td></tr><tr><td>Top slab</td><td>4235</td></tr><tr><td>Roof slab</td><td>4235</td></tr><tr><td>Concourse</td><td>0</td></tr><tr><td>Base slab</td><td>0</td></tr><tr><td colspan="2">Badi Chaupar</td></tr><tr><td>Top slab</td><td>1248</td></tr><tr><td>Roof slab</td><td>0</td></tr><tr><td>Concourse</td><td>0</td></tr><tr><td>Base slab</td><td>0</td></tr></table> <p>Top slab work at Tripolia & Chandpole sides has been completed at Chhoti Chaupar.</p> <p>D-wall construction at Chhoti Chaupar is under progress.</p> <p>Top slab work at Badi Chaupar is under process.</p> <p>D-wall construction at Badi Chaupar is under progress</p>	Location	Area (sqm)	Chhoti Chaupar		Top slab	4235	Roof slab	4235	Concourse	0	Base slab	0	Badi Chaupar		Top slab	1248	Roof slab	0	Concourse	0	Base slab	0
Location	Area (sqm)																																														
Chhoti Chaupar																																															
Top slab	7000																																														
Roof slab	7000																																														
Concourse	7000																																														
Base slab	7000																																														
Badi Chaupar																																															
Top slab	7000																																														
Roof slab	7000																																														
Concourse	7000																																														
Base slab	7000																																														
Location	Area (sqm)																																														
Chhoti Chaupar																																															
Top slab	4235																																														
Roof slab	4235																																														
Concourse	0																																														
Base slab	0																																														
Badi Chaupar																																															
Top slab	1248																																														
Roof slab	0																																														
Concourse	0																																														
Base slab	0																																														
11	<p>Establishment of construction camp:</p> <p>➤ A construction camp for laborers has been established near to casting yard area in November 2014.</p>	<p>Casting Yard, Bhankrota</p> <table><tr><td>Number of blocks</td><td>9</td></tr><tr><td>Total Camp Area</td><td>6227 sq.m</td></tr><tr><td>Capacity</td><td>9X48</td></tr><tr><td colspan="2">Facilities to be provided</td></tr><tr><td>Bathing room</td><td></td></tr><tr><td>Dining room</td><td></td></tr><tr><td>Urinal& toilet</td><td></td></tr><tr><td>Drinking water with cooling facility</td><td></td></tr><tr><td>fans</td><td></td></tr></table>	Number of blocks	9	Total Camp Area	6227 sq.m	Capacity	9X48	Facilities to be provided		Bathing room		Dining room		Urinal& toilet		Drinking water with cooling facility		fans		<p>Completed.</p> <table><tr><td>Number of blocks</td><td>9</td></tr><tr><td>Area of each block</td><td>692sqm</td></tr><tr><td>Workers staying</td><td>190</td></tr><tr><td colspan="2">Facilities installed</td></tr><tr><td>Bathing room</td><td>Yes</td></tr><tr><td>Dining room</td><td>Yes</td></tr><tr><td>Urinal& toilet</td><td>Yes</td></tr><tr><td>Drinking water with cooling facility</td><td>Yes</td></tr><tr><td>fans</td><td>Yes</td></tr></table>	Number of blocks	9	Area of each block	692sqm	Workers staying	190	Facilities installed		Bathing room	Yes	Dining room	Yes	Urinal& toilet	Yes	Drinking water with cooling facility	Yes	fans	Yes								
Number of blocks	9																																														
Total Camp Area	6227 sq.m																																														
Capacity	9X48																																														
Facilities to be provided																																															
Bathing room																																															
Dining room																																															
Urinal& toilet																																															
Drinking water with cooling facility																																															
fans																																															
Number of blocks	9																																														
Area of each block	692sqm																																														
Workers staying	190																																														
Facilities installed																																															
Bathing room	Yes																																														
Dining room	Yes																																														
Urinal& toilet	Yes																																														
Drinking water with cooling facility	Yes																																														
fans	Yes																																														

S.N.	Activities	Location	Status																				
		<table><tr><td>playground</td><td></td></tr></table>	playground		<table><tr><td>playground</td><td>Yes</td></tr></table>	playground	Yes																
playground																							
playground	Yes																						
12	Other Facilities: ➤ Batching Plant, ➤ Laboratory, ➤ RO Plant ➤ Chiller Plant ➤ Diesel Generating Set ➤ Briquette Boiler	<p>Following facilities are provided at casting Yard, Bhankrota:</p> <table><tr><th>Item</th><th>Capacity</th></tr><tr><td>Batching Plant</td><td>(i) 30 cum/hr (ii) 60 cum/hr</td></tr><tr><td>Quality Control Laboratory</td><td>Installed</td></tr><tr><td>RO Plant</td><td>2 kl/hr</td></tr><tr><td>Chiller Plant</td><td>100 TR</td></tr><tr><td>Diesel Generating Set</td><td>500 KVA</td></tr><tr><td>Briquette Boiler</td><td>2 TPH</td></tr></table>	Item	Capacity	Batching Plant	(i) 30 cum/hr (ii) 60 cum/hr	Quality Control Laboratory	Installed	RO Plant	2 kl/hr	Chiller Plant	100 TR	Diesel Generating Set	500 KVA	Briquette Boiler	2 TPH	Completed.						
Item	Capacity																						
Batching Plant	(i) 30 cum/hr (ii) 60 cum/hr																						
Quality Control Laboratory	Installed																						
RO Plant	2 kl/hr																						
Chiller Plant	100 TR																						
Diesel Generating Set	500 KVA																						
Briquette Boiler	2 TPH																						
13	Establishment and operation of quarry/ borrow area: For the construction work following material is sourced: ➤ Sand ➤ Aggregate ➤ Cement ➤ Steel	<p>Quarry area and borrow area of construction material is as under:</p> <table><tr><th>Material</th><th>Quarry / borrow area</th></tr><tr><td>Sand</td><td>Banas</td></tr><tr><td>Aggregate</td><td>Shakun, Lakher</td></tr><tr><td>Cement</td><td>Lafarge</td></tr><tr><td>Steel</td><td>SAIL, VIZAG,TATA</td></tr></table>	Material	Quarry / borrow area	Sand	Banas	Aggregate	Shakun, Lakher	Cement	Lafarge	Steel	SAIL, VIZAG,TATA	<p>Volume of the material extracted is as under:</p> <table><tr><th>Material</th><th>Quantity (MT)</th></tr><tr><td>Sand</td><td>7551.532 52487.442*</td></tr><tr><td>Aggregate</td><td>10750.127 60203.717*</td></tr><tr><td>Cement</td><td>3848.02 20396.49*</td></tr><tr><td>Steel</td><td>1197.22 7883.18*</td></tr></table> <p>* Up to date quantity</p> <div></div>	Material	Quantity (MT)	Sand	7551.532 52487.442*	Aggregate	10750.127 60203.717*	Cement	3848.02 20396.49*	Steel	1197.22 7883.18*
Material	Quarry / borrow area																						
Sand	Banas																						
Aggregate	Shakun, Lakher																						
Cement	Lafarge																						
Steel	SAIL, VIZAG,TATA																						
Material	Quantity (MT)																						
Sand	7551.532 52487.442*																						
Aggregate	10750.127 60203.717*																						
Cement	3848.02 20396.49*																						
Steel	1197.22 7883.18*																						

II. COMPLIANCE TO SAFEGUARDS PROVISIONS IN AGREEMENTS UNDER THE PROJECT

A. Compliance to Loan Agreement

24. The environmental and social safeguard requirements are explicit provided in the Loan Agreement 3062-IND between ADB and State of Rajasthan through the Urban Development and Housing Department (UDH) and Jaipur Metro Rail Corporation (JMRC). These loan agreement provisions and compliance status are provided in Table 2.

Table 2: Status of Compliance to Environmental Provisions of the Loan Agreement

S.N.	Environmental Provision	Compliance Status
1	<p>Schedule 4. Item 7(a):</p> <p><u>Conditions for awards of contracts, commencement of Works</u></p> <p>7. As condition for award of any contract under the project the EA shall ensure the following:</p> <p>a. JMRC shall not award any Works contract which involves environmental impacts until JMRC incorporated the relevant provisions from the EMP and SHE into the Works contract,</p>	<p>Complied.</p> <p>SHE (Safety, Health and Environment) Manual and Environmental Management Plan (EMP) is a part of bidding document. Section 6 of Contract Agreement includes condition of contract on SHE and EMP, requiring the Contractor to implement the EMP and comply with requirements of SHE.</p>
2	<p>Schedule 4. Item 8:</p> <p><u>Conditions for award of contracts; commencement of Works</u></p> <p>8. "As a condition for commencement of Works contract under the Project which involves environmental impacts and if it requires environmental clearances, the State through the JMRC shall ensure that the final approval of environmental clearances including the EIA, SHE, from appropriate <i>authority</i> has been obtained."</p>	<p>Complied.</p> <p>The project did not require environmental clearance, as railways including metro projects in India are not included in the EIA Notification 2006 of Gol.</p>
3	<p>Schedule 5. Item 3:</p> <p><u>Environment</u></p> <p>3. "The Borrower shall ensure or cause the State through JMRC to ensure that the preparation, design, construction, implementation, operation and decommissioning of the Project facilities comply with (i) all applicable laws and regulations of the Borrower and State</p>	<p>Being complied.</p> <p>➤ Requirements on permits and clearance are being followed. The contract has obtained Consent to Establish (CTE) batching plant and casting yard from the Rajasthan</p>

	<p>relating to environment, health, and safety including SHE; (ii) the Environmental Safeguards; and (iii) all measures and requirements set forth in the EIA and the EMP, and any corrective or preventative actions set forth in a Safeguards Monitoring Report.”</p>	<p>State Pollution Control Board in the reporting quarter. The contractor will apply for Consent to Operate (CTO) batching plant and casting yard in the upcoming quarter. Appendix 6</p> <ul style="list-style-type: none"> ➤ SHE is strictly being complied with. ➤ Requirements of EIA and EMP are being implemented.
4	<p>Schedule 5. Item 4(a):</p> <p><u>Land Acquisition and Involuntary Resettlement</u></p> <p>4 (a) Where the need arises, the Borrower shall ensure or cause the State through JMRC to ensure that all land and all rights-of-way required for the Project, and all Project facilities are made available to the Works contractor in accordance with the schedule agreed under the related Works contract and all land acquisition and resettlement activities are implemented in compliance with (i) all applicable laws and regulations of the Borrower and State relating to land acquisition and involuntary resettlement; (ii) the Involuntary Resettlement Safeguards; and (c) all measures and requirements set forth in the respective RP, and any corrective or preventative actions set forth in a Safeguards Monitoring Report.</p>	<p>Being complied.</p> <p>All land acquisition and resettlement activities are implemented as per provisions of Indian Law.</p>
5	<p>Schedule 5. Item 4 (b)</p> <p><u>Land Acquisition and Involuntary Resettlement</u></p> <p>4 (b) Without limiting the application of the Involuntary Resettlement Safeguards, or the RP, the Borrower shall ensure or cause the State through JMRC to ensure that no physical or economic displacement takes place in connection with the Project until: (a) compensation and other entitlements have been provided to affected people in accordance with the RP; and (b) a comprehensive income and livelihood restoration program has been</p>	<p>Being complied.</p> <p>Compensation and other entitlements are being provided to affected people in accordance with applicable laws by JMRC.</p>

	established in accordance with the RP.	
6	<p>Schedule 5. Item 5</p> <p><u>Indigenous Peoples</u></p> <p>5. Where the need arises, the Borrower shall ensure or cause the State through JMRC to ensure that the preparation, design, construction, implementation and operation of the Project, and all Project facilities comply with (a) all applicable laws and regulations of the Borrower and the State relating to indigenous peoples; (b) the Indigenous Peoples Safeguards; and (c) all measures and requirements set forth in the respective IPP, and any corrective or preventative actions set forth in a Safeguards Monitoring Report.</p>	<p>Not applicable.</p> <p>No issues on Indigenous peoples have arisen during the reporting period.</p>
7	<p>Schedule 5. Item 6(a) & 6(b)</p> <p><u>Human and Financial Resources to Implement Safeguards Requirements</u></p> <p>6 (a) "The Borrower shall ensure or cause the State through JMRC to ensure that all necessary budgetary and human resources to fully implement the EMP, and the RP and the IPP as required"</p> <p>6 (b) "The Borrower shall ensure or cause the State through JMRC to ensure that at least one expert each is designated to supervise implementation of the EMP, and the RP and the IPP as required"</p>	<p>Being complied.</p> <ul style="list-style-type: none"> ➤ Safeguards cell comprising of 06 officers has been established in JMRC since 2013. ➤ A JV of M/s Abha Narain Lambah Associates and M/s Shashank Mehendale & Associates has been engaged as Heritage Consultant through ICB. ➤ The Heritage Consultant is to monitor the heritage structures lying along the metro route of Phase 1B. ➤ JMRC has also engaged 3 senior Archaeological Consultants to supervise the excavation of Chhoti Chaupar and Badi Chaupar. ➤ Safeguards experts are part of the PMC (DMRC) team and civil works contractor team. ➤ Adequate budget allocation has been made for implementation of safeguards activities.

8	<p>Schedule 5. Item 7(a)</p> <p><u>Safeguards – Related Provisions in Bidding Documents and Works Contracts.</u></p> <p>7 (a) “comply with the measures and requirements relevant to the contractor set forth in the EIA, the EMP, SHE, the RP and the IPP as applicable (to the extent they concern impacts on affected people during construction), and any corrective or preventative actions set out in a Safeguards Monitoring Report.</p>	<p>Being complied.</p> <p>Safeguards experts are part of the PMC (DMRC) and civil works contractor teams are implementing safeguard measures. Adequate budget allocation is being made for implementation of safeguards activities.</p>
9	<p>Schedule 5. Item 7(b)</p> <p><u>Safeguards – Related Provisions in Bidding Documents and Works Contracts.</u></p> <p>7 (b) “make available a budget for all such environmental and social measures”</p>	<p>Being complied.</p>
10	<p>Schedule 5. Item 7(c)</p> <p><u>Safeguards-Related Provisions in Bidding Documents and Works Contract.</u></p> <p>7 (c) “provide the JMRC with a written notice of any unanticipated environmental, resettlement or indigenous peoples risks if any, or impacts that arise during construction, implementation or operation of the Project that were not considered in the EIA, the EMP, and the RP and the IPP if any;”</p>	<p>Being complied.</p> <p>Appropriate measures are being and will be taken to address these issues, as they arise.</p>
11	<p>Schedule 5. Item 8(a)</p> <p><u>Safeguards – Related Provisions in Bidding Documents and Works Contracts.</u></p> <p>8 (a) submit quarterly Safeguards Monitoring Reports to ADB and disclose relevant information from such reports to affected persons promptly upon submission”</p>	<p>Being complied.</p> <p>Quarterly Environmental and Social Monitoring Reports are being timely submitted by JMRC to ADB. The reports are also being disclosed on ADB and JMRC websites.</p>
12	Schedule 5. Item 8(b)	

	<p><u>Safeguards – Related Provisions in Bidding Documents and Works Contracts.</u></p> <p>8 (b) “if any unanticipated environmental and/or social risks and impacts arise during construction, implementation or operation of the Project that were not considered in the EIA, the EMP, SHE, and RP and IPP as applicable, promptly inform ADB of the occurrence of such risks or impacts, with detailed description of the event and proposed corrective action plan.</p>	Being complied.
13	<p>Schedule 5. Item 8(c)</p> <p><u>Safeguards – Related Provisions in Bidding Documents and Works Contracts.</u></p> <p>8 (c) Report any breach of compliance with the measures and requirements set forth in the EMP, SHE and the RP or the IPP if any, promptly after becoming aware of the breach.</p>	Being complied.
14	<p>Schedule 5. Item 9</p> <p>9. The Borrower shall ensure or cause the State through JMRC to ensure that no proceeds of the Loan under the Project are used to finance any activity included in the list of prohibited investment activities provided in Appendix 5 of ADB’s Safeguard Policy Statement (2009).</p>	Being complied
15	<p>Schedule 5. Item 10</p> <p><u>Other Social Measures</u></p> <p>10. The EA shall ensure that civil works contracts under the Project follow all applicable labor laws of the Borrower and State and that these further include provisions to the effect that contractors; (i) carry out HIV/AIDS awareness programs for labor and disseminate information at worksites on risks of sexually transmitted diseases and HIV/AIDS as part of health and safety measures for those employed during construction; and (ii) follow and implement all statutory provisions on labor (including not employing or using children as labor, equal pay for equal work), health,</p>	<p>Complied.</p> <ul style="list-style-type: none"> ➤ Various awareness programs have been conducted during the reporting period. ➤ HIV/AIDS awareness programs are conducted on regular basis. ➤ Special programs were conducted on 5th& 6th June 2016 as part of World Environment Day celebration. ➤ Monthly environmental training, physical training and general housekeeping training are

	<p>safety, welfare, sanitation, and working conditions. Such contracts shall also include clauses for termination in case of any breach of the stated provisions by the contractors.</p>	<p>conducted in line with India Government's Swachha Bharat Abhiyan.</p> <p>Details of Awareness Programs and Meetings are provided in Appendix 2</p>
16	<p>Schedule 5. Item 11</p> <p>11. The EA shall ensure the safety and status of the heritage sites and structures involved in the Project site at its own cost and in this regard ensure all appropriate steps included as detailed in the PAM.</p>	<p>Being complied.</p> <ul style="list-style-type: none"> ➤ In the bidding document, provision was made to conduct Baseline Building condition survey, wherein the structural stability of structures lying on 30 m on either side of the route alignment of Phase 1B was recorded so as to help monitor any changes which may occur during construction. ➤ JMRC through CEC (AIMIL) got the Building Condition Survey before commencement of work at site. ➤ For the purpose of monitoring heritage structures along with the metro route alignment of Phase 1B, JMRC has engaged Heritage Consultant M/s Abha Narain Lambah Associates and M/s Shashank Mehendale & Associates (JV). ➤ Mitigation and preventive measures are being taken up by M/s CEC in order to avoid any damage.
17	<p>Schedule 5. Item 12</p> <p><u>Gender</u></p> <p>12. The EA shall ensure that the Project is undertaken in conformity with the stakeholder communication strategy as agreed between ADB, the Borrower, State, and JMRC and referred in the PAM.</p>	<p>Being complied.</p>

B. Compliance to Project Administration Manual

25. The Project Administration Manual³ (PAM), describes how the JMRC will implement the project and deliver the results on time, with quality, within budget, and in accordance with government and Asian Development Bank (ADB) policies and procedures. The PAM is mandatory and serves as the main document describing implementation details. The status of implementing the safeguards requirements set out in PAM are provided in Table 3.

Table 3: Compliance to PAM

SN	Details	Compliance Status
1.	<p>Section VII.</p> <p>Safeguards</p> <p>40. Implementation of SHE and EIA.</p> <p>The safeguards cell within JMRC will coordinate and ensure that all environment safeguard requirements under the project are met. The SHE and EIA report including site specific EMP will be included in the contract documents. The contractors must include in their bid adequate budget for implementation of all items in the SHE and EIA. The safeguards cell through the project management consultant (Delhi Metro Rail Corporation) will monitor and report on the environmental compliance of contractors with the SHE and EIA and ensure proper implementation of the grievance and redress mechanism. Key implementation activities for each stage of the project are as follows:</p>	<p>Being complied.</p> <p>Sample monthly monitoring report is provided in Appendix 3.</p>
2.	<p>(i)Pre-construction:</p> <p>All contractors will complete the following activities no later than 30 days from the issuance of Notice to Proceed:</p> <ol style="list-style-type: none"> 1. Submit appointment letter and resume of the Contractor's Health and Safety Officer (HSO) who will be the on-site focal person for environment safeguards; 	<p>Being complied.</p> <p>HSO's CV was submitted on 9 May 2014 and it was approved by GC on 15 May 2014.</p>
	<ol style="list-style-type: none"> 2. HSO will engage CSC-Environment Specialist, and JMRC safeguards cell to a meeting to discuss in detail the SHE and EIA seek clarification and recommend corresponding revisions if necessary; 	<p>SHE and EIA have been discussed in detail by HSO with CSC-Environment Specialist, and JMRC safeguards cell. Details of meetings provided in Appendix 2.</p>

³<http://www.adb.org/sites/default/files/project-document/79731/46417-001-pam.pdf>

SN	Details	Compliance Status
	3. HSO will request CSC-ES copy of monthly monitoring formats and establish deadlines for submission;	Formats for Monthly Monitoring Report have been finalized with CSC-Environment Specialist. Monitoring report is being sent on monthly basis in prescribed format.
	4. HSO will submit for CSC-ES approval an action plan to secure all permits and approvals needed during construction stage such as for operation of crushers and hot mix plants, transport and storage of hazardous materials, waste disposal sites, use of ground water etc.	HSO has submitted plan and action is being taken accordingly.
	5. HSO will submit for approval of CSC-ES the construction camp layout before its establishment where camps are required, and	Camp has been constructed as per approved layout diagram.
	6. Before start of construction, the contractor will post signs in and around the construction site with information on the names, positions, contact numbers, and addresses of key people for receiving grievances	Adequate relevant signage has been displayed. Photolog is in Appendix 1 .
3.	(ii)Construction: The JMRC safeguards cell through the PMC will monitor the Contractor's compliance to the SHE and EIA. In case of non-conformances, the safeguards cell will recommend corrective measures and ensure their timely implementation. If any unanticipated impacts become apparent, the safeguards cell will inform ADB. If required the EIA report will be updated, and mitigation measures and resources to address the new impacts will be identified	Being complied.
4.	(iii)Post-construction: The safeguards cell through the PMC will certify works completed in accordance with SHE and EIA and ensure all construction sites are satisfactorily rehabilitated and restored or otherwise recommend withholding of payments	Not yet due. Will be done in accordance with SHE & EIA.
5.	41. PMC Environmental Specialist: JMRC will ensure PMC (Delhi Metro Rail Corporation) to provide an Environmental Specialist who will, full time during construction, to monitor compliance by the contractor to the	Complied. Mr. S.A. Verma, Sr. AGM/DMRC /Delhi is designated by PMC as its

SN	Details	Compliance Status
	<p>SHE and EIA in support of JMRC safeguard cell. The key qualification and experience consist of (a) minimum of a Master's Degree in Environmental Impact Assessment (EIA) or Environmental Engineering or related subjects; and (b) experience of minimum of 5 years of working experience in conducting Environmental Assessments, implementing and/or supervising environment management activities in infrastructure projects. The objective is to ensure contractor's compliance to the Safety Health and Environment (SHE) Guidelines and EIA in accordance with the requirements of the ADB Safeguard Policy Statement (SPS) 2009 as well as relevant policies of the Government of India. The main output is the Quarterly monitoring report during the construction period. The responsibilities include:</p>	<p>Environmental Specialist to monitor compliance by the Contractor for SHE and EIA. His assistants are doing full time monitoring in Jaipur.</p>
6.	<ul style="list-style-type: none"> Review EIA report including site specific EMP and SHE guidelines to understand the environmental issues in the project area and mitigation and monitoring requirements of the project. 	<p>Complied.</p> <p>EIA, EMP and SHE guidelines have been reviewed.</p>
	<ul style="list-style-type: none"> Update the site specific EMP if there are any significant changes in the project scope or environmental conditions to incorporate all new environmental issues and mitigation measures 	<p>Being complied.</p> <p>EMP will be updated as per requirements.</p>
	<ul style="list-style-type: none"> Prepare monitoring checklists/ templates for daily or weekly monitoring on implementation of the SHE and site specific EMP by the contractor. 	<p>Complied.</p> <p>Site specific monitoring checklists/ templates for daily or weekly monitoring on implementation of the SHE and EMP has been prepared.</p>
	<ul style="list-style-type: none"> Organize a consultation meeting with JMRC safeguards cell, contractors Health and Safety Officers (HSO), Site Engineer and Heritage Expert before the start of physical works to clarify roles and responsibilities of each party. After start of physical works organize a coordination meeting at least every quarter to provide updates, clarify and follow up on pending issues etc. 	<p>Being complied.</p> <p>A consultation meeting between JMRC's Safeguard Cell, Contractor, Health and Safety Officers (HSO), Site Engineer and Heritage Expert held before the start of physical work to clarify roles and responsibilities of each party.</p>

SN	Details	Compliance Status
		Coordination meetings in between JMRC's Safeguard Cell, Contractors, Health and Safety Officers (HSO), Site Engineer and Heritage Expert are being held regularly.
	<ul style="list-style-type: none"> Where necessary organize technical training programs to enhance the field level staff's understanding on environmental issues such as health impacts of dust and noise, waste/debris disposal and management, safety issues etc. 	<p>Being complied.</p> <p>Environmental training programs are conducted on regular basis. The training is conducted by contractor's HSO. If required additional training will be provided by third party agencies on environmental issues. Details of training sessions are provided in Appendix 2.</p>
	<ul style="list-style-type: none"> Monitor implementation of the SHE and site specific EMP by the contractor on a daily or weekly basis. In doing so complete the daily or weekly monitoring checklists. 	<p>Being complied.</p> <p>Monitoring of implementation of SHE and site specific EMP are being done by Contractor's HSO on regular basis. SHE meeting is held with participation from JMRC, DMRC and Contractor and sub-contractors to ensure compliance and implementation of SHE requirements and EMP.</p>
	<ul style="list-style-type: none"> Provide site based technical advice to the contractors where necessary during construction activities 	<p>Site based technical advice to the contractors is being given by DMRC experts.</p>
	<ul style="list-style-type: none"> Co-ordinate with the contractor's site engineers on monitoring and data collection on noise and vibration generated during tunnelling works and operation of heavy machinery 	<p>PMC's environment team is coordinating with contractor's site engineers on monitoring and data collection on noise and vibration generated during operation of heavy machinery. It will also be monitored during tunnelling works.</p>
	<ul style="list-style-type: none"> Coordinate with the Heritage Expert on getting data on monitoring and status of heritage structures above ground. 	<p>PMC's environment team is coordinating with the Heritage Expert on getting data on monitoring and status of heritage structures above ground.</p>

SN	Details	Compliance Status
	<ul style="list-style-type: none"> Facilitate the functioning of the Grievance Redress Mechanism and maintain proper records of all environment related grievances and details on how they were addressed. 	<p>A system is in place to facilitate the functioning of the Grievance Redress Mechanism and maintain proper records of all environment related grievances and details on how they are addressed.</p>
	<ul style="list-style-type: none"> Prepare quarterly Environmental Monitoring reports based on monitoring site visits, completed checklists and quarterly meetings for submission to JMRC safeguards cell and ADB. Amongst other environment safeguard issues, the monitoring report must cover: <ul style="list-style-type: none"> compliance to the SHE and site specific EMP by the contractor vibration monitoring activities conducted by contractor's engineers grievances redress mechanism monitoring and status of heritage sites above ground 	<p>Noted for compliance.</p> <ul style="list-style-type: none"> For compliance of the SHE and site specific EMP by the contractor regular visit is being done by the Environmental team of CSC. For monitoring of the vibration during the construction instrumentation has been done by M/s CEC as per approval given by CSC. The monitoring will be done by a third party agency i.e. M/s. AIMIL. Grievances redress mechanism is in place. For monitoring the status of heritage site above the ground a Heritage Consultant i.e. M/s Abha Narain Lambah Associates and M/s Shashank Mehendale and Associates (JV) has been appointed by JMRC. During the tunneling the team of heritage consultant will be at site to monitor the status of buildings and heritage structures along the metro route.
7.	<p>42. Monitoring of Heritage Structures</p> <p>JMRC through DMRC will retain at its own cost the current Heritage architect as the Heritage site expert during construction of the underground metro section. The expert will be responsible for conducting a baseline survey of heritage sites above the metro alignment and conducting regular monitoring of the status of the heritage sites throughout the construction period. The expert will be responsible for coordinating</p>	<p>Being complied.</p> <ul style="list-style-type: none"> JMRC through competitive bidding has engaged heritage consultant M/s Abha Narain Lambah Associates and M/s Shashank Mehendale & Associates (JV) to monitor the heritage structures lying along

SN	Details	Compliance Status
	<p>necessary procedures if any historical/traditional artifacts are found during tunneling works. He/she will also provide advice on technical measures during construction to prevent damages to the heritage structures. In the event of any damage to a heritage structure he/she will immediately alert JMRC and recommend appropriate mitigation or restoration measures. Key outputs are: (a) Monthly monitoring report; (b) No damage on heritage structures; and (c) in the event of damage, implementation of immediate restoration and mitigation measures. The main responsibilities are:</p>	<p>the metro route of Phase 1B.</p> <ul style="list-style-type: none"> ➤ JMRC has also engaged 3 senior Archaeology Consultants to supervise the excavation of Chhoti Chaupar and Badi Chaupar. ➤ Heritage Consultant got conducted Baseline survey for existing building's condition along the metro route and has submitted Building Inventory report. ➤ Structural survey of buildings along the metro route has also conducted and submitted report, wherein they categorized buildings under 3 categories <ol style="list-style-type: none"> 1. Unstable Structures requiring preventive propping and immediate demolition/ evacuation. 2. Part of structure unstable requiring propping & partial replacement /demolition. 3. No major instability. <p>These reports have been shared with ADB and concerned local agency who will be further taking necessary action.</p> <p>A re-evaluation for the structural condition of the shops along Chandpole launching site (from Chandpole gate to Chhoti Chaupar) was conducted by the Joint team of JMRC, DMRC and M/s CEC engineers. Preventive measures like propping of the verandahs and the shops along the above length have been taken by contractor. The consolidated list of unstable structures requiring immediate attention will be further shared with</p>

SN	Details	Compliance Status
		local agency (Jaipur Municipal Corporation) for further course of action.
8.	<ul style="list-style-type: none"> At least one month before the start of construction activities conduct a baseline survey of all heritage structures above the metro alignment and record detailed information including, but not limited to: list of heritage structures with details on location and distance from the metro alignment, exact height of structures above ground, existence of cracks/ damages prior to start of construction, detailed photographs etc. Monitor the condition of the heritage structures on a monthly basis throughout the construction period and compare the status with the baseline status to ensure that there are no changes from the baseline condition. Coordinating necessary procedures if any historical/traditional artifacts are found during tunnelling works. Provide advice on technical measures during construction to prevent damages to the heritage structures. In the event of observation in any damage to any heritage structure/s immediately alert JMRC and recommend appropriate mitigation or restoration measures. Provide technical advice on and supervise the mitigation or restoration activity. Prepare a monitoring report on a monthly basis to record activities implemented and monitoring findings and submit to JMRC safeguards cell as well the Environmental Specialist. Findings of the report will be included in the quarterly environmental monitoring report that will be prepared by the environmental specialist. 	<p>Complied.</p> <ul style="list-style-type: none"> ➤ Before the start of construction activity, Building Condition Survey of all structure along the metro route with photograph of existing cracks and damages was conducted by CEC through AIMIL. ➤ Before the start of construction activity, Baseline Survey of all the structure along the metro route with detailed photographs was conducted by Heritage Consultant i.e. M/s Abha Narain Lambah Associates and M/s Shashank Mehandale and Associates (JV). ➤ Based on the reports and survey submitted by Heritage consultant, CEC is regularly monitoring status of buildings and the status is reported through daily and weekly reports. ➤ Heritage Consultant entrusted to advice on measures during construction to prevent damages to the heritage structures. ➤ Heritage Consultant is submitting monitoring report on monthly basis to record activities implemented and monitoring findings to JMRC.
9.	<p>Section VII- Safeguards</p> <p>b) Social – Involuntary resettlement.</p> <p>44. If any changes or additional land requirements or involuntary resettlement</p>	<p>Being complied.</p> <p>6 Temples at Chhoti Chaupar, which were infringing the station</p>

SN	Details	Compliance Status
	<p>impacts are identified, a resettlement plan will be prepared in accordance with the ADB <i>Safeguard Policy Statement (2009)</i> and the same is further approved by ADB before award of related civil works contract and implemented before commencement of the relevant section of the civil works contract as applicable.</p>	<p>box area have all been rehabilitated and shifted to a newly constructed Temple complex at Old Atish market land as per their satisfaction of Temple Trusts.</p> <p>Government is continuously in touch with the stakeholders and is in process of ensuring that sentiments of people at large are not hurt. Rozgareshwar Temple at Chhoti Chaupar will be relocated back to its original position after completion of Station work at Chhoti Chaupar.</p> <p>7 temples at Badi Chaupar have been identified which are infringing the station box area. These temples are still to be relocated.</p> <p>Lately the government is in discussion with all the representatives of temples of Badi Chaupar and will be shifting one of the temple Gauri Shankar Mahadev to the plot behind Manak Chowk Thana. The discussions are in progress for final decision.</p>
10	<p>Section VII - Safeguards</p> <p>c) Social – Indigenous people</p> <p>45. In case of any adverse impacts if identified during implementation on indigenous people, the JMRC will ensure that the Indigenous Peoples Plan (IPP) is prepared in accordance with the ADB <i>Safeguard Policy Statement (2009)</i> and the same is further approved by ADB before award of related civil works contract and implemented before commencement of the relevant section of the civil works contract as applicable.</p>	<p>Not Applicable.</p>
11	<p>Section VIII - Gender and Social Dimensions</p> <p>47 Gender consultation and participation</p> <p>Meaningful consultations that are gender</p>	<p>Complied.</p>

SN	Details	Compliance Status
	<p>inclusive and responsive will be carried out as early as in the project preparation stage and will be carried out on an ongoing basis throughout the project cycle.</p> <p>JMRC shall ensure that the bidding documents provide clauses to ensure that all civil works contractors comply with labor laws by not employing child labor; encouraging the employment of the poor, particularly women; and not offering different wages to men and women on work of equal value.</p>	<p>This provision is a part of the bidding document.</p>
12	<p>Section VIII - Gender and Social Dimensions</p> <p>49. HIV and AIDS</p> <p>JMRC will ensure that all civil works contractors (i) carry out awareness programs for labor on the risks of sexually transmitted diseases/AIDS and human trafficking; and (ii) disseminate information at worksites on the risks of sexually transmitted diseases and HIV/AIDS as part of health and safety measures for those employed during construction. Contracts for the project will include specific clauses on these undertakings, and compliance will be strictly monitored by JMRC.</p>	<p>Complied.</p> <p>Periodically awareness about HIV/AIDS is discussed in morning tool box talk and apart from this the medical officer visits the labour camp and explains the risk of sexually transmitted disease on periodic basis. Appendix 2.</p>
13	<p>Section VIII - Gender and Social Dimensions</p> <p>50. Health.</p> <p>JMRC shall ensure that contractors provide adequately for the health and safety of construction workers and further ensure that bidding documents include measures on how contractors will address this, including an information and awareness raising campaign for construction workers on sexually transmitted diseases, HIV/AIDS, and human trafficking.</p>	<p>Complied.</p> <p>Various type of awareness programme has been conducted during this period. Apart from this monthly environmental training, physical training and general housekeeping training are conducted in line with India Government's Swachh Bharat Abhiyan.</p>
14	<p>Section VIII - Gender and Social Dimensions</p> <p>51. Labor</p> <p>JMRC shall ensure that:</p>	<p>Complied.</p>

SN	Details	Compliance Status
	<p>i. civil works contractors comply with all applicable labor laws and regulations, do not employ child labor for construction and maintenance activities, and provide appropriate facilities for women and children in construction campsites;</p> <p>ii. people directly affected by the projects are given priority to be employed by the contractor;</p> <p>iii. contractors do not differentiate wages between men and women for work of equal value; and</p> <p>iv. specific clauses ensuring these will be included in bidding documents. The construction supervision consultants monitor the provisions.</p>	<p>➤ Civil work contractor is complying with all applicable labour laws and regulations.</p> <p>➤ No child labour is employed.</p> <p>➤ Preference is being given to people directly affected by the project.</p> <p>➤ Complying with equal remuneration Act.</p> <p>➤ Specific clause for ensuring labour law etc. has been included in the bidding document.</p>
15	<p>Section IX - Performance Monitoring, Evaluation, Reporting and Communication</p> <p>B. Monitoring.</p> <p>Disclosure of Environmental Assessments and Monitoring Reports</p> <p>ADB and JMRC will disclose on their respective websites the EIA Report. The quarterly monitoring reports will also be disclosed on the ADB website.</p>	<p>Being complied.</p> <p>EIA report has been disclosed on ADB and JMRC websites.</p> <p>Also 1st Semi Annual and subsequent Quarterly Environmental and Social Monitoring Reports are also disclosed on ADB and JMRC websites. www.jaipurmetrorail.in</p> <p>This is the 6th quarterly report (April 2016 –June 2016) on environmental and social safeguards compliance.</p>
16	<p>Section IX - Performance Monitoring, Evaluation, Reporting and Communication</p> <p>B. Monitoring</p> <p>55. Safeguards monitoring - Resettlement</p> <p>If impact is identified during project implementation, a monitoring system will be</p>	<p>Being complied.</p>

SN	Details	Compliance Status
	established based on the ADB <i>Safeguard Policy Statement (2009)</i> and Government of India regulations.	All resettlement and relocation issues will be settled on mutually agreed terms.
17	Section IX - Performance Monitoring, Evaluation, Reporting and Communication B. Monitoring 56. Indigenous People If impact is identified during project implementation, a monitoring system will be established based on the ADB <i>Safeguard Policy Statement (2009)</i> and Government of India regulations.	No impact is identified.
18	Section IX - Performance Monitoring, Evaluation, Reporting and Communication B. Monitoring 58. Grievance Redress Mechanism Grievances related to the implementation of the project, particularly regarding the land acquisition and R&R will be acknowledged, evaluated, and responded to the complainant with corrective actions. Any grievance regarding the land acquisition and R&R is received by OSD (Land), JMRC and is addressed through the decision of the "Negotiation Committee".	Being complied JMRC regularly conducts meetings with project affected people and maintains proper documentation to track their redressal. The details are at Table 12 in this report.

C. Compliance to the Civil Works Contract Agreement

26. The contractor is liable to comply with the safeguards clauses included in the contract agreement. Table 4 below provides an update on the status of safeguards compliance by the civil works contractor.

Table 4: Compliance to the safeguards Clauses of the Civil Work Contract

S.N.	Description	Compliance Status
1	GCC Sub Clause 4.8 Safety Procedures The Contractor shall: a) comply with all applicable safety regulations, b) take care for safety of all persons	Being complied. Contractor is taking adequate measures

S.N.	Description	Compliance Status
	<p>entitled to be on the Site,</p> <p>c) use reasonable efforts to keep the Site and Works clear of unnecessary obstruction so as to avoid danger to these persons,</p> <p>d) provide fencing, lighting, guarding and watching of the Works until completion and taking over under Clause 10 [Employer's Taking Over], and</p> <p>e) Provide any Temporary Works (including roadways, footways, guards and fences) which may be necessary, because of the execution of the Works, for the use and protection of the public and the owners and occupiers of adjacent land.</p>	<p>to comply with regulations on safety of workers.</p>
2	<p>GCC Sub-Clause 6.7</p> <p>Health and Safety</p> <p>The Contractor shall at all times take all reasonable precautions to maintain the health and safety of the Contractor's Personnel. In collaboration with local health authorities, the Contractor shall ensure that medical staff, first aid facilities, sick bay and ambulance service are available at all times at the Site and at any accommodation for Contractor's and Employer's Personnel, and that suitable arrangements are made for all necessary welfare and hygiene requirements and for the prevention of epidemics.</p> <p>The Contractor shall appoint an accident prevention officer at the Site, responsible for maintaining safety and protection against accidents. This person shall be qualified for this responsibility, and shall have the authority to Issue instructions and take protective measures to prevent accidents. Throughout the execution of the Works, the Contractor shall provide whatever is required by this person to exercise this responsibility and authority.</p> <p>The Contractor shall send, to the Engineer, details of any accident as soon as practicable after its occurrence. The</p>	<p>Being complied.</p> <p>Contractor is taking measures as per the provision of SHE, which is also a part of bidding document.</p> <p>A medical room has been established at site with all basic facilities. Around the clock ambulance facility is also available at site.</p> <p>The contractor has tie-up with three hospitals viz, Rawal Hospital, Bhankrota near casting yard, Maxx Hospital near tunnel site and SMS Hospital for any emergencies. Emergency mock drill is conducted on monthly basis to check the efficacy of the system.</p> <p>HSO is also working as accident prevention officer.</p> <p>Being complied.</p>

S.N.	Description	Compliance Status
	Contractor shall maintain records and make reports concerning health, safety and welfare of persons, and damage to property, as the Engineer may reasonably require.	
	<p>PCC Sub-Clause 4.8 and 6.7</p> <p>Safety Procedures and Health & Safety</p> <p>“The Contractor shall throughout the execution of the Works including the carrying out of any testing, commissioning (including Integrated Testing and Commissioning), or remedying of any defects:</p> <ul style="list-style-type: none"> (a) take full responsibility for the adequacy, stability, safety and security of the Works, Plant, Rolling Stock, Contractor's Equipment, Temporary Works, operations on Site and methods of manufacture, installation, construction and transportation; (b) have full regard for the safety of all persons on or in the vicinity of the Site (including without limitation persons to whom access to the Site has been allowed by the Contractor), comply with all relevant safety regulations, including provision of safety gear, and insofar as the Contractor is in occupation or otherwise is using areas of the Site, keep the Site and the Works (so far as the same are not completed and occupied by the Employer) in an orderly state appropriate to the avoidance of injury to all persons and shall keep the Employer indemnified against all injuries to such persons; (c) provide and maintain all lights, guards, fences and warning signs and watchmen when and where necessary or required by the Engineer or by laws or by any relevant authority for the protection of the Works and for the safety and convenience of the public and all persons on or in the vicinity of the Site; and (d) where any work would otherwise be carried out in darkness, ensure that all 	<p>Being complied.</p> <p>Adequate health and safety measures are being implemented as per the provision of SHE, which is also a part of bidding document.</p>

S.N.	Description	Compliance Status
	<p>parts of the Site where work is being carried out are so lighted as to ensure the safety of all persons on or in the vicinity of the Site and of such work.</p> <p>Contractor is required to take note of all the necessary provisions in Employer's Safety, Health and Environment Manual (SHE Manual) and the Contractor's price shall be inclusive of all the necessary costs to meet the prescribed safety standards.</p> <p>Precaution shall be taken by the Contractor to ensure the health and safety of his staff and labour. The Contractor shall, in collaboration with and to the requirements of the local health authorities, ensure that medical staff, first aid facilities, sick bay and ambulance service are available at the accommodation and on the Site at all times, and that suitable arrangements are made for all necessary welfare and hygiene requirements and for the prevention of epidemics. The Contractor shall maintain records and make reports concerning health, safety and welfare of persons, and damage to property, as per the Engineer's requirement and will ensure complete compliance with relevant clauses of Employer's Health, Safety and Environment Manual (SHE Manual).</p> <p>The Contractor's Site Safety Plan shall be developed from his Outline Safety Plan as per Employer's Requirements and SHE Manual of the Employer. The Contractor shall appoint a member of his staff at the Site to be responsible for maintaining the safety, and protection against accidents, of personnel on the Site. This person shall be qualified for his work and shall have the authority to issue instructions and take protective measures to prevent accidents.</p>	
	<p>Safety Precautions</p> <p>Within 8 weeks of the date of Notice to Proceed, the Contractor shall submit a detailed and comprehensive contract-specific Site Safety Plan based on the</p>	<p>Being complied.</p> <p>Contractor has submitted site specific Safety plan and the same have been</p>

S.N.	Description	Compliance Status
	<p>Employer's Safety, Health and Environmental Manual (SHE Manual). The Contractor is required to make himself aware of all the requirements of the Employer's Safety, Health and Environmental Manual in this regard and comply with them. The Site Safety Plan shall include detailed policies, procedures and regulations which, when implemented, will ensure compliance with Sub-Clauses 4.8 and 6.7 of the General Conditions of Contract.</p>	approved by CSC.
	<p>GCC Sub-Clause 4.18</p> <p>Protection of the Environment</p> <p>The Contractor shall take all reasonable steps to protect the environment (both on and off the Site) and to limit damage and nuisance to people and property resulting from pollution, noise and other results of his operations.</p> <p>The Contractor shall ensure that emissions, surface discharges and effluent from the Contractor's activities shall not exceed the values indicated in the Employer's Requirements, and shall not exceed the values prescribed by applicable laws.</p>	Being complied.
	<p>PCC Sub-Clause 4.18</p> <p>Protection of the Environment</p> <p>The Contractor shall be responsible and liable for any stoppage, closure or suspension of the works due to any contravention of statutory requirements relating to the protection of the environment and shall indemnify and keep indemnified the Employer in this regard.</p> <p>The Contractor's Site Environmental Plan shall be developed from his Employer's Safety, Health and Environmental Manual (SHE Manual), as per the Employer's Requirements and Special Conditions of Contract. Nothing extra shall be payable to</p>	Being complied.

S.N.	Description	Compliance Status
	<p>the Contractor on this account and his Bid price shall be inclusive of expenditure required to be incurred for working as per SHE Manual.</p> <p>Outline Environmental Plan means the environmental plan forming part of the Tender, setting out, in summary form, the Contractor's proposed means of complying with his obligations in relation to environmental quality. Site Environmental Plan means the site environmental plan including all supplements thereto, or any amended or varied version thereof, as submitted by the Contractor in accordance with Employer's Safety, Health and Environmental Manual (SHE Manual), this Clause and which has received the Engineer's consent. The Site Environmental Plan shall include detailed policies, procedures and regulations which, when implemented, will ensure compliance with this Clause. The Contractor is required to make himself aware of all the requirements of the Employer's SHE Manual in this regard and comply with them.</p> <p>Within 8 weeks of the date of the Notice to Proceed, the Contractor shall submit a detailed and comprehensive Site Environmental Plan based on the Employer's Safety, Health and Environmental Manual (SHE Manual), and shall include such further material, which the Contractor considers necessary and relevant.</p> <p>Upon the Engineer notifying his consent to the Site Environmental Plan, or any supplemental part thereof, the Contractor shall adhere to the principles and procedures contained in such document save to the extent that the Engineer may give his consent to any amended or varied version thereof.</p> <p>The Contractor shall provide all necessary access, assistance and facilities to enable the Engineer and the Employer to monitor</p>	

S.N.	Description	Compliance Status
	and conduct tests to verify that the Site Environmental Plan is being properly and fully implemented.”	

III. COMPLIANCE TO THE ENVIRONMENTAL MANAGEMENT PLAN

27. The environmental management plan (EMP) for the project was provided in Annexure 4 of the EIA report and also attached to the contract documents. As per EMP, five (05) environmental management activities were required to be implemented during the pre-construction stage (PC 1 – PC5); ten (10) activities are required to be implemented during the construction stage (C1.0 – C1.4, C.1.4.1 and C2 – C6); and three (03) activities are required to be implemented during the operation stage (O1 – O3). The following Table 5 lists out the status of activities during the pre-construction and construction stage as of June 2016.

Table 5: Status of Compliance to the EMP

SN	Activity	Mitigation measures	Compliance attained (Yes, No, Partial)	Comment/Reasons for Partial or Non-Compliance	Issues for further action and target dates
PRE-CONSTRUCTION STAGE					
PC1	Contractor Preparatory Works (Upon issuance of Notice to Proceed)	The Contractor will complete the following activities no later than 30 days upon issuance of Notice to Proceed			
		1) Submit appointment letter and resume of the Contractor's Health and Safety Officer (HSO) and environmental focal person to CSC.	Yes. Mr. Ramaraju has been appointed as Contractor's HSO and he is working full time on site. CV was submitted to CSC.		
		2) HSO will engage CSC-Environment Specialist to a meeting to discuss in detail the EMP, seek clarification and recommend corresponding revisions if necessary	Yes. EMP and SHE have been discussed with CSC-Environment Specialist.		
		3) HSO will request CSC-ES copy of monthly monitoring formats and establish deadlines for submission.	Yes. Formats and schedule of monthly monitoring reports has been finalized. Sample attached in Appendix 3 & 4.		
		4) HSO will submit for CSC-ES approval an action plan to secure all permits and approvals needed to be secured during construction stage which include but not limited to-	Yes.		
		i). operation of crushers and hot mix plants,	Partial. No crushers and hot mix plant have been established by contractor. However the permit for the	Consent to Establish (CTE) batching plant has been obtained from Rajasthan State Pollution Control Board on 05.05.2016. Appendix 6.	

SN	Activity	Mitigation measures	Compliance attained (Yes, No, Partial)	Comment/Reasons for Partial or Non-Compliance	Issues for further action and target dates
			batching plant has not been secured yet.		
		ii) transport and storage of hazardous materials (e.g. fuel, lubricants, explosives),	Yes		
		iii) waste disposal sites and disposal management plan,	No, under process	Application for securing authorization for storage of hazardous waste at site will be processed with the consent to operate application form	
		iv) temporary storage locations,	Yes		
		v) water use, and	Permission has been obtained from state authority for extraction of ground water for drinking purpose at Chhoti Chaupar.	Application for extraction of ground water for construction purpose will be submitted to authority immediately. Currently, water demand is met from extraction of ground water and also through water tankers supplied by private agencies.	Action plan for securing approvals to be submitted by contractor.
		vi) emission compliance of all vehicles. Arrangements to link with government health programs on hygiene, sanitation, and prevention of communicable diseases will also be included in the action plan.	Yes.		
		5) HSO will submit for approval of CSC-ES the construction camp layout before its establishment.	Yes, Construction camp has been established as per approved layout plan.		
PC2	Coordinate with the Jaipur Development Authority on Traffic	The Contractors will discuss and coordinate the implementation of the traffic re-routing scheme particularly in Chhoti Chaupar and Badi Chaupar when it starts the cut and cover activities and the hauling and disposal of excavated materials to the	Yes, Proper traffic management plan is in place in coordination with		

SN	Activity	Mitigation measures	Compliance attained (Yes, No, Partial)	Comment/Reasons for Partial or Non-Compliance	Issues for further action and target dates
	Management Plan to avoid nuisance from traffic congestion	<p>Ambabari village.</p> <p>At the minimum, the traffic management plan will have the following components: construction traffic, ensuring access to properties, accommodating pedestrians, parking, access by construction vehicles, faulty traffic lights and problem interchanges, use of public roads, parking provision during construction, use of residential streets and traffic diversion due to temporary road closures, and construction and use of temporary access roads.</p>	government agencies.		
PC3	Community Liaison to avoid complaints and/or address complaints if any	<p>To ensure that ongoing feedback is provided on the progress of the JMRP together with feedback on the environmental management performance of the project.</p> <p>Contractor will provide a minimum of two (2) weeks notification to directly affected residents, businesses and other relevant groups of the intended construction commencement date. In providing a mechanism for communication between the contractor and the community and informing the public of construction details (timing, expected impacts), the concessionaire will undertake consultation and information activities.</p>	Yes		
PC4	Ground staking to address chance find of artifacts	<p>At least 30 days before the start of tunneling, the Contractor with supervision from the Archeology Department will employ a ground penetrating radar (GPR), detect the presence of buried artifacts along the tunnel alignment.</p> <p>The Contractor, in behalf of the JMRC, will coordinate with the Archeology Department to designate an on-site representative during the entire duration of the project.</p>	<p>Yes.</p> <p>GPR survey has already been submitted and has been uploaded on JMRC website.</p> <p>https://www.jaipurmetrorail.in/pdf/2015.04.16%20GPR%20Received%20from%20CEC.pdf</p>		

SN	Activity	Mitigation measures	Compliance attained (Yes, No, Partial)	Comment/Reasons for Partial or Non-Compliance	Issues for further action and target dates
			JMRC is coordinating with Archeology Department for excavation work.		
PC5	Briefing on working near heritage resource to avoid damages to heritage resources and avoid cultural conflicts	<p>All workers will undergo a briefing with the Archeology Department to ensure safeguarding of heritage resource and cultural/religious practices.</p> <p>A proof of compliance to this requirement to include the name of participants and date and location of briefing will form part of the monthly report to the CSC.</p>	<p>Yes.</p> <p>Briefing is being carried out by the Archaeological Consultant namely Mr. R.D. Singh, Dr. S.K. Sharma and Mr. P.K. Jain engaged by JMRC on regular basis.</p>		
CONSTRUCTION STAGE					
C1.0	Avoid damage to the following heritage resources during tunnel boring namely Chandpole Gate, IsarLat, Jantar Mantar, Hawa Mahal, Chhoti Chaupar, and Badi Chaupar.	No heritage resources are inadvertently damaged during construction.	<p>Yes.</p> <p>No heritage resources are inadvertently damaged during construction.</p>	Complying through instrumentation & online monitoring of structures of historic importance.	
C1.1	To avoid ground settlement under the Chandpole Gate during tunnel boring	<p>The contractor will ensure that no inadvertent damage is incurred to the Chandpole gate.</p> <p>Estimated settlement under the Chandpole gate is less than 5mm. The contractor will ensure that the design value is not exceed and the trigger value = 3.5mm and Allowable value = 4.2 meters are implemented.</p>	<p>Yes. Complied</p> <p>➤ Under passing scheme prepared by M/s Omikron Kappa, of Greece, structural consultant of M/s CEC has been</p>		

SN	Activity	Mitigation measures	Compliance attained (Yes, No, Partial)	Comment/Reasons for Partial or Non-Compliance	Issues for further action and target dates
		<p>Tilt meters will be installed at key positions on the gate to ensure the 2/1000 design value is observed with trigger and allowable values of 1.4/1000 and 1.7/1000, respectively</p> <p>Crack meters will be installed at key positions to ensure design value of 3.0mm is not exceeded with 2.1mm trigger value and 2.5 mm allowable value</p> <p>The contractor will immediately cease all operation if any of the trigger values are breached. The CSC will advise the contractor mitigation measures and practices to control settlement, tilt, and cracks to include but not limited to structural reinforcement and operation parameters of the TBM.</p> <p>The contractor will ensure that no structural damage is incurred and cosmetic damages are repaired under the supervision and control of the Jaipur Archeology Department.</p>	<p>proof checked by M/s Ayesa of Spain.</p> <p>➤ Structural consultant of Heritage consultant has also given his comments on the underpassing scheme of M/s CEC.</p> <p>➤ Under passing scheme of Chandpole gate has also been proof checked by IIT Delhi.</p> <p>➤ Work will be done as per approved method statement & GCC</p>		
C1.2	To avoid cosmetic and structural damages to the structures along the underground metro alignment along Chandpole Bazar and Tripola Bazar due to vibration from the tunnel boring machine	Expected vibration at the Chandpole Gate during tunneling is 0.682 mm/s which is lower than internationally accepted 5mm/s. However, to be on the safe side and as practice in DMRC, the Contractor is to ensure that vibration levels at the Chandpole Gate foundation will not exceed 2.0 mm/s	Complied		

SN	Activity	Mitigation measures	Compliance attained (Yes, No, Partial)	Comment/Reasons for Partial or Non-Compliance	Issues for further action and target dates
C1.3	To minimize surface noise from excavating equipment in Chhoti and Badi Chaupar and avoid disturbance to patients in the Pink City Hospital near Chandpole, Chaudhary Hospital, Maharaja School at the corner of ChhotiChaupar. To avoid damage and nuisance to JantarMantar, and HawaMahal.	<p>The contractor will ensure that noise from construction activities does not result to exceedances of relevant limits prescribed in the Indian Ambient Air Quality Standards for Commercial Area and Silence Zone. Mitigation measures to be implemented by the Contractors are:</p> <ol style="list-style-type: none"> 1) liaise with local residents on how to best minimize construction noise along the Chhoti and BadiChaupars. 2) local residents and shop owners should be informed of the nature and duration of intended activities prior to commencement and kept updated as to changes in the management and mitigation plan 3) equipment compounds will be located off-site 4) noise barriers will be installed at critical work areas particularly around the Chaupars 5) enclose especially noisy activities if above the noise limits 6) employ transportable noise screens between noise sources and identified noise sensitive areas for the duration of noisy construction activities 7) maximize the possibility of scheduling noisy activities at the same time to minimize the duration of exposure <p>Noise from vehicles particularly for hauling of excavated materials to the dump site will be controlled through strict adherence to operating and maintenance instructions, routing of heavy vehicles way from noise sensitive areas whenever possible, conform with speed limits, and construction vehicles will only use routes specified in the traffic management plan.</p>	<p>Yes,</p> <p>Only newly manufactured equipment & regular servicing of equipment is being used in construction.</p> <p>Noise monitoring is being done and necessary mitigation measures are taken as required.</p>		
C1.4	To ensure careful demolition and	The project calls for the demolition of the Chhoti and BadiChaupar and its restoration to its original condition as a requirement from Jaipur	<p>Yes,</p> <p>➤ JMRC through competitive</p>		

SN	Activity	Mitigation measures	Compliance attained (Yes, No, Partial)	Comment/Reasons for Partial or Non-Compliance	Issues for further action and target dates
	proper restoration of Chhoti and Badi Chaupars	Development Authority. The demolition and restoration will be under the supervision and control of these agencies.	<p>bidding has engaged heritage consultant M/s Abha Narain Lambah Associates and M/s Shashank Mehendale & Associates (JV) to monitor the heritage structures lying along the metro route of Phase 1B.</p> <p>➤ JMRC has also engaged 3 senior Archaeology Consultants to supervise the excavation of Chhoti Chaupar and Badi Chaupar.</p> <p>➤ The work will be done as per approved method statement. Also the work will be done under the supervision of said agencies.</p>		
C1.4.1	To address Chance heritage finds during the cut and fill operations	Please refer to FIDIC Sec. 4.24 Fossils. Recording (including chain of custody) will be made by the contractor to be validate by the CSC, and expert verification will be made by the Jaipur Archeology Department. Temporary work stoppage in the immediate area of the chance find for up to 72 hours to allow for the on-site	<p>Yes</p> <p>During the excavation of Chhoti Chaupar, Gomukhs were extracted & were</p>		

SN	Activity	Mitigation measures	Compliance attained (Yes, No, Partial)	Comment/Reasons for Partial or Non-Compliance	Issues for further action and target dates
		representative of Archeology Department to visit the site to make an assessment and provide instructions. Work in the areas adjacent to the chance find will continue as provided in the detailed design.	handed over to Archeological & Museum Dept., Government of Rajasthan. Similar practice will be undertaken during Badi Chaupar		
C2	To avoid the following issues from spoil disposal activities: generation of sediment laden runoff from the work site during monsoon; Contamination of disposal sites from construction debris; Community hazard of uncollected and improperly disposed materials.	<p>A spoil management plan will be implemented that details the location of spoil disposal sites, transporting soil, and disposing of soil. The Contractor will perform the following:</p> <ol style="list-style-type: none"> 1) disposed spoils on permitted sites as instructed by the JMRC 2) ensure the adequacy of the disposal site to handle the volume of spoils the will be generated 3) Prepare, submit and seek approval from the CSC a spoil dump plan that provides the: i) dump size, layout, and form, ii) means of controlling water and wind erosion, iii) measures to prevent spoil dump contamination, vehicular, and public access. 4) Explore the possibility of using spoil materials to rehabilitate borrow pits to 5) All hauling vehicles should be maintained at an acceptable working order and serviced regularly 6) Haul vehicles should be routed away from noise sensitive areas 7) Speed limit in built up areas is 40 km/h 8) All haul vehicles should be covered or soil sprayed with water before leaving the site specially during windy condition 9) Spoil dumps shall have slopes no steeper than 1V:2.5H 10) Final shaping, topsoiling, and immediate revegetation 	<p>Yes,</p> <p>Are being disposed in the approved area only.</p> <p>All other conditions are also being fulfilled.</p>		

SN	Activity	Mitigation measures	Compliance attained (Yes, No, Partial)	Comment/Reasons for Partial or Non-Compliance	Issues for further action and target dates
		11) No vehicles are to be allowed to enter in revegetated spoils dump			
C3	To avoid depletion of groundwater and competition with existing groundwater users due groundwater Extraction for the construction works	<p>The Contactor shall secure permission for groundwater extraction from CGWA pertinent groundwater authorities before establishing borewells.</p> <p>Water conservation and recycling will be observed in all aspects of constructions to include water main breaks, watering roads for dust control, spraying concrete, equipment cleaning and site clean-up.</p>	Partial,	Application is being submitted.	
C4	To avoid nuisance from temporary damage or shifting in utilities particularly buried water pipes and electrical lines and disruption of essential services	<p>The Contractor will ensure that the public will be minimally affected when constructing in close proximity to essential services through:</p> <ol style="list-style-type: none"> 1) coordinate and secure necessary permits for utility shifting with the Jaipur Development Authority and other service utility agencies to locate al services prior to construction in any particular area 2) inform residents of planned interruptions through local media, fliers, and public address system 3) all planned interruptions schedules will be submitted to the safeguards cell JMRC no later than 10 working days before the interruption 4) all affected landowners, tenants, institutions, and businesses to be notified in writing prior to commencement and kept updated in changes of schedule 5) in the event of unforeseen disruptions, the contractor will take all reasonable actions to have the service promptly restored 6) relevant utility agencies will be informed of the construction proximity to essential service line 	<p>Yes,</p> <p>Care is taken to avoid inconvenience to uses by shifting as per instruction of concerned authorities.</p>		

SN	Activity	Mitigation measures	Compliance attained (Yes, No, Partial)	Comment/Reasons for Partial or Non-Compliance	Issues for further action and target dates
		<p>and be kept on standby in the event of unforeseen disruption</p> <p>All unplanned interruption will be immediately reported to the safeguards cell within 24 hour through an incident report.</p>			
C5	To address occupational health and safety issues of the construction workers and local community	The contractor will comply with the occupational health and safety requirements as provided in SHE.	Yes		
C6	Implementation of Cleanup Operations and Restoration and Rehabilitation	Contractor shall prepare site restoration plans, which shall be subject for review and approval by the CSC, JMRC Safeguard Cell, Jaipur Development Authority and the Archeology Department to ensure consistency with zoning and town plans. The clean-up and restoration operations are to be implemented by the Contractor prior to demobilization. All spaces excavated and not occupied by the foundation or other permanent works shall be refilled with earth up to surface of surrounding ground.	Not yet due.		

IV. ACTIVITIES UNDERTAKEN FOR PROTECTION AND MONITORING OF HERITAGE STRUCTURES

A. Findings in Badi Chaupar and Chhoti Chaupar

28. Under Jaipur Metro Rail Project Phase 1B, an underground Metro line is under construction from Chandpole to Badi Chaupar. While Metro tunnel will be constructed using Tunnel Boring Machines, the two underground Metro Stations at Chhoti Chaupar and Badi Chaupar will be constructed by cut and cover method, requiring excavation from top to bottom.

29. To enable construction of underground stations at Chhoti Chaupar and Badi Chaupar, the dismantling of existing Chaupars and excavation underneath was necessary. In this regard, historical background of Chaupars was studied, both the Chaupars were well documented. The two layers of water tank at both the Chaupars with tunnels on all four cardinal direction were encountered. Under the guidance of heritage consultant M/s Abha Narain Lambah Associates and JMRC archaeology consultants the excavation of the tanks were taken up. Documentation including detailed drawings, photography and videography of the all the layers of old water tanks of Chaupars have been prepared. Gaumukhs of both the Chaupars have been handed over to Albert Museum for safe keeping.



30. Both the water tanks at Chhoti Chaupar and Badi Chaupar will be restored at their present site after construction of underground stations. JMRC has ensured and approved designs, wherein the water tanks have been incorporated over the station design. Designs have been approved by heritage consultant of JMRC.

B. D-Wall Construction

31. The D-walls (Diaphragm Walls) act as a structural member for the station box. Prior to the commencement of the D-walls, the utilities are diverted. The construction of D-walls is executed through grabbing machines after completion of the guide wall which act as the guide for the excavation. During the operations the grabbing machines remove the soil, the soil is stabilized using Polymud to avoid the collapse of soil. After reaching the desired level, the

grabbing operations are stopped and the reinforcement cage is lowered into the excavated area and concrete is poured through tremie.

32. To monitor the impact of the operations we have provided tilt meters, crack meter and settlement meters to measure the impact and report any abnormality in the reading. Apart from the above, to protect the existing verandahs, we have done the propping and jacking and also in the shops identified as critical.

C. Chandpole Gate Tunnel Underpass Scheme/ Isarlat Side Pass Scheme

1. Chandpole Gate Tunnel Underpass Scheme



33. Chandpole Gate is coming right in the center of alignment, attracting maximum settlement, but original drawings relating to its foundation were not available. Therefore, the foundation of Chandpole Gate has been physically examined by a team of engineers, by making several trial pits around the gate.

34. For the determination of the structure's foundation, special survey was carried out by CEC and nine trial pits were executed in certain locations near the gate.

35. The foundation of Chandpole Gate has been found to be in a sound condition which can sustain the impact of tunnel-making underneath.

36. To assess the ground settlement due to tunneling by TBM & its effect on structural safety of Chandpole Gate, a detailed 3D analysis has been carried out by M/s Omikron Kappa – Indus Consultrans JV and a detailed report submitted.

37. As per this report, considering that Chandpole gate is in category "Slight" according to the pre-condition survey, "negligible" damage is expected for settlements <6.7mm and angular distortion <1/750. As already derived from the 3D analysis, the maximum calculated settlements and angular distortion are 5mm and 1/1200 respectively, values which are related with "negligible" damage even in the case of "High" vulnerable structures.

38. Considering all the above, a set of values were established for the displacement and deflection of the Chandpole Gate, as presented in the following table.

Measurement	Trigger Level	Alarm Level	Limit values
Settlements	4mm	5mm	6mm

Angular Distortion	1/1400	1/1200	1/1000
--------------------	--------	--------	--------

39. On the advice of Archaeology & Museums Department, the work of further examination/proof check of underpassing scheme of Chandpole Gate was assigned to Indian Institute of Technology (IIT) Delhi. After conducting the proof check of underpassing scheme of Chandpole Gate, IIT Delhi has reported that analysis and other details given in the report are in order. The scheme of Chandpole Gate underpassing by Tunnel Boring Machines is considered safe as it will have no impact on the stability of existing Chandpole Gate.

40. Archaeology & Museums Department, GoR, vide its letter dated 19.06.2015 has issued license under Rule 20 of the Rajasthan Monuments, Archaeological sites and Antiquities Rules, 1968 for construction of twin metro tunnels under Chandpole Gate. The license validity was extended time to time and finally for 2 months i.e. up to 18.02.2016 by the Archaeology & Museums Department, GoR vide its letter dated 15.12.2015.

41. Now both TBMs have crossed underneath Chandpole Gate, the gate sustained no damage during the tunneling process.

2. Isarlat Side Pass Scheme



42. As per report of structural expert of Heritage Consultants, Abha Narain Lambah Associates & Shashank Mehendale & Associates (JV), physical condition of Isarlat is found to be generally sound and it is located at safe distance from the tunnel axis. There will be no adverse impact on the Isarlat during tunnel construction.

43. However, as advised by the structural expert of heritage consultants, a detailed study of Isarlat was taken up through Omikron Kappa, on the lines of the detailed study already carried out for Chandpole Gate. Proof check of the structure/report will be done by IIT Delhi.

44. JMRC will seek permission for conducting instrumentation monitoring from A&M Dept, GoR

D. Results of the Ground Penetrating Radar

1. Introduction

45. Ground penetrating radar survey is a non-destructive geophysical method that produces a continuous cross-sectional profile or record of subsurface features, without drilling, probing, or

digging. Ground penetrating radar (GPR) profiles are used for evaluating the location and depth of buried objects and to investigate the presence and continuity of natural subsurface conditions and features. It is a high-resolution geophysical method, which is based on the propagation of high frequency electromagnetic waves. The GPR method images structures in the ground that are related to changes in dielectric properties. In sediments, the water content primarily causes the changes in dielectric properties.

2. Study Area

46. In order to prioritize the scanning work, the entire stretch between Chandpole & Badi Chaupar has been sub-divided into following sectors:

Sector-1: Along the tunnel alignment for the stretch between Chandpole Metro station to Chhoti Chaupar.

Sector-2: Chhoti Chaupar Metro station.

Sector-3: Along the tunnel alignment for the stretch between Chhoti Chaupar to Badi Chaupar.

3. Conclusion

47. Survey using Ground Penetration Radar with 100 MHz paired antenna has provided scanning down to a depth of 22m.

48. The interpretation of all these scans shows that two distinct layers exists upto the scanned depth for the entire stretch between Chandpole and Badi Chaupar. This is depicted in the scans provided at Figure 10 to 27 of the report. The 3-dimensional model (surface and block) provides variation in terms of depth for the two layers. The drill hole core too in the area indicates presence of two layers of silty sand/sandy silt as defined by grain size analysis of the soil as per geotechnical report. A small portion in the entire stretch indicates more reflective zone which could be on account of anomalous material such as presence of metallic substance, high moisture content or an object.

49. A part of the entire stretch was also taken up for utility survey. This indicates the importance of GPR survey for locating utilities before excavating the area. This helps in planning the excavation work without damaging the existing utilities.

50. The summary report of the GPR done for the project is available online at JMRC webportal.

V. SUMMARY OF ENVIRONMENTAL MONITORING

A. Summary of Inspection Activities

51. A total of 08 SHE Walk inspections were conducted by the CSC-ES during the reporting period. Further details on the inspections carried out and key findings are provided in Table 6.

Table 6: Field Inspections carried out during reporting period

Date of Inspection	Location	Participants	Key Findings
08.04.2016	Chandpole	12	Safety & Environment
08.04.2015	Badi Chaupar	09	Safety & Environment

Date of Inspection	Location	Participants	Key Findings
15.04.2016	Chhoti Chaupar	07	Safety & Environment
22.04.2016	Badi Chaupar	11	Safety & Environment
29.04.2016	Casting Yard	14	Safety & Environment
13.05.2016	Badi Chaupar	12	Safety & Environment
20.05.2016	Chhoti Chaupar	13	Safety & Environment
27.05.2016	Badi Chaupar	07	Safety & Environment
03.06.2016	Chhoti Chaupar	24	Safety & Environment
11.06.2016	Chhoti Chaupar	13	Safety & Environment
17.06.2016	Chhoti Chaupar	11	Safety & Environment

Note: Sample copy of SHE Walk attached with Appendix 2.

B. Monitoring of Cracks, Settlements of Structures

52. The entire area where the stations as well as the tunnels underpasses fall under heritage structures. In order to observe the conditions and behaviors of the structures during the operations, monitoring is being done through instrumentations.

53. **Location and Quantity of Instrument which is installed:** Chandpole area we have installed Inclinator in the D-Wall of Shaft area. In Chhoti Chaupar station area we have installed some building instruments. Photographs of tilt, crack and other instruments in working is given in Appendix-9.

54. Monitoring Frequency at Station, C&C and Launching Shaft

SN	INSTRUMENT	FREQUENCY
1	Inclinometer	Once daily during excavation then once weekly
2	Soil Settlement Marker	Once daily during excavation then once weekly
3	Pavement Settlement Marker	Once daily during excavation then once weekly
4	Crack Meter	Once daily during excavation then once weekly
5	Tilt Meter	Once daily during excavation then once weekly

Note: Monitoring frequency may be changed depending upon whether any deformation is observed.

55. **Inclinometer Model AIM-741 or equivalent:** The purpose of inclinometer monitoring is to observe and monitor any lateral movements within structures or strata and analysis whether remedial works are required to subdue any such movements.

56. **Tilt meter-Model AIM-5410 or equivalent:** Portable tilt meters are mainly used to monitor buildings, structures, utilities, etc. As well as the inclination and rotation of retaining walls, dams, piers, piles, etc. It may also be used to evaluate the performance of bridges, struts and the stability of structures in land slide areas.

57. The portable tilt consists of components: tilt meter, and



EAN-70 meter system three plate, tilt readout unit.

58. **Crack meter- Model AIM-100SC or equivalent:** The crack meter is suitable for measuring structured cracks ranging from 0.5 to 100 mm with a hairline cursory mark in two directions i.e. vertical and horizontal. The advantages of this instrument are: reliable and accurate, simple to install, simple to operation and low cost. This is very simple and accurate instrument to monitor the hair crack. The mechanical crack meter is made of polycarbonate transparent sheet with graduated marks. The both sheets will be assembled on crack with the help of fasteners.



59. **Bi- Reflex Target:**



60. The bi-reflex target is one of the surveying equipment to measure deformations and settlements of the structures surrounding the construction site. It is rugged precise and low cost with an accuracy of $\pm 0.1\text{mm}$.

61. Summary of results

Sl. No.	Instrument	Total instrument	Max. deflection observed	Trigger level	Alarm level	Limit level
Monitoring period- April 2016						
1	Tilt meter	189	$\pm 0.040^\circ$	$\pm 0.08^\circ$	$\pm 0.10^\circ$	$\pm 0.11^\circ$
2	Crack meter	54	0.0 mm	± 3.0	± 5.0	
3	Bi-reflex Target	204	± 4.0 mm	± 7.0 mm	± 9.0 mm	± 10.0 mm
4	Building settlement marker (BSM)	198	-6.00 mm	± 14.0 mm	± 18.0 mm	
5	Pavement settlement marker (PSM)	77	-5.00mm	± 14.0 mm	± 18.0 mm	
Monitoring period- May 2016						
1	Tilt meter	250	-0.040°	$\pm 0.08^\circ$	$\pm 0.10^\circ$	$\pm 0.11^\circ$
2	Crack meter	73	0.0 mm	± 3.0 mm	± 5.0 mm	
3	Bi-reflex Target	311	± 3.0 mm	± 7.0 mm	± 9.0 mm	± 10.0 mm
4	Building settlement marker (BSM)	247	± 3.0 mm	± 14.0 mm	± 18.0 mm	
5	Pavement settlement marker (PSM)	77	- 3mm	± 14.0 mm	± 18.0 mm	
6	Inclinometer	2				
Monitoring period- June						
1	Tilt meter	254	0.04°	$\pm 0.08^\circ$	$\pm 0.10^\circ$	$\pm 0.11^\circ$
2	Crack meter	79	0.7mm	± 3.0 mm	± 5.0 mm	
3	Bi-reflex Target	311	-4 mm	± 7.0 mm	± 9.0 mm	± 10.0 mm
4	Building settlement marker (BSM)	271	-4 mm	± 14.0 mm	± 18.0 mm	
5	Pavement settlement marker (PSM)	88	- 3mm	± 14.0 mm	± 18.0 mm	
6	Inclinometer	2	-1.71 mm	± 18.0 mm	± 23.0 mm	

C. Vibration Monitoring:

62. **Need for Vibration Monitoring:** The construction of underground rail and road infrastructures in metropolitan and cosmopolitan cities are mostly through developed area under challenging soil conditions. The alignment of structure is passing through densely inhabited areas with many heritage structures falling in the zone of influence of construction activities.

63. Construction vibration sources generate elastic waves in soil and have a wide range of energy, displacement, velocity and acceleration transmitted on the ground. These may be harmful to adjacent and remote structures, sensitive instruments and people. Their effects range

from serious disturbance of working conditions for sensitive devices and people, to visible structural damage.

64. It is important to assess the dynamic effect before the beginning of construction activities and at the time of construction. Therefore monitoring of construction vibrations have to be started prior to the beginning of construction works at a site and be continued during construction to provide the safety and serviceability of sound and vulnerable structures.

65. It is required to carry out base line monitoring to determine the Pear Particle Velocity and their respective frequency band that are persisting even before carrying out any construction activities. The recorded values shall form the base line and shall be compared to the corresponding values recorded during construction activities and the influence of construction may be determined accordingly.

Table 7: Vibration Monitoring

Station/ Tunnel	Location (Shop/House No.)	Land Mark	Structure Id (BCS)	Category
Chhoti Chaupar	Shop No. 189	In front Corner Column	CP-CC- UP-0071	Very Severe
CP to CC Tunnel	Up Line Wall Design No. 31 Left Wall while entering the wall 30 cm. In & 40 cm. from Corner (near CP- 0016)	Chandpole Wall UP	CP-0016	Very Severe
CP to CC Tunnel	Up Line Small Gate near Noor Bhai Pahalwan Shop aprox 3.5 mtr before & 30 cm. in From Small Gate.	Chandpole Gate	CP-CC- DN-0154	Severe
Chhoti Chaupar	Up Line Verandah of Shop No.379 Left Col. From Shop Just before 25 CM. From Left Col. Direction L-R for distance. (RHS Col. Of Shop No. 380).	In front Corner Column	CC-BC- DN-0001	Very Severe

Photograph of the location where Vibration Monitoring Reading has been taken.





D. Noise Monitoring

66. Noise level survey was conducted by 3rd party M/s. EKO PRO Engineering pvt.Ltd at all project sites for Day & Night shifts viz Bhankrota, Chandpole launching shaft Area, Pink City Hospital, Chhoti Chaupar, Maharaja school, Chaudhry Hospital, Krishna temple, Hawa Mahal, and Jantar Mantar for Day & Night shifts.

67. It has been observed from the results that no major noise level exceedance was recorded at any site except at Hawa Mahal for day time. Results are summarised in Table 8 and 9 and graphical representation of results are also given below. Complete monitoring reports are provided in Appnedix 4.

Table 8: Noise Monitoring Results (Day time)

Date	Leq Day dB(A)							
	Location							
	Casting Yard	Chand pole	Maharaja School	Chaudhri hospital	Pinkcity Hospital	Krishna Temple	Jantar Mantar	Hawa Mahal
14.04.2016 to 19.04.2016	68.5	67.6	60.3	58.1	62.1	64.3	61.4	65.3
11.05.2016 to 14.05.2016	65.5	69.1	64.2	60.7	61.4	61.5	63.0	68.8
16.06.2016 to 19.06.2016	62.2	70.4	61.2	57.7	63.7	60.8	65.1	68.9

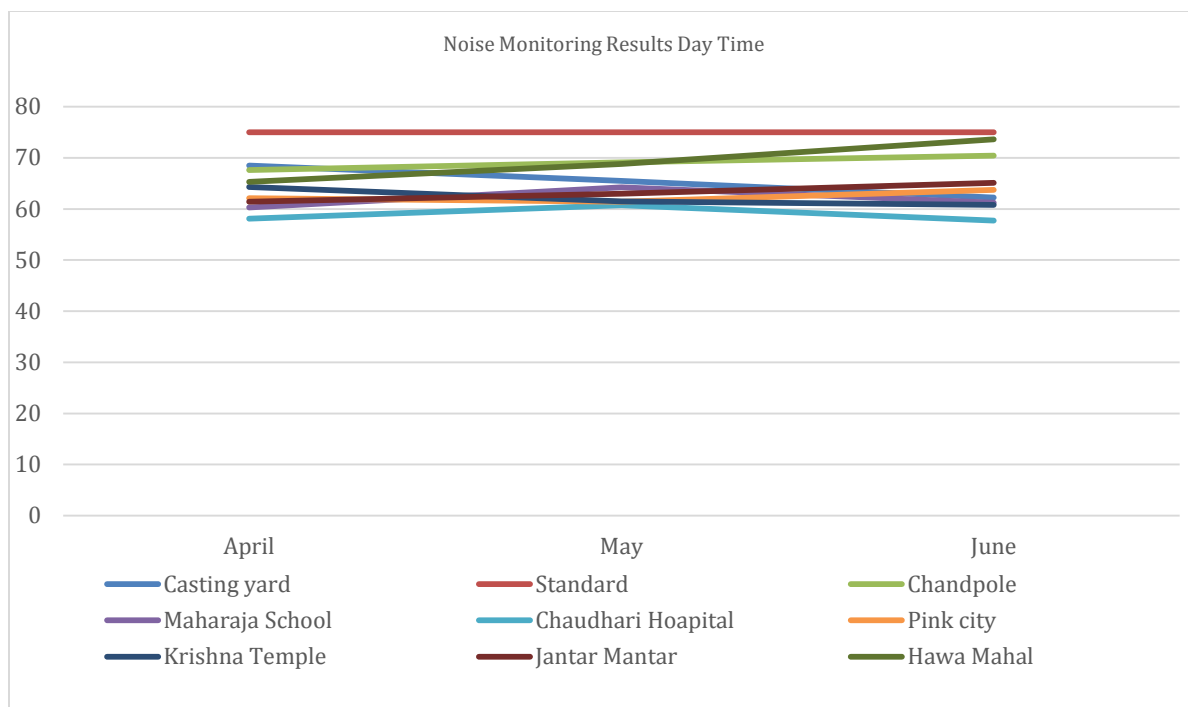
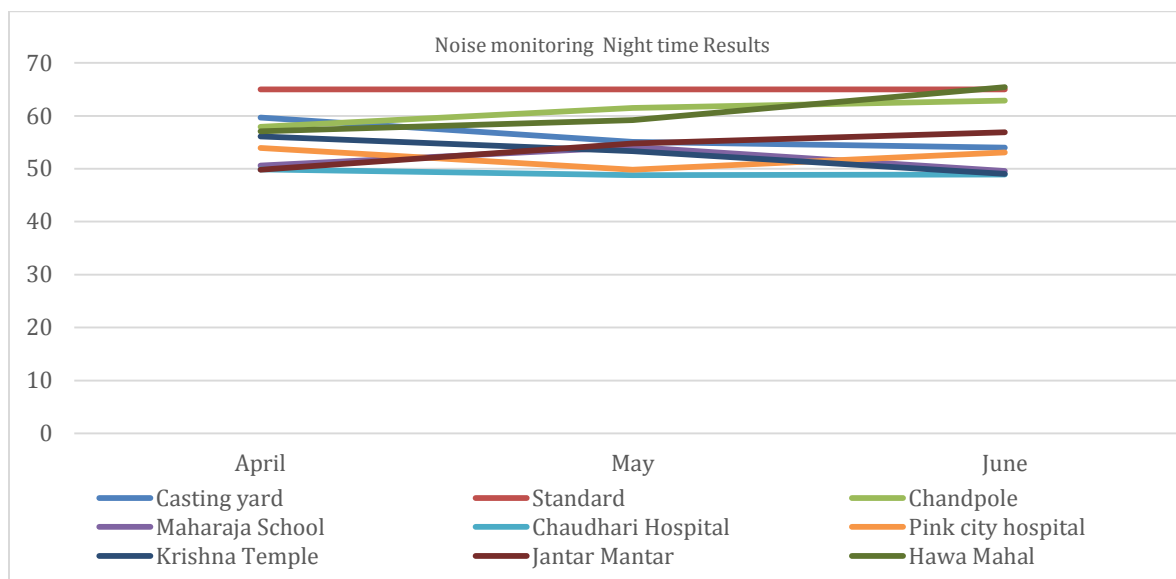


Table 9: Noise Monitoring Results (Night time)

Date	Leq Night dB(A)							
	Location							
	Casting Yard	Chand pole	Maharaja School	Chaudhri hospital	Pinkcity Hospital	Krishna Temple	Jantar Mantar	Hawa Mahal
14.04.2016 to 19.04.2016	59.7	57.9	50.6	49.9	53.9	56.1	49.8	57.1
11.05.2016 to 14.06.2016	55.1	61.5	54.1	48.8	49.8	53.3	54.8	59.2
16.06.2016 to 19.06.2016	54.0	62.9	49.6	48.9	53.1	49.0	56.9	60.7



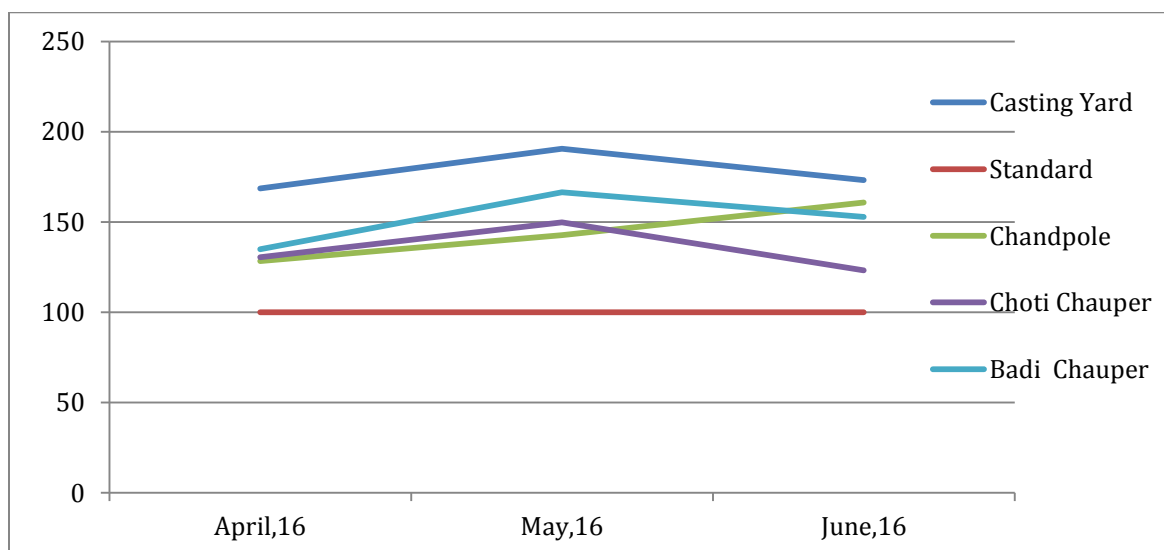
E. Air Quality

68. The ambient status of five major air pollutants viz. Total Suspended Particulate Matter (TSPM); PM₁₀, Sulphur Dioxide (SO₂), Oxides of Nitrogen (NO_x) and Carbon Monoxide (CO) representing the quality of pollution level have been assessed by monitoring air quality at four locations viz. Casting Yard, Chandpole launching shaft, Chhoti Chaupar & Badi Chaupar. The air quality monitoring results indicate that PM₁₀ concentration exceeds the limits specified by CPCB for all sites. However, except at casting yard in the month of May the concentration of PM₁₀ was below the baseline concentration value of 180 µg/m³ (2012 monitoring) for all sites.

69. Air monitoring was carried out from April 2016 to June 2016. Test results are summarised in Table 10. Complete monitoring reports are given in **Appendix 4**.

Table-10: Air Quality Monitoring Results

Date	PM ₁₀ (Unit µg/m ³)			
	Location			
	Casting Yard	Chandpole	Chhoti Chaupar	Badi Chaupar
14.04.2016 to 17.04.2016	168.6	128.3	130.5	134.9
11.05.2016 to 14.05.2016	190.6	142.6	149.8	166.4
16.06.2016 to 19.06.2016	173.2	160.8	135.2	152.8



70. **Air Pollution Control:** The mitigation measures, which have adopted to reduce the air pollution are: all transportation of construction materials should be covered manner. To minimize dust emission due to handling of aggregate and cement at site, there are two time sprinkling of water on the internal roads. Vehicle speed restriction of 5-10 km/hrs have been followed at site, tyre washing facility have been provided for cleaning of vehicles/tyres at Chandpole exit gate.

F. Water Quality

71. Water samples were collected from nearby bore wells during May, 2016 to check the quality of the water. Quarterly water analysis results are compared with IS 10500:2012 and found within permissible limited. Results are summarised in Table 11 and monitoring reports are provided in **Appendix 4. Table 11: Water Quality Monitoring Results**

Sr. No	Parameters	Units	Results	
Sample Identification			Casting Yard	Chandpole
1.	pH(at 25 °C)	-	7.42	7.30
2.	Turbidity	NTU	< 1.0	< 1.0
3.	Conductivity	µs/cm	141.5	160.0
4.	Total Dissolved Solids	mg/L	92.00	104.00
5.	Total Suspended Solids	mg/L	<5.0	<5.0
6.	Oil and Grease	mg/L	ND	ND
7.	Dissolve Oxygen	mg/L	5.4	5.9
8.	E.coli	Per 100 ml	Absent	Absent

VI. SOCIAL AND RESETTLEMENT IMPACTS

A. Impacts on Structures

A.1 Shifting of Temples

72. When the work of Phase 1B started it was found that 6 temples fell within the station box area of Chhoti Chaupar and Badi Chaupar where digging is necessary for construction of stations, required immediate relocation. Three of these temples were at Chhoti Chaupar & another three at Badi Chaupar, as under:

1. Hanuman Mandir (Chhoti Chaupar)
2. Shiv Mandir (Chhoti Chaupar)
3. Rojgareshwar Mandir (Chhoti Chaupar)
4. Shiv Mandir (Badi Chaupar)
5. Ganesh Mandir (Badi Chaupar)
6. Hanuman Mandir (Badi Chaupar)

73. As per the decision taken by High Power Committee chaired by Chief Secretary GoR, an office order was issued on 16.10.2014, that GAD land at Tripolia Bazar i.e. Tanwar Ji ka Nauhra (around 200 mt from Chhoti Chaupar) which has two courtyards admeasuring 542 sqmt and 645 sqmt respectively be handed over to Jaipur Metro Rail Corporation for relocation of 6 temples and development of Two Wheeler Parking, respectively.

74. The possession of the land was taken over by JMRC from Public Works Department on 17.11.2014.



Figure a: Location of Tanwar Ji Ka Nauhra (Land identified for temple relocation)

75. As the planning and designing of station at Chhoti Chaupar and Badi Chaupar progressed, 7 additional temples were identified which either infringed the entry exit structure or came in mid of the traffic diversion scheme. The detail of the additional temples is as below:

1. Barah ling Mahadev (Chhoti Chaupar)
2. Rameshwar Mahadev (Chhoti Chaupar)
3. Bajrangbali Mandir (Chhoti Chaupar)
4. Peepleshwar Mahadev (Badi Chaupar)
5. Mahadev Ji/Mataji/Hanuman Mandir (Badi Chaupar)
6. Mahadev Mandir (Badi Chaupar)
7. Mahadev/Hanuman Mandir (Badi Chaupar)

76. Proper documentation and measurement were taken and recorded for all the temples.

77. Necessary measures have been taken for relocation of identified temples and 6 Temples of Chhoti Chaupar have already been relocated at Old Atish market.

78. On 11.05.2015/12.05.2015, six temples of Chhoti Chaupar were shifted to Old Atish Market and Murti Sthapna was done along with proper ritual ceremony.



79. As per earlier directions, following was the status of the matter related to shifting of 7 temples at Badi Chaupar is as below:

Temple No.	Temple Name	Owner Name	Existing Area (sqmt)	Proposed Shifting to	Area Allocated at new site
1	Shiv Mandir, Sh Gaurishankarji, On Median towards Chhoti Chaupar	Sh. Jeetendra Vyas	2.747	Tanwar Ji Ka Nauhra	6.25 sqmt (2.5 x 2.5 mt)
2	Dhruv Mukhi Mahaveer Hanuman Mandir, NW Khanda	Sh. Abhishek Sharma	3.781	Ramnagariya Yojana	45 sqmt (Plot No. A363)
3	Ganesh ji Shivalay Mandir, SE Khanda	Sh. Vishnu Kr Sharma	3.132	Rajarampura Awasiya Yojana	45 sqmt (Plot No. 229)
4	Peepleshwar Mahadev, Hanumanji, Ganesh mandir- SW Khanda	Sh. Rajnarayan Vyas	8.02	Tanwar Ji Ka Nauhra	8.00 sqmt (3.2 x 2.5 mt)
5	Mahdev ji, Mataji, Hanuman Mandir- SE Khanda	Sh. Purushotam Bharti	39.97	Tanwar Ji Ka Nauhra	40.0 sqmt (6.325 x 6.325 mt)
6	Mahadev Mandir, Outside Police thana- NE Khanda (Shri Jamneshwar Mahadev Trust)	Sh. Dinesh Vyas	5.096	Ramnagariya Yojana	Combined Plot (Plot A434) 90 sqmt
7	Mahadev /Hanuman Mandir, Outside Police thana- NE Khanda (Shri Amneshwar Mahadev Trust)		4.899	Ramnagariya Yojana	

Ongoing construction work at Tanwar ji Ka Nauhra (Badi Chaupar Temple Shifting)



80. All matters related to compensation and relocation of temples at Chhoti & Badi Chaupar are being dealt with at the level of Collector, Jaipur.

81. Government is continuously in touch with the stakeholders and is in process of ensuring that sentiments of people at large are not hurt. Rozgareshwar Temple at Chhoti Chaupar will be relocated back to its original position after completion of Station work at Chhoti Chaupar.

82. Lately the government is in discussion with all the representatives of temples of Badi Chaupar and will be shifting one of the temple Gauri Shankar Mahadev to the plot behind Manak Chowk Thana. The discussion are in progress for final decision.

B. Land Acquisition and Resettlement

83. For the purpose of easing the traffic diversion near Sanjay Circle, Chandpole, JMRC has processed for acquisition of 3 shops located at Sansar Chand Road. Details are given below:

SN	Shop Detail	Name of Shop Owner	Name of Shopkeeper	Area (sq.m)
1	Shekhawat Rajput Dhaba (Part of Shop No. 12)	Mohd. Salim, S/o Yaseen Khan	Mukut Bihari, Satynarayan, S/o Banshilal Mehra	7.49
2	Bharat Cold Drink (Part of Shop No. 12)			3.90
3	Shiv Pan Bhandar (Part of Shop No. 12)		Bihari Lal S/o Nandlal Saini	1.30
4	DCB ATM	Smt. Mamta Kanwar W/o Sohan Singh Shekhawat	DCB Bank	5.46



84. Considering the time required for land acquisition process per new Land Acquisition Act of GOI, it was agreed and decided by JMRC (in consultation and discussion with shop owners) to resettle the shop owners on the other side of the road near Chandpole station (Near Church land). Besides resettling shops, JMRC also agreed to provide assistance during relocation process including any loss of income during the relocation process. Shop owners also agreed that new shops will be rented to same shopkeepers who are currently running these shops.

85. The shopowners have given their consent to the proposal. JMRC is in the process of getting written consents from shopowners and shifting will be done in consultations with shop owners before start of work near these shops.

86. The site selected for relocation of these shops is getting prepared and construction is ongoing. Very soon the shop owners will be given possession of the newly constructed shops.



VII. PUBLIC CONSULTATIONS AND ADDRESSING OF GRIEVANCES

A. Public Consultations carried out

87. Consultations are being held regularly with the local people in the project area including relevant government agencies, the business associations in the project are such as the Chandpole Bazaar Vyapar Mandal and Tripolia Bazaar Vyapar Mandal.

88. JMRC has taken all possible measures to ensure that following concerns are regularly addressed:

- a) Heritage character of Jaipur
- b) Traffic diversion during construction
- c) Inclusion of all key stakeholders

89. During the period of this report (April 2016–June 2016) following consultations were held:

Table 12: Consultations held during the reporting period

Date	Venue	Participants	Detail of discussion held	Action Taken
16.04.2016	Tripoliya Bazar	President, Vyapar Mandal Tripoliya	To discuss proposed plan for Traffic Diversion	Through the president of Vyapar Mandal, the business community was informed about the plan for Traffic Diversion.
22.04.2016	Tripoliya Bazar	Representatives from Vyapar Mandal	Deployment of Traffic Marshals	Discussion was held to take inputs from Vyapar Mandal over the Traffic diversion plan and specific requirements

Date	Venue	Participants	Detail of discussion held	Action Taken
03.05.2016	Ramganj Construction Site	Shopkeepers of Ramganj side	Matter related to barricading required for traffic diversion and construction work	Discussion was held, inputs were taken and accordingly barricading and Traffic Marshals were deployed on site.
16.05.2016	Ramganj	Ramganj Vyapar Mandal	To discuss the progress of Metro work, traffic diversion	Representatives and office bearers of Vyapar Mandal were apprised of the Steps taken by JMRC for smooth construction work and traffic diversion.

B. Complaints and Requests Received

90. During the period of reporting (April 2016 to June 2016) no written grievances and requests application was received from the local people in the project area.

VIII. UNANTICIPATED SAFEGUARD ISSUES

91. During the reporting period from April 2016 to June 2016, no such anticipated safeguard issues were come across.

IX. CONCLUSION

A. Summarize the overall Progress of Implementation of safeguard Measures⁴

92. The implementation of environmental management measures in this project face some difficulties but it can be concluded that the overall progress of implementing environmental and social safeguard measures show a highly satisfactory level. Table 13 shows a comparative scenario of implementing environmental management measures for each package.

Table 13: Overall Progress

Site Safety	Workers Safety	Protection of Environment	Protection of Heritage structures	Statutory Approvals	Filling of Checklists	Overall Rank
1	1	1	2	2	1	2

B. Problems Identified and Actions Recommended

93. During the previous reporting period (January 2016-March 2016) some of the issues were identified such as follow-up with regulatory / government agencies to get pending

⁴Overall sector environmental management progress could be described in qualitative terms or be evaluated based on a ranking system, such as the following:

1. Very Good
2. Good
3. Fair
4. Poor
5. Very Poor

Additional explanatory comments should be provided as necessary.

approvals/permits, full time environmental specialist by the CSC, proper documentations and record keeping, and information disclosure. However, these issues are still pending.

94. Table 14 present the actions that are proposed in the previous monitoring report and actions taken to address these problems:

Table 14: Status of Actions suggested in previous Monitoring Report

Action Recommended	Measures Taken	Remarks
Follow-up with regulatory / government agencies to get pending approvals/permits.	Consent to Establish (CTE) for batching plant has been obtained from Rajasthan Pollution Control Board. Application for Consent to operate (CTO) along with authorization for storage of hazardous waste will be processed in the coming quarter. Permission to extract ground water from CGWA will be pursued.	Expedite process to get pending clearance on priority basis.
PMC's environmental specialist to provide technical support and guidance to the contractor and JMRC on full time basis	DMRC has deputed junior expert to the site to provide technical support to contractor and JMRC.	Full time environmental specialist is required at site. JMRC to take action on priority.
Appoint a consultant for community mobilization and more effecting community liaison particularly with regard to heritage issues, safety issues, utility shifting and anticipated temporary suspension of services. He will also facilitate Consultation with concerned stakeholders to clearly explain particularly to people who do not have access to the internet, the precautionary measures being taken to protect the heritage structures and to retrieve the lost layers of history.	A JV of M/s Abha Narain Lambah Associates and M/s Shashank Mehendale & Associates has been engaged as Heritage Consultant through ICB. JMRC has also engaged 3 senior Archaeological Consultants to supervise the excavation of Chhoti Chaupar and Badi Chaupar. These consultants together with JMRC are responsible for maintaining regular communications with communities and stakeholders.	Continuous follow up required.
Improvements in maintenance of records and reporting of interactions and communication with the stakeholders.	Records of the stakeholder and community interactions are being maintained at Contractor, DMRC and JMRC end.	

95. Finally, according to the field observations and investigations it was able to identify that the most of the environmental requirements are being complied with regulations. Actions such as regular follow up with regulatory agencies to get pending permits; mobilization of full time environmental staff from supervision consultant side, and contineous coordination with

shopkeepers and temple authorities to relocate the temples and shops require immediate followup.

APPENDICES

1. Photolog
2. Record of SHE Training
3. Sample format of Monthly SHE report
4. Environment Quality Monitoring Report
5. Monthly Report of Heritage Consultant
6. Consent to Establish letter from State Pollution Control Board
7. Muck disposal site photographs and details
8. Tree transplantation details
9. Photographs of tilt, crack and other instruments in working.

Appendix 1: Photolog of Progress



View of tunnel towards Badi Chauper and Chandpole



View of TBM-2



View of TBM-1



<p>Monthly SHE Committee meeting</p>  <p>Tally Board system at Chandpole</p>	<p>Labour Camp at Casting Yard</p>  <p>Soil Excavation at Chhoti Chaupar</p>
 <p>World Environment Day Celebration</p>	 <p>Environment Awareness Training</p>
 <p>Tree sampling at Police Head Quater site</p>	 <p>Awarding the Best Environmental practices</p>



Awarding BEST ENVIRONMENTAL PRACTICES to Mr. Suresh Seetaram Hedge Station Manager Chhoti Chaupar



96 Hrs training



Manually Water sprinkling for Dust control on site access.



Mosquito control on Site

Appendix 2: Record of SHE Trainings

1. Details of SHE training conducted in the month of April 2016 to June, 2016

Month of April Training

SN	DATE	LOCATION	TOPIC	NO. OF PERSON	REMARKS
1.	06/04/2016	Casting yard	Eye Protection & Eye Wash Procedure	68	
2.	07/04/2016	Casting yard	Preparedness of Secured Health life	12	
3.	09/04/2016	Casting yard	Electrical Safety	10	
4.	14/04/2016	Casting yard	Electrical Safety	11	
5.	15/04/2016	Casting yard	Environment Management System & Pollution Control	07	
6.	19/4/2016	Casting yard	Safe Welding Work Procedures	18	
7.	25/4/2016	Casting yard	Safe Working Procedures during concrete work	19	
8.	07/4/2016	Chandpole	World Health day	93	
9.	10/4/2016	Chandpole	Emergency Preparedness	21	
10.	13/4/2016	Chandpole	Tunnel Safety	22	
11.	14/4/2016	Chandpole	Material Lifting	21	
12.	21/4/2016	Chandpole	Material Handling	22	
13.	22/4/2016	Chandpole	Lifting & Rigging Work	12	
14.	22/4/2016	Chandpole	Tunnel Hazards	22	
15.	22/4/2016	Chandpole	Safe Material Lifting & Shifting	20	
16.	27/4/2016	Chandpole	Material Lifting & Shifting	54	
17.	06/4/2016	Chhoti Chaupar	Lifting & Rigging	14	
18.	10/4/2016	Chhoti Chaupar	Welding Cutting & Bending	13	
19.	12/4/2016	Chhoti Chaupar	SHE Emergency Preparedness	15	
20.	19/4/2016	Chhoti Chaupar	Permit to work System	19	
21.	23/4/2016	Chhoti Chaupar	Power Actuated Hand tools	18	
22.	29/4/2016	Chhoti Chaupar	Electrical mechanical Inspection	15	
23.	5/4/2016	Badi Chaupar	Electrical Safety	17	
24.	13/4/2016	Badi Chaupar	Behaviour Based safety Management	10	
25.	14/4/2016	Badi Chaupar	Fire Fighting	34	
26.	20/4/2016	Badi Chaupar	Importance of PPE's at work place	12	
27.	25/4/2016	Badi Chaupar	Waste Management System	20	
28.	27/4/2016	Badi Chaupar	Lifting & Shifting	17	

Month of May Training

SN	DATE	LOCATION	TOPIC	NO. OF PERSON	REMARKS
1.	3-5-2016	Casting yard	Safe work with Machineries	12	
2.	6-5-2016	Casting yard	Safe welding & gas Cutting work	7	
3.	10-5-2016	Casting yard	Safe lifting & rigging work	15	
4.	17-5-2016	Casting yard	Manual Material Handling	12	
5.	24-5-2016	Casting yard	Safe Working in hot climate	11	
6.	2-5-2016	Chandpole	Electrical Safety	39	
7.	5-5-2016	Chandpole	Environmental Impact Aspect & Risk Assessment	10	
8.	6-5-2016	Chandpole	Welding & gas cutting work	8	
9.	6-5-2016	Chandpole	Gas cutting	6	
10.	7-5-2016	Chandpole	Wire rope Sling Inspection	8	
11.	12-5-2016	Chandpole	Fire Hazard & prevention	23	
12.	13-5-2016	Chandpole	Precaution While Scaffolding Erection	12	
13.	13-5-2016	Chandpole	Heat related problems & disease diarrhoea	22	
14.	14-5-2016	Chandpole	Behaviour Based safety	20	
15.	14-5-2016	Chandpole	Behaviour Based safety	16	
16.	15-5-2016	Chandpole	Confined Space	22	
17.	19-5-2016	Chandpole	Heat Stress & Heat stroke	22	
18.	19-5-2016	Chandpole	Heat Stress & Heat stroke	21	
19.	23-5-2016	Chandpole	Permit to work system	23	
20.	23-5-2016	Chandpole	Permit to work system	22	
21.	25-5-2016	Chandpole	Work At Height	23	
22.	25-5-2016	Chandpole	Work At Height	16	
23.	25-5-2016	Chandpole	Hot work	07	
24.	27-5-2016	Chandpole	CPR Training	14	
25.	27-5-2016	Chandpole	Material Handling	22	
26.	28-5-2016	Chandpole	Tunnel Safety	19	
27.	3-5-2016	Chhoti Chaupar	Heavy lifting operation	8	
28.	14-5-2016	Chhoti Chaupar	Scaffolding erection & inspection	19	
29.	16-5-2016	Chhoti Chaupar	Safe operation of power tools	20	
30.	16-5-2016	Chhoti Chaupar	Welding cutting & Binding	12	
31.	21-5-2016	Chhoti Chaupar	Fire Fighting	23	
32.	23-5-2016	Chhoti Chaupar	First Aid & CPR	20	
33.	26-5-2016	Chhoti Chaupar	Behavior Based Safety	16	
34.	31-5-2016	Chhoti Chaupar	Permit to work	29	
35.	7-5-2016	Badi Chaupar	Lifting & rigging	13	
36.	13-5-2016	Badi Chaupar	PTW & Hot work Safety	10	
37.	13-5-2016	Badi Chaupar	Lifting & safe work procedures	10	
38.	20-5-2016	Badi Chaupar	Use of Fire Extinguisher	22	
39.	23-5-2016	Badi Chaupar	Defensive driving training	18	

40.	27-5-2016	Badi Chaupar	Electrical Safety	6	
41.	30-5-2016	Badi Chaupar	Work Permit System	9	
42.	31-5-2016	Badi Chaupar	Work Rope Inspection	13	

Month of June Training

SN	DATE	LOCATION	TOPIC	NO. OF PERSON	REMARKS
1.	02-06-2016	Casting yard	Permit to work system	06	
2.	07-06-2016	Casting yard	CPR Training	19	
3.	08-06-2016	Casting yard	Welding & Gas cutting	7	
4.	10-06-2016	Casting yard	Roofing work & handling concrete	7	
5.	14-06-2016	Casting yard	Safe lifting work	11	
6.	18-06-2016	Casting yard	Waste management system ,Hazards identification & risk analysis	15	
7.	21-06-2016	Casting yard	Electrical & mechanical inspection	05	
8.	24-6-2016	Casting yard	Behavior base safety	16	
9.	2-06-2016	Chandpole	Importance of Safety PPE's	08	
10.	3-06-2016	Chandpole	Precaution in confined space entry	19	
11.	3-06-2016	Chandpole	Precaution in confined space entry	18	
12.	04-06-2016	Chandpole	Work At Height	08	
13.	06-06-2016	Chandpole	Work At Height	12	
14.	06-06-2016	Chandpole	Environmental awareness on world environmental days	17	
15.	09-06-2016	Chandpole	Safe lifting operation	16	
16.	09-06-2016	Chandpole	Safe lifting operation	15	
17.	10-06-2016	Chandpole	lifting operation	10	
18.	13-06-2016	Chandpole	work Permit system	18	
19.	13-06-2016	Chandpole	work Permit system	19	
20.	13-06-2016	Chandpole	Right tools for right jobs	15	
21.	13-06-2016	Chandpole	Use of full body harness	22	
22.	14-06-2016	Chandpole	First aid provided during snake bite ,symptoms & precaution	19	
23.	15-06-2016	Chandpole	Procedure of Risk assessment & Environmental Aspect Impact	08	
24.	17-06-2016	Chandpole	Traffic Safety	05	
25.	17-06-2016	Chandpole	Integrated management Policy & Waste Management System.	19	
26.	18-06-2016	Chandpole	CPR Training	06	
27.	23-06-2016	Chandpole	Procedure of chemical handling	07	
28.	24-06-2016	Chandpole	Material carry by Manual Handling	20	
29.	24-06-2016	Chandpole	Precaution in hot work	12	
30.	24-06-2016	Chandpole	Right tools for right jobs	22	

31.	24-06-2016	Chandpole	Safe lifting operation	17	
32.	29-06-2016	Chandpole	Emergency preparedness plan	21	
33.	29-06-2016	Chandpole	Electrical hazards & precaution	22	
34.	06-06-2016	Chhoti Chaupar	Welding cutting & Binding	11	
35.	10-06-2016	Chhoti Chaupar	Procedure of signaling	02	
36.	10-06-2016	Chhoti Chaupar	Power activated hand tools	12	
37.	13-06-2016	Chhoti Chaupar	Waste management system	19	
39.	14-06-2016	Chhoti Chaupar	Operator emergency response & preparedness	10	
40.	15-06-2016	Chhoti Chaupar	Rigging	02	
41.	15-06-2016	Chhoti Chaupar	Operator emergency response & preparedness	07	
42.	21-06-2016	Chhoti Chaupar	Lifting operation	05	
43.	23-06-2016	Chhoti Chaupar	Fire safety	20	
44.	04-06-2016	Badi Chaupar	Electrical Safety	12	
45.	06-06-2016	Badi Chaupar	Environmental management	18	
46.	07-06-2016	Badi Chaupar	Emergency plan & procedure	29	
47.	08-06-2016	Badi Chaupar	Method statement	12	
48.	13-06-2016	Badi Chaupar	SHE Emergency response	04	
49.	14-06-2016	Badi Chaupar	Traffic management system	17	
50.	15-06-2016	Badi Chaupar	Emergency plan	10	
51.	18-06-2016	Badi Chaupar	Hand & power tool operation	18	
52.	18-06-2016	Badi Chaupar	Electrical earthing checking	07	
53.	21-06-2016	Badi Chaupar	CPR Training	05	
54.	02-06-2016	Casting yard	Permit to work system	06	
55.	07-06-2016	Casting yard	CPR Training	19	
56.	08-06-2016	Casting yard	Welding & Gas cutting	7	
57.	10-06-2016	Casting yard	Roofing work & handling concrete	7	



96 hrs training



Emergency Mock drill Training



Safety Training



Environmental Training on waste management & method of disposal .



Pre-start work training



world Environment Day celebration at site



Drinking Water point



Welfare facilities



IBD Safety Audit By Mr. Nigel Maw

OHS Performance Assessment

Element	2015	2016
Worksite Conditions	76%	86%
Workforce on Site	78%	83%
Management	54%	77%
Training and Competence	81%	80%
Documentation	66%	92%
Overall	70%	86%

Provisional calculation - to be confirmed in the Audit Report

70

OHS Performance Assessment

Appendix 3: Sample format of Monthly SHE report



**CONTINENTAL
ENGINEERING
CORPORATION**

**MONTHLY SAFETY, HEALTH & ENVIRONMENTAL
REPORT JUNE- 2016**

DOCUMENT No. RP/JMRC/SHE/UG1B/PHOF/024
Revision =00 , Date 06.06.2016

	PREPARED BY	REVIEWED BY	APPROVED BY
Signature :			
NAME :	S.K. Dewedi	Deepak Sharma	Christopher Mark Cooper
DESIGNATION :	Senior Environment Engineer	Chief SHE Manager	Project leader
DATE :	7 th July, 2016	8 th July, 2016	8 th July, 2016


DESIGN AND CONSTRUCTION OF
TUNNEL BETWEEN CHANDPOLE
AND BADI CHOUPER AND
REVERSAL LINE BY SHIELD
TBM, UNDERGROUND METRO
STATION AT CHOTI CHOUPER
AND BADI CHOUPER BY CUT &
COVER METHOD ON EAST-WEST
CORRIDOR OF JAIPUR METRO
(PHASE 1B) AT JAIPUR,
RAJASTHAN,
INDIA
CONTRACT NO: JP/EW/1B/C1

MONTHLY SAFETY, HEALTH & ENVIRONMENTAL REPORT JUNE, 2016

SHE
SUBMITTAL

Sl. No.	DESCRIPTION OF ITEMS	PAGE NO.
A.	Index	
B.	Project Details	01 - 01
1.	Monthly Man Hours Details	02 - 02
2.	Monthly Accident/ Incident Details	03 - 03
3.	SHE Committee Details	04 - 04
4.	Details of SHE Training conducted in the month	05 - 08
5.	SHE Inspection	09 - 20
6.	SHE Internal Audit details like Electrical Audit etc.	21 - 100
7.	SHE Communication Details	101 - 158
8.	Air quality/Noise monitoring	159 - 166
9.	Toolbox talks Details	167 - 168
10.	PPE details	169 - 178
11.	Details on IP 44 panel boards, lighting poles, welding and cutting equipment, Ladder, Hoists, Lifting Tools & Tackles.	177 - 178
12.	Monthly Lux meter study results	179 - 202
13.	Housekeeping Details	203 - 212
14.	Barncade Maintenance Details	213 - 218
15.	No. of Critical excavations	219 - 222
16.	Health & Welfare activities	223 - 228
17.	Safety Walk	225 - 228
18.	SHE Activities planned for next Month	229 - 246
19.	Annexure 1 (Mock drill)	247 - 247
20.	Annexure 2 (Air, noise & water)	248 - 261
21.	Annexure 3 (MARS)	262 - 273
		274 - 275

Appendix 4: Environment Quality Monitoring Report



EKO PRO ENGINEERS PVT. LTD.
Environmental Consultants and Analytical Laboratory
(An ISO 9001:2008 Certified Company)

Contact : +91 - 9810243870

Office & Laboratory : 32/41, South Side of G. T. Road, UPS/IDC Industrial Area, Ghaziabad - 201 009, UP, INDIA.
e-mail : email@ekopro.in, eis@ekopro.in, ekoproengineers@gmail.com, website : www.ekopro.in
Contact No. : 9711159210, 9871800216, 9711159337, 9818405427. EPA8X No. : +91-120-2800950, 2867931

TEST REPORT

Ambient Air Quality Monitoring

Test Report No. :	EKO/ENV-AA/109/200616	Issue Date	30/06/2016
Issued To	CEC INTERNATIONAL CORPORATION Plot No- 860 Village & Post, Keshavpura Casting Yard Bakhrota, Almer Road Jaipur		
Sample Description	Ambient Air		
Sample Drawn on	17/06/2016 To 18/06/2016		
Sample Drawn by	EPEPL(Mr. Krishan Kant Mishra)		
Sample Received on	20/06/2016		
Sampling Location	Near Chhoti Chauper		
Sampling Plan & Procedure	SOP-AAQ/15		
Analysis Duration	20/06/2016 To 29/06/2016		
Sampling Time	24 Hrs		
Ambient Temperature (deg °C)	39.0		
Average Flow Rate of SPM (m ³ /min)	1.1		
Average Flow Rate of Gases (lpm.)	1.0		
Weather Conditions	Clear		
Remark (If any)	NA		

RESULTS

S.No.	PARAMETER	Test Methods	Results	Units	LIMIT AS PER EPA*
1	Particulate Matter (PM10)	IS-5182 (P-23)	135.2	µg/m ³	100.0
2	SPM	IS-5182 (P-4)	272.6	µg/m ³	-
3	Sulphur dioxide (as SO ₂)	IS-5182 (P-2) Improved West & Geake	15.0	µg/m ³	80.0
4	Nitrogen Dioxide (as NO ₂)	IS-5182 (P-6)	31.4	µg/m ³	80.0
5	Carbon Monoxide (as CO)	IS-5182 (P-10) Grab Method	<1.15	mg/m ³	4.0

*Details as per EPA, 1986 National Ambient Air Quality Standards, date 18.11.2009

Notes :

End of Report

- The results given above are related to the tested sample, as received & mentioned parameters.
The customer asked for the above tests only.
- This test report will not be generated again, either wholly or in part, without written permission of the Laboratory.
- This test report will not be used for any publicity/legal purpose.
- This test samples will be disposed off after two weeks from the date of issue of test report, unless until specified by the customer.
- Responsibility of the Laboratory is limited to the invoiced amount only.



For EKO PRO ENGINEERS PVT. LTD.

Authorized Signatory

Analytical Services - Analysis of Environment, Food, Building Material, Petroleum & Material Samples in the field of Chemical, Mechanical & Biological Disciplines.
Consulting Services - EIA, SIA, EC Compliances, DMP, Risk Analysis, Designing of ETP, APCS, RWH Systems, Environmental Audit & **Page No:1/1**



Contact : +91 - 9810243870

EKO PRO ENGINEERS PVT. LTD.

Environmental Consultants and Analytical Laboratory

(An ISO 9001:2008 Certified Company)

Office & Laboratory : 32/41, South Side of G. T. Road, UPSIDC Industrial Area, Ghaziabad - 201 009, UP, INDIA.
 e-mail : email@ekopro.in, eia@ekopro.in, ekoproengineers@gmail.com, website : www.ekopro.in
 Contact No. : 9711159210, 9871800216, 9711159337, 9818405427. EPABX No. : +91-120-2800950, 2867931

TEST REPORT**Ambient Air Quality Monitoring**

Test Report No. :	EKD/EA-AA/108/200616	Issue Date	30/06/2016
Issued To	CEC INTERNATIONAL CORPORATION Plot No- 860 Village & Post, Keshavpura Casting Yard Bakhrota, Almer Road Jaipur		
Sample Description	Ambient Air		
Sample Drawn on	17/06/2016 To 18/06/2016		
Sample Drawn by	EPEPL(Mr. Krishan Kant Mishra)		
Sample Received on	20/06/2016		
Sampling Location	Near Badi Chauper (near Hawamahal)		
Sampling Plan & Procedure	SOP-AAQ/15		
Analysis Duration	20/06/2016 To 29/06/2016		
Sampling Time	24 Hrs		
Ambient Temperature (deg °C)	39.0		
Average Flow Rate of SPM (m ³ /min)	1.1		
Average Flow Rate of Gases (lpm.)	1.0		
Weather Conditions	Clear		
Remark (if any)	NA		

RESULTS

S.No.	PARAMETER	Test Methods	Results	Units	LIMIT AS PER EPA*
1	Particulate Matter (PM10)	IS 5182 (P-23)	152.8	µg/m ³	100.0
2	SPM	IS 5182 (P-4)	260.4	µg/m ³	-
3	Sulphur dioxide (as SO ₂)	IS 5182 (P-2) Improved West & Geake	8.6	µg/m ³	80.0
4	Nitrogen Dioxide (as NO ₂)	IS 5182 (P-6)	21.0	µg/m ³	80.0
5	Carbon Monoxide (as CO)	IS 5182 (P-10) Grab Method	<1.15	mg/m ³	4.0

*Details as per EPA-1986 National Ambient Air Quality Standards, date 18.11.2009

Notes :

1. The results given above are related to the tested sample, as received & mentioned parameters.
The customer asked for the above tests only.
2. This test report will not be generated again, either wholly or in part, without written permission of the Laboratory.
3. This test report will not be use for any publicity/legal purpose.
4. This test samples will be disposed off after two weeks from the date of issue of test report, unless until specified by the customer.
5. Responsibility of the Laboratory is limited to the invoiced amount only.

End of Report

For EKO PRO ENGINEERS PVT. LTD.

Authorized Signatory

Analytical Services - Analysis of Environment, Food, Building Material, Petroleum & Material Samples in the field of Chemical, Mechanical & Biological Disciplines.
 Consulting Services - EIA, SIA, EC Compliances, DMP, Risk Analysis, Designing of ETP, APCs, RWH Systems, Environmental Audit & Page No: 1/1



Contact : +91 - 9810243870

EKO PRO ENGINEERS PVT. LTD.

Environmental Consultants and Analytical Laboratory

(An ISO 9001:2008 Certified Company)

Office & Laboratory : 32/41, South Side of G. T. Road, UPSIDC Industrial Area, Ghaziabad - 201 009, UP, INDIA.
 e-mail : email@ekopro.in, eia@ekopro.in, ekoproengineers@gmail.com, website : www.ekopro.in
 Contact No. : 9711159210, 9871800216, 9711159337, 9818405427, EPABX No. : +91-120-2800950, 2867931

TEST REPORT**Ambient Air Quality Monitoring**

Test Report No. :	EK0/EA-AA/107/200616	Issue Date :	30/06/2016
Issued To	CEC INTERNATIONAL CORPORATION Plot No- 860 Village & Post, Keshavpura Casting Yard Bakhrota, Almer Road Jaipur		
Sample Description	Ambient Air		
Sample Drawn on	16/06/2016 To 17/06/2016		
Sample Drawn by	EPEPL(Mr. Krishan Kant Mishra)		
Sample Received on	20/06/2016		
Sampling Location	Near Casting Yard		
Sampling Plan & Procedure	SOP-AAQ/15		
Analysis Duration	20/06/2016 To 29/06/2016		
Sampling Time	24 Hrs		
Ambient Temperature (deg °C)	38.0		
Average Flow Rate of SPM (m³/min)	1.1		
Average Flow Rate of Gases (lpm.)	1.0		
Weather Conditions	clear		
Remark (if any)	NA		

RESULTS

S.No.	PARAMETER	Test Methods	Results	Units	LIMIT AS PER EPA*
1	Particulate Matter (PM10)	IS:5182 (P-23)	173.2	µg/m ³	100.0
2	SPM	IS:5182 (P-4)	320.8	µg/m ³	-
3	Sulphur dioxide (as SO ₂)	IS:5182 (P-2) Improved West & Gaeke	14.0	µg/m ³	80.0
4	Nitrogen Dioxide (as NO ₂)	IS:5182 (P-6)	29.1	µg/m ³	80.0
5	Carbon Monoxide (as CO)	IS:5182 (P-10) Grab Method	<1.15	mg/m ³	4.0

*Details as per EPA-1986 National Ambient Air Quality Standards, date 18.11.2009

Notes :

- The results given above are related to the tested sample, as received & mentioned parameters.
The customer asked for the above tests only.
- This test report will not be generated again, either wholly or in part, without written permission of the Laboratory.
- This test report will not be used for any publicity/legal purpose.
- This test samples will be disposed off after two weeks from the date of issue of test report, unless until specified by the customer.
- Responsibility of the Laboratory is limited to the invoiced amount only.

End of Report

For EKO PRO ENGINEERS PVT. LTD.

Authorized Signatory

Analytical Services - Analysis of Environment, Food, Building Material, Petroleum & Material Samples in the field of Chemical, Mechanical & Biological Disciplines.
Consulting Services - EIA, SIA, EC Compliances, DMP, Risk Analysis, Designing of ETP, APCs, RWH Systems, Environmental Audit & Regs. Modif.



EKO PRO
ENGINEERS PVT. LTD.
SAVE THE ENVIRONMENT

Contact : +91 - 9810243870

EKO PRO ENGINEERS PVT. LTD.
Environmental Consultants and Analytical Laboratory
(An ISO 9001:2008 Certified Company)

Office & Laboratory : 32/41, South Side of G. T. Road, UPSIDC Industrial Area, Ghaziabad - 201 009, UP, INDIA.
e-mail : email@ekopro.in, eis@ekopro.in, ekoproengineers@gmail.com, website : www.ekopro.in
Contact No. : 9711159210, 9871800216, 9711159337, 9818405427, EPABX No. : +91-120-2800950, 2867931

TEST REPORT

Ambient Air Quality Monitoring

Test Report No. :	EK0/EV-AA/106/200616	Issue Date	30/06/2016
Issued To	CEC INTERNATIONAL CORPORATION Plot No- 860 Village & Post, Keshavpura Casting Yard Bakhrota, Ajmer Road Jaipur		
Sample Description	Ambient Air		
Sample Drawn on	16/06/2016 To 17/06/2016		
Sample Drawn by	EPEPL(Mr. Krishan Kant Mishra)		
Sample Received on	20/06/2016		
Sampling Location	Near Chandpole Metro Station		
Sampling Plan & Procedure	SOP-AAQ/15		
Analysis Duration	20/06/2016 To 29/06/2016		
Sampling Time	24 Hrs		
Ambient Temperature (deg °C)	38.0		
Average Flow Rate of SPM (m ³ /min)	1.1		
Average Flow Rate of Gases (lpm.)	1.0		
Weather Conditions	Clear		
Remark (if any)	NA		

RESULTS

S.No.	PARAMETER	Test Methods	Results	Units	LIMIT AS PER EPA*
1	Particulate Matter (PM10)	IS 5182 (P-23)	160.8	µg/m ³	100.0
2	SPM	IS 5182 (P-4)	241.0	µg/m ³	-
3	Sulphur dioxide (as SO ₂)	IS 5182 (P-2) Improved West & Geake	12.2	µg/m ³	80.0
4	Nitrogen Dioxide (as NO ₂)	IS 5182 (P-6)	27.4	µg/m ³	80.0
5	Carbon Monoxide (as CO)	IS 5182 (P-10) Grab Method	<1.15	mg/m ³	4.0

*Details as per EPA-1986 National Ambient Air Quality Standards, date 18.11.2009

Notes :

End of Report

- The results given above are related to the tested sample, as received & mentioned parameters.
The customer asked for the above tests only.
- This test report will not be generated again, either wholly or in part, without written permission of the Laboratory.
- This test report will not be used for any publicity/legal purpose.
- This test samples will be disposed off after two weeks from the date of issue of test report, unless until specified by the customer.
- Responsibility of the Laboratory is limited to the invoiced amount only.



For EKO PRO ENGINEERS PVT. LTD.

Authorized Signatory

Analytical Services - Analysis of Environment, Food, Building Material, Petroleum & Material Samples in the field of Chemical, Mechanical & Biological Disciplines.
Consulting Services - EIA, SIA, EC Compliances, DMP, Risk Analysis, Designing of ETP, APCs, RWH Systems, Environmental Audit & Page 10 of 11



Contact : +91 - 9810243870

EKO PRO ENGINEERS PVT. LTD.

Analytical Division

(An ISO 9001:2008 Certified Company)

Office & Laboratory : 32/41, South Side of G. T. Road, UPSIDC Industrial Area, Ghaziabad - 201 009, UP, INDIA.
 Contact No. : 9711159210, 9711159427, SMS/Whatsapp No. : 9711163422; E-mail : email@ekopro.in, ekoproengineers@gmail.com, website : www.ekopro.in

TEST REPORT**Noise Monitoring**

Test Report No. : EKO/EV-NM/112/200616

Issue Date : 22/06/2016

Issued To

: CEC INTERNATIONAL CORP INDIA PVT. LTD
 (Jaipur Project)
 Old Police Headquarter
 Near Hawamahal
 Jaipur

Sample Description : Ambient Noise
 Sample Drawn on : 17/06/2016 To 18/06/2016
 Sample Drawn by : EPEPL (Mr. Krishan Kant Mishra)
 Sample Received on : 20/06/2016
 Sampling Location : Chotti Chauper (Maharaja School)
 Sampling Plan & Procedure : SOP-N/01
 Environmental Conditions : Normal
 Analysis Duration : 20/06/2016 To 21/06/2016
 Remark (if any) : NA

S.No.	PARAMETER	TEST METHOD	RESULTS		LIMITS AS PER ENVIRONMENT (PROTECTION) ACT*
			Lday db(A)	LNight db(A)	
1	Leq (24 Hrs.)	SOP-N/94/01	57.3		
2	L Day		61.2	-	75.0
3	L Night		-	49.6	70.0
4	L dn		55.4		
5	L Max (24 Hrs.)		77.1	66.8	
6	L Min (24 Hrs.)		50.2	38.4	
7	L 90		56.4	43.3	
8	L 50		60.1	48.2	
9	L 10		63.8	52.6	

* Details as per EPA-1986 Ambient Noise Quality Standards, Schedule-III, (Rule-3).

** End of Report **

Notes :

1. The results given above are related to the observed values at the time of monitoring. The customer asked for the above tests only.
2. This test report will not be generated again, either wholly or in part, without prior written permission of the Laboratory.
3. The test report will not be used for any publicity/legal purpose.
4. Responsibility of the Laboratory is limited to the invoiced amount only.

For EPEPL
 GHAZIABAD
 (Authorized Signatory)



EKO PRO ENGINEERS PVT. LTD.

Analytical Division
(An ISO 9001:2008 Certified Company)

Office & Laboratory : 32/41, South Side of G. T. Road, UPSIDC Industrial Area, Ghaziabad - 201 009, UP, INDIA.
Contact No. : 9711159210, 9711159427, SMS/Whatsapp No. : 9711183422; E-mail : email@ekopro.in, ekoproengineers@gmail.com, website : www.ekopro.in

TEST REPORT

Noise Monitoring

Test Report No. : EKO/EV-NM/111/200616

Issue Date : 22/06/2016

Issued To

: CEC INTERNATIONAL CORP INDIA PVT. LTD
(Jaipur Project)
Old Police Headquarter
Near Hawamahal
Jaipur

Sample Description : Ambient Noise
Sample Drawn on : 17/06/2016 To 18/06/2016
Sample Drawn by : EPEPL (Mr. Krishan Kant Mishra)
Sample Received on : 20/06/2016
Sampling Location : Badi Chauper (Hawamahal)
Sampling Plan & Procedure : SOP-N/01
Environmental Conditions : Normal
Analysis Duration : 20/06/2016 To 21/06/2016
Remark (if any) : NA

S.No.	PARAMETER	TEST METHOD	RESULTS		LIMITS AS PER ENVIRONMENT (PROTECTION) ACT*
			Lday db(A)	LNight db(A)	
1	Leq (24 Hrs.)	SOP-N/94/01	66.1		-
2	L Day		68.9	-	75.0
3	L Night		-	60.7	70.0
4	L dn		64.8		
5	L Max (24 Hrs.)		85.3	69.7	
6	L Min (24 Hrs.)		51.3	41.2	
7	L 90		63.1	54.3	
8	L 50		67.1	58.6	
9	L 10		71.4	63.9	

* Details as per EPA-1986 Ambient Noise Quality Standards, Schedule-III, (Rule-3).

** End of Report **

Notes :

1. The results given above are related to the observed values at the time of monitoring. The customer asked for the above tests only.
2. This test report will not be generated again, either wholly or in part, without prior written permission of the Laboratory.
3. The test report will not be used for any publicity/legal purpose.
4. Responsibility of the Laboratory is limited to the invoiced amount only.





Contact : +91 - 9810243870

EKO PRO ENGINEERS PVT. LTD.

Analytical Division

(An ISO 9001:2008 Certified Company)

Office & Laboratory : 32/41, South Side of G. T. Road, UPSIDC Industrial Area, Ghaziabad - 201 009, UP, INDIA.
 Contact No. : 9711150210, 9711159427, SMS/Whatsapp No. : 9711163422; E-mail : email@ekopro.in, ekoproengineers@gmail.com; website : www.ekopro.in

TEST REPORT**Noise Monitoring**

Test Report No. : EKO/EV-NM/110/200616

Issue Date : 22/06/2016

Issued To

: CEC INTERNATIONAL CORP INDIA PVT. LTD
 (Jaipur Project)
 Old Police Headquarter
 Near Hawamahal
 Jaipur

Sample Description : Ambient Noise
 Sample Drawn on : 17/06/2016 To 18/06/2016
 Sample Drawn by : EPEPL (Mr. Krishan Kant Mishra)
 Sample Received on : 20/06/2016
 Sampling Location : Near Krishna Temple
 Sampling Plan & Procedure : SOP-N/01
 Environmental Conditions : Normal
 Analysis Duration : 20/06/2016 To 21/06/2016
 Remark (if any) : NA

S.No.	PARAMETER	TEST METHOD	RESULTS		LIMITS AS PER ENVIRONMENT (PROTECTION) ACT*
			Lday db(A)	LNight db(A)	
1	Leq (24 Hrs.)	SOP-N/94/01	56.8		
2	L Day		60.8	-	75.0
3	L Night		-	49.0	70.0
4	L dn		54.9		
5	L Max (24 Hrs.)		76.6	62.3	
6	L Min (24 Hrs.)		50.2	37.9	
7	L 90		56.0	42.8	
8	L 50		59.6	47.4	
9	L 10		63.3	52.3	


* Details as per EPA-1986 Ambient Noise Quality Standards, Schedule-III, (Rule-3).

** End of Report **

Notes :

1. The results given above are related to the observed values at the time of monitoring. The customer asked for the above tests only.
2. This test report will not be generated again, either wholly or in part, without prior written permission of the Laboratory.
3. The test report will not be used for any publicity/legal purpose.
4. Responsibility of the Laboratory is limited to the invoiced amount only.





EKO PRO ENGINEERS PVT. LTD.
Analytical Division
(An ISO 9001:2008 Certified Company)

Contact : 4911 9812/4912

Office & Laboratory : 32/41, South Side of G. T. Road, UPSIDC Industrial Area, Ghaziabad - 201 009, UP, INDIA.
 Contact No. : 9711159210, 9711159427, SMS/Whatsapp No. : 9711163422, E-mail : email@ekopro.in, ekoproengineers@gmail.com, website : www.ekopro.in

TEST REPORT

Noise Monitoring

Test Report No. : EKO/EV-NM/109/200616

Issue Date : 22/06/2016

Issued To : CEC INTERNATIONAL CORP INDIA PVT. LTD
 (Jaipur Project)
 Old Police Headquarter
 Near Hawamahal
 Jaipur

Sample Description : Ambient Noise
Sample Drawn on : 17/06/2016 To 18/06/2016
Sample Drawn by : EPEPL (Mr. Krishan Kant Mishra)
Sample Received on : 20/06/2016
Sampling Location : Near Pink City Hospital
Sampling Plan & Procedure : SOP-N/01
Environmental Conditions : Normal
Analysis Duration : 20/06/2016 To 21/06/2016
Remark (if any) : NA


S.No.	PARAMETER	TEST METHOD	RESULTS		LIMITS AS PER ENVIRONMENT (PROTECTION) ACT*
			Lday db(A)	LNight db(A)	
1	Leq (24 Hrs.)	SOP-N/94/01	60.1		
2	L Day		63.7	-	75.0
3	L Night		-	53.1	70.0
4	L dn		58.4		
5	L Max (24 Hrs.)		80.0	68.4	
6	L Min (24 Hrs.)		51.2	41.2	
7	L 90		59.0	47.4	
8	L 50		62.9	51.5	
9	L 10		66.0	56.4	

* Details as per EPA-1986 Ambient Noise Quality Standards, Schedule-III, (Rule-3).

** End of Report **


Notes :

- The results given above are related to the observed values at the time of monitoring. The customer asked for the above tests only.
- This test report will not be generated again, either wholly or in part, without prior written permission of the Laboratory.
- The test report will not be used for any publicity/legal purpose.
- Responsibility of the Laboratory is limited to the invoiced amount only.



Analytical Services - Analysis of Environment, Food, AYUSH, Cosmetics, Building Material, Petroleum & Material Samples in the field of Chemical, Mechanical & Biological Disciplines.
 Consulting Services - EIA, SIA, EC Compliances, DMP, Risk Analysis, Designing of ETP/APCS, RWH Systems, Environmental Audit & other studies, Ground Water & Soil Investigation.

Page 1 of 1



EKO PRO
EKO PRO ENGINEERS PVT. LTD.
SAFEGUARDING THE ENVIRONMENT

Contact : +91 - 9810243870

EKO PRO ENGINEERS PVT. LTD.
Analytical Division
(An ISO 9001:2008 Certified Company)

Office & Laboratory : 32/41, South Side of G. T. Road, UPSIDC Industrial Area, Ghaziabad - 201 009, UP, INDIA.
Contact No. : 9711159210, 9711159427, SMS/Whatsapp No. : 9711163422; E-mail : email@ekopro.in, ekoproengineers@gmail.com, website : www.ekopro.in

TEST REPORT

Noise Monitoring

Test Report No. : EKO/EV-NM/108/200616 **Issue Date : 21/06/2016**

Issued To : CEC INTERNATIONAL CORP INDIA PVT. LTD
(Jaipur Project)
Old Police Headquarter
Near Hawamahal
Jaipur

Sample Description : Ambient Noise
Sample Drawn on : 16/06/2016 To 17/06/2016
Sample Drawn by : EPEPL (Mr. Krishan Kant Mishra)
Sample Received on : 20/06/2016
Sampling Location : Near Jantar Mantar
Sampling Plan & Procedure : SOP-N/01
Environmental Conditions : Normal
Analysis Duration : 20/06/2016 To 21/06/2016
Remark (if any) : NA


S.No.	PARAMETER	TEST METHOD	RESULTS		LIMITS AS PER ENVIRONMENT (PROTECTION) ACT*
			Lday db(A)	LNight db(A)	
1	Leq (24 Hrs.)	SOP-N/94/01	62.3		
2	L Day		65.1	-	75.0
3	L Night		-	56.9	70.0
4	L dn		61.0		
5	L Max (24 Hrs.)		81.5	69.3	
6	L Min (24 Hrs.)		50.3	37.4	
7	L 90		60.3	51.0	
8	L 50		64.1	56.0	
9	L 10		67.6	59.7	

* Details as per EPA-1986 Ambient Noise Quality Standards, Schedule-III, (Rule-3).

** End of Report **

Notes :


- The results given above are related to the observed values at the time of monitoring. The customer asked for the above tests only.
- This test report will not be generated again, either wholly or in part, without prior written permission of the Laboratory.
- The test report will not be used for any publicity/legal purpose.
- Responsibility of the Laboratory is limited to the invoiced amount only.



For E. P. B. C.
GHAZIABAD
(Authorised Signatory)

Analytical Services - Analysis of Environment, Food, AYUSH, Cosmetics, Building Material, Petroleum & Material Samples in the field of Chemical, Mechanical & Biological Disciplines.
Consulting Services - EIA, SIA, EC Compliances, DMP, Risk Analysis, Designing of ETP, APCs, RWH Systems, Environmental Audit & other studies, Ground Water & Soil Investigation.

Page 1 of 1



EKO PRO
EKO PRO ENGINEERS PVT. LTD.
SAVE THE ENVIRONMENT

Contact : +91 - 9810243672

EKO PRO ENGINEERS PVT. LTD.
Analytical Division
(An ISO 9001:2008 Certified Company)

Office & Laboratory : 32/41, South Side of G. T. Road, UPSIDC Industrial Area, Ghaziabad - 201 009, UP, INDIA.
Contact No. : 9711158210, 9711158427, SMS/Whatsapp No. : 9711163422, E-mail : email@ekopro.in, ekoproengineers@gmail.com, website : www.ekopro.in

TEST REPORT

Noise Monitoring

Test Report No. : EKO/EV-NM/107/200616

Issue Date : 22/06/2016

Issued To : CEC INTERNATIONAL CORP INDIA PVT. LTD
(Jaipur Project)
Old Police Headquarter
Near Hawamahai
Jaipur

Sample Description	: Ambient Noise
Sample Drawn on	: 16/06/2016 To 17/06/2016
Sample Drawn by	: EPEPL (Mr. Krishan Kant Mishra)
Sample Received on	: 20/06/2016
Sampling Location	: Near Casting Yard
Sampling Plan & Procedure	: SOP-N/01
Environmental Conditions	: Normal
Analysis Duration	: 20/06/2016 To 21/06/2016
Remark (if any)	: NA


S.No.	PARAMETER	TEST METHOD	RESULTS		LIMITS AS PER ENVIRONMENT (PROTECTION) ACT*
			Lday db(A)	LNight db(A)	
1	Leq (24 Hrs.)	SOP-N/94/01	59.4		
2	L Day		62.2	-	75.0
3	L Night		-	54.0	70.0
4	L dn		58.1		
5	L Max (24 Hrs.)		78.6	69.5	
6	L Min (24 Hrs.)		45.6	36.8	
7	L 90		57.4	46.7	
8	L 50		61.1	51.4	
9	L 10		64.7	57.6	

* Details as per EPA-1986 Ambient Noise Quality Standards, Schedule-III, (Rule-3).

** End of Report **

Notes :

- The results given above are related to the observed values at the time of monitoring. The customer asked for the above tests only.
- This test report will not be generated again, either wholly or in part, without prior written permission of the Laboratory.
- The test report will not be used for any publicity/legal purpose.
- Responsibility of the Laboratory is limited to the invoiced amount only.




(Authorized Signatory)

Analytical Services - Analysis of Environment, Food, AYUSH, Cosmetics, Building Material, Petroleum & Material Samples in the field of Chemical, Mechanical & Biological Disciplines.

Consulting Services - EIA, SIA, EC Compliances, DMP, Risk Analysis, Designing of ETP, APCs, RMH Systems, Environmental Audit & other studies, Ground Water & Soil Investigation.

Page 1 of 1



EKO PRO ENGINEERS PVT. LTD.
Analytical Division
(An ISO 9001:2008 Certified Company)

Contact : +91 - 9810243870

TEST REPORT
Noise Monitoring

Test Report No. : EKO/EV-NM/114/200616

Issue Date : 22/06/2016

Issued To : CEC INTERNATIONAL CORP INDIA PVT. LTD
(Jaipur Project)
Old Police Headquarter
Near Hawamahal
Jaipur

Sample Description : Ambient Noise

Sample Drawn on : 16/06/2016 To 17/06/2016

Sample Drawn by : EPEPL (Mr. Krishan Kant Mishra)

Sample Received on : 20/06/2016

Sampling Location : Near Chandpole Metro Station

Sampling Plan & Procedure : SOP-N/01

Environmental Conditions : Normal

Analysis Duration : 20/06/2016 To 21/06/2016

Remark (if any) : NA


S.No.	PARAMETER	TEST METHOD	RESULTS		LIMITS AS PER ENVIRONMENT (PROTECTION) ACT*
			Lday db(A)	LNight db(A)	
1	Leq (24 Hrs.)	SOP-N/94/01	67.9		
2	L Day		70.4	-	75.0
3	L Night		-	62.9	70.0
4	L dn		66.7		
5	L Max (24 Hrs.)		83.0	69.9	
6	L Min (24 Hrs.)		61.2	53.0	
7	L 90		67.5	59.6	
8	L 50		70.1	62.7	
9	L 10		72.1	64.7	

* Details as per EPA-1986 Ambient Noise Quality Standards, Schedule-III, (Rule-3).

** End of Report **

Notes :

- The results given above are related to the observed values at the time of monitoring. The customer asked for the above tests only.
- This test report will not be generated again, either wholly or in part, without prior written permission of the Laboratory.
- The test report will not be used for any publicity/legal purpose.
- Responsibility of the Laboratory is limited to the invoiced amount only.



(Authorised Signatory)

Analytical Services - Analysis of Environment, Food, AYUSH, Cosmetics, Building Material, Petroleum & Material Samples in the field of Chemical, Mechanical & Biological Disciplines.
Consulting Services - EIA, SIA, EC Compliances, DMP, Risk Analysis, Designing of ETP, APCs, RWH Systems, Environmental Audit & other studies, Ground Water & Soil Investigation.

Page 1 of 1



EKO PRO ENGINEERS PVT. LTD.
Analytical Division
(An ISO 9001:2008 Certified Company)

Contact : +91 - 9810243870

Office & Laboratory : 32/41, South Side of G. T. Road, UPSIDC Industrial Area, Ghaziabad - 201 009, UP, INDIA.
Contact No. : 9711159210, 9711159427, SMS/Whatsapp No. : 9711163422, E-mail : email@ekopro.in, ekoproengineers@gmail.com, website : www.ekopro.in

TEST REPORT

Noise Monitoring

Test Report No. : EKO/EV-NM/113/200616

Issue Date : 22/06/2016

Issued To

: CEC INTERNATIONAL CORP INDIA PVT. LTD
(Jaipur Project)
Old Police Headquarter
Near Hawamahal
Jaipur

Sample Description : Ambient Noise
Sample Drawn on : 16/06/2016 To 17/06/2016
Sample Drawn by : EPEPL (Mr. Krishan Kant Mishra)
Sample Received on : 20/06/2016
Sampling Location : Chaudhary Hospital
Sampling Plan & Procedure : SOP-N/01
Environmental Conditions : Normal
Analysis Duration : 20/06/2016 To 21/06/2016
Remark (if any) : NA

S.No.	PARAMETER	TEST METHOD	RESULTS		LIMITS AS PER ENVIRONMENT (PROTECTION) ACT*
			Lday db(A)	LNight db(A)	
1	Leq (24 Hrs.)	SOP-N/94/01	54.8		
2	L Day		57.7	-	75.0
3	L Night		-	48.9	70.0
4	L dn		53.3		
5	L Max (24 Hrs.)		69.8	59.6	
6	L Min (24 Hrs.)		40.6	39.8	
7	L 90		53.9	45.7	
8	L 50		57.5	48.0	
9	L 10		59.4	51.3	


* Details as per EPA-1986 Ambient Noise Quality Standards, Schedule-III, (Rule-3).

** End of Report **

Notes :

1. The results given above are related to the observed values at the time of monitoring. The customer asked for the above tests only.
2. This test report will not be generated again, either wholly or in part, without prior written permission of the Laboratory.
3. The test report will not be used for any publicity/legal purpose.
4. Responsibility of the Laboratory is limited to the invoiced amount only.





EKO PRO ENGINEERS PVT. LTD.
Environmental Consultants and Analytical Laboratory
(An ISO 9001:2008 Certified Company)

Contact : +91 - 9810243870

Office & Laboratory : 32/41, South Side of G. T. Road, UPSIDC Industrial Area, Ghaziabad - 201 009, UP, INDIA.
e-mail : email@ekopro.in, eia@ekopro.in, ekoproengineers@gmail.com, website : www.ekopro.in
Contact No. : 9711159210, 9871800216, 9711159337, 9818405427, EPA8X No. : +91-120-2800950, 2867931

TEST REPORT**Water Sample Analysis**

Test Report No. :	EK0/EV-WA/115/160516	Issue Date	23/05/2016
Issued To :	CEC INTERNATIONAL CORPORATION Plot No- 860 Village & Post, Keshavpura Casting Yard Bakhrota, Ajmer Road Jaipur		
Sample Description	Ground Water		
Sample Drawn on	14/05/2016		
Sample Drawn by	EPEPL(Mr. Harish Kumar)		
Sample Received on	16/05/2016		
Sampling Location	From Chandpole Metro Station		
Sampling Plan & Procedure	SOP-W/66		
Sample Quantity	1.0 Litre		
Environmental Condition	Normal		
Analysis Duration	16/05/2016 To 21/05/2016		
Remark (If any)	NA		

RESULTS

S.No.	PARAMETER	Test Methods	Result	Units	IS: 10500 : 2012 (Limits)	
					Acceptable	Permissible
1	Turbidity	IS : 3025 (P-10)	< 1.0	NTU	1.0	5.0
2	pH	IS : 3025 (P-11)	7.30	-	6.5-8.5	No relaxation
3	Oil & Grease	IS : 3025 (P-39)	ND	mg/L	-	-
4	Total Dissolved Solids	IS : 3025 (P-16)	104.0	mg/L	500.0	2000.0
5	Total Suspended Solids	IS : 3025 (P-17)	< 5.0	mg/L	-	-
6	Conductivity	IS : 3025 (P-14)	160.0	µs/cm	-	-
7	Dissolved Oxygen	IS : 3025 (P-38)	5.9	mg/L	-	-
8	E.coli	IS : 1622	Absent	Per 100 mL	Shall not be detectable in 100ml sample	-


Notes :

End of Report

- The results given above are related to the tested sample, as received & mentioned parameters.
The customer asked for the above tests only.
- This test report will not be generated again, either wholly or in part, without written permission of the Laboratory.
- This test report will not be use for any publicity/legal purpose.
- This test samples will be disposed off after two weeks from the date of issue of test report, unless until specified by the customer.
Sample received for biological tests will be destroyed after 7 days from the date of issue of test report.
- Responsibility of the Laboratory is limited to the invoiced amount only.

For EKO PRO ENGINEERS PVT. LTD.

Authorized Signatory.



EKO PRO ENGINEERS PVT. LTD.
Environmental Consultants and Analytical Laboratory
(An ISO 9001:2008 Certified Company)

Contact : +91 - 9810243870

EKO PRO ENGINEERS PVT. LTD.
Environmental Consultants and Analytical Laboratory
(An ISO 9001:2008 Certified Company)

Office & Laboratory : 32/41, South Side of G. T. Road, UPSIDC Industrial Area, Ghaziabad - 201 009, UP, INDIA.
e-mail : email@ekopro.in, eia@ekopro.in, ekoproengineers@gmail.com, website : www.ekopro.in
Contact No. : 9711159210, 9871800216, 9711159337, 9818405427, EPABX No. : +91-120-2800950, 2867931

TEST REPORT

Water Sample Analysis

Test Report No. :	EK0/EV-WA/114/160516	Issue Date	23/05/2016
Issued To	CEC INTERNATIONAL CORPORATION Plot No- 860 Village & Post, Keshavpura Casting Yard Bakhrota, Ajmer Road Jaipur		
Sample Description	Ground Water		
Sample Drawn on	14/05/2016		
Sample Drawn by	EPEPL(Mr. Harish Kumar)		
Sample Received on	16/05/2016		
Sampling Location	From Casting Yard		
Sampling Plan & Procedure	SOP-W/66		
Sample Quantity	1.0 Litre		
Environmental Condition	Normal		
Analysis Duration	16/05/2016 To 21/05/2016		
Remark (if any)	NA		

RESULTS

S.No.	PARAMETER	Test Methods	Result	Units	IS: 10500 : 2012 (Limits)	
					Acceptable	Permissible
1	Turbidity	IS : 3025 (P-10)	< 1.0	NTU	1.0	5.0
2	pH	IS : 3025 (P-11)	7.42	-	6.5-8.5	No relaxation
3	Oil & Grease	IS : 3025 (P-39)	ND	mg/L	-	-
4	Total Dissolved Solids	IS : 3025 (P-16)	92.0	mg/L	500.0	2000.0
5	Total Suspended Solids	IS : 3025 (P-17)	< 5.0	mg/L	-	-
6	Conductivity	IS : 3025 (P-14)	141.5	µs/cm	-	-
7	Dissolved Oxygen	IS : 3025 (P-38)	5.7	mg/L	-	-
8	E.coli	IS : 1622	Absent	Per 100 mL	Shall not be detectable in 100ml sample	-

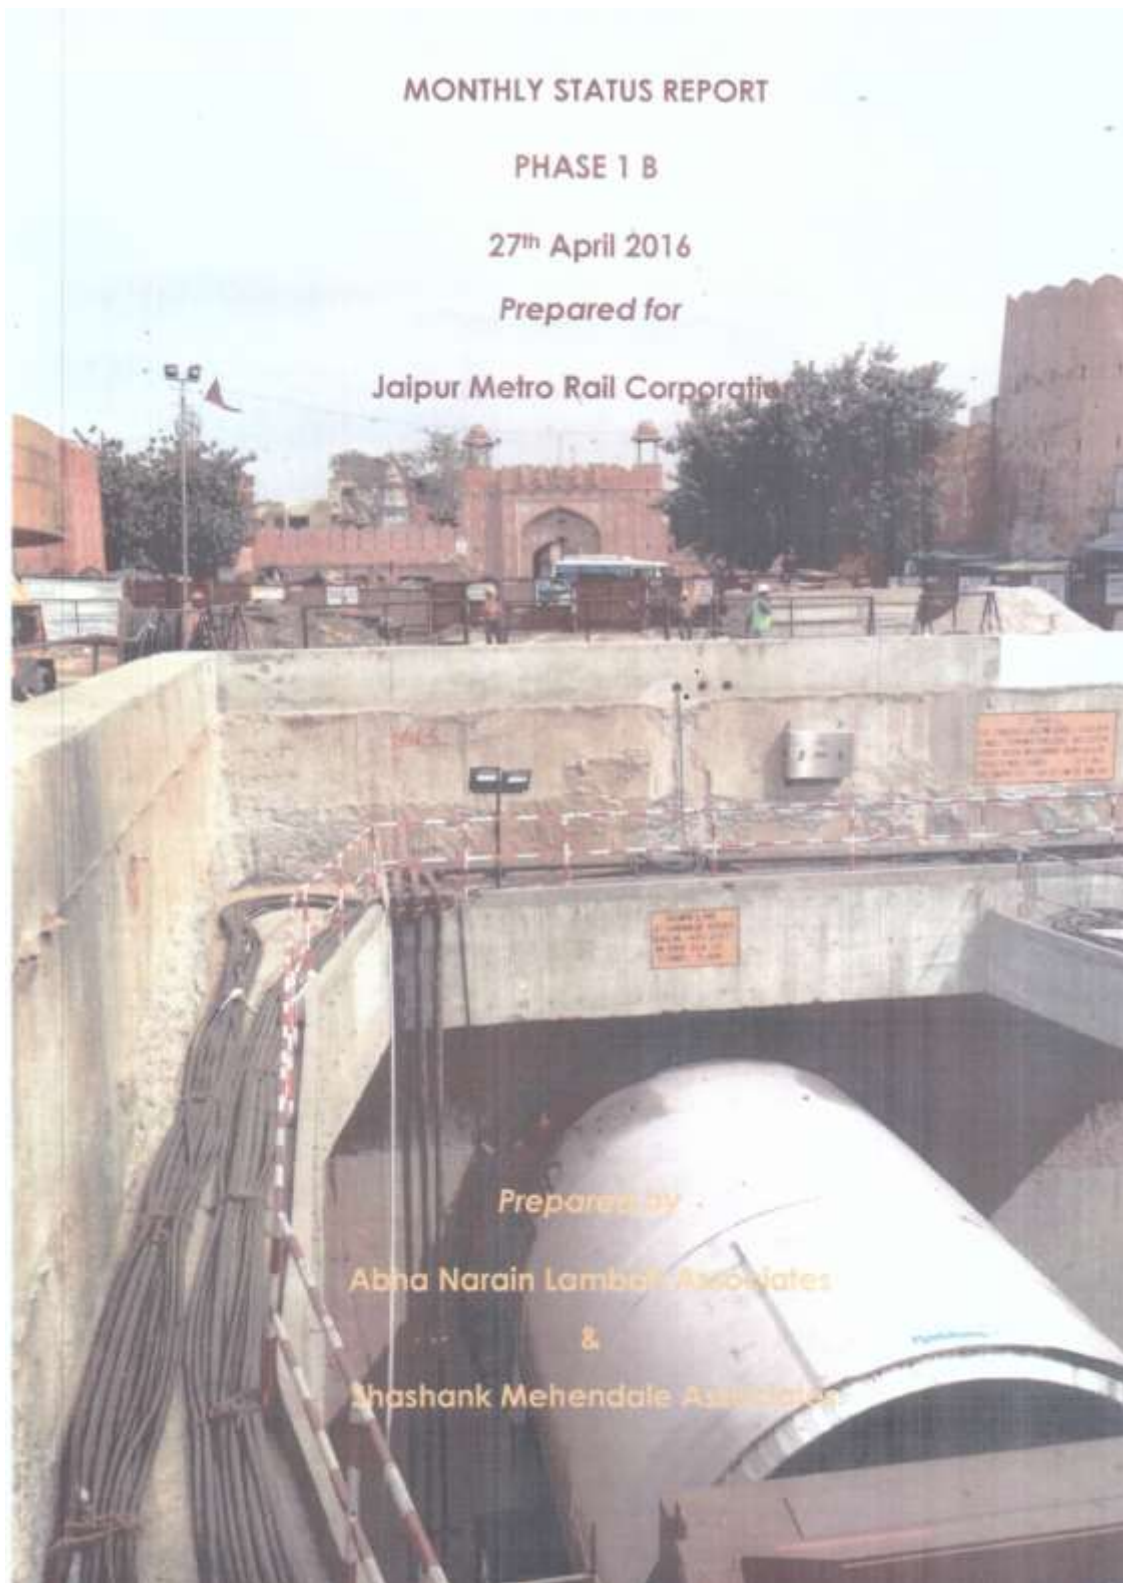
End of Report

Notes :

- The results given above are related to the tested sample, as received & mentioned parameters.
The customer asked for the above tests only.
- This test report will not be generated again, either wholly or in part, without written permission of the Laboratory.
- This test report will not be used for any publicity/legal purpose.
- This test samples will be disposed off after two weeks from the date of issue of test report, unless until specified by the customer.
Sample received for biological tests will be destroyed after 7 days from the date of issue of test report.
- Responsibility of the Laboratory is limited to the invoiced amount only.

For EKO PRO ENGINEERS PVT. LTD

Authorized Signatory

Appendix 5: Monthly Report of Heritage Consultant

Abha Narain Lambah & Associates and
Shashank Mehendale & Associates (JV)

Monitoring of Heritage Structures for Jaipur
Metro Rail Line 1 Phase B Project

Structural Report

1st April 2016 – 31st April 2016

Site Inspections by M/s Shashank Mehendale & Associates were carried out in this month to monitor the progress of works, with JMRC, DMRC and CEC officials on 22nd April 2016.

Non Key Experts Visits

Mr. Shashank Mehendale

22nd April 2016 – JMRCCL has instructed for joint visit for Shop No. 102

Abha Narain Lambah & Associates and
Shashank Mehendale & Associates (JV)

Monitoring of Heritage Structures for Jaipur
Metro Rail Line 1 Phase B Project

Site Visit on 22nd April as instructed by JMRCL

Following structures were visited during visit. Observations are –

1) **Shop No 102 near Tripolia Gate**

Letter from advocate and CEC were provided by JMRCL. Site was visited by the undersigned in presence of M/s. JMRCL, M/s. DMRC and M/s. CEC representative.

A) Settlement in flooring is observed at entrance below entrance arch of shop and inside shop. Also Plaster delamination and cracks are observed. It is observed that the shop had cracks and was declared as partially unstable by Heritage consultants and it was recommended to provide suitable stabilising measures. Vibrations felt might be due to the condition of the structure.

B) Settlement was not noticed originally as rightly pointed out by M/s. CEC however the settlement seems to be in floor and not the structure as the arch on opening is not showing any signs of settlement. Also the verandah is not showing any settlement. Thus it is not likely that the settlement could be due to work carried out for metro. The settlement seems minor and can be grouted and filled by PCC.



Floor Settlement is observed inside the shop



Crack is observed on verandah Slab, Floor settlement is observed at verandah

2) Naval Kishor Temple.

A) The breached crack meters to be monitored With respect to ambient reading prior to commencing the work. Damaged crack meters to be re-installed considering TBM is approaching.

B) Structure seems to show some movement and careful monitoring should be done and further corrective measures should be initiated, incase of any breach of settlement sensor or crack meters.

C) CEC mentioned about few difficulties in implementing the scheme same can be reviewed if sodesired.



Damaged Crack Meters

3) Hanuman Temple Pujari's Residence :

Urgent measure is to provide row of 3 props connected by a wooden Chavi, where masonry pillar seems to have cracked significantly. Propping to be also provided in kitchen area. Long term issues like floor settlement due to hollowness, same can be repaired with compaction, packing with rubble and grouting/ PCC. Distress mapping is required to suggest guidelines for repairs.



Cracked Masonry Pillar and Arch where propping is required

Shashank Mehendale,
Structural Consultant for Monitoring of Heritage Structures

Appendix 6: Consent to establish letter from Rajasthan State Pollution Control Board

Regional Office Jaipur (S)
Rajasthan State Pollution Control Board
4, Jhalana Institutional Area Jhalana Doongri,
Jaipur Rajasthan
Phone: 5159699 Fax: 5159699



Registered

File No : F(Tech)/Jaipur(Sanganer)/2805(1)/2016-2017/321-322

Order No: 2016-2017/Jaipur (S)/5609

Dispatch Date: 05/05/2016

Unit Id : 66141

M/s Contiental Engineering Corporation

Continental Engineering Corporation C/o JMREC City

Place Premises Jalevi Chowk Jaipur , Jaipur

Tehsil:Jaipur

District:Jaipur

Sub: Consent to Establish under section 25/26 of the Water (Prevention & Control of Pollution) Act, 1974 and under section 21(4) of Air (Prevention & Control of Pollution) Act, 1981.

Ref: Your application(s) for Consent to Establish dated 19/06/2015 and subsequent correspondence.

Sir,

Consent to Establish under the provisions of section 25/26 of the Water (Prevention & Control of Pollution) Act, 1974 (hereinafter to be referred as the Water Act) and under section 21 of the Air (Prevention & Control of Pollution) Act, 1981, (hereinafter to be referred as the Air Act) as amended to date and rules & the orders issued thereunder **is hereby granted** for your **Industry** situated / proposed at **Village Keshavpura Teh Sanganer, Nera Kamla Nehru Floyover, Jaipur Tehsil:Sanganer District:Jaipur** , Rajasthan under the provisions of the said Act(s). This consent is granted on the basis of examination of the information furnished by you in consent application(s) and the documents submitted therewith, subject to the following conditions:-

- 1 That this Consent to Establish is valid for a period from **19/06/2015** to **31/05/2018** or **date of Commencement of production / commissioning of the project or activities whichever is earlier** .
- 2 That this Consent is granted for manufacturing / producing following products / by products or carrying out the following activities or operation/processes or providing following services with capacities given below.

Particular	Type	Quantity / Capacity
READY MIX CONCRETE	By Product	6000 M3/MONTH
Tunnel Rings	Service	2350 PCS PER MONTH

- 3 That in case of any increase in capacity or addition / modification / alteration or change in product mix or process or raw material or fuel the project proponent is required to obtain fresh consent to establish.



Regional Office Jaipur (S)
Rajasthan State Pollution Control Board
 4, Jhalana Institutional Area Jhalana Doongri,
 Jaipur, Rajasthan
 Phone: 5159699 Fax: 5159699

Registered

File No : F(Tech)/Jaipur(Sanganer)/2805(1)/2016-2017/321-322

Order No : 2016-2017/Jaipur (S)/5609

Dispatch Date: 05/05/2016

Unit Id : 66141

- 4 That the control equipment as proposed by the applicant shall be installed before trial operation is started for which prior consent to operate under the provision of the **Water Act and Air Act** shall be obtained. This consent to establish shall not be treated as consent to operate.
- 5 That the quantity of effluent generation and disposal along with mode of disposal for the treated effluent shall be as under:

Type of effluent	Max. effluent generation (KLD)	Quantity of effluent to be recycled (KLD)	Quantity of treated effluent to be disposed (KLD) and mode of disposal
Domestic Sewage	6.000	4.000	2.000 Septic Tank and Soakpit

- 6 That the sources of air emissions along with pollution control measures and the emission standards for the prescribed parameters shall be as under:



Regional Office Jaipur (S)
Rajasthan State Pollution Control Board
4, Jhalana Institutional Area Jhalana Doongri,
Jaipur Rajasthan
Phone: 5159699 Fax: 5159699

Registered

File No : F(Tech)/Jaipur(Sanganer)/2805(1)/2016-2017/321-322

Order No : 2016-2017/Jaipur (S)/5609

Dispatch Date: 05/05/2016

Unit Id : 66141

Sources of Air Emissions	Pollution Control Measures	Prescribed	
		Parameter	Standard
Boiler(150KG/HOUR)	ADEQUATE STACK HEIGHT , Cyclone	--	--
DG Set (1 No.)(225KVA)	ACOUSTIC ENCLOSURE , ADEQUATE STACK HEIGHT	--	--
DG Set (2 No.)(160KVA EACH)	ACOUSTIC ENCLOSURE , ADEQUATE STACK HEIGHT	--	--
DG Set (2 Nos.)(1000KVA EACH)	ACOUSTIC ENCLOSURE , ADEQUATE STACK HEIGHT	--	--
DG Set (3 No.)(125KVA EACH)	ACOUSTIC ENCLOSURE , ADEQUATE STACK HEIGHT	--	--
DG Set (5 Nos.)(500KVA EACH)	ACOUSTIC ENCLOSURE , ADEQUATE STACK HEIGHT	--	--



Regional Office Jaipur (S)
Rajasthan State Pollution Control Board
 4, Jhalana Institutional Area Jhalana Doongri,
 Jaipur Rajasthan
 Phone: 5159699 Fax: 5159699

Registered

File No : F(Tech)/Jaipur(Sanganer)/2805(1)/2016-2017/321-322

Order No: 2016-2017/Jaipur (S)/5609

Dispatch Date: 05/05/2016

Unit Id : 66141

- 7 That the **Industry** will comply with the standards as prescribed vide MOEF notification No. GSR 826(E) dated 16th November, 2009 with respect to National Ambient Air Quality Standards.
- 8 This consent is not evidence for ascertaining entitlement of land.
- 9 That the industry shall obtain necessary permissions from Competent authority and District Administration, Jaipur for establishment of the plant.
- 10 That unit shall maintain zero discharge status outside the premises.
- 11 That the water used for cooling purpose shall be kept under recirculation.
- 12 That unit shall carryout plantation within the premises in at least 33% of the total plot area.
- 13 That unit shall have to achieve prescribed standards as per EP Act, 1986 and shall maintain requisite Pollution Control Measures to achieve prescribed standards all the time.
- 14 That unit shall not dig any bore-well or abstract Ground Water without prior permission from the Central Ground Water Authority & the State Board.
- 15 That unit shall carry out all activities/ operations within covered shed and suitable air pollution control arrangements will be installed to control fugitive air emissions generated from the process or handling of raw materials.
- 16 That this consent to establishment shall be subject to compliance of any direction or order passed by court of law in the matter.
- 17 That if the project cost exceed Rs. 504 Lacs, the unit shall take/obtain modification in consent to establish/operate after paying fee as applicable.
- 18 That you shall apply for the consent to operate before 120 days from the commencement of the production activities.
- 19 That you shall not increase pollution load (Water & Air) and no change shall be allowed in production process/plant & machinery etc.
- 20 That the industry shall ensure disposal of domestic waste-water in scientific manner to avoid ground-water contamination in and around the area.
- 21 That, notwithstanding anything provided hereinabove, the State Board shall have power and reserves its right, as contained **under section 27(2) of the Water Act and under section 21(6) of the Air Act** to review anyone or all the conditions imposed here in above and to make such variation as it deemed fit for the purpose of compliance of the Water Act and Air Act.



Regional Office Jaipur (S)
Rajasthan State Pollution Control Board
4, Jhalana Institutional Area Jhalana Doongri,
Jaipur Rajasthan
Phone: 5159699 Fax: 5159699

Registered

File No : F(Tech)/Jaipur(Sanganer)/2805(1)/2016-2017/321-322

Order No : 2016-2017/Jaipur (S)/5609

Dispatch Date: 05/05/2016

Unit Id : 66141

22 That the grant of this **Consent to Establish** is issued from the environmental angle only, and does not absolve the project proponent from the other statutory obligations prescribed under any other law or any other instrument in force. The sole and complete responsibility, to comply with the conditions laid down in all other laws for the time-being in force, rests with the industry/ unit/ project proponent.

23 That the grant of this **Consent to Establish** shall not, in any way, adversely affect or jeopardize the legal proceedings, if any, instituted in the past or that could be instituted against you by the State Board for violation of the provisions of the Act or the Rules made thereunder.

This **Consent to Establish** shall also be subject, beside the aforesaid specific conditions, to the general conditions given in the enclosed Annexure. The project proponent will comply with the provisions of the **Water Act and Air Act** and to such other conditions as may, from time to time, be specified by the State Board under the provisions of the aforesaid Act(s). Please note that, non compliance of any of the above stated conditions would tantamount to revocation of **Consent to Establish** and project proponent / occupier shall be liable for legal action under the the relevant provisions of the said Act(s).

Yours Sincerely

Regional Officer[Jaipur (S)]

Copy To:-

1 Master File.

Regional Officer[Jaipur (S)]



Appendix 7: Muck disposal details

a) Quantity of Muck Disposal

Quantity of Muck Disposal April to June 2016	
Months	Quantities
April	28717.885 M ³
May	7411.161 M ³
June	11876.426 M ³

b) no. of trucks used for the same

Number of Trucks April to June 2016	
Months	Number of Muck Disposal trucks
April	1771 TRIPS
May	503 TRIPS
June	861 TRIPS

c) Average quantity of muck daily

Average quantity of muck daily April to June 2016	
Months	Average quantity of muck daily
April	957.262M3
May	239.069 M3
June	395.880 M3

d). Details of disposal site including photographs

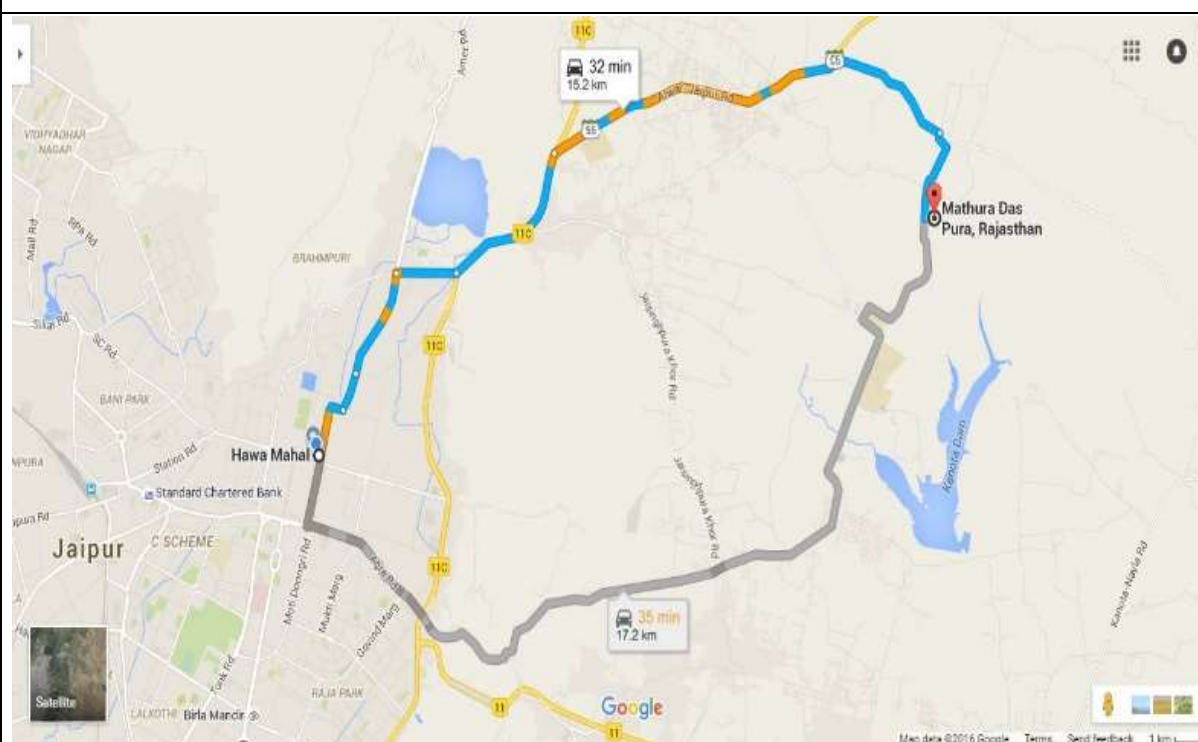
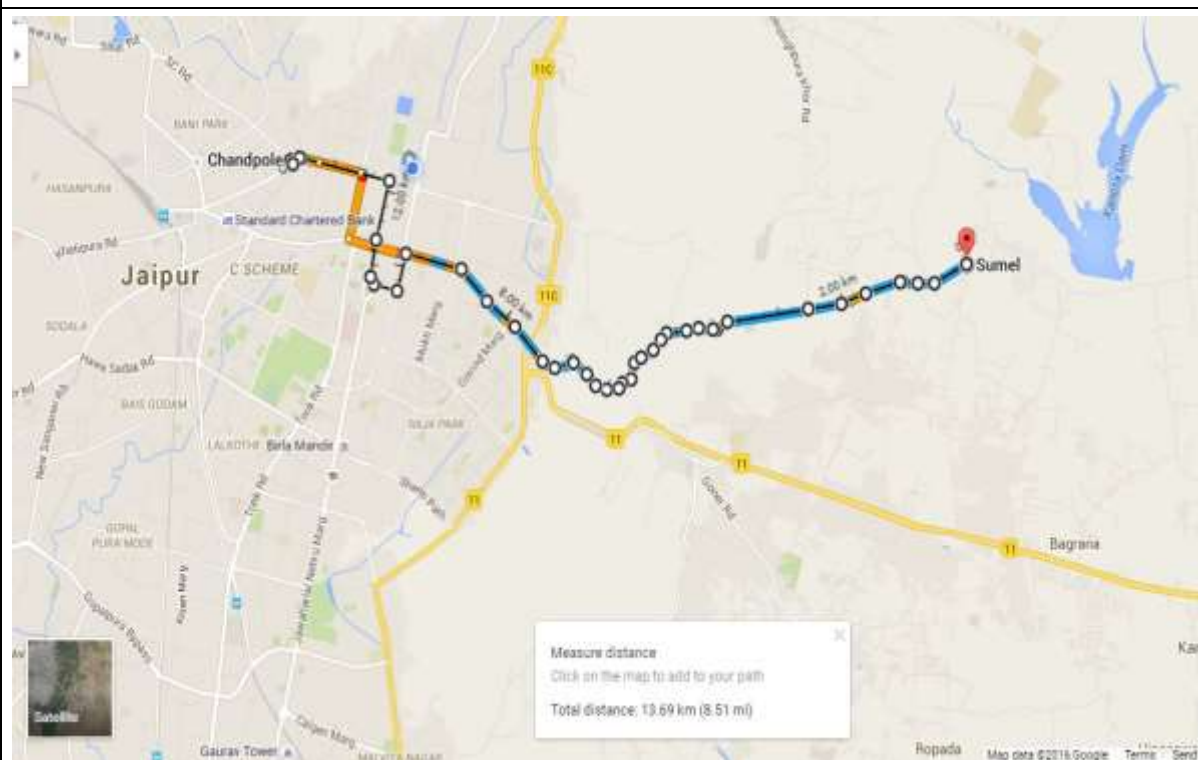
Photographs of disposal (loaded and taken)site

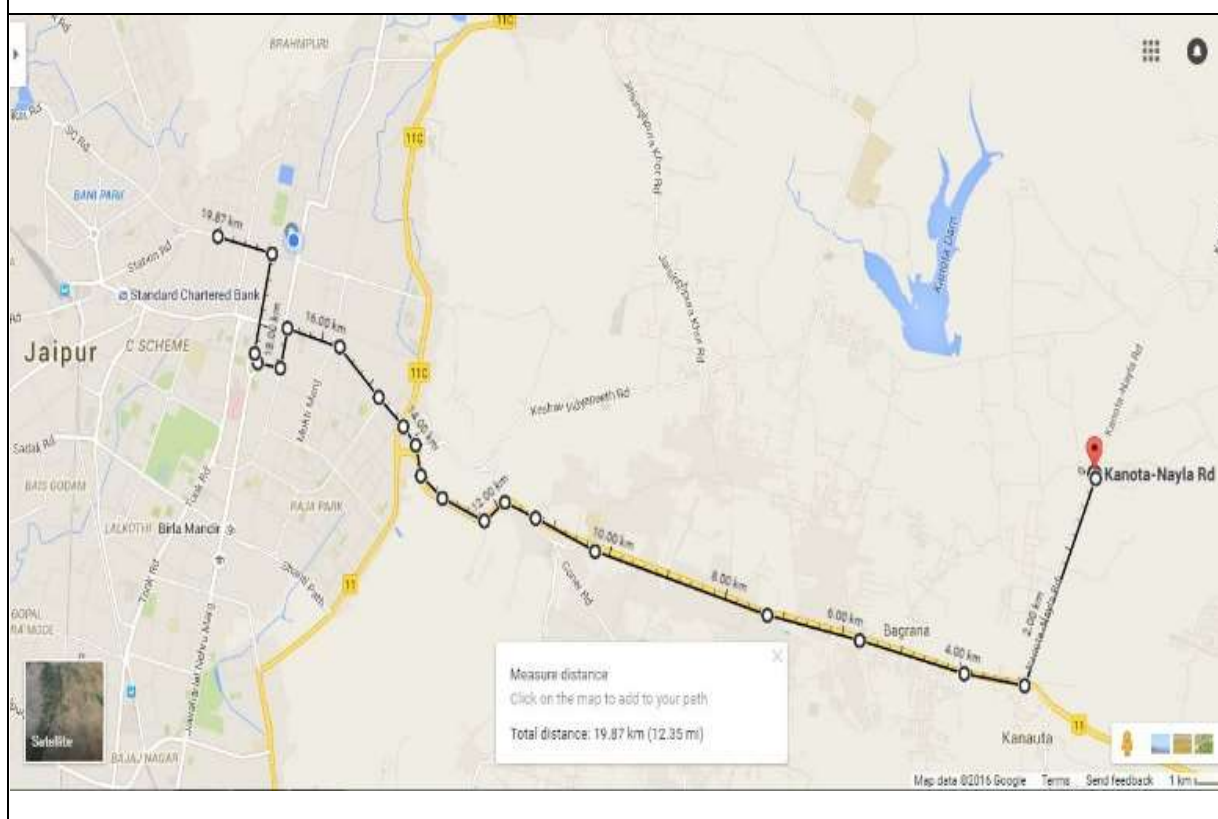
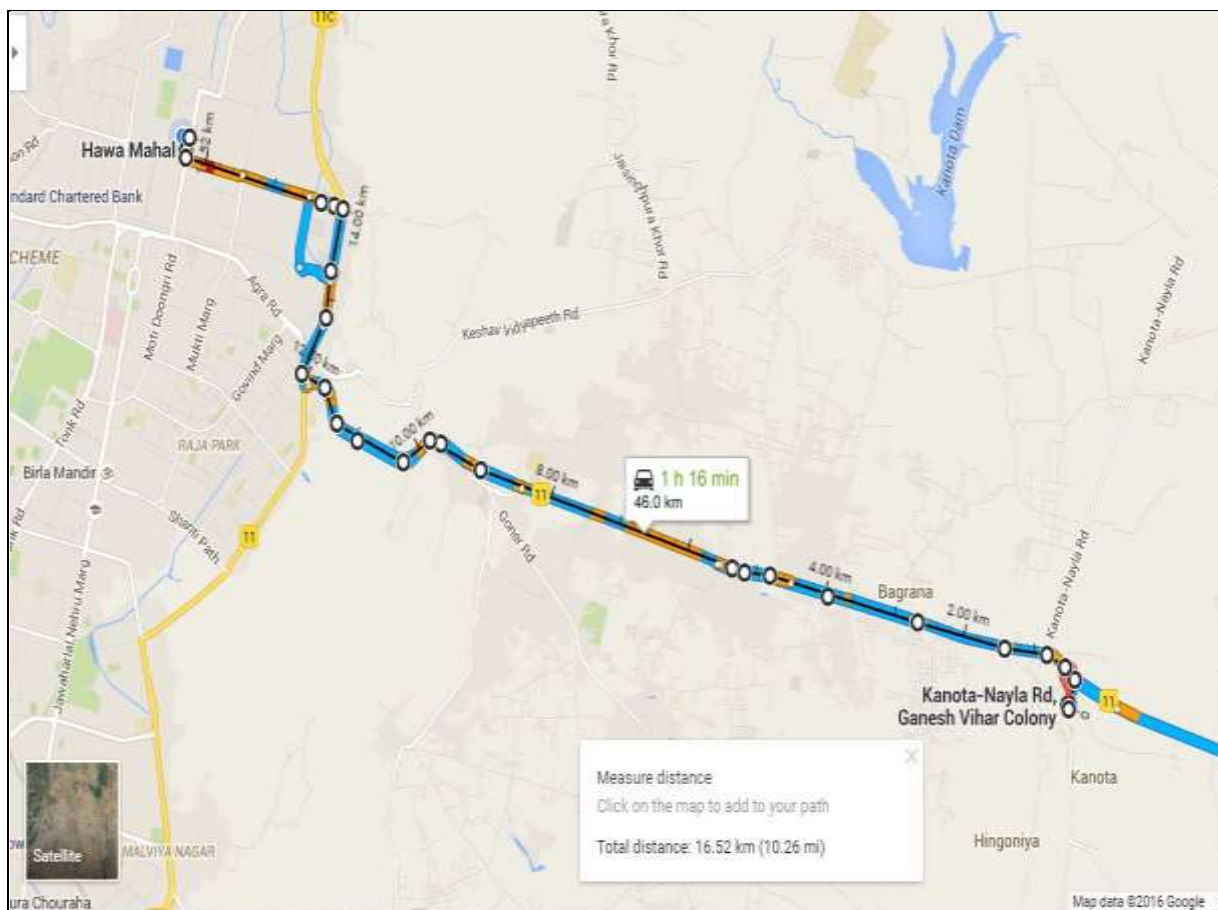
		
<p>Excavated muck stored in muck pit at</p>	<p>Excavated soil stored at surface</p>	<p>Muck loaded into dumper by L&T Komatsu long boom excavator from muck pit</p>
		
<p>Loaded dumper had reached at wheel washing facilities for tires cleaning</p>	<p>Workers are covering loded dumper with the tarpaulin.</p>	<p>For cleaning the tyre on wheel wash station</p>




		
<p>Cleaning the tyre of Loaded dumper before entering the public road.</p>	<p>Ready loaded dumpers is going for outside from site.</p>	<p>Loaded dumper is going through public road for muck disposal.</p>
		
<p>Loaded dumper is going on public road</p>	<p>Dumping yard of Mathura Daspura</p>	<p>Dumping yard of Mathura Daspura</p>



Route Map



Map showing route for muck disposal
 (Sumel, Mathuradaspora, Govindpura/Ropada & Langariyawas)













Appendix 8: Tree transplantation details					
		CONTINENTAL ENGINEERING CORPORATION JMRC-1B PROJECT JP/EW/1B/C1			Location: Ghat Ki Ghuni
		List of 1 st phase surviving transplanted trees			
SI No	Previous location	Current Location	year of tree transplantation	Photographs	Remarks
1.	Chhoti Chaupar	Ghat Ki Ghuni	2014		
2.	Chhoti Chaupar	Ghat Ki Ghuni	2014		



SI No	Previous location	Current Location	year of tree transplantation	Photographs	Remarks
3.	Chhoti Chaupar	Ghat Ki Ghuni	2014		Survived
4.	Chhoti Chaupar	Ghat Ki Ghuni	2014		



SI No	Previous location	Current Location	year of tree transplantation	Photographs	Remarks
5.	Chhoti Chaupar	Ghat Ki Ghuni	2014		
6.	Badi Chaupar	Ghat Ki Ghuni	2014		



			CONTINENTAL ENGINEERING CORPORATION JMRC-1B PROJECT JP/EW/1B/C1			Location: Ramnivas Bagh	
			List of 2 nd phase surviving transplanted trees				
SI No	Tree No.	Tree Name	Previous location	Current Location	Date of tree transplantation	Photographs	
1.	81	Gulmohar	Badi Chaupar	Ramniwas Garden	09.09.2015		
2	91	Begunvillia	Chhoti Chaupar	Ramniwas Garden	25.8.2015		



SI No	Tree No.	Tree Name	Previous location	Current Location	Date of tree transplantation	Photographs
3	88	Ashok	Chhoti Chaupar	Ramniwas Garden	03.09.2015	
4	78	Gulmohar	Badi Chaupar	Ramniwas Garden	05.09.2015	
5	67	Ashoka	Badi Chaupar	Ramniwas Garden	07.09.2015	

SI No	Tree No.	Tree Name	Previous location	Current Location	Date of tree transplantation	Photographs
6	86	Ashoka	Badi Chaupar	Ramniwas Garden	07.09.2015	
7	68	Ashoka	Badi Chaupar	Ramniwas Garden	09.09.2015	

SI No	Tree No.	Tree Name	Previous location	Current Location	Date of tree transplantation	Photographs
8	76	Ashoka	Badi Chaupar	Ramniwas Garden	10.09.2015	
9	96	Gulmohar	Chhoti Chaupar	Sylvan forest Bio-diversity forest	26.08.2015	

SI No	Tree No.	Tree Name	Previous location	Current Location	Date of tree transplantation	Photographs
10	98	Gulmohar	Chhoti Chaupar	Sylvan forest Bio-diversity	26.08.2015	
11.	90	Shahtute	Badi Chaupar	Sylvan forest Bio-diversity	27.08.2015	

SI No	Tree No.	Tree Name	Previous location	Current Location	Date of tree transplantation	Photographs
1 2	89	Gulmohar	Badi Chaupar	Sylvan Bio-diversity forest	04.09.2015	
1 3	94	Bed	Chhoti Chaupar	Sylvan Bio-diversity forest	02.11.2015	

SI No	Tree No.	Tree Name	Previous location	Current Location	Date of tree transplantation	Photographs
1 4	108	Pipal	PS Chhoti Chaupar	Sylvan Bio-diversity forest	04.11.2015	
1 5	146	Shisam	Badi Chaupar	Sylvan Bio-diversity forest	06.11.2015	

Appendix 9: Photographs of tilt, crack and other instruments in working

Tilt, crack and other instruments in working	
	
Building settlement Marker	Crack Meter
	
Inclinometer In D-wall	Optical Target



Pavement Settlement Marker



Tilt Plate



Vibration Monitoring
