

Social Monitoring Report

Semiannual Report
February 2017

India: Railway Sector Investment Program

Prepared by Ministry of Railways for the Government of India and the Asian Development Bank.

This social monitoring report is a document of the borrower. The views expressed herein do not necessarily represent those of ADB's Board of Directors, Management, or staff, and may be preliminary in nature.

In preparing any country program or strategy, financing any project, or by making any designation of or reference to a particular territory or geographic area in this document, the Asian Development Bank does not intend to make any judgments as to the legal or other status of any territory or area.

**Indian Government
Ministry of Railways
Asian Development Bank**

**Multitranche Financing Facility No. 0060-IND
Loans No. 2793-IND, 3108-IND
Railway Sector Investment Program
Track Doubling and Electrification on Critical Routes**


**Resettlement and Rehabilitation Implementation Status
Semi Annual Report April 2016 – September 2016**





Document Identification


Project Name :	Railway Sector Investment Program
	ADB MFF no. 0060-IND
	ADB Loans no. 2793-IND, 3108-IND
	Track Doubling and Electrification on Critical Routes
Report Name :	General Consultant Half yearly R&R Report No. 7, September 2016
Reference	R&R_September 2016

Preparation, Review and Authorisation

Prepared by :	Dr. Sudesh Kaul	Signature : 
Organisation :	General Consultant	
Position :	Resettlement Expert	Date :

Checked by :	Prem Narayan Shukla / Jean-Francois Pinet	Signature : 
Organisation :	General Consultant	
Position :	Dy. Team Leader /Team Leader	Date : 29/11/16

Reviewed by :	Ramashray Pandey	Signature : 
Organisation :	RVNL	
Position :	General Manager/Corporate Coordination	Date : 29/11/16

Approved by :	Vijay Anand	Signature : 
Organisation :	RVNL	
Position :	Director Projects	Date : 02/12/16

Revision, Preparation, Review Issue

Revision	Date	Subject	Prepared by	Reviewed by

Contents

Executive Summary	1
1. Background	3
2. Evolution during the relevant period	5
3. Current issues	6
4. Status	10
4.1 Sambalpur–Titlagarh project	10
4.2 Raipur–Titlagarh project	12
4.3 Daund-Gulbarga project	12
4.4 Hospet-Tinaighat project	12
4.5 Electrification of Pune-Guntakal project.....	16
4.6 Summary table	17
Annexure I: R&R training report of Raipur-Titlagarh project	27
Annexure II: R&R training report of Sambalpur-Titlagarh	32
Annexure III: Letter from South Western Railway regarding direct purchase.....	37
Annexure IV: R&R photographs taken during training at RVNL, Hubli	39
Annexure V: R&R photographs taken at Raipur during field visit in May 2016.....	40
Annexure VI: R&R photographs during field visit at Raipur-Titlagarh in August 2016.....	41
Annexure VII: R&R photographs during field visit at Sambalpur-Titlagarh in September 2016	44

Table

Table 1: Detail of Projects	3
Table 2: Impact of additional requirements in HT	14
Table 3: Status of land acquisition in HT.....	15
Table 4: Financial status of compensation in HT	16
Table 5: Status of land Acquisition and Resettlement.....	22
Table 6: Details regarding Rehabilitation and Resettlement.....	26

Figure

Figure 1: Map of India showing track doubling and electrification projects	3
--	---

Abbreviation

ADB	Asian Development Bank
BPL	Below Poverty Line
CPM	Chief Project Manager
DG	Daund – Gulbarga
DGPS	Differential Global Position System
DM	District Magistrate
DPs	Displaced Persons
EA	Executing Agency
FHH	Female Headed Household
GAD	General Arrangement Drawing
GC	General Consultant
GCC	General Conditions of Contract
GRC	Grievance Redressal Cell
HT	Hospet – Tinaighat
HHs	House Holders
IA	Implementing Agency
India	Indian Government
INR	Indian Rupees
IP	Indigenous People
IPP	Indigenous Peoples Plan
IPPF	Indigenous Peoples Planning Framework
IR	Inception Report
LAO	Land Acquisition Officer
MOR	Ministry of Railways
NEFT	National Electronic Funds Transfer
NGO	Non-Governmental Organisation
NTH	Non-Title Holder
OSRC	Orissa Space Applications Centre
PAP/APs	Project Affected Persons
PG	Pune – Guntakal
PMC	Project Management Consultant
PWD	Public Works Department
RAP	Resettlement Action Plan
RFCTLARR	Right to Fair Compensation and Transparency in Land Acquisition, Rehabilitation and Resettlement Act
R&R	Resettlement and Rehabilitation
RO	Resettlement Officer
RP	Resettlement Plan
RT	Raipur – Titlagarh
RTGS	Real Time Gross Settlement
RVNL	Rail Vikas Nigam Limited
SC	Scheduled Caste

SIA	Social Impact Assessment
SLAO	Special Land Acquisition Officer
ST	Scheduled Tribe
ST	Sambalpur – Titlagarh
TH	Title Holder
USD	United States Dollars

Executive Summary

The current report is the semiannual Social Safeguard Monitoring Report prepared to comply with the loan covenants covering the period from April to September 2016 and is as per ADB's Public Communications Policy which requires disclosures of documents related to monitoring of safeguard policies and for posting on ADB's portal.

Non-Government Organization (NGO) Sugam International Sansthan:

For Hospet-Tinaighat project, M/s. Sugam International Sansthan, the NGO for implementation of the resettlement plan did not get a further extension of their contract after expiry of the 2nd extension on 4/1/2016 because of their continuous non performance. RVNL has appointed two local experts in consultation with General Consultant to carry out the balance R&R activities of the project. The Social Expert of General Consultant has given them a first training in Hubli on 16 June during which he handed over templates of documents to be used during implementation of R&R activities.

For Raipur-Titlagarh and Sambalpur-Titlagarh projects, the extension of time given to NGO ended on August 2016. It is expected that the NGO would be given a new extension of time by RVNL in coming months to complete the balance work of R&R.

Land Acquisition:

The land acquisition is limited to Hospet-Tinaighat and Sambalpur-Titlagarh projects. There was little progress during this period for land acquisition because of uncertainties in the legal framework due to evolutions of land acquisition laws.

Seeing that land acquisition is one of the key issues affecting the progress of doubling projects, Railway Ministry has allowed for direct purchase of land from landowners through direct negotiation with fixation of price by district level committee. Direct purchase from landowners is applicable to those states where state governments have formulated policies under section 108 of RFCTLARR Act 2013.

For Hospet-Tinaighat doubling project, consent for direct purchase of land from landowners through Revenue Department of Government of Karnataka has been given by Railway Ministry on 20/5/2016. Now, negotiations are going on with landowners for direct purchase of land through Revenue department at district level. During the last six months no land has been acquired but it is expected that with the implementation of direct purchase policy the progress of land acquisition with increase in coming months.

For Sambalpur-Titlagarh project only 4.45 acres of private land and 9.668 acres of Government land could be taken in possession so far. Government of Odisha is yet to frame policy for direct purchase of land for acquisition of private land.

Resettlements:

Resettlements are taking place in the 4 doubling projects.

During the period, resettlement activities have taken place mostly in the Raipur-Titlagarh and Sambalpur Titlagarh projects. For all the Non-Title Holders (NTHs) identified in Sambalpur-Titlagarh project, full and final second installment has been paid during August 2016. 50 NTHs of Chandinagar and 123 NTHs of Parwati Nagar in Raipur-Titlagarh project have been paid 1st and 2nd installment.

Global progress:

The calculated global progress of implementation of R&R activities across the various projects at the end of September 2016 is as under:

S. No	Name of the Project	Global progress
1.	Doubling of Daund-Gulbarga	100%
2.	Doubling of Hospet-Tinaighat	45%
3.	Doubling of Sambalpur-Titlagarh	35%
4.	Doubling of Raipur-Titlagarh	90%
5.	Electrification of Pune-Guntakal	N/A

1. Background

Five Railway projects are financed by the present ADB loans.

S. No	Project Name	Length (in Km.)	Location (State)	Project components
1	Daund-Gulbarga	225	Maharashtra and Karnataka	Doubling
2	Sambalpur-Titlagarh	182	Odisha	Doubling
3	Raipur-Titlagarh	203	Chhattisgarh and Odisha	Doubling
4	Hospet-Tinaighat	245	Karnataka	Doubling
5	Pune-Guntakal	641	Maharashtra, Karnataka, and Andhra Pradesh	Electrification

Table 1: Detail of Projects

The location of the projects is shown as red and blue in the map (Figure 1) here under:

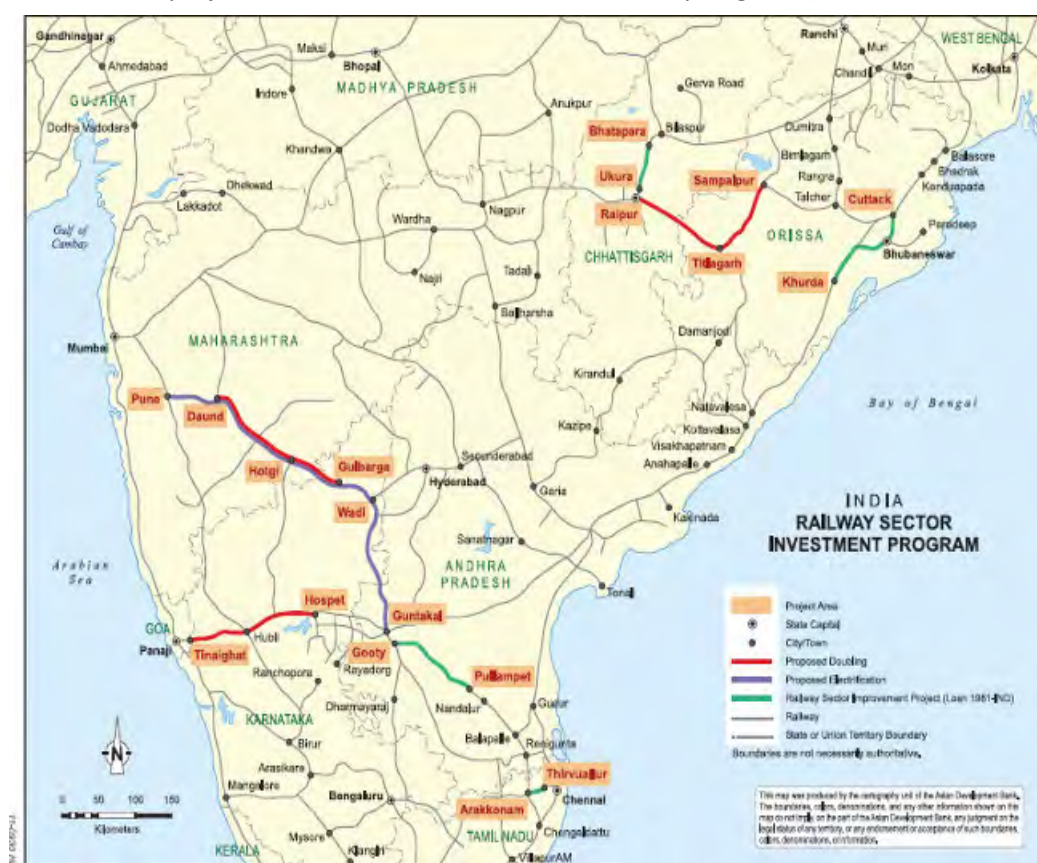


Figure 1: Map of India showing track doubling and electrification projects

In general, the resettlement planning documents related to above projects were disclosed in September 2011. Out of five projects only two, namely Sambalpur-Titlagarh and Hospet-Tinaighat doubling projects require land acquisition. The other two doubling projects (Daund-Gulbarga and Raipur-Titlagarh) involve resettlement of non-titleholders only. In Pune-Guntakal electrification project there is no land acquisition or resettlement of TH & NTH.

The current Semi Annual Report is the Social Safeguard Monitoring Report prepared to comply with the loan covenants covering the period from April 2016 to September 2016. As usual, this report covers resettlement and social safeguard monitoring results to comply with the spirit of ADB policy.

2. Evolution during the relevant period

The main activities during this 6 months period up to September 2016 are the continuation of disbursements to Affected Persons (APs) as per the approved micro plans in the Raipur-Titlagarh (RT), Sambalpur-Titlagarh (ST) and Hospet-Tinaighat (HT) projects. Further, income restoration and skill upgradation training programme for the project affected persons have been conducted at RT and ST project in August 2016.

Several meetings have been conducted for direct purchase of land from landowners in HT project during this period. The policy formulated by state government provides for acquisition of land through direct negotiation with fixation of price/compensation by District level Committee as allowed in section 108 of the Act (RFCTLARR Act 2013).

The cumulative global progress at the end September 2016 is as follows:

S. No	Name of Project	Global progress
1.	Doubling of Daund-Gulbarga	100%
2.	Doubling of Hospet-Tinaighat	45%
3.	Doubling of Sambalpur-Titlagarh	35%
4.	Doubling of Raipur-Titlagarh	90%
5.	Electrification of Pune-Guntakal	N/A

3. Current issues

Implementation of the new land acquisition Bill 2015:

The previous United Progressive alliance (UPA) government passed the bill “The right to fair compensation and transparency in Land acquisition, Rehabilitation resettlement act 2013 (RFCTLARR2013)” in September 2013 which came into force from 1st January 2014. The Act replaced the Land Acquisition Act, 1894, enacted during British rule. However, the new government (National democratic alliance) decided to amend it via an ordinance in December 2014 and later as a Bill in March 2015 to make it more infrastructure friendly. One of the main objective of the ordinance was to do away with cumbersome and time consuming Social Impact Assessment Studies for infrastructure projects.

The new bill “The Right to Fair Compensation and Transparency in Land Acquisition, Rehabilitation and Resettlement (Amendment) Bill 2015”, also known as Land Bill 2015 introduced the by new government in March 2015 could not get approval in Parliament and was referred to a Joint Committee in May 2015 comprising Member of Parliament from both houses to make out a bill acceptable to all parties. Meanwhile, after lapse of ordinances over land acquisition on 31 August 2015 the Central Government has not re-promulgated the ordinance and instead allowed the state Governments to formulate their own laws or amend central law in this regard to expedite developments. Now, a seventh extension has been given by parliament in July 2016 to extend the time for presentation of the Report of the Joint Committee up to the last day of the winter session, December 2016.

The main feature of this new land bill “The Right to Fair Compensation and Transparency in Land Acquisition, Rehabilitation and Resettlement (Amendment) Bill , 2015” with respect to our project is that if it becomes Act in coming months it would relieve State Governments from conducting Social Impact Assessment (SIA) study for acquisition of land thereby saving considerable time and money.

Since above new bill (Land bill 2015) introduced by the Central Government has not come in force, the Right to Fair Compensation and Transparency in Land Acquisition, Rehabilitation and Resettlement (RFCTLARR) Act, 2013 passed by previous Government is still having legal vaildity. Now, most of the State Governments have framed policies in terms of section 108 of the Act (RFCTLARR Act 2013) for land acquisition in their respective states. Under this section State Government can frame policies to give higher compensation than mentioned in the Act. The policy formulated by most of the states provide for acquisition of land through direct negotiation with fixation of price/compensation by District level Committee. Some of the State Governments are insisting that all land acquisition be acquired through direct negotiation only. Thus there is no uniformity regarding the route to be followed for land acquisition among State Governments.

Regarding Railway projects, this issue has been examined and Railway Board has issued a circular containing the following decisions:

1. *In case of Doubling, Traffic facilities, Passenger amenities works and other works, normally requirement of land is minimal as most of the land required is available with Railways, therefore acquisition of land can be done through direct negotiation if the State Government has formulated policy/guidelines under section 108 of RFCTLARR Act 2013. If State Government has not formulated*

any policy that acquisition of land has to be either through RA Act 2016 or RFCTLARR Act 2013.

2. *In case of New Lines and Gauge Conversion, acquisition should be carried out either through RA Act 2016 or RFCTLARR Act 2013. For projects which have been declared as Special Railway Project, land should be acquire through RAA 2008.*

However, if the left over/balance acquisition due to missing plots from bulk acquisition, deviation in the boundaries while interpreting the revenue map, change in Khasra number, additional requirement to accommodate minor alteration necessitated due to unforeseen technical, social or environmental considerations is less than 10% of the total acquisition of land for particular phase (if phasing has been done in advance) or targeted stretch, than balance land can be acquired through direct negotiation through policy formulated by State Government in term of section 108 of RFCTLARR Act 2013, with approval of General Manager.

3. *In case all land acquisition in a State, either by State Government or by Central Government agencies, is being done through direct negotiation only and State Government is categorically stating that they are not in a position to acquire land through RFCTLARR Act 2013 and are not ready/willing to spare/associate any District officials as competent authority for facilitating acquisition under RA Act 2008, than land for New Line/Gauge Conversion can also be acquired through direct negotiation through the policy/guidelines formulated by the respective state in term of section 108 of RFCTLARR Act 2013 passed by Ministry of Law And Justice (Legislative Department) on 30/05/2015 with approval of General Manager.*

Non-Government Organization (NGO):

For Hospet-Tinaighat project:

M/s. Sugam International Sansthan, the NGO for implementation of the resettlement plan at Hospet-Tinaighat project did not get further extension of their contract after expiry of 2nd extension on 4/1/2016 because of their continuous non performance. RVNL has appointed two local experts in June for a period of six months consultation with GC to carry out the balance R&R activities of the project. The Social Expert of GC has given them a first training in Hubli on 16 June during which he handed over templates of documents to be used during implementation of R&R activities.

For Raipur-Titlagarh and Sambalpur-Titlagarh projects:

During this period, the Social Expert of the General Consultants has visited Raipur-Titlagarh and Sambalpur-Titlagarh projects to assess progress of R&R activities and the need to extend further the contract of the NGO for the unfinished tasks with NTHs at Raipur.

The NGO Contract Agreement for Implementation of Resettlement Plan for project affected persons of Raipur-Titlagarh and Sambalpur-Titlagarh sections was signed on 23 January 2012. The contract was extended up to August 2016 to complete all the pending works on RT and ST projects. Still some pending work has been observed at Raipur and there was a request to extend further the contract of the NGO by

another 3 months. NGO has introduced a request for extension of time to the CPM Raipur and this request is in process. Till September no approval has been granted to NGO.

The General Consultant recommends that the NGO be asked to implement the RP as per the agreement. The contract is a Lump Sum Price with Milestones, so no item can be removed without modifying the contract. As per the clause 1.12 the contract can be modified with mutual consent.

The training of Affected Persons (APs) was an essential component in the implementation of the R&R activities. The objective being to upgrade/enhance the skills of the APs so that they may utilize these skills in income generating or any other economic activity so that the quality of life or the socio-economic condition of the APs is improved.

During August 2016, training programs have been organized in different locations of project area to train the affected persons. The NGO played an active role in coordination of the training programs ranging from transporting the APs to the training center, follow up of training program etc. Male and female both were trained in the training programs.

Each entitled AP has got a training toolkit, that contained one bag, pen, pad, training book and training material to start the income earning/enhancing pursuits. Each AP who attended training program has been given a training certificate also. Breakfast, lunch and transport facility has also been given to each AP.

For the Raipur-Titlagarh project, income restoration and skill upgradation training programme for the affected persons of Chandinagar and Parwati Nagar was held from 8th August to 10th August, 2016. For Mahasamund and Kantabaji it was held from 11th August to 13th August, 2016. Total 140 PAPs out of 144 PAPs attended the training programmes. (Detailed report in Annexure I).

For the Sambalpur-Titlagarh project, income restoration and skill upgradation training programme for the affected persons of Khetajpur, Guhratikra and Balangir was held from 27th August to 29th August, 2016. Total 12 PAPs out of 14 PAPs attended the training programme. (Detailed report in Annexure II).

Direct Purchase of land through Revenue Department:

In the previous months, South Western Railway had received from districts Land Acquisition offices covering Hospet-Tinaighat project proposals of direct purchase of land through Revenue Department. They sought opinion from Railways, so that this option can be exercised with prior approval of acquiring authority. If the land is purchased directly from the landowners, the purchase can be completed within a span of 3 to 4 months. The proposal for the direct purchase of land was sent to Advisor (land) Ministry of Railway on 29 March 2016.

Railway Board, Ministry of Railways, has communicated its approval to RVNL on 20/5/16 for direct purchase of land from landowners through Revenue Department of Government of Karnataka for Hospet- Tinaighat doubling project with condition that compensation amount should not be less than specified in Land Acquisition and Rehabilitation Act (LARRA) 2013.

Disbursement of compensation for acquisition of land and assets will be done through Land Acquisition Officer of Revenue Department of District and project authorities will disburse R&R benefits to Project Affected Persons (PAPs) and communities. For this purpose, Collector of each District will convene a meeting in which each and every component of Resettlement Action Plan (RAP) implementation and land acquisition will be finalized.

Several direct purchase meetings have been conducted at Hospet-Tinaighat project during this period but till date no final negotiation has been successful. Negotiation are continuing.

The land acquisition is proposed in 4 districts namely Belgaum, Darward, Koppal and Gadag. The Joint Measurement Survey (JMS) with Revenue department is in progress and the valuation is also in progress by the concerned Public Works Department (PWD).

4. Status

The current status of field work of land acquisition and resettlement plan implementation of different projects is provided in table 3.

The status per project is as follows:

4.1 Sambalpur–Titlagarh project

This project passes through four districts namely Sambalpur, Sonepur/Subarnapur, Bargarh and Balangir in state of Odisha.

Resettlement:

For the 14 affected persons of Khetajpur, Guhratikra and Balangir first and second installment have been transferred in their respective accounts in the month of April 2016 and August 2016. The land is totally free from any encumbrances.

Income restoration and skill upgradation training programme for the affected persons of Khetajpur, Guhratikra and Balangir was held from 27th August to 29th August, 2016. Total 12 PAPs out of 14 PAPs attended the training programme (detailed report in Annexure II).

Land acquisition:

The total requirement of land is estimated 138.764 acres (56.16 ha): (1) Private Land: acres 76.678 (2) Government Land: acres 46.746 (3) Forest Land: acres 15.340.

Name of the District	Private Land
Sambalpur	(a) 4.62 acres (1.870 ha) Private Land acquisition required in 5 villages. (b) Possession taken for acres 4.45 in 3 villages. (c) U/s 19(1) declaration to be issued for acres 0.17 in 2 villages. (d) Sub-Collector/SBP visited site on 27/04/16 to verify displacement/ RR issue for balance acres 0.170 in 2 villages. (e) SLAO/SBP sent proposal for issue of 19(1) notification for acres 0.170 in 2 villages on 12/09/16 to the Joint Secy. to Govt, RDM Deptt., Govt of Odisha, BBSR.
Baragarh	(a) 21.425 acres (8.670 ha) private land acquisition required in 26 villages. (b) As per the demand of NCDS/BBS, fund of 2,320,377 INR towards SIA Study has been deposited on 04/03/16. (c) AGM/C/RVNL/SBP pursued the issue of SIA with Sate Coordinator/NKCDS on 26/07/16 and 19/09/16
Bolangir	(a) 41.448 acres (16.774 ha) Private Land acquisition required in 32 villages. (b) As per the demand of NCDS/BBS, fund of 2,418,680 INR towards SIA Study has been deposited on 26/02/16. (c) AGM/C/RVNL/SBP pursued the issue of SIA with Sate Coordinator/NKCDS on 26/07/16 and 19/09/16.
Sonepur	(a) 9.185 acres (3.717 ha) Private Land acquisition required in 8 villages.

	<p>(b) U/s 19(1) declaration to be issued for 9.185 acres in 8 villages.</p> <p>(c) As per the demand of Collector/Sonepur, fund demand for 13,88,35,510 INR for cost of acres 8.845 of private land in 7 villages Rampur Tahasil has been received vide letter dtd. 01/06/16 (for 6 villages) and 07/06/16 (for one village). The same has been deposited with Spl.LAO/SBP on 24/06/16 by Dy. CE/Con/SBP. For balance one village for acres 0.340 fund demand received from State Govt and payment under process.</p> <p>(d) Further, he has demanded differential amount of 1,579,738 INR in village Cherupalli towards cost of land vide letter No. 6634 dtd. 20/06/16. (Earlier Collector/ Sonepur has demanded fund of 4,563,899 INR and now demanded of fund of 6,143,637 INR due to multiplying factor mistake in the estimate by State Govt.). This is under process to be deposited with Spl.LAO/SBP very soon.</p> <p>(e) SLAO/SBP sent proposal for issue of 19(1) notification for acres 9.185 in 8 villages on 12/09/16 to the Joint Secy. to Govt, RDM Deptt., Govt of Odisha, BBSR</p>
--	---

Government Land

<p>(a) Total Govt. Land required: 46.746 acres (64 villages).</p> <p>(b) Out of 46.746 acres of Govt. Land required for the project in Sambalpur, Baragarh, Sonepur and Bolangir District, alienation has been sanctioned for 1.921 acres in 15 villages of Baragarh district and 4.380 acres in 23 villages of Bolangir District, 2.310 acres in 1 village in Sambalpur District and 1.057 acres in 7 villages in Sonepur District.</p> <p>(c) Lease deed executed for 7.297 acres with concerned Sub-Registrar office.</p> <p>(d) Balance 37.078 acres of Govt. Land is yet to be alienated by State Govt.</p> <p>(e) Lease deed executed for 7.297 acres and balance 2.371 acres Lease deed under process.</p>

Forest Land

<p>(a) 15.340 acres (6.208 ha) of Forest Land diversion is required in 4 villages for the entire Sambalpur – Titlagarh Doubling Rail Project.</p> <p>(b) In compliance to observations made by Nodal/Officer of PCCF office, hard copies are submitted with concerned DFOs and District Collectors on 04/05/16.</p> <p>(c) Observations given by DFO/SBP on 05/07/16 and DFO/BRGA on 24/05/16 are under compliance by RVNL.</p> <p>(d) Enumeration of trees under Balangir district has been completed and certified by FROs/BLGR and TIG done on 19/09/16. Consolidated reply to the observation of DFO/BLGR is under process.</p>

There may be some additional land requirements due to design changes in layout of station yards. The additional requirements of land in section Sambalpur-Titlagarh has not been finalized till now.

4.2 Raipur-Titlagarh project

The alignment of Raipur-Titlagarh project passes through two states: Chhattisgarh and Odisha. In Chhattisgarh section the alignment passes through two districts namely Raipur and Mahasamund. There is no land acquisition in this project.

RVNL Raipur has revised the total compensation to 18,318,478 INR to rehabilitate 261 PAPs.

For Kantabaji area of Odisha state, the total no of PAPs is 23, 2nd and final disbursement for the 23 PAPs has been completed and the land is totally free from encumbrances.

For Mahasamund area of Chhattisgarh state, the total no. of PAPs is 45. 2nd and final disbursement for those 45 PAPs has been completed and land is totally free from encumbrances.

For Parvati Nagar at Raipur of Chhattisgarh state, the total no. of PAPs is 143. First installment for 143 PAPs was completed in the month of February 2016. During this period the second installment for the 123 PAPs has been transferred in their respective accounts. Now the land is mostly free and out of 143, 123 PAPs have removed their existing structures from the Corridor of Impact (COI).

For Ekta Nagar at Raipur of Chhattisgarh state, all the affected PAPs have vacated their structures as they have been provided alternative shelter in the nearby area by the District Administration. The land is totally free from any encumbrances.

For Chandinagar at Raipur of Chhattisgarh state, the total no. of PAPs is 50. Identity cards have been distributed for 49 PAPs. During this period the first installment for 49 PAPs has been transferred in their respective accounts.

Income restoration and skill upgradation training programme for the affected persons of Chandinagar and Parvati Nagar was held from 8th August to 10th August 2016. Mahasamund and Kantabaji was held from 11th August to 13th August 2016. Total 140 PAPs out of 144 PAPs attended the training programme. (see photographs in Annexure VI).

4.3 Daund-Gulbarga project

There was no land acquisition in Daund-Gulbarga project. The NGO had completed the R&R activities as per the approved Micro plan for NTH except for training. All NTHs have given in writing that there was need of trainings as they are working in some nearby factory. The GC social expert has collected all the relevant papers for final completion of this section. No Grievances have been reported by any PAP. The GC social expert recommends closing this project.

4.4 Hospet-Tinaighat project

This project is situated in the state of Karnataka. The total scope of land acquisition has now been revised to 27.325 acres (11.06 ha).

No NTH were found in this project. The Micro plan for resettlement allowance has been approved for 25 out of total 43 PAPs. An amount of 370,000 INR of entitlements has been disbursed in three stages to 25 PAPs/House Holders (HHs).

Grievance Redressal Committee (GRC) letters have been issued by District Magistrate (DM) concerned.

Assistance for resettlement/NGO

The contract of M/s. Sugam International Sansthan for implementation of the resettlement plan after getting extensions for consecutive 2 years expired on 4/1/2016. As NGO constantly failed to deploy requisite manpower, RVNL had decided not to extend the contract of NGO M/s. Sugam International Sansthan beyond 04/01/2016 for this project.

On termination of this contract, RVNL corporate office advised the PIU to appoint a local agency or local experts in consultation with GC to carry out the balance R&R activities of the project.

The letter for mobilization of those local experts for implementation of balance resettlement plan has been sent and two persons have been mobilized from 15 June 2016 at RVNL Hubli.

The Social Expert of GC has given them a first training in Hubli on 16 June during which he handed over templates of documents to be used (see Annexure IV).

The social expert of GC will keep monitoring closely the work of those local experts.

Land acquisition – direct purchase through Revenue Department

The District authorities of Koppal and Gadag vide letters dated 17/2/2016 and 20/1/2016 respectively had suggested direct purchase of land through Revenue Department to avoid further delay in land acquisition. It has been informed by District Authorities that as per the new land acquisition Act, the time involved to undergo the process would be around 2 years. Alternatively, if the land is purchased directly from the land owners, purchase of land can be completed within a span of 3 to 4 months. The proposal for the direct purchase of land was sent to Advisor (land), Ministry of Railway on 29 March 2016.

Railway Board, Ministry of Railways, has communicated its approval to RVNL on 20/5/2016 for direct purchase of land from landowners through Revenue Department of Government of Karnataka for Hospet-Tinaighat doubling project with condition that compensation amount should not be less than specified in LAAR act 2013.

South Western Railway has requested District Magistrate Koppal on 4 June 2016 to make necessary arrangements for direct purchase of required land in Koppal District. It is expected that request from zonal Railway for direct purchase of land for other Districts would soon follow.

A copy of the letter from South Western Railway showing village wise requirement of land for acquisition in Koppal district is attached as Annexure –III

Land acquisition - requirements

The revised total land acquisition requirement under this project is now 27.325 acres in districts of Koppal, Gadag and Dharwad. So far, 19.00 acres had been notified under clause 6(1) of Land Acquisition Act and 8.325 acres is proposed to be acquired through direct purchase.

The project comprised major land acquisition in Koppal district for four Railway Stations. To minimize land acquisition, the scope of yard construction in Munirabad has been restricted to Railway land only. Similarly, in Munirabad-Bhanpur section construction of extension of minor bridges has been restricted to Railway land by constructing retaining walls.

There are some savings in land acquisition but also some additional requirements in station yards due to design changes.

The additional requirements are in Gadag, Alnawar and Devarai yards.

The reasons for those additional requirements are:

- Provision for public and bullock carts movement (extra 27 Gunta)
- Increase in Loop line length from 500 m to 750 m.
- Encountering high bank and extension of yard.

NAME OF THE VILLAGE	Package no	Revised Land after Joint Measurement Survey (JMS) With RVNL & Revenue Dept proposed for direct purchase			Impact on Social Safeguards	Remarks
		A	G	a		
Betagari ,Gadag (Gadag DT)	HT-2	0	27	0	Two buildings are affected and the valuation is under process by PWD department but General Consultant social expert will verify during his field visit proposed in November 2016.	For public and bullock carts movement extra taken 27 Gunta
Alnawar new proposal (Dharwad DT)	HT-3	1	1	0	At present no Social Impact found only agriculture land is affected but General Consultant social expert will verify during his field visit proposed in November 2016.	Loop line increasing from 500 m to 750 m
Devarai new proposal (Belgaum DT)	HT-3	3	30	0	At present no Social Impact found only agriculture land is affected but General Consultant social expert will verify during his field visit proposed in November 2016.	Due to high bank and extension of yard
Grand Total		5	18	0		

Table 2: Impact of additional requirements in HT

Land acquisition - progress

Several meetings have been conducted for direct purchase of land from landowners at District level. Some of landowners from Sonpur and Bhanapur village have not agreed with rate offered by District Collector office based on State government guidelines. However, negotiations are going on with those landowners.

The land acquisition is ongoing in 4 districts namely Belgaum, Darward, Koppal and Gadag. The Joint Measurement Survey (JMS) with Revenue department for direct purchase is in progress at above districts. Also, the valuation by the state Public Works Department (PWD) is in progress for the structures coming in proposed extension of yards.

The present status of land acquisition in Hospet-Tinaighat project is as follows:

As on 30-09-2016																
NAME OF THE VILLAGE	Package no	Total land acquisition scope			Notification 6(1) issued for Land acquisition			Land yet to be taken over			Revised Land proposed for direct purchase			Revised Land afetr JMS proposed for direct purchase		
		A	G	a	A	G	a	A	G	a	A	G	a	A	G	a
ANNIGERI (Darwad)	HT-2	1	22	0	1	22	0	0	0	0	0	0	0	0	0	0
ANNIGERI (Darwad Govt. Agriculture University)	HT-2	1	1	0	1	1	0	0	0	0	0	0	0	0	0	0
SOMAPUR (Koppal)	HT-1	8	6	0	4	16	0	3	30	0	0	31	0	0	29	0
BHANAPUR (Koppal)	HT-1	3	32	0	1	31	0	2	1	0	1	2	0	0	34	0
HOSSALLI (Munirabad) (Koppal)	HT-1	2	26	0	1	25	0	1	1	0	0	23	0	0	16	0
KOPPALL (Koppal)	HT-1	13	3	0	6	14	0	6	29	0	4	12	0	4	18	0
TALABALA (Bhanapur) (Koppal)	HT-1	2	11	0	2	11	0	0	0	0	0	0	0	0	0	0
KAMPASAGAR (Munirabad) (Koppal)	HT-1	2	19	0	0	0	0	2	19	0	0	28	0	0	38	0
Munirabad Additional (Koppal)	HT-1	0	22	0	0	0	0	0	22	0	0	22	0	0	22	0
1.Total as per June 2016		35	22	0	19	0	0	16	22	0	7	38	0	7	37	0
New proposal																
Gadag (Gadag)	HT-2	0	0	0	0	0	0	0	0	0	0	27	0	0	27	0
Alnawar new proposal (Darwad)	HT-3	0	0	0	0	0	0	0	0	0	1	1	0	1	1	0
Devarai new proposal (Belgaum)	HT-3	0	0	0	0	0	0	0	0	0	3	30	0	3	30	0
2.Total as per new proposals in July 2016		0	0	0	0	0	0	0	0	0	5	18	0	5	18	0
A = Acres G = Gunta a = anna 1 Acre = 40 Gunta 1 Gunta = 16 anna																

Table 3: Status of land acquisition in HT

Financial status of compensation against land acquisition and resettlement as on 30/9/16												
S No	Name of district	name of village/station	Total nos of PAPS	Total Nos of NTH	Total nos of TH	Total compensation paid against land purchase to THs upto Sep 2016			Total Resettlement Allowance paid upto Sep 2016		Total resettlement pending	
						No. of TH	Amount	Land acquired in acres	No of PAPS	Amount	No of PAP	Amount
1	Koppal	Koppal/Koppal	6	0	6	0	₹ 0	6.35	1	₹ 8,000	5	₹ 60,000
2	Koppal	HOSSALLI/Munirabad	4	0	4	4	₹ 1,328,453	1.625	4	₹ 62,000	0	₹ 0
3	Koppal	SOMPUR/Sompur	7	0	7	0	₹ 0	4.4	4	₹ 62,000	3	₹ 24,000
4	Darwad	ANNIGERI/Annigeri	11	0	11	3	₹ 368,750	2.575	11	₹ 178,000	0	₹ 0
5	Koppal	TALABALA/Bhanapur	3	0	3	3	₹ 1,182,099	2.275	2	₹ 26,000	1	₹ 8,000
6	Koppal	BHANAPUR/Bhanapur	12	0	12	1	₹ 191,029	1.775	3	₹ 34,000	9	₹ 102,000
7	Koppal	Kampasagar /Munirabad										
8	Gadag	Bettageri/Gadag										
9												
10												
Total			43	0	43	11	₹ 3,070,331	19.000	25	₹ 370,000	18	₹ 194,000

Table 4: Financial status of compensation in HT

Pending compensation of 432,520 INR has been released against land acquisition made in Koppal over previous period.

Resettlement:

No NTH in this project.

TH compensated: 11

Still to be compensated: 18

4.5 Electrification of Pune-Guntakal project

No land acquisition and no TH & NTH in this project.

4.6 Summary table

Status of Land Acquisition with resettlement plan implementation of different projects is as follows:

Item No	Indicators	Section					
		Raipur-Titlagarh project (Odisha Section)	Raipur-Titlagarh project (Chhattisgarh Section)	Sambalpur-Titlagarh project	Hospet-Tinaighat project	Daund-Gulbarga project (Karnataka Section)	Daund-Gulbarga project (Maharashtra Section)
1	Appointment of the RP implementation NGO	Sugam International Sansthan. (Request for extension submitted by NGO to CPM)	Sugam International Sansthan. (Request for extension submitted by NGO to CPM)	Sugam International Sansthan.	2 persons from Sree Manjunatha Enterprises providing support from 16/6/16 (Sugam International Sansthan end of contract on 4/1/2016)	Sugam International Sansthan end of contract on 4/1/2016	Sugam International Sansthan end of contract on 4/1/2016
2	No. of displaced households	23	238	666 (14 NTH)	43	NIL	5
3	No. of displaced persons	76	621	2343 (92 NTH)	173	NIL	20
4	No. of physically displaced households	23	238	22 NTH	NA	NIL	NIL
5	No. of physically displaced persons	73	238	92 NTH	NA	NIL	NIL

		Section					
Item No	Indicators	Raipur-Titlagarh project (Odisha Section)	Raipur-Titlagarh project (Chhattisgarh Section)	Sambalpur-Titlagarh project	Hospet-Tinaighat project	Daund-Gulbarga project (Karnataka Section)	Daund-Gulbarga project (Maharashtra Section)
6	No. of economically displaced households	NIL	136	644 TH	43	NIL	NIL
7	No. of economically displaced persons	NIL	238	2251 TH	173	NIL	NIL
8	Total number of titleholders being displaced	NIL	NIL	644	43	NIL	NIL
9	Total number of non titleholders being displaced	23	238	22	NIL	NIL	5
10	Entitlement matrix disclosed	Yes	Yes	Yes	Yes	Yes	Yes
11	Number of identity cards issued to the displaced persons	Identity cards released to 23 PAPs in Kantabanji area	Identity cards distributed to all PAPs	Identity cards distributed to all PAPs (14 PAPs)	Identity cards distributed to PAPs of 5 villages (25 PAPs)	NA	5

		Section					
Item No	Indicators	Raipur-Titlagarh project (Odisha Section)	Raipur-Titlagarh project (Chhattisgarh Section)	Sambalpur-Titlagarh project	Hospet-Tinaighat project	Daund-Gulbarga project (Karnataka Section)	Daund-Gulbarga project (Maharashtra Section)
12	Micro plans prepared for titleholders	Not required	Not required	After award by Deputy Land Acquisition Officer (DLAO)	Revised corrected micro plan has been approved in May 2015	Not required	Not required
13	Micro plans prepared for non- titleholders	Completed and submitted (23 NTH)	Completed and submitted (238 NTH)	Completed and submitted (14 NTH)	NA	NA	Yes
14	Micro plans prepared for CPRs	NA	NA	NA	NA	NA	NA
15	Micro plans approved for TH	NA	NA	Not yet	Approved	NA	NA
16	Micro plans approved for NTH	Approved	Approved	Approved	NA	Approved	Approved
17	Micro plans approved for CPRs	NA	NA	NA	NA	NA	NA
18	Quantum of private land to be acquired	NIL	NIL	76.678 acres	now revised from 35.22 to 31.37 acres	NIL	NIL
19	Progress on LA	NA	NA	Requisition for LA submitted	Out of revised 31.37 acres 19	NIL	NIL

		Section					
Item No	Indicators	Raipur-Titlagarh project (Odisha Section)	Raipur-Titlagarh project (Chhattisgarh Section)	Sambalpur-Titlagarh project	Hospet-Tinaighat project	Daund-Gulbarga project (Karnataka Section)	Daund-Gulbarga project (Maharashtra Section)
				and completed for Government, forest and private land for Sambalpur, Sonepur, Baragarh and Balangir districts	acres was already notified under 6(1). Balance 12.37 acres to be acquired under direct purchase		
20	Whether compensation distributed to DPs	2 nd /final installment of compensation has been distributed to all 23 nos DPs of Kantibaji area	2 nd and final installment has been distributed to all 45 DPs of Mahasumund area whereas 2 nd instalment of compensation paid for 123 DPs of Parwati Nagar	1 st and 2 nd instalment of compensation paid to 14 nos NTHs in April/August 2016	Distributed to 12 PAPs under Phase-I in December 2013. Distributed to 8 PAPs under Phase II in April 2014. Distributed to 5 PAPs under Phase-III in Sep 2015	NA	1st instalment of assistance has been distributed on 24/12/12 2nd/final installment has been distributed on 24/08/2013. Total 5 PAPs identified as Squatters has been compensated in two installment for 858,037 INR

		Section					
Item No	Indicators	Raipur-Titlagarh project (Odisha Section)	Raipur-Titlagarh project (Chhattisgarh Section)	Sambalpur-Titlagarh project	Hospet-Tinaighat project	Daund-Gulbarga project (Karnataka Section)	Daund-Gulbarga project (Maharashtra Section)
21	Whether assistance distributed to DPs	Yes	Yes	Yes	Not yet	NA	All the PAPs are working in nearby Cement factory-Hotagi and are getting 10,000 INR to 15,000 INR per month, and they have given in writing that they don't need any training as they are already employed
22	Whether GRC formed	GRC formed at 1 district (Balangir)	GRC formed at 2 district (Mahasumund and Raipur)	GRC formed in all 4 districts	Special Land acquisition Officer cum Assistant Commissioner has been nominated as a Chairman of GRC and DGM/RVNL as member of GRC from PIU	NA	Yes
23	Complaints to GRC received/resolved	NIL	NIL	NIL	NIL	NIL	NIL
24	Consultations held with DPs	3 places	4 places	5 places	13 places	NA	Yes

		Section					
Item No	Indicators	Raipur-Titlagarh project (Odisha Section)	Raipur-Titlagarh project (Chhattisgarh Section)	Sambalpur-Titlagarh project	Hospet-Tinaighat project	Daund-Gulbarga project (Karnataka Section)	Daund-Gulbarga project (Maharashtra Section)
25	Relocation	Completed	Completed at Mahasamund , Ekta Nagar, Khantabaji, partly Parwati Nagar and Chandi Nagar in process	Completed	NA	NA	Completed
26	Inventory of losses of Displaced Persons (DPs)	Completed	Completed	Completed	Completed	Completed	Completed
27	Impact on Indigenous People/STs with kind of impact	Completed (STs not found)	Completed (STs not found)	Completed (STs not found)	Completed (STs not found)	Completed (STs not found)	Completed (STs not found)

Table 5: Status of land Acquisition and Resettlement

Details regarding status of R&R implementation as on 30 September 2016

S. No	Name of Project	Length of line (in kms)	Length of section free from R&R	Area of land to be acquired	No. of HHs/PAPs	Status of R&R implementation
1.	Raipur-Titlagarh doubling project (Odisha section)	99.94	98.85 kms	Nil	261/261	Identification and verification of PAPs has been revised and completed and submitted. Joint Measure Survey (JMS) has also been completed. GRC formed. Valuation of structures have also been completed and micro plan has been prepared and has been submitted on 09/09/2013 by NGO at total rehabilitation cost of 87,386,088 INR for 681 HHs. However, R&R expert of GC advised to minimize the Right of Way (ROW) and was agreed by PMC and RVNL. Actual COI (Corridor of Impact) was work out by NGO, RVNL and Revenue Officer. Micro plan has been revised and completed on 12/11/2013 at total R&R cost of 19,714,627 INR for 265 HHs based on actual COI. Micro plan approved and Identity cards distribution was started in Odisha section. Revised micro plans was approved in August 2015 for Mahasamund and Kantabanji areas bringing the new total to 235 HHs. Identity card distributed to 42 PAPs in Mahasamund District in Chhattisgarh section. Bond paper of PAPs completed. Assistance distributed through RTGS. Paid in September 2015. For Parwati Nagar of Raipur area, revised (Micro Plan) was submitted by NGO in September and in December 2015 short listing 143

S. No	Name of Project	Length of line (in kms)	Length of section free from R&R	Area of land to be acquired	No. of HHs/PAPs	Status of R&R implementation
2.	Raipur-Titlagarh doubling project (Chhattisgarh section)	98.01	96.60 kms	Nil	238/621	PAPs for amount of 9,844,847 INR was finalized for disbursement. Micro plan for Chandi Nagar for 50 PAPs has been approved in February 2016 for disbursement. 1 st installment disbursement for 49 PAPs of Chandinagar and 2 nd installment for 123 PAPs of Parwati Nagar have been paid in July/August 2016.

S. No	Name of Project	Length of line (in kms)	Length of section free from R&R	Area of land to be acquired	No. of HHs/PAPs	Status of R&R implementation
3.	Sambalpur–Titlagarh doubling project	182.00	125.00 kms	76.678 acres	TH 644/2251 NTH 14/14	<p>TH: Requisition for LA submitted for government and private land for Sambapalur, Sonepur Bargargh and Balangir Districts.</p> <p>NTH: Identification and verification and Joint measurement report completed on 02/07/2013. Micro Plan prepared on 27/09/2013 at total rehabilitation cost of 6,657,962 INR for 65 HHs. However, Revenue officer (RO) provided actual corridor of Impact (COI) and track plan which was reviewed by RVNL representative and NGO with GC. Micro plan was revised accordingly and completed and submitted on 28/10/2013 for a total R&R cost of 4,419,511 INR for 38 NTHs. Micro plan was reviewed on behalf of PIU Sambalpur. Rehabilitation cost of 4,419,511 INR for 38 NTHs reduced to 33,40,643 INR for 14 NTHs 1st instalment of compensation has been released to all 14 NTHs in April 2016. 2nd and final installment has been paid in August 2016.</p>
4.	Hospet–Tinaighat doubling project	201.31	195.31 kms	31.37 acres revised to 35.22 acres	43/173	<p>Identification and verification of PAPs has been completed and data updation work has also been completed and submitted.</p> <p>Micro plan is finalized and Identity cards have been issued to PAPs of Koppal, Hosalli, Sompur and Annigeri villages.</p> <p>Disbursement of allowances to PAPs (12 Nos.) under phase - I was conducted during 3rd week of December 2013 and (08 Nos) under Phase – II during the first week of April 2014.</p> <p>19.0 acres of land notified 6(1) for acquisition. 8.24 acres of land to be acquired through direct purchase. Compensation in village Hosahalli yard Munirabad district Koppal 2 PAPs have collected the check from the Revenue Department for 432,520 INR in July 2016.</p>

S. No	Name of Project	Length of line (in kms)	Length of section free from R&R	Area of land to be acquired	No. of HHs/PAPs	Status of R&R implementation
5.	Daund–Gulbarga doubling project (Karnataka section)	46	46 kms	0	0	NA
6.	Daund–Gulbarga doubling project (Maharashtra section)	179	176 kms	0	5/20	Total 5 PAPs identified as Squatters has been compensated in two installment of 858,037 INR. All the PAPs are found working in a nearby Cement factory-Hotagi and are getting INR 10,000 to 15,000 per month and they have given in writing that they don't need any training. The GC social has collected all the relevant papers for final completion of this section. GC Social Expert recommends to close this project.

Table 6: Details regarding Rehabilitation and Resettlement

Annexure I: R&R training report of Raipur-Titlagarh project**SUGAM INTERNATIONAL SANSTHAN**

B-109 VIBHUTI KHAND, GOMTI NAGAR,

Lucknow – 226 010 (UP)

☎: +91 9936828202 & 9453929192, Fax: (0522) 2720185 Email- sugamko.sis@gmail.com

SIS/HQ/RVNL/RP-TIT-SBP/2016/114**the 31st Aug 2016.**

To,

The Chief Project Manager
 Rail Vikas Nigam Limited
 Project Implementation Unit
 Raipur

Sub: The Implementation of Resettlement Plan in Raipur-Titlagarh Doubling Rail Line Project State of Chhattisgarh And Orissa, Sambhalpur-Titlagarh Doubling Rail Line Subproject State of Orissa. **Training Programme for Non Title Holder Families .**

Sir,

In reference to above mentioned subject, it is submitted that we have organized Income Restoration and skill up gradation training program for the affected persons of the village Chandinagar, Parwatinagar, 08.08.2016 to 10.08.2016 and Mahasamund kantabagi from 11.08.2016 to 13.08.2016, as per approved Microplan.

We have completed Training Programme Successfully. Total 144 out of 140 PAPs of these villages have imparted in Training camp. The report has been prepared and is being submitted for your kind perusal and suggestions to improve the forthcoming training camps.

Thanking you !

Yours faithfully

Anil kumar

Project Co-ordinator

Sugam International Sansthan

Encl. Training Report (Pages 4)

Copy to: 1. Dr. Sudesh Kaul (GC) R&R Expert Egis india Pvt Ltd, for kind perusal and suggestions please.


2. Shri. R.K. Thakur General Consultant Egis india Pvt Ltd, for kind perusal and suggestions please.

SUGAM INTERNATIONAL SANSTHAN

B-109 VIBHUTI KHAND, GOMTI NAGAR,

Lucknow – 226 010 (UP)

☎: +91 9936828202 & 9453929192, Fax: (0522) 2720185 Email- sugamko.sis@gmail.com



Training Report

- Training Camps:**
1. Parwatinagar- From 08th Aug. to 10th Aug. 2016.
 2. Bagbahara- From 11th Aug. to 13th Aug. 2016.

Contractor's construction work is ongoing in Villages of section-1 of stretch-2, Raipur to Titlagarh.

which resulted more responsibility of NGO in this field area. We have provided the Replacement cost of Structure for which assistance has been paid, to the project affected Persons. In the mean time we have organized the income restoration & skill up gradation training programme for the affected persons of the village Parwatinagar Chandinagar; at Public place Parwatinagar from 8.08.2016 to 10.08.2016. and for Mahasamund, Kantabagi at Public place bagbahra from 11.08.2016 to 13.08.2016.

The programme and place were scheduled and APs were informed for the schedule in advance by our field staff some days before. We have invited DGM and CPM of the PIU, Team Leader and R & R Expert of Supervision consultant also informed about the programme as well as local representatives of the concerned villages. supervision consultant R.K.Thakur attended the camp. Proper Training Materials were prepared along with stationery for the Trainees. The programmes were hosted by the Key Professional of the project.

In the camp first day registration and distribution of training materials and stationery was Distributed to eligible PAPs. We have invited all eligible PAPs to



attend the Training Program and verified them with our approved microplan and registered them in our attendance register. There were some old age PAPs who requested that their family member is the best eligible person to attend this skill upgradation camp on behalf of



them, we have allowed them to attend the camp. Training Program was organized at distance of 1km from affected village Parwatinagar, Chandinagar. Our Trainer Mr. Aslam Parvez, (Director, Data Perfumery works) introduced him self to impart training according to pre option of eligible PAPs. The PAPs, we have provided vehicles for their Facatey to attend training Programs. There was an introductory session about the training and aspects of utilization of skills and services of the trainings.

2nd day was scheduled for non agricultural and alternative livelihood skills training. Deputy General Managar S.Das and Supervision consultant Sh. R.K Thakur visited the training camp



and addressed to trainees and explained the need and utility of the Training Programs income restoration. Our Trainer Mr. Aslam Parvez, (Director, Data Perfumery works) supported with their team of one Assistants imparted training.



All the trainees were introduced about the making of candle, artistic Candle, Agarbati Rolling, perfumery and pain Balm making in phase. They introduced the subject of 1st candle making and artistic candle,



and performed candle making they were supported with varieties of dies for variation of candle's shape and structure, the trainees themselves made many type of candles. Some Mistakes were indentified and correct procedures were demonstrated. Their participation was very active and they learned the skills. They have been given details for purchase of Raw Materials and Places for procurement. They were told if they work in groups, production could be higher and they will be in position to bargain for the rates of sale.



3th day was scheduled for non agricultural and alternative livelihood skills training; trainer Mr. Aslam Parvez, (Director, Data Perfumery works) supported with their team of one Assistants talked about skills for washing powder, Fenyal making at home with use of




some chemicals which are normally available in local market. Trainees themselves mixed the chemicals

and noted the formula and quantities in provided notebooks .women trainees were much interested in these process and they have various questions regarding availability of materials and process which were answered by trainers same proceedings were



repeted in demonstration of making of toilet cleaner and Fenyal. In the course of the training they were given details of Backward and Forward linkages for adoption of their activities also.

Almost all the trainers talked about improvement and up gradation of income levels of present status. All the trainers talked about the rail as become to improved communication and improving the reach to market. after training Programs PAPs including women learnt about the linkage of business interprises to improve their income.



Anil kumar

Project Co-ordinator
Sugam International Sansthan

Annexure II: R&R training report of Sambalpur-Titlagarh**B-109 VIBHUTI KHAND, GOMTI NAGAR,**

Lucknow – 226 010 (UP)

☎: +91 9936828202 & 9453929192, Fax: (0522) 2720185 Email- sugamko.sis@gmail.com

SIS/HQ/RVNL/RP-TIT-SBP/2016/115**the 05/09/2016.**

To,

The Chief Project Manager
 Rail Vikas Nigam Limited
 Project Implementation Unit
 Waltaire Vishakhapatnam (A.P)

Sub: The Implementation of Resettlement Plan in Raipur-Titlagarh Doubling Rail Line Project State of Chhattisgarh And Orissa, Sambhalpur-Titlagarh Doubling Rail Line Subproject State of Orissa. **Training Programme for Non Title Holder Families .**

Sir,

In reference to above mentioned subject, it is submitted that we have organized Income Restoration and skill up gradation training program for the affected persons of the village Khetajpur, Guhratikra, Balageer From 27.08.2016 to 29.08.2016, as per approved Microplan.

We have completed Training Programme Successfully. Total 14 out of 12 PAPs of these villages have imparted in Training camp. The report has been prepared and is being submitted for your kind perusal and suggestions to improve the forthcoming training camps.

Thanking you !

Yours faithfully

Anil Kr
 Authorized Representative
 Sugam International Consultant
 (Anil Kumar)

Encl. Training Report (Pages 4)

Project Coordinator

Copy to: Sh. Sudesh Kaul (GC) R&R Expert Egis india Pvt Ltd, for kind perusal and suggestions please.

SUGAM INTERNATIONAL SANSTHAN**B-109 VIBHUTI KHAND, GOMTI NAGAR,**

Lucknow – 226 010 (UP)

☎: +91 9936828202 & 9453929192, Fax : (0522) 2720185 Email- sugamlko.sis@gmail.com

**Training Report****Training Camps: 1. Balageer From 27th Aug. to 29th Aug. 2016.**

Contractor's construction work is ongoing in Villages of stretch-2, Raipur to Titlagarh -Sambalpur which resulted more responsibility of NGO in this field area. We have provided the Replacement cost of Structure for which assistance has been paid, to the project affected Persons. In the mean time we have organized the income restoration & skill up gradation training programme for the affected persons of the village Khetrajpur, Balageer, Guhratikra, at Public place Balageer from 27.08.2016 to 29.08.2016.

The programme and place were scheduled and APs were informed for the schedule in advance by our field staff some days before. We have invited DGM and CPM of the PIU, Team Leader and R & R Expert of Supervision consultant also informed about the programme as well as local representatives of the concerned villages. Proper Training Materials were prepared along with stationery for the Trainees. The programmes were hosted by the Key Professional of the project.

In the camp first day registration and distribution of training materials and stationery was Distributed to eligible PAPs. We have invited all eligible PAPs to attend the Training Program and verified them with our approved microplan and registered them in our attendance register. There were some old age PAPs who requested that their family member is the best eligible



person to attend this skill upgradation camp on behalf of them, we have allowed them to attend the camp. Training Program was organized at distance of km from affected village Khetrajpur, Balageer, Guhratikra. Our Trainer Mr. Pappu Dubey, (Director, Data Perfumery works) introduced him self to impart training according to pre option of eligible PAPs. The PAPs, we have provided vehicles for their Facatey to attend training Programs. There was an introductory session about the training and aspects of utilization of skills and services of the trainings.



2nd day was scheduled for non agricultural and alternative livelihood skills training and addressed to trainees and explained the need and utility of the Training Programs income restoration. Our Trainer Mr. Pappu Dubey, (Director, Data Perfumery works) supported with their team of one Assistants imparted training.



All the trainees were introduced about the making of candle, artistic Candle, Agarbati Rolling, perfumery and pain Balm making in phase. They introduced the subject of 1st candle making and artistic candle, and performed candle making they were supported with verities of dies for variation of candle's shape and structure, the trainees themselves made many type of candles. Some



Mistakes were identified and correct procedures were demonstrated. Their participation was very active and they learned the skills. They have been given details for purchase of Raw Materials and Places for procurement. They were told if they work in groups, production could be higher and they will be in position to bargain for the rates of sale.


3th day was scheduled for non agricultural and alternative livelihood skills training; trainer Mr. Pappu Dubey, (Director, Data Perfumery works) supported with their team of one Assistants talked about skills for washing powder,



Fenyl making at home with use of some chemicals which are normally available in local market. Trainees themselves mixed the chemicals and noted the formula and quantities in provided notebooks. Women trainees were much interested in these process and they have various questions regarding availability of materials and process which were answered by trainers. Same proceedings were repeated in demonstration of making of toilet cleaner and Fenyl. In the course of the training they were given details of Backward and Forward linkages for adoption of their activities also.



Almost all the trainers talked about improvement and up gradation of income levels of present status. All the trainers talked about the rail as become to improved communication and improving the reach to market. after training Programs PAPs including women learnt about the linkage of business enterprises to improve their income.




(Anil Kumar)

(Project Coordinator)

Sugam International Sansthan

Annexure III: Letter from South Western Railway regarding direct purchase

SOUTH WESTERN RAILWAY



Office of the,
 Deputy Chief Engineer,
 Construction / PP
 Hubli

No. _____ **Date:** 04-06-2016

To
The District Commissioner
Koppal District,
Koppal

Sub : Hospet-Tinaighat Rail Doubling Project: **Acquiring of Land under Direct Purchase - Reg**

Ref : REV/LAQ/107/Comp No:19817/2015-16 dated 17.02.2016 (Copy enclosed)

Vide above referred letter from your office, it was advised to communicate willingness for direct purchase of left over land. As such, now Railway board has communicated its consent to opt for direct purchase of left over land, required for doubling project.

In view of the above the minimum requirement of land is again reviewed critically out of the balance left over land for acquisition, which was applied earlier vide letter No. DCE/CN/PP/HPT-TGT/D/RVNL/175 dated 14.08.2012 (copy enclosed).

Accordingly the village wise details of land required to be acquired urgently are as under:

Sl. No.	Name of the village	Survey Number (Hissa No)	Extent of land required	
			Acres	Guntas
1	Kampasagar	190	00	28
		Total of (1)	00	28
2	Munirabad	63	00	22
		Total of (2)	00	22
3	Hosahalli	59 (1)	00	11
		59 (2)	00	12
		Total of (3)	00	23
4	Koppal	1 (2)	00	14
		1 (3)	00	16
		735 (3)	00	09
		682	00	17
		Girini	02	36
		Total of (4)	04	12
5	Bhanapur	9 (2)	0	08
		10	0	04
		6	00	18
		8 (2)	00	12
		Total of (5)	01	02
6	Sompur	82	0	07
		83	0	24
		Total of (6)	00	31
		Total (1+2+3+4+5+6)	07	38

M.V.

Relevant ROR and land plans are enclosed herewith alongwith detailed statement of land requirement.

Revenue plans are also enclosed for your ready reference.

You are requested to arrange for direct purchase of the land of about 07 Acres 38 Guntas, at an earliest duly conducting joint measurement survey.

Thanking You

Yours Sincerely

M.V. 08/06/2016
Deputy Chief Engineer
Construction/PP/Hubballi

Encl: As above (03 sets of proposal for LA).

Copy to: 1) AC/Koppal: for kind information & necessary action please
2) ADC/Koppal: for kind information & necessary action please
3) CE/CN/South/BNC: for kind information
4) CPM/RVNL/Bangalore: for kind information

Annexure IV: R&R photographs taken during training at RVNL, Hubli



Annexure V: R&R photographs taken at Raipur during field visit in May 2016



Annexure VI: R&R photographs during field visit at Raipur-Titlagarh in August 2016







Annexure VII: R&R photographs during field visit at Sambalpur-Titlagarh in September 2016



