

Social Monitoring Report

Bi-annual Social Monitoring Report
January 2017

PAK: MFF – Power Distribution Enhancement Investment Program (Tranche 2)

Prepared by Hyderabad Electric Supply Company, Sindh for the Asian Development Bank.

NOTES

- (i) The fiscal year (FY) of the Government of the Islamic Republic of Pakistan and its agencies ends on 30 June.
- (ii) In this report “\$” refer to US dollars.

This social monitoring report is a document of the Borrower. The views expressed herein do not necessarily represent those of ADB's Board of Directors, Management, or staff, and may be preliminary in nature.

In preparing any country program or strategy, financing any project, or by making any designation of or reference to a particular territory or geographic area in this document, the Asian Development Bank does not intend to make any judgments as to the legal or other status of any territory or area.



Re: Fw: Loans 2727-PAK/2972-PAK: PDEIP, Tranches 2 and 3- HESCO's Bi-Annual Social Monitoring Reports and Bi-Annual Environment Monitoring Reports

Jose Tiburcio Nicolas to: Liaqat Ali

17/01/2017 10:15 PM

Cc: Ehtesham Z. Khattak, Safia Shafiq, Zhang Lei, Muhammad Zeeshan, Ashfaq Khokhar

Dear Liaqat sb,

Thanks for sharing the bi-annual social monitoring report (July-December 2016) submitted by HESCO for T2 and T3. I have reviewed both documents and endorse their acceptance and uploading on the ADB website for disclosure. Please advise us when these have been disclosed so we can reflect in our records.

I noted that for T3, regular site visits are being conducted, orientation on safeguards requirements to contractors are being made and restoration works for completed subprojects are being monitored. Efforts are also being made to ensure timely payment of compensation. For T2, most works and compensation have been completed, except for the Shikarpur-Larkana TL.

Please remind HESCO to continue close coordination and regular communication with the DPs (particularly the complainant in one of the subproject) is maintained to reduce risk of escalating complaints. Remind them too on the importance of expediting the compensation payments for Shikarpur-Larkana TL where civil works have been completed.

Regards,

Tito S. Nicolas

Senior Social Development Specialist (Safeguards)
Pakistan Resident Mission
North Wing Level 8, Serena Office Complex
Khayaban-e-Suhrawardy, G-5, Islamabad, Pakistan
email: jnicolas@adb.org
+92 51 2600351-69/ 208 7300 ext 219
+92 305 9419662 (mobile)



Liaqat Ali

Dear Safia/Tito: Please review your respective a...

13/01/2017 04:23:39 PM

From: Liaqat Ali/PRM/ADB
To: Safia Shafiq/Consultants/ADB@ADB, Jose Tiburcio Nicolas/CWRD/ADB@ADB
Cc: Zhang Lei/CWRD/ADB@ADB, Ehtesham Z. Khattak/PRM/ADB@ADB
Date: 13/01/2017 04:23 PM
Subject: Fw: Loans 2727-PAK/2972-PAK: PDEIP, Tranches 2 and 3- HESCO's Bi-Annual Social Monitoring Reports and Bi-Annual Environment Monitoring Reports

Dear Safia/Tito:

Please review your respective area monitoring reports and provide your comments, if any and/or clearance for disclosure of the

Regards,

Liaqat Ali, Project Analyst, Pakistan Resident Mission

Level 8, North, Serena Office Complex, G-5, Islamabad/Pakistan
Tele: (92-51) 2600351-69/2087210 Fax: (92-51) 2600365-66/2087397-98
email: lali@adb.org.

----- Forwarded by Liaqat Ali/PRM/ADB on 13/01/2017 04:21 PM -----

From: "Chief Engineer (Dev) HESCO PMU" <cedevhesco@gmail.com>
To: lali@adb.org
Date: 13/01/2017 04:19 PM
Subject: Re: Loans 2727-PAK/2972-PAK/3096-PAK: PDEIP, Tranches 2, 3 and 4 - Submission of Bi-Annual Social Monitoring Reports and Bi-Annual Environment Monitoring Reports

Dear Mr. Liaqat Ali,
Enclosed please find Bi-Annual Environmental and Social Monitoring Reports under ADB Tranche-II & III in respect of HESCO for the period from July 2016 to Dec 2016 for review.

Regards

**Chief Engineer (Dev),
PMU,HESCO, Hyderabad**

On Tue, Jan 3, 2017 at 3:00 AM, <lali@adb.org> wrote:

Dear Chief Engineers:

Please urgently, but not later than 15 January 2017 submit the bi-annual social monitoring and bi-annual environment monitoring reports covering the period 1 July 2016 to 31 December 2016 for the above tranches for our review and comments. The reports should cover the comments sent to your staff on time to time basis.

Regards,

Liaqat Ali, Project Analyst, Pakistan Resident Mission
Level 8, North, Serena Office Complex, G-5, Islamabad/Pakistan
Tele: (92-51) 2600351-69/2087210 Fax: (92-51) 2600365-66/2087397-98
email: lali@adb.org.



Bi-annual Environment Tranche 2(July-Dec) 2016.pdfBi-annual Environment Tranche 3 (July-Dec 2016).pdf



Tranche III-Bi-annual Social Monitoring Report(July-Dec 2016).pdf



Tr-II Bi-annual Social Monitoring Report(JULY-DEC 2016).pdf

HYDERABAD ELECTRIC SUPPLY COMPANY (HESCO)



SOCIAL SAFEGUARD MONITORING REPORT

For the Period: July - Dec, 2016

Project Number: 2727 – PK, Tranche – II
[July – Dec 2016]

Islamic Republic of Pakistan

Power Distribution Enhancement Investment Project
(PDEIP) – Tranche – II

Multi – Tranche Financing Facility (MFF)

Financed by the ASIAN DEVELOPMENT BANK

Prepared By:

(Mr. Asif Sheeraz / Mr. Sulman)

Environment & Social Safeguards Section – Project Management Unit

Office of the Chief Engineer (Development)

HYDERABAD ELECTRIC SUPPLY COMPANY (HESCO),

Bungalow No.A-1 HESCO Power Wing Colony

Hussainabad Hyderabad.

Ph. No. 022-9260070

Fax No.022-9260 525

E-mail: cedevhesco@gmail.com

www.hesco.gov.pk

TABLE OF CONTENTS

Abbreviations	4
1. Introduction of the Company.....	5
1.1. About Project Management Unit (PMU)	5
2. Brief Detail of the Project	5
2.1- Objectives of the Project.....	6
2.2- Scope Of Work.....	6
3. Findings/ Observations of visited Project Sites	7
3.1 New 132kV Jacobabad-II Grid Station Site and Transmission Line	7
3.2 Conversion of 66 kV to 132 kV Sukkur Grid Station and Allied Transmission Line	7
3.3 Conversion of 66 kV to 132 kV Larkana Grid Station and Allied Transmission Line	7
3.4 Conversion of 66 kV to 132 kV Talhar Grid Station and allied Transmission Line	8
3.5 Second circuit Stringing of 132 kV T/L Shikarpur - Larkana	8
3.6 Second circuit Stringing of 132 kV Sanghar-Kandiari- MirpurKhas T/L.....	8
3.7 Construction of Dadu-Meher-Larkana 132kV DC T/L (New) Transmission Line.....	9
4. Compensation Status.....	10
5. Social Safeguard Work Status.....	12
6- Social Safeguard Awareness and Training.....	12
7- Site restoration Of completed Sub-Projects	13
8- Conclusion	13
Annexure A : Reporting to the E&SS by the Contractor.....	14
Annexure B: Land acquisition documents of Jacobabad II Grid Station.	15
Annexure C: Compensation Payments: Details of feed for Talhar Grid Station	25
Annexure D: Compensation Payments Details of 132 kV Arain Road- Sukkur City Transmission Line.	28

Annexure E: Compensation Payments Details of 132 kV Dadu-Mehar-Larkana Transmission Line.	29
Annexure F : Grievance Redressal Mechanism.....	34
Annexure G: Grievance Redressal Committee	35
Annexure H : Consultation Pictures	36

ABBREVIATIONS

ADB	Asian Development Bank
AH	Affected Household
APs	Affected Persons
EMP	Environmental Management Plan
ESM	Environmental & Social Monitor
E&SS	Environment & Social Safeguard
GoP	Government of Pakistan
GSC	Grid System Construction
HESCO	Hyderabad Electric Supply Company
km	Kilometer
kV	Kilo-Volt
LARP	Land Acquisition and Resettlement Plan
MFF	Multi-Tranche Financing Facility
PEPCO	Pakistan Electric Power Company
PMU	Project Management Unit
RoW	Right of Way
SEPCO	Sukkur Electric Power Company
T/L	Transmission Line

INTRODUCTION OF THE COMPANY

Hyderabad Electric Supply Company Limited; HESCO is a Public Limited Utility Company, established in 1998 under Companies Ordinance 1984 responsible for distribution of Electric Power within its territorial jurisdiction and presently serving around 0.9 Million customers (Domestic, Commercial, Agricultural, Industrial and others) in twelve Districts of Sindh Province.

1.1. ABOUT PROJECT MANAGEMENT UNIT (PMU)

To effectively plan, execute and monitor the Power Distribution Enhancement Investment Program (Tranche II), a Project Management Unit (PMU) has been established under Chief Engineer (Development) comprising of five sections i.e. Planning, Scheduling & Coordination, Procurement, Finance and Environment & Social Safeguard along with the Project Director (GSC) for physical execution of grid stations and transmission lines.

2. BRIEF DETAIL OF THE PROJECT

Existing conditions of the HESCO power distribution and transmission system are inadequate to meet rapidly growing demand for electrical power. To cope with this situation, the existing power infrastructure has to be improved and upgraded. The overall contribution of power infrastructure requires institutional arrangements, capacity building that support strategic management of the sector, planning and management of investments.

The **basic information/ data about the loan** are here as under:-

Loan Number: (ADB TA Loan No. 2727-PAK)

Project Title:- Power Distribution Enhancement Investment Program,
Multi-Tranche Financing Facility PDEPMFF-Tranche-II

Borrower:- GOP/ HESCO

Executing Agency:- PEPCO

Implementing Agency:- HESCO

Location of the Project:- The Sub-Projects under Tranche-II are in Sanghar, Mirpurkhas, Shikarpur, Larkana, Sukkur, Badin, Dadu and Jacobabad Districts of Sindh Province.

2.1-OBJECTIVES OF THE PROJECT

HESCO through GoP has undergone a Project Financing agreement with Asian Development Bank for:

1. Strengthening the capacity of Power Distribution and Transmission networks.
2. To meet the increasing electricity demand in the selected areas more efficiently.
3. To upgrade the existing power infrastructure.

2.2-SCOPE OF WORK

There are 7 Nos. of projects under ADB Tranche-II. Detail is as under:

1. Construction of 01 No. of New 132 kV Grid Station and allied Transmission Line.
2. Conversion of 03 Nos. of Grid Substations from 66kV to 132kV and allied Transmission Line
3. Second Circuit stringing of 02 Nos. 132 kV Transmission Lines
4. Construction of 01 No. 132 kV Transmission Line

Overall the proposed MFF has been designed to address both investment and institutional aspects in electric power sector. Development objectives / project purpose will be fully achieved after completion of the proposed Sub-projects.

3. FINDINGS/ OBSERVATIONS OF VISITED PROJECT SITES

Findings/ Observations noted during the site visit. Its details are as follows:

3.1 NEW 132KV JACOBABAD-II GRID STATION SITE AND TRANSMISSION LINE

- The Sub-project is 100 % complete and energized in the month of September 2014.
- HESCO had purchased 8.3 acres of land from one landowner on voluntary sale basis against negotiated price for construction of new grid station. The purchase land was an empty dry patch for no constructive use since 6 years therefore no social impacts were associated with the construction of grid station. (Sale Deed attached in Annexure B).
- However, there were some potential social impacts associated with the construction of transmission line that passed through private farmland affecting crops. The compensation payment of foundation and stringing work was paid to all the affectees.
- There were no complaints received.

3.2 CONVERSION OF 66 KV TO 132 KV SUKKUR GRID STATION AND ALLIED TRANSMISSION LINE

- The sub-project is 100 % complete and energized in the month of August 2014.
- The conversion works were carried out totally within the boundary of the existing grid station without acquiring additional land so there was no potential social impact associated with this part of the subproject.
- The Transmission line consisted of 12 towers and 30 poles. Out of total 12 towers 8 towers are in private farmland. The compensation for all the foundation and stringing work for these towers has been paid. The details are given in chapter 4 and Annexure D.
- There were no complaints received.

3.3 CONVERSION OF 66 KV TO 132 KV LARKANA GRID STATION AND ALLIED TRANSMISSION LINE

- The sub-project is 100 % complete and energized in the month of September 2014.
- The Grid station work was totally inside the existing grid land so no social issues were arisen.
- The transmission line consisted of 12 poles and 3 towers.
- The complete compensation payment has been paid in January 2015.
- There were no complaints received.

3.4 CONVERSION OF 66 KV TO 132 KV TALHAR GRID STATION AND ALLIED TRANSMISSION LINE

- The sub-project was energized in August 2014.
- The conversion work was carried out totally within the boundary of the existing grid station without acquiring additional land so there was no any social issue associated with this aspect.
- The compensation payments for the crop damage during the transmission line work were paid on time. (Annexure C)
- Overall the sub-project area community is satisfied by the benefits of this activity and there were no complaints received.

3.5 SECOND CIRCUIT STRINGING OF 132 KV T/L SHIKARPUR - LARKANA

- The sub-project is complete with stringing of 248 towers.
- The compensation payment is in process with the scrutiny of revenue record.
- Overall the load management situation has improved in the area and the community is over it.

3.6 SECOND CIRCUIT STRINGING OF 132 KV SANGHAR-KANDIARI-MIRPURKHAS T/L

- The sub-project is complete with stringing of 220 towers.
- The compensation payment is complete without any complaint.
- Public consultation meeting was carried out with general public, adjacent community at the Mirpurkhas Grid station and they gave positive views.

3.7 CONSTRUCTION OF DADU-MEHAR-LARKANA 132KV DC T/L (NEW) TRANSMISSION LINE

- The foundation work of 362 towers and 79 erection of towers has been completed and the compensation payments of 52 foundations have been paid.
- Training of the social and environmental aspects is being regularly conducted to the contractor's staff through meetings.
- Complaint registers have been placed at the project sites and community has been informed about it along-with Public information brochure. There is delay in compensation payment but in this month new cheques have been issued which will be disbursed shortly. (Annexure E)
- For the delay in the compensation payment Project Director (GSC), SEPCO has been regularly informed through continuous verbal and oral correspondence to make compensation payments on time.

4. COMPENSATION STATUS

LARP(s) Status TRANCHE-II Till Dec 2016										
Sr. No.	Sub Project No.	Sub Project Name	LARP Survey Period / Cut-off Date	Original LARP Submission	Revised LARP Submission	Revised LARP approved by ADB	Compensation Status			Remarks
							Foundation Stage	Erection Stage	Stringing Stage	
1	H-1	Conversion of 66KV Sukkur GS into 132KV along with Transmission Line	April, 2013	26/11/2009	30/04/2013		Done	N/A	Done	Foundation and stringing payments have been paid to all the affected household.
2	H-2	Conversion of 66KV Larkana GS into 132KV along with Transmission Line	May, 2013	14/12/2009	13/05/2013	May, 2013	Done	N/A	Done	Foundation and stringing payments has been paid to all the affected household.

3	H-3	Conversion of 66KV Talhar GS into 132KV along with Transmission Line	Feb, 2013	15/12/2009	25/04/2013		Done	N/A	Done	Foundation and stringing payments has been paid to all the effected household.
4	H-5	New Jacobabad GS along with TL	June, 2013	25/07/2013	N/A	August, 2013	Done	N/A	Done	Having total 5 towers on private farm land. Foundation and erection work completed. Compensation has been paid to all the affected household.
5	H-6	Second circuit Stringing of Sanghar-Kandiari-Mirpur Khas 132KV T/L	April, 2013	15/12/2009	28/06/2013		N/A	N/A	Done	Civil works have been completed and compensation is payments are also complete.
6	H-7	Second circuit Stringing of Shikarpur-Larkana 132KV T/L	May, 2013	15/12/2009	30/05/2013		0	0	0	Civil works have been complete and compensation is about to be started
7	H-8	Construction of Larkana-Mehar-Dadu 132KV DC T/L (New)	Sep, 2014	15/12/2009	24/09/2014	October, 2014	52 affectees paid	0	0	Foundation work of 362 towers have been completed and erection of 79 towers completed.

5. SOCIAL SAFEGUARD WORK STATUS

Land Acquisition and Resettlement Plans (LARP):

(i) All LARPs and DDR Reports in respect of HESCO sub-projects under Tranche-II (both in English & Urdu versions) have been translated, typed/edited and uploaded/ displayed on HESCO official websites. (www.hesco.gov.pk) and at each sub-project site.

(ii) All the LARPs of subprojects had been revised/updated on actual basis for Tranche-II and the same were submitted to the Asian Development Bank for review.

(iii) Regular meetings with ESM of Dadu-Mehar-Larkana were held to reach out to the problems at site and fortnightly monitoring sheets were required from him (Annexure A).

(iv) Urdu version of Environmental Management Plan (EMP) after translation was provided to the Contractors and placed at each grid site during construction work and available at HESCO Website.

(v) Environmental & Social Complaint Register is made available on each active project site to record complaints of affected household / persons at each project site. All the complaints received are of late compensation payments and the same has been regularly apprised to the SEPCO authorities in written form and they have started issuing new cheques.

(vi) Grievance redressal committee has been constituted and documented procedure for grievance redressal is functional (Annexure G).

SOCIAL SAFEGUARD AWARENESS AND TRAINING.

On site/ on job trainings were arranged at the on the active site i-e Dadu-Maher-Larkana Transmission line sub-project regarding environmental issues, social issues, housekeeping, communicable diseases especially Dengue, Malaria, Airborne, Waterborne diseases & drugs, defensive driving, site restoration after the work and overall implementation of the Land Acquisition and Resettlement Plan (LARP) of the Tranche-II sub-projects. (Annexure H)

7- SITE RESTORATION OF COMPLETED SUB-PROJECTS

The completed sub-project sites have been visited to monitor site restoration. It was observed that all the completed sites have been restored. It was observed that as earlier communicated to the locals, they have used the land under the tower for agriculture purpose and do not have any issue with the restoration work. Pictures and statements at (Annexure H)

8- CONCLUSION

The main is the timely payment of the compensation to the affectees of the project and we are in continuous touch with SEPCO to make it faster. As of Dec 2016, HESCO has completed compensation at Talhar Transmission Line sub-project, Larkana Transmission Line sub-project, Jacobabad transmission line sub-project Sanghar-Kandiari-Mirpurkhas 2nd stringing transmission line sub-project and Sukkur transmission line sub. The compensation payment of all the completed sub-projects is complete. The Shikarpur-Larkana second stringing of transmission line and Dadu-Maher-Larkana transmission line compensation is in process. The Project Director SEPCO is asked to expedite the payment procedure.

ANNEXURE A : REPORTING TO THE E&SS BY THE CONTRACTOR.**Social Monitoring check list for contractors.**Project title: Construction 132 kv TL Larkana-Mehar-Dadu Date: 31/12/2016Project location: Larkana-Mehar Lot-11Name of contractor: Construction & Project Management Services**Questions**

1-Was the community informed about the detailed events during the construction of grid station/transmission line?

✓
Yes

No

2-How was the community informed?

By consultation and meetings

3-Is the Grievance Redressal Mechanism distributed in the community and pasted at the sub-project site?

Yes

4-Is there any document available at the Project Site showing the overall scope of work like LARP and LARF?

Yes

5- How many Towers have been laid the foundation, erected and stringing completed?

FOUNDATION

ERECTION

STRINGING

363

79

6-Is the compensation payment started to the affected Household (tower affected)?

If yes then how many tower affectees have been paid?

Yes 52, While new**cheques have also been issued.**

7-Is the labor instructed to keep the local norms and traditions while entering villages and other community places?

Yes

8-Did the Sub-project involve community labour or hired labour from outside?

Yes9-Was child labour involved? **No**10-Additional comments (if any)? **No any**

ANNEXURE B: LAND ACQUISITION DOCUMENTS OF JACOBABAD II GRID STATION.

PAKISTAN Register No. 803 10,000 RS.

TEN THOUSAND RUPEES

25 17.11.2009
Abdul Malik 8/6 Mehay Ali Jamali
J.C.D. 1,45,700/-
Shafiqur Rehman

Note Urgent fee Rs. 400/-
four hundred only recovered
side receipt No. Dated

Note Urgent fee Rs. 400/-
four hundred only recovered
side receipt No. 115. Dated 23/11/09

B. No. 871
Presented in the Office of
the Sub-Registrar Jacobabad
on 23.11.2009 between
the hours of 3.30-3.45

Received Fees as under
Registration fee 48500/-
Copying fee 200/-
Instrument fee 5/-
Stamping fee 5/-
Total 48805/-


Zafar Ali Bhatti
Sub-Registrar, Jacobabad

Zafar Ali Bhatti
Sub-Registrar, Jacobabad

SALE DEED

THIS INDENTURE made on this 23rd day of December 2009
between Amriddin s/o Ali Nawaz Golato, adult, muslim, CNIC No. 43102-6790839-
D, resident of Goth Ali Nawaz Khan Golato, Taluka and District Jacobabad. Hereinafter
together with his heirs, successors-in-interest and assigns, where the context so required
called the VENDOR of the one part A. S. D.

Contd. ... On p.02



02 -

A N D

HYDERABAD ELECTRIC SUPPLY COMPANY (HESCO)


Hyderabad through Mr. Abdul Malik Jamali s/o Mehdi Ali Jamali, (CNIC No- 45403-9690740-3) Executive Engineer, Civil Construction Division (GSC) HESCO Hyderabad, hereinafter called the 'VENDEE' of the other part.

Contd., on p. 3

[Handwritten signature]

[Handwritten signature]

[Handwritten signature]



25 17.11.2009
 Abdul Malik s/o Mehar Ali Jamali
 JCD 1,45,700/-
 Shafiqur-Rehman

- 03 -


WHEREAS the Vendor is the sole and exclusive owner of the property
 viz: agricultural land bearing revenue Survey No. 158 total measuring 09 acres and 02
 ghuntas situated in Delh Michabpur Taluka and District Jacobabad, out of which the
 Vendor hereby convey 08 acres and 12 ghuntas to Hyderabad Electric Supply Company
 Hyderabad, in full share thereinafter referred to as the "SAID LAND").

[Handwritten signature]

[Handwritten signature]

Contd. On p - 04

[Handwritten signature]




Handwritten text in Urdu, likely a title or description of the structure shown in the photograph above.

Handwritten text in Urdu, likely a title or description of the structure shown in the photograph above.

Handwritten text in Urdu, likely a description or report related to the structure shown in the photograph above.


Handwritten text in Urdu, likely a signature or date at the end of the document.



28. 1908.
 29. 1908.
 30. 1908.

$$\frac{\partial}{\partial t} \left(\frac{1}{2} \rho v^2 \right) + \nabla \cdot (\rho v \otimes v) = -\nabla \cdot (\rho v \otimes u) + \nabla \cdot (\rho u \otimes v) + \nabla \cdot (\rho u \otimes u) + \nabla \cdot (\rho v \otimes v)$$

— 10 —



- 06 -


and assigns unto the Vendor, all that piece or parcel of land 08 acres and 17 ghasa, a land out of revenue Survey Nos. 158, situated in Teh. Mehrobpur, Taluka and District Jacobabad, and more particularly described or delineated in the map or plan hereto annexed, together with all trees, plants, liberties, privileges, easements and appurtenances whatsoever to the same, belonging or in any way appertaining to and all the estate, right, title, claim or demand, of the Vendor and to and every part thereof **TO HAVE AND TO HOLD** the same unto and to the absolute use and benefit of the Vendee and his successors and assigns in full proprietary right free from all encumbrances **FOREVER**

[Handwritten signature]

[Handwritten signature]

Contd. on p. 107

[Handwritten signature]



25 17.11.2007
 Abdul Malik S/o M. Ghazal Ali
 JCO 1,45,700/-
 Asst. Sub-Registrar

- 07 -


2. AND the Vendor hereby covenant with the Vendee that he has good right title and power to sell and convey the same to the Vendee, in manner aforesaid, free from encumbrances and dispute of any nature and that the Vendee may at all times hereafter peaceably and quietly possess and enjoy the same without any interruption, claim or demand from or by the Vendor or any person or persons lawfully or equitably claiming for or under him AND that the Vendor shall whenever reasonably so required execute and do any such further act, assurance or things as may be deemed necessary by the Vendee

[Signature]

Contd. on p. 08

[Signature]

[Handwritten notes]



08 -


3. THAT it is also agreed by the Vendor that the boundaries of said land shall be restricted according to the convenience of Vendee as per survey measurements demarcation carried out by Director of Settlements, Survey & Land Records Sindh Hyderabad / Survey Superintendent Farkana, alongwith representative of Vendee Executive Engineer, Civil Construction Division (GSC) HESCO Hyderabad. In case any dispute arises as to the ownership of said land or any part thereof, the Vendor shall be solely responsible to immediately make all the consequent losses good to the Vendee.

Contd. ... On p. 09

[Handwritten signature]

[Handwritten signature]

[Handwritten text: 13.01.2010]



25 17.11.2009
 Abdul Wahid So. M. Ali, Jamali
 T. 00 1-45, 7000
 Sub-Registrar, Jacobabad

- 01 -

4. THAT the Vendor further hereby covenants with the purchaser that the property under sale is free from all the charges and encumbrances of whatsoever nature and is not sold out, mortgaged, exchanged or gifted to any one prior to this. If any time found to be incorrect the Vendor shall be responsible for the same.

5. THAT the Vendor has today viz. 23.12.2009 handed over vacant physical possession of said land at site to Mr. Shafiq-Ul-Rehman Donkai, Sub-Divisional Officer (Civil) GSC HESCO Sukkur, official representative of the Vendor.

Contd. on p. 10

[Signature]


[Signature]

[Signature]

PAKISTAN

Register No: 505

10,000 RS.



25 17.4.2007
 Abdul Malik & Nihar Ali Jamali
 S.O. D. 1st Floor
 Shaheed R. Park

6. THAT the Vendee shall bear all the expenses pertaining to the execution of this Sale-Deed and mutation of said land in the revenue record in favour of HESCO Hyderabad.

7. THAT the said land property is situated within the jurisdiction of Sub-District and District Registration Jacobabad.

RE

ABDUL MALIK JAMALI

Executive Engineer

Civil Construction Division (GSC) HESCO (HYD).

V E N D E E

CAMIRUDDIN S/O ALI NAWAZ GOLATO

CNIC NO. 43192-6790539-1

V E N D O R

WITNESSES:

ANNEXURE C: COMPENSATION PAYMENTS: DETAILS OF FEED FOR TALHAR GRID STATION**HESCO HYDERABAD ELECTRIC SUPPLY COMPANY**PHONE NO. 0223886552
FAX NO. 0223886471OFFICE OF THE PROJECT DIRECTOR
GSC HESCO C-9 NTPS COLONY
T.M.KHAN ROAD HYDERABAD

NO. PD/GSC/HESCO/HYD

DATED: 24-07-2013

OFFICE ORDER.

As per Clause 15.18 of Section-XV of Book of Financial power (Revised 2007 of NTDC) regarding payment of crops compensation the effective land owner (an individual basis) the sanction is hereby accorded for crops compensation of Concrete work for 132KV Feed Far Talhar T/Line, prepared & submitted by XEN T/L © Division GSC HESCO Hyderabad vide his letter No. 1518-19 dated 19-07-2013.

Sr. No.	Name & Fathers's Name Of Land Owner with NIC No.	T/No. S/No.	Name affected area in Ghunta.	Rate of crop per Ghunta.	Crop wise compensation.	Total Amount (Rs.)
1	Ahsan Ali Jatal S/o Muhammad Hashim Jatal NIC No. 41105-7721296-1	TNa.01	Sugarcan-08	4800/-	38400/-	38400/-
2	Mola Bux Khawaja S/o Bhale Dino Khawaja NIC No. 41105-5297881-5	TNo.02	Sugarcan-07	4800/-	33600/-	33600/-
3	Mola Bux Khawaja S/o Bhale Dino Khawaja NIC No. 41105-5297881-5	TNa.03	Sugarcan-08	4800/-	38400/-	38400/-
4	Nizar Ali S/o Faiz Muhammad Khawaja NIC No. 41105-9185884-3	TNo.04	Sugarcan-08	4800/-	38400/-	38400/-
5	Nizar Ali Khawaja S/o Nawaz Ali Khawaja NIC No. 41105-8290014-1	TNo.04 (Passage)	Sugarcan-05	4800/-	24000/-	24000/-
6	Mst Shahnaz D/o Allah Dino Khawaja NIC No. 41105-8674676-0	TNa.05	Sugarcan-08	4800/-	38400/-	38400/-

attached.

The rates supply by ALAO GSC HESCO Hyderabad, from Mukhtar Kar (Revenue) Talhar is

DA/

06 No. Crops Compensation Cases (In Original) along with relevant documents.

[Signature]
PROJECT DIRECTOR
GSC HESCO HYDERABAD

CC TO:

1. The General Manager (Dev) PMU HESCO Hyderabad.
2. The Project Manager PES (Pvt) Ltd HESCO Power Wing Colony Hyd.
3. The XEN T/L © Division GSC HESCO Hyderabad, w/r to his letter No. mentioned above, along with 06 Nos. original vouchers & allied relevant supporting documents.
4. The Assistant Manager (CA) GSC HESCO Hyderabad.
5. The A.L.A.O GSC HESCO Hyderabad.

CC-FP Talhar-24713 (A 3)

- 1 -

HESCO HYDERABAD ELECTRIC SUPPLY COMPANYOffice of the Project Director GSC HESCO
Water Wing Colony Hussainabad HyderabadEmail: pdgshescohyd@hoinmail.com

Phone No. 022-9260123

Fax No. 022-9260124

No. PD/GSC/HESCO/HYD/1322-30

Dated: 01/04/2014

OFFICE ORDER.

As per clause 15.18 of Section-XV, S.No-III of book of Financial power (Revised-2007 of NTDC) regarding payment of Crops Compensation the effectives land owner (on individual basis) the sanction is hereby accorded for Crops Compensation of Erection & Stringing work for 132KV Feed for Tallhar Transmission Line, prepared & submitted by XEN T-1 Division GSC HESCO Hyderabad, vide his letter No.979/80 Dated, 21.03.14.

S#	Name and Fathers Name of Land Owner with NIC No.	T/No. S/No.	Name affected area in Gunta	Rate of Crop per Gunta	Crop wise compensation	Total Amount RS:
1	Mr. Ahsan Ali Jatoi S O Muhammad Hashim Jatoi NIC NO:41105-7721296-1	01-F-S	Sugarcane-8	4800/-	38400/-	38400/-
2	Mr. Hassan Ali S O Inam Dino Laghari NIC NO:41105-2649855-1	1-2-S(P)	Sugarcane-5	4800/-	24000/-	24000/-
3	Mr. Azhar Hussain Khawaja S O Mola Bux Khawaja NIC NO:42000-3322713-9	2-F-S	Sugarcane-8	4800/-	38400/-	38400/-
4	Mr. Ayyaz Hussain S O Mola Bux Khawaja NIC NO:41303-3324348-7	2-3-S(P)	Sugarcane-4	4800/-	19200/-	19200/-
5	-do-	3-F(P)	Sugarcane-4	4800/-	19200/-	19200/-
6	Mr. Mazhar Hussain Khawaja S O Haji Mola Bux Khawaja NIC NO:41105-0247860-1	3-F-S	Sugarcane-7	4800/-	33600/-	33600/-
7	Aslam Hussain Khawaja S O Faiz Muhammad NIC NO:41105-7068545-1	3-4-S(P)	Sugarcane-6	4800/-	28800/-	28800/-
8	Mr. Nizar Ali S O Faiz Muhammad Khawaja NIC NO:41105-9185884-3	4-F-S	Sugarcane-8	4800/-	38400/-	38400/-
9	Mr. Nisar Ali Khawaja S O Nawaz Ali Khawaja NIC NO:41105-8290014-1	4 & 5-1(P)-S	Sugarcane-5	4800/-	24000/-	24000/-

9/04/2014

10	Mr. Deedar Ali S/O Allah Dino Khawaja NIC NO:41105-8196620-1	4-5-S(P)	Sugarcane-4	4800/-	19200/-	19200/-
11	Mst: Shalmaz D/O Allah Dino Khawaja NIC NO:41105-8674676-0	5-F-S	Sugarcane-8	4800/-	38400/-	38400/-

The rates supply by ALAO Qanoongo GSC HESCO Hyderabad, from Mukhtiarkar (Revenue) Talhar is attached.

DA/as above.

11 Nos Crops Compensation Cases
(In Original) along with relevant documents.


PROJECT DIRECTOR
GSC HESCO HYDERABAD
10/04/2014

C.C.TO:

- 1. The Chief Engineer (Dev) PMU HESCO Hyderabad.
2. The XEN T.E. Division GSC HESCO Hyd, w.r to his letter No.979-80 Dated 21.03.2014, along with 11-Nos original vouchers & allied relevant supporting documents
3. The Assistant Manager (C.A) GSC HESCO Hyderabad.
4. The A.L.A.O GSC HESCO Hyderabad.

ANNEXURE D: COMPENSATION PAYMENTS DETAILS OF 132 KV ARAIN ROAD-SUKKUR CITY TRANSMISSION LINE.

HYDERABAD ELECTRIC SUPPLY COMPANY
 Building No. A-1 HESCO Power Wires Colony
Delive to Mr. Asif Sherg Sb.

OFFICE OF THE PROJECT DIRECTOR GSC SEPCO SUKKUR
 NO. PD/GSC/SEPCO/SUK/1733-35 Dated: 10-7-2014

OFFICE ORDER
 In accordance with the instructions NO: 2 to the reference of financial power book for distribution companies (DSCs) of Jan-03 the sanction of the following is hereby accorded vide delegation of financial power (Revised 2007), Section XV, Sub Section 15-18 (NTDC), for payment of crop compensation to the affected land owner (On individual basis) Erection and Stringing work of 132KV T-Line Arain Road-Sukkur City, prepared process & submitted by the Executive Engineer T&G @ Division GSC SEPCO Sukkur vide his office letter No. XEN/T&G/GSC/SEPCO/SUK/3035-37, dated. 08.07.2014.

S. #	Name & Father's name of Land owner with N.C. No.	T. NO.	S. No.	Name of affected crop	Area in ghunta	Rate as per Ghunta	Crop wise compensation	Total Amount (Rs)
1.	Mr. Ghulam Mustafa S/O Muhammad Farid Bhutto 45504-0448726-9	2	2312	Vegetables	9	4000	36000	36000.00
2.	Mr. Ghulam Mustafa S/O Muhammad Farid Bhutto 45504-0448726-9	2	2313	Wheat	2	16000	32000	32000.00
3.	Mr. Ghulam Mustafa S/O Muhammad Farid Bhutto 45504-0448726-9	2	2314	Vegetables	10	4000	40000	40000.00
4.	Mr. Ghulam Mustafa S/O Muhammad Farid Bhutto 45504-0448726-9	2	2315	Vegetables	10	4000	40000	40000.00
5.	Mr. Ghulam Mustafa S/O Muhammad Farid Bhutto 45504-0448726-9	2	2316	Vegetables	9	4000	36000	36000.00
6.	Mr. Ghulam Mustafa S/O Muhammad Farid Bhutto 45504-0448726-9	2	2317	Vegetables	10	4000	40000	40000.00
7.	Mr. Abdull-Hafeez S/O Ghulam Mustafa Farid 45504-0310424-3	2	2318	Vegetables	8	4000	32000	32000.00

c.c.to:
 2. The Executive Engineer, T&G Division GSC SEPCO Sukkur.
 The Assistant Manager, (E&A) GSC SEPCO Sukkur.
 The Assistant Land Acquisition Officer GSC SEPCO Sukkur.

**PROJECT DIRECTOR
 GSC SEPCO SUKKUR**

Office of the Project Director 2200 S. 25th Avenue
Email: 2200S25th@comcast.com Phone #: 071-5651445 FAX #: 071-5657432

100 21 350 SEPCO/SUK/1284-81.

Dated:- 20-06-2011

In accordance with the instructions NO: 02 to the reference of financial power book for distribution companies (Discoms) of Jan-03 the sanction of the following is hereby accorded vide sanction of financial power (Revised-2007), Section XV, Sub Section 15-18 (NTDC), for payment of cost compensation to the effective land owner (On individual basis) for the concrete & erection work of 132KV Transmission Line feed for Dadu-Mehar-Larkana Grid Station, prepared proposal & submitted by the Executive Engineer T&G @ Division GSC SEPCO Sukkur vide his office letter NO. XSN-T&G/GSC/SEPCO/SUK/153-53 dated 11.05.2010.

29

7	Mr. Muhammad Wajid Bhatti S/O Rajib	17	Lossen	1	5000	15000	15000.00
	41205-4950842-7	394					
8	Mr. Nazeer Ahmed Khan S/O Muhammad Bux Khan	22	Wheat	9	1875	16875	16875.00
	41205-2290951-5	397					
9	Mr. Nazeer Ahmed Khan S/O Muhammad Bux Khan	22	Wheat	7	1875	13125	13125.00
	41205-2290951-5	397					
10	Mr. Nazeer Ahmed Khan S/O Muhammad Bux Khan	26	Wheat	8	1875	15000	15000.00
	41205-2290951-5	279/1					
10	Mr. Nazeer Ahmed Khan S/O Muhammad Bux Khan	26	Wheat	2	1875	16875	16875.00
	41205-2290951-5	279/1					
12	Mr. Zubair Ahmed S/O Sultan Ahmed Khan	27	Wheat	12	975	11700	11700.00
	41205-2282764-5	234					
13	Mr. Zubair Ahmed S/O Sultan Ahmed Khan	27	Lossen	5	5000	25000	25000.00
	41205-2282764-5	233					
14	Mstr. Jannat W/O Tharo Khan Bhatti	25	Wheat	8	1875	15000	15000.00
	41205-6254953-4	384/1					
15	Mstr. Jannat W/O Tharo Khan Bhatti	25	Wheat	7	1875	13125	13125.00
	41205-6254953-4	275/1					
16	Mr. Imdad Hussain S/O Gulam Hyder	24	Lossen	4	5000	20000	20000.00
	41205-3378085-7	248					
17	Mr. Imdad Hussain S/O Gulam Hyder	24	Lossen	3	5000	15000	15000.00
	41205-3378085-7	248					
18	Mr. Imdad Hussain S/O Gulam Hyder	24	Wheat	10	975	9750	9750.00
	41205-3378085-7	248					

19	Mr. Muhammad Daud S/O Khan Muhammad Panwar 42401-1230224-9	95 411/2	Wheat Jowar	11 10	975 650	10725 6500	17225.00
20	Mr. Abdul Kareem Urf Abdul Qadir S/O Khanan Khan Urf M Khan 41203-9455925-7	68 197	Wheat	10	975	9750	9750.00
21	Mr. Abdul Kareem Urf Abdul Qadir S/O Khanan Khan Urf M Khan 41203-9455925-7	88 197	Wheat	12	975	11700	11700.00
22	Mr. Ali Nawaz Khan S/O Qurban Ali Khan Bhurgri 41203-1682993-5	85 315	Wheat Lassan	10 1	975 9000	9750 9000	18750.00
23	Mr. Ali Nawaz Khan S/O Qurban Ali Khan Bhurgri 41203-1682993-5	84/85 3.5	Wheat	12	975	11700	11700.00
24	Mr. Zulufiqar S/O Muhammad Ali Siyal 41203-6007453-7	45 414	Onion	9	1875	16875	16875.00
25	Mr. Zulufiqar S/O Muhammad Ali Siyal 41203-6007453-7	45 467	Wheat	10	975	9750	9750.00
26	Mr. Aslam Khan S/O Muhammad Ramzan Laghari 412055-980086-7	83 207	Wheat Onion	6 5	975 1875	5850 9375	15225.00
27	Mr. Aslam Khan S/O Muhammad Ramzan Laghari 412055-980086-7	83 207	Wheat	9	975	8775	8775.00
28	Mr. Ghulam Ali S/O Rasool Bux Malkani 43203-1359937-1	19 421/1	Wheat	11	1250	13750	13750.00
29	Mr. Ghulam Ali S/O Rasool Bux Malkani 43203-1359937-1	19 421/1	Wheat	13	1250	16250	16250.00
30	Mr. Muhammad Ayoub S/O Ghulam Hyder Bhatti 41205-8616151-3	21 360	Wheat	9	1875	16875	16875.00

31	Mr. Muhammad Ayoob S/O Ghulam Hyder Bhatti	21	Wheat	7	1875	13125	13125.00
	41205-8616151-3	360					
32	Mr. Iqbal Bux S/O Imam Bux Dero	42	Losson	2	9000	18000	18000.00
	41205-9898303-1	164					
33	Mr. Iqbal Bux S/O Imam Bux Dero	42	Losson	2	9000	18000	18000.00
	41205-9898303-1	164					
34	Mr. Ali Nawaz Khan S/O Qurban Ali Khan	84	Wheat	12	975	11700	11700.00
	41203-1682993-5	333/4					
35	Mr. Niaz Ali Khoso S/O Badal Khan	32	Wheat	12	975	11700	21700.00
	41205-5956413-9	179/2	Losson	2	5000	10000	
36	Mr. Khan Muhammad S/O Haji Ahmed Panwhar	93	Wheat	8	975	7800	20925.00
	41203-9380466-9	383/3	Onion	7	1875	13125	
37	Mr. Ghulam Muhammad S/O Tharo Khan Bhatti	23	Losson	5	5000	25000	25000.00
	41205-2284582-3	384/1					
38	Mr. Muhammad Bachal S/O Dost Muhammad	86	Wheat	10	975	9750	18750.00
	41203-6151179-3	326/3	Losson	1	9000	9000	
39	Mr. Khan Muhammad Sariyo S/O Sadullah	104	Onion	2	1875	3750	21750.00
	41203-3594788-5	605/1	Losson	2	9000	18000	
40	Mr. Saeed Ahmed S/O Wahid Bux Junejo	102	Onion	5	1875	9375	18150.00
	41203-856871-5	554	Wheat	9	975	8775	
41	Mr. Noor Nabi S/O Haji Muhammad Siddique	114	Wheat	8	975	7800	17175.00
	41203-7374656-7	314	Onion	5	1875	9375	
42	Mr. Abdul Karim S/O Muhammad Chuttal	112	Wheat	9	975	8775	13975.00
	41203-4701672-7	91	Jowar	8	650	5200	

44	Mr. Hafiz Ghulam Qadir S/O Ghulamullah	93	Wheat	8	1300	10400	10400.00
	43202-3342698-5	109					
45	Mr. Muhammad Uris S/O Nasrullah	81	Wheat	8	1300	10400	10400.00
	43202-0406439-3	61					
46	Mr. Niaz Ali S/O Buxal Khan	81	Wheat	8	1300	10400	10400.00
	42201-1078219-5	131					
47	Mr. Niaz Ali S/O Buxal Khan	81	Wheat	8	1300	10400	10400.00
	42201-1078219-5	128					
48	Mr. Juman Mugheri S/O Ghulam Khan	82	Wheat	8	1300	10400	10400.00
	43202-6714086-3	122					
49	Mr. Juman Mugheri S/O Ghulam Khan	82	Wheat	8	1300	10400	10400.00
	43202-6714086-3	122					
50	Mr. Muhammad Ghulam S/O Gello Khan	82	Wheat	8	1300	10400	10400.00
	43402-0363478-1	124/1					
51	Mr. Hafiz Ghulam Qadir S/O Ghulamullah	93	Wheat	10	1300	13000	13000.00
	43202-3342698-5	109					
52	Mr. Irfan Ali S/O Insan Ali Manesar	239	Wheat	13	1875	24375	24375.00
	41205-6007693-7	409					
	Mr. Pir Ali Akbar Shah S/O Mr. Juman Shah	177	Lossan	1	18750	18750	18750.00
	41202-1381500-9	118					

PROJECT DIRECTOR
GSC SEPCO SUKKUR

Chief Engineer (Dev) PMU SEPCO SUKKUR

Executive Engineer TAO Division GSC SEPCO SUKKUR, w/o to the above

Manager (CA) GSC SEPCO SUKKUR

ANNEXURE F : GRIEVANCE REDRESSAL MECHANISM

GRIEVANCE REDRESSAL MECHANISM

All stake holders, interested / affected persons and general public are notified that Hyderabad Electric Supply Company Limited (HESCO) in Districts of Larkana, Jacobabad, Shikarpur, Mehar, Dadu, Badin, Talhar, Sanghar, Kandhari and Mirpurkhas is carrying out work of construction of new Grid stations, extensions, augmentation and conversion of Grid Stations under ADB Tranche-II of following Sub-Projects.

- 1 Construction of New 132 kV Jacobabad-II Grid station and allied 132 kV Transmission Line.
- 2 Conversion of 66 kV Sukkur City Grid Station into 132 kV Grid Station and allied 132 kV Transmission Line.
- 3 Conversion of 66 kV Larkana Grid Station into 132 kV Grid Station and allied 132 kV Transmission Line.
- 4 Conversion of 66 kV Talhar Grid Station into 132 kV Grid Station and allied 132 kV Transmission Line.
- 5 Second Circuit Stringing of Sanghar-Kandhari-Mirpurkhas 132 kV Transmission Line.
- 6 Second Circuit Stringing of Shikarpur-Larkana 132 kV Transmission Line.
- 7 Construction of Larkana-Mehar-Dadu 132 kV Double Circuit Transmission Line (New).

All stake holders, interested / affected persons and general public are informed that if they have any kind of grievance related to the project work, they are requested to register their complaint along with their contact number in Environmental and Social Complaint Register which is already available at respective project site. Any action or mitigation measure shall be taken in minimum of 10 days and this would be informed to the complainant. For any further information, you can contact Environmental and Social Cell HESCO.

1. Dy. Manager (Environment & Social Safeguard)

PMU HESCO Hyderabad
Mobile: 0340-8886066

2. Assistant Manager (Social Impact)

PMU HESCO Hyderabad
Mobile: 0340-8886072

ANNEXURE G: GRIEVANCE REDRESSAL COMMITTEE



HYDERABAD ELECTRIC SUPPLY COMPANY

Bungalow No. A-1 HESCO Power Wing Colony Hussainabad Hyderabad

www.hesco.gov.pk

Phone No. 022-926 0070, Fax No. 022-9260525

No. GED/HR/Secy-PMU/GE/Dir/HR/SS/ 313/09/13

Dated: 21/09/2013

OFFICE ORDER

The Grievance Redressal Committee comprising the following is hereby constituted for Power Distribution & Enhancement Investment Project under Asian Development Project and Electricity Distribution & Transmission Improvement (EDTIP) project under the World Bank.

1. Manager (Procurement) PMU	Convener
2. Deputy Manager (E&SS) PMU	Member
3. Land Acquisition Officer	Member
4. SDO (Concerned T/L or G/C)	Member
5. Asstt. Manager (Social Impact) PMU	Member/Secretary
6. Environment & Social Inspector (Consultant)	Member
7. Community Representative	Member

The committee will be responsible to address the grievance of the community, Land owners and squatters during the different phases of the project (i.e. Land Acquisition, Resettlement Issues, Compensation as per Land Acquisition & Resettlement Framework & Land Acquisition & Resettlement Plan).



Chief Engineer (DEV)
PMU, HESCO Hyderabad

CC to:


1. Project Director GSC, HESCO, Hyderabad.
2. Project Director GSC, SEPCO, Sukkur.
3. XEN (GC), HESCO, Hyderabad.
4. XEN (TL) HESCO, Hyderabad.
5. XEN (T&G), SEPCO, Sukkur.
6. Members concerned.
7. Master File.

ANNEXURE H : CONSULTATION PICTURES

Consultation at 132 Jacobabad Grid Station with Mr. Ali Dost Golato landlord of tower No. 4 and 5. He is satisfied with the restoration of tower sites.

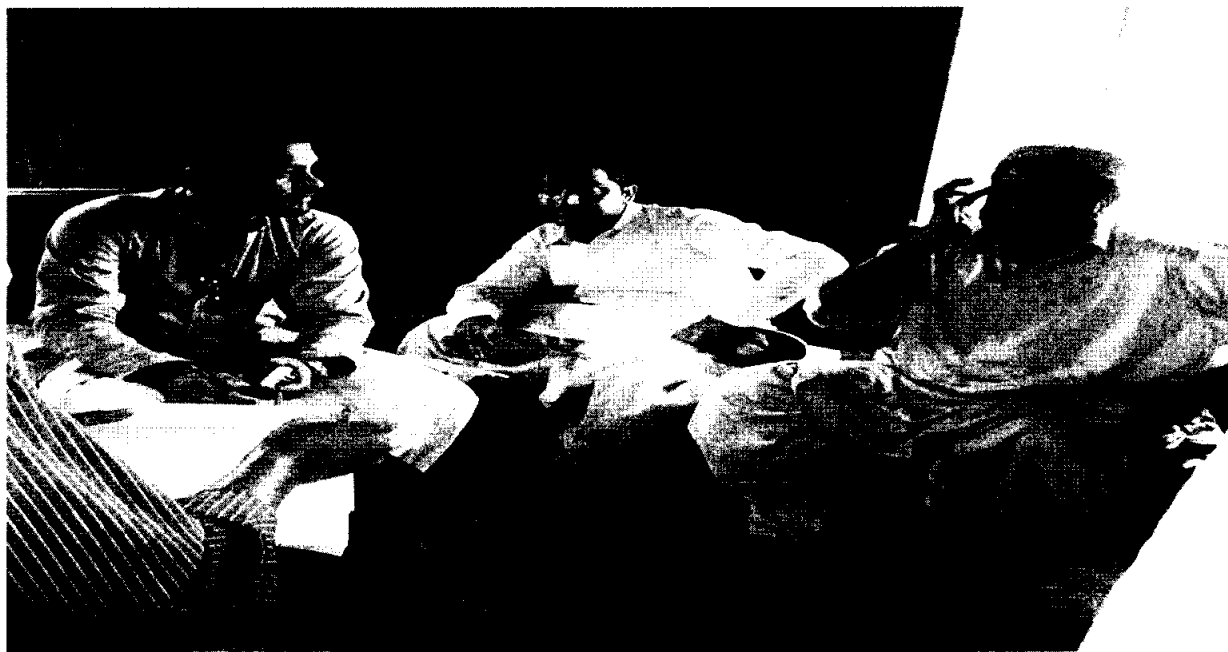

The land is supremely used for agriculture after restoration at Jacobabad site

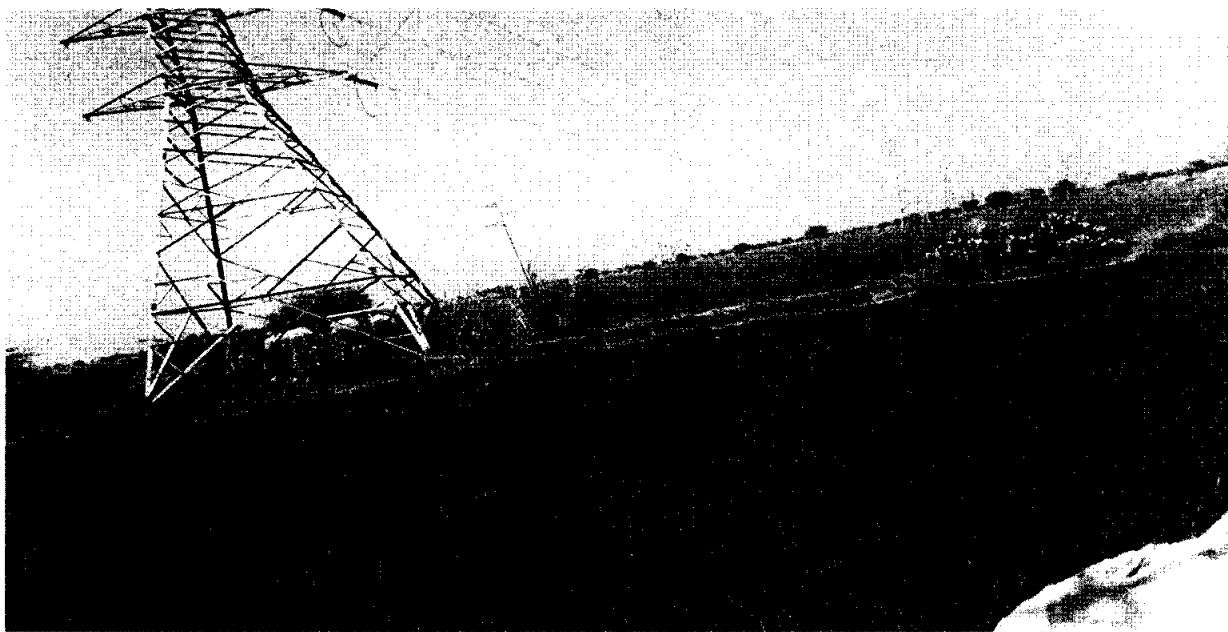

Consultation near 132 Sukkur Grid Station with Mr. Hafeez Bhutto landlord of tower No. 4. He is satisfied with the restoration of tower sites



Restoration of Shikarpur Larkana transmission line



On site training at Dadu-Maher-Larkana

