

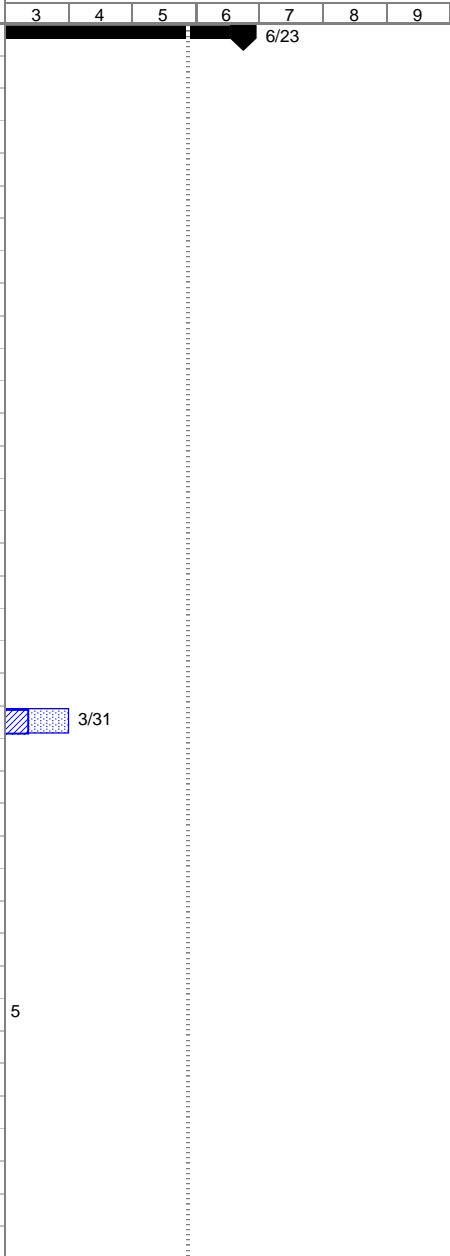
PROCUREMENT PLAN
COMPONENT 1 : Reconstruction of Public Infrastructure

54838 v1



Public Disclosure Authorized

Public Disclosure Authorized

| ID | CAZA | ID PROJECT | MUNICIPALITY / VILLAGE | Bid Package Cost Estimate | Original Contract Amount \$ | contract after variation order | Proc. Method | WB Review | Forecasted Proc. Duration | Project Duration | % Work Complete |
|-----|----------------|--------------|------------------------|---------------------------|-----------------------------|--------------------------------|--------------|-----------|---------------------------|------------------|-----------------|
| 1 | BATCH 1 | | | \$11,378,050.67 | \$11,132,849.98 | \$11,763,735.46 | | | | | |
| 79 | AKKAR | NL/AK/03-G01 | AANDKIT | \$23,925.00 | \$17,481.61 | \$17,481.61 | NS | Post | 270 days | 60 days | 100% |
| 84 | AKKAR | NL/AK/49-G01 | KABEIT | \$31,760.00 | \$31,442.40 | \$26,325.55 | NS | Post | 270 days | 60 days | 100% |
| 100 | AKKAR | NL/AK/33-G01 | MAZRAAT BALDEH | \$2,263.00 | \$2,252.02 | \$2,252.02 | NS | Post | 225 days | 30 days | 100% |
| 152 | AKKAR | NL/AK/52-G01 | KWAIKHAT | \$75,502.67 | \$75,125.15 | \$75,125.15 | NCB | Post | 240 days | 60 days | 100% |
| 153 | AKKAR | NL/AK/24-G01 | HALBA | \$71,803.00 | \$71,731.53 | \$71,731.53 | NCB | Post | 240 days | 60 days | 100% |
| 154 | | | | | | | | | | | |
| 82 | BAABDA | ML/BA/44-G01 | WADI CHAHROUR EL-SOUFL | \$30,100.00 | \$29,797.35 | \$29,797.35 | NS | Post | 270 days | 60 days | 100% |
| 99 | BAABDA | ML/BA/05-G01 | BAABDA | \$461,960.00 | \$461,960.00 | \$518,425.33 | NCB | Prior | 240 days | 150 days | 100% |
| 16 | BAALBAK | BK/BA/08-G01 | BRITAL | \$74,287.00 | \$70,200.27 | \$70,200.27 | NS | Post | 270 days | 90 days | 100% |
| 71 | BAALBAK | BK/BA/45-G01 | JENTA | \$5,862.00 | \$5,803.00 | \$5,803.05 | NS | Post | 270 days | 30 days | 100% |
| 72 | BAALBAK | BK/BA/30-G01 | NABBY CHIT | \$10,715.00 | \$10,608.00 | \$10,608.00 | NS | Post | 270 days | 30 days | 100% |
| 73 | BAALBAK | BK/BA/44-G01 | HAOUCH ELRAFKA | \$8,508.00 | \$8,338.00 | \$8,337.84 | NS | Post | 270 days | 60 days | 100% |
| 77 | BAALBAK | BK/BA/07-G01 | BOUDAY | \$23,919.00 | \$21,407.21 | \$21,407.21 | NS | Post | 270 days | 60 days | 100% |
| 80 | BAALBEK | BK/BA/06-G01 | BEDNAYEL | \$28,253.00 | \$27,688.30 | \$27,688.30 | NS | Post | 270 days | 60 days | 100% |
| 46 | BEKAA OUEST | BK/BO/17-G01 | MACHGHARA | \$4,117.00 | \$3,952.00 | \$3,952.00 | NS | Post | 270 days | 60 days | 100% |
| 56 | BEKAA OUEST | BK/BO/16-G01 | LEBBAYA | \$16,508.00 | \$16,426.00 | \$16,424.71 | NS | Post | 150 days | 60 days | 100% |
| 74 | BEKAA OUEST | BK/BO/02-G01 | AITANIT | \$36,495.00 | \$35,582.30 | \$35,538.75 | NS | Post | 270 days | 60 days | 100% |
| 164 | BEKAA OUEST | BK/BO/24-G01 | SOULTAN YAAKOU | \$16,408.00 | \$16,243.92 | \$16,243.92 | NS | Post | 225 days | 60 days | 100% |
| 97 | BENT JBEIL | NA/BJ/21-G01 | YAROUN | \$433,361.00 | \$479,819.85 | \$550,104.60 | NCB | Prior | 270 days | 240 days | 100% |
| 98 | BENT JBEIL | NA/BJ/30-G01 | MAROUN ELRASS | \$656,699.00 | \$691,682.54 | \$795,328.21 | NCB | Prior | 270 days | 270 days | 100% |
| 105 | BENT JBEIL | NA/BJ/27-G01 | FROUN | \$21,582.00 | \$21,560.00 | \$21,560.08 | NS | Post | 225 days | 60 days | 100% |
| 106 | BENT JBEIL | NA/BJ/08-G01 | CHAKRA DOUBEY | \$49,225.33 | \$49,176.11 | \$49,176.11 | NS | Post | 225 days | 60 days | 100% |
| 109 | BENT JBEIL | NA/BJ/32-G01 | GHANDOURIET | \$33,150.00 | \$33,130.00 | \$33,130.11 | NS | Post | 240 days | 60 days | 100% |
| 114 | BENT JBEIL | NA/BJ/31-G01 | BEIT YAHOUN | \$39,909.00 | \$39,869.09 | \$39,869.09 | NS | Post | 225 days | 60 days | 100% |
| 115 | BENT JBEIL | NA/BJ/22-G01 | YATER | \$59,328.00 | \$55,175.35 | \$55,175.35 | NCB | Post | 240 days | 90 days | 100% |
| 126 | BENT JBEIL | NA/BJ/33-G01 | RCHAF | \$156,594.00 | \$156,280.81 | \$179,238.80 | NCB | Post | 240 days | 150 days | 100% |
| 127 | BENT JBEIL | NA/BJ/20-G01 | TEBNINE | \$33,866.00 | \$33,815.53 | \$33,815.53 | NS | Post | 225 days | 60 days | 100% |
| 128 | BENT JBEIL | NA/BJ/18-G01 | SOULTANIEH | \$58,842.00 | \$58,812.58 | \$58,812.58 | NCB | Post | 240 days | 60 days | 100% |
| 129 | BENT JBEIL | NA/BJ/12-G01 | HADATHA | \$183,092.00 | \$183,923.37 | \$211,467.34 | NCB | Post | 240 days | 120 days | 100% |
| 134 | BENT JBEIL | NA/BJ/01-G01 | AIN EBEL | \$45,782.00 | \$45,438.00 | \$52,253.70 | NS | Post | 240 days | 60 days | 100% |
| 135 | BENT JBEIL | NA/BJ/04-G01 | AYTAROUN | \$309,439.00 | \$308,819.96 | \$355,142.95 | NCB | Prior | 240 days | 240 days | 100% |
| 136 | BENT JBEIL | NA/BJ/05-G01 | BEIT LIF | \$57,171.00 | \$56,884.81 | \$56,884.81 | NCB | Post | 240 days | 60 days | 100% |
| 137 | BENT JBEIL | NA/BJ/13-G01 | KAFRA | \$67,619.00 | \$59,842.22 | \$59,842.22 | NCB | Post | 240 days | 60 days | 100% |
| 139 | BENT JBEIL | NA/BJ/34-G01 | KOUNINE | \$132,627.00 | \$132,560.42 | \$152,382.50 | NCB | Post | 240 days | 90 days | 100% |
| 140 | BENT JBEIL | NA/BJ/35-G01 | JMAYJMEH | \$65,425.00 | \$65,294.15 | \$65,294.15 | NCB | Post | 240 days | 60 days | 100% |
| 157 | BENT JBEIL | NA/BJ/06-G01 | BARAACHIT | \$106,305.00 | \$106,251.52 | \$106,251.52 | NCB | Post | 240 days | 90 days | 100% |
| 158 | BENT JBEIL | NA/BJ/36-G01 | HANINE | \$40,467.66 | \$39,779.72 | \$39,779.72 | NS | Post | 225 days | 60 days | 100% |



Project: Procurement Plan
Updated: Fri 5/28/10

EXECUTION PHASE 
WORK STOPPING DUE TO THE RAIN SEASON 

Summary 
PROCUREMENT PHASE 



PROCUREMENT PLAN
COMPONENT 1 : Reconstruction of Public Infrastructure

| ID | CAZA | ID PROJECT | MUNICIPALITY / VILLAGE | Bid Package Cost Estimate | Original Contract Amount \$ | contract after variation order | Proc. Method | WB Review | Forecasted Proc. Duration | Project Duration | % Work Complete | | | | | | | |
|-----|-----------|--------------|------------------------|---------------------------|-----------------------------|--------------------------------|--------------|-----------|---------------------------|------------------|-----------------|---|---|---|---|---|---|---|
| | | | | | | | | | | | | 3 | 4 | 5 | 6 | 7 | 8 | 9 |
| 22 | BENTJBEIL | NA/BJ/23-G01 | RAMIEH | \$128,675.00 | \$128,031.60 | \$128,031.60 | NS | Post | 270 days | 120 days | 100% | | | | | | | |
| 26 | BENTJBEIL | NA/BJ/09-G01 | DEBBEL 1 | \$127,883.00 | \$125,965.10 | \$125,965.10 | NS | Post | 270 days | 120 days | 100% | | | | | | | |
| 27 | BENTJBEIL | NA/BJ/09-G02 | DEBBEL 2 | \$29,634.00 | \$29,559.25 | \$29,559.25 | NS | Post | 225 days | 60 days | 100% | | | | | | | |
| 28 | BENTJBEIL | NA/BJ/25-G01 | KAWZAH 1 | \$129,529.00 | \$119,532.00 | \$119,531.87 | NS | Post | 270 days | 120 days | 100% | | | | | | | |
| 29 | BENTJBEIL | NA/BJ/25-G02 | KAWZAH 2 | \$28,334.00 | \$28,262.50 | \$28,262.50 | NS | Post | 225 days | 60 days | 100% | | | | | | | |
| 30 | BENTJBEIL | NA/BJ/24-G01 | SRIBINNE | \$124,415.00 | \$124,104.00 | \$124,103.96 | NS | Post | 270 days | 120 days | 100% | | | | | | | |
| 31 | BENTJBEIL | NA/BJ/26-G01 | KALAWEIH | \$30,383.00 | \$30,352.95 | \$34,901.73 | NS | Post | 270 days | 60 days | 100% | | | | | | | |
| 38 | BENTJBEIL | NA/BJ/29-G01 | AITA ELJABAL 1 | \$130,000.00 | \$129,349.17 | \$129,349.17 | NS | Post | 150 days | 120 days | 100% | | | | | | | |
| 39 | BENTJBEIL | NA/BJ/29G-02 | AITA ELJABAL 2 | \$24,624.00 | \$24,253.98 | \$24,253.98 | NS | Post | 225 days | 60 days | 100% | | | | | | | |
| 49 | BENTJBEIL | NA/BJ/10-G01 | DEIR ENTAR | \$49,697.00 | \$46,218.21 | \$46,218.21 | NS | Post | 270 days | 60 days | 100% | | | | | | | |
| 50 | BENTJBEIL | NA/BJ/28/G01 | BORJ KALAWEIH | \$38,392.00 | \$38,353.28 | \$38,353.28 | NS | Post | 270 days | 60 days | 100% | | | | | | | |
| 64 | BENTJBEIL | NA/BJ/17-G01 | SAFAD EL BATIKH | \$40,796.00 | \$40,592.35 | \$40,592.35 | NS | Post | 270 days | 60 days | 100% | | | | | | | |
| 66 | BENTJBEIL | NA/BJ/14-G01 | KFAR DOUNINE | \$44,118.00 | \$43,376.50 | \$43,374.84 | NS | Post | 270 days | 60 days | 100% | | | | | | | |
| 69 | BENTJBEIL | NA/BJ/11-G01 | HARYSS 1 | \$130,000.00 | \$123,650.17 | \$123,650.17 | NS | Post | 270 days | 120 days | 100% | | | | | | | |
| 70 | BENTJBEIL | NA/BJ/11-G02 | HARYSS 2 | \$114,000.00 | \$113,601.00 | \$113,601.00 | NCB | Post | 240 days | 90 days | 100% | | | | | | | |
| 91 | BENTJBEIL | NA/BJ/16-G01 | RMEICH | \$64,152.00 | \$63,831.24 | \$63,831.24 | NS | Post | 270 days | 90 days | 100% | | | | | | | |
| 138 | BENTJBEIL | NA/BJ/15-G01 | KHERBET SILM | \$24,178.00 | \$24,057.11 | \$24,057.11 | NS | Post | 225 days | 60 days | 100% | | | | | | | |
| 151 | BENTJBEIL | NA/BJ/19-G01 | TAIRRY | \$64,771.00 | \$63,475.25 | \$63,475.25 | NCB | Post | 240 days | 60 days | 100% | | | | | | | |
| 52 | CHOUF | ML/CH/22-G01 | CHHIM | \$71,257.00 | \$70,900.40 | \$70,900.40 | NS | Post | 270 days | 90 days | 100% | | | | | | | |
| 68 | HASBAYA | NA/HA/05-G01 | HASBAYA | \$41,920.00 | \$41,467.80 | \$41,467.80 | NS | Post | 270 days | 90 days | 100% | | | | | | | |
| 76 | HASBAYA | NA/HA/04-G01 | FERDISS | \$18,464.00 | \$14,063.94 | \$14,063.94 | NS | Post | 150 days | 60 days | 100% | | | | | | | |
| 116 | HASBAYA | NA/HA/09-G01 | KFARCHOUBA | \$66,718.00 | \$59,502.33 | \$59,502.33 | NCB | Post | 240 days | 90 days | 100% | | | | | | | |
| 59 | JEZZINE | SL/JE/01-G01 | AICHET | \$25,630.00 | \$25,333.00 | \$20,160.68 | NS | Post | 150 days | 60 days | 100% | | | | | | | |
| 60 | JEZZINE | SL/JE/21-G01 | RIHAN | \$29,744.00 | \$24,667.06 | \$24,667.06 | NS | Post | 270 days | 60 days | 100% | | | | | | | |
| 144 | JEZZINE | SL/JE/25-G01 | SOUJOUJ | \$20,128.00 | \$20,078.01 | \$20,078.01 | NS | Post | 225 days | 60 days | 100% | | | | | | | |
| 167 | JEZZINE | SL/JE/20-G01 | MLIKH | \$22,056.00 | \$18,871.11 | \$18,871.11 | NS | Post | 225 days | 60 days | 100% | | | | | | | |
| 57 | MARJEYOUN | NA/MA/19-G01 | KASIR | \$18,521.00 | \$18,382.42 | \$18,382.42 | NS | Post | 270 days | 60 days | 100% | | | | | | | |
| 58 | MARJEYOUN | NA/MA/05-G01 | EBLE EL SAKI | \$17,513.00 | \$17,425.44 | \$17,425.44 | NS | Post | 270 days | 60 days | 100% | | | | | | | |
| 61 | MARJEYOUN | NA/MA/15-G01 | BANI HAYAN | \$32,734.00 | \$32,675.41 | \$32,674.25 | NS | Post | 270 days | 60 days | 100% | | | | | | | |
| 75 | MARJEYOUN | NA/MA/17-G01 | BLATE | \$17,420.00 | \$17,332.90 | \$17,332.90 | NS | Post | 270 days | 60 days | 100% | | | | | | | |
| 86 | MARJEYOUN | NA/MA/02-G01 | BOURJ EL MOULOUK | \$22,414.00 | \$22,340.20 | \$22,333.53 | NS | Post | 270 days | 60 days | 100% | | | | | | | |
| 87 | MARJEYOUN | NA/MA/18-G01 | SARADA & OMRA | \$18,957.00 | \$18,917.00 | \$18,917.00 | NS | Post | 270 days | 60 days | 100% | | | | | | | |
| 89 | MARJEYOUN | NA/MA/16/G01 | DEBBINE | \$38,580.00 | \$38,387.10 | \$38,387.10 | NS | Post | 270 days | 60 days | 100% | | | | | | | |
| 94 | MARJEYOUN | NA/MA/01-G01 | ADEYSEH | \$292,448.85 | \$247,375.00 | \$247,375.00 | NCB | Prior | 270 days | 150 days | 80% | | | | | | | |
| 95 | MARJEYOUN | NA/MA/09-G01 | KFAR KILA | \$197,455.00 | \$196,612.46 | \$226,078.43 | NCB | Post | 270 days | 150 days | 100% | | | | | | | |
| 96 | MARJEYOUN | NA/MA/20-G01 | RUB TLATINE | \$404,687.00 | \$426,550.95 | \$490,520.00 | NCB | Prior | 270 days | 150 days | 100% | | | | | | | |
| 101 | MARJEYOUN | NA/MA/27-G01 | AADCHIT KSIR | \$44,714.00 | \$44,280.06 | \$44,280.06 | NS | Post | 225 days | 60 days | 100% | | | | | | | |
| 102 | MARJEYOUN | NA/MA/07-G01 | MARJEYOUN | \$135,952.00 | \$134,932.36 | \$155,153.55 | NCB | Post | 240 days | 90 days | 100% | | | | | | | |

5/14

5

Project: Procurement Plan
Updated: Fri 5/28/10

EXECUTION PHASE 
WORK STOPPING DUE TO THE RAIN SEASON 

Summary 
PROCUREMENT PHASE 



PROCUREMENT PLAN
COMPONENT 1 : Reconstruction of Public Infrastructure

| ID | CAZA | ID PROJECT | MUNICIPALITY / VILLAGE | Bid Package Cost Estimate | Original Contract Amount \$ | contract after variation order | Proc. Method | WB Review | Forecasted Proc. Duration | Project Duration | % Work Complete | | | | | | | |
|-----|-----------|--------------|------------------------|---------------------------|-----------------------------|--------------------------------|--------------|-----------|---------------------------|------------------|-----------------|---|---|---|---|---|---|---|
| | | | | | | | | | | | | 3 | 4 | 5 | 6 | 7 | 8 | 9 |
| 103 | MARJEYOUN | NA/MA/08-G01 | KHABRIKHA | \$200,608.00 | \$200,282.46 | \$230,318.82 | NCB | Prior | 240 days | 120 days | 100% | | | | | | | |
| 104 | MARJEYOUN | NA/MA/21-G01 | KANTRA | \$89,900.00 | \$67,425.00 | \$67,425.00 | NCB | Post | 240 days | 60 days | 100% | | | | | | | |
| 110 | MARJEYOUN | NA/MA/23-G01 | MAJDELSILM | \$79,342.00 | \$75,884.00 | \$75,884.00 | NCB | Post | 240 days | 90 days | 100% | | | | | | | |
| 117 | MARJEYOUN | NA/MA/22-G01 | BLIDA | \$21,905.00 | \$21,685.62 | \$21,685.62 | NS | Post | 225 days | 60 days | 100% | | | | | | | |
| 118 | MARJEYOUN | NA/MA/06-G01 | HOULA | \$21,074.00 | \$21,067.01 | \$21,067.01 | NS | Post | 225 days | 60 days | 100% | | | | | | | |
| 119 | MARJEYOUN | NA/MA/12-G01 | MAIS ELJABAL | \$39,600.00 | \$39,591.41 | \$39,591.41 | NS | Post | 225 days | 60 days | 100% | | | | | | | |
| 120 | MARJEYOUN | NA/MA/24-G01 | MARKABA | \$139,019.00 | \$138,602.28 | \$138,598.01 | NCB | Post | 240 days | 120 days | 100% | | | | | | | |
| 124 | MARJEYOUN | NA/MA/25-G01 | SAWANEH* | \$34,142.00 | \$30,703.52 | \$34,115.02 | NS | Post | 225 days | 60 days | 100% | | | | | | | |
| 125 | MARJEYOUN | NA/MA/26-G01 | TOULINE | \$26,494.00 | \$26,414.68 | \$24,441.35 | NS | Post | 225 days | 60 days | 100% | | | | | | | |
| 130 | MARJEYOUN | NA/MA/04-G01 | DEIR MIMAS | \$46,895.00 | \$46,843.42 | \$53,855.36 | NS | Post | 225 days | 60 days | 100% | | | | | | | |
| 131 | MARJEYOUN | NA/MA/13-G01 | TAIBEH | \$109,788.00 | \$109,238.73 | \$109,238.73 | NCB | Post | 240 days | 60 days | 100% | | | | | | | |
| 159 | MARJEYOUN | NA/MA/11-G01 | KLAIAAT | \$193,155.00 | \$191,991.00 | \$220,790.15 | NCB | Post | 240 days | 90 days | 100% | | | | | | | |
| 2 | NABATIEH | NA/NA/33-G01 | AABA | \$10,125.00 | \$10,023.42 | \$10,023.42 | NS | Post | 270 days | 60 days | 100% | | | | | | | |
| 3 | NABATIEH | NA/NA/07-G01 | HABBOUCH | \$28,670.00 | \$27,722.60 | \$27,643.32 | NS | Post | 270 days | 60 days | 100% | | | | | | | |
| 4 | NABATIEH | NA/NA/06-G01 | DOUAIR | \$18,350.00 | \$17,983.00 | \$16,574.25 | NS | Post | 270 days | 60 days | 100% | | | | | | | |
| 5 | NABATIEH | NA/NA/14-G01 | KAAKAEIT AL-JISR | \$34,276.00 | \$33,933.24 | \$33,933.24 | NS | Post | 270 days | 60 days | 100% | | | | | | | |
| 6 | NABATIEH | NA/NA/16-G01 | KFAR SYR | \$23,808.00 | \$23,570.00 | \$23,569.92 | NS | Post | 270 days | 60 days | 100% | | | | | | | |
| 7 | NABATIEH | NA/NA/17-G01 | KFAR TEBNIT | \$47,500.00 | \$47,262.50 | \$43,052.98 | NS | Post | 270 days | 60 days | 100% | | | | | | | |
| 8 | NABATIEH | NA/NA/20-G01 | KSSAIBET | \$29,272.00 | \$29,249.70 | \$29,249.70 | NS | Post | 270 days | 60 days | 100% | | | | | | | |
| 9 | NABATIEH | NA/NA/31-G01 | ZEFTA | \$42,680.00 | \$42,253.00 | \$42,253.00 | NS | Post | 270 days | 60 days | 100% | | | | | | | |
| 17 | NABATIEH | NA/NA/34-G01 | ADCHIT | \$44,809.00 | \$30,665.48 | \$30,665.48 | NS | Post | 270 days | 90 days | 100% | | | | | | | |
| 18 | NABATIEH | NA/NA/35-G01 | CHOUKIN | \$45,197.00 | \$45,179.78 | \$45,179.78 | NS | Post | 270 days | 90 days | 100% | | | | | | | |
| 19 | NABATIEH | NA/NA/29-G01 | ZAOUTAR EL GHARBIET | \$67,821.00 | \$60,061.00 | \$69,064.33 | NS | Post | 270 days | 90 days | 100% | | | | | | | |
| 23 | NABATIEH | NA/NA/02-G01 | ANSSAR | \$58,590.00 | \$46,039.00 | \$32,881.59 | NS | Post | 150 days | 90 days | 100% | | | | | | | |
| 24 | NABATIEH | NA/NA/03-G01 | ARAB SALIM | \$115,319.00 | \$109,841.60 | \$109,841.60 | NS | Post | 150 days | 120 days | 100% | | | | | | | |
| 43 | NABATIEH | NA/NA/09-G01 | HOUMYN EL FAOUKA | \$7,384.00 | \$7,162.00 | \$7,161.83 | NS | Post | 270 days | 30 days | 100% | | | | | | | |
| 45 | NABATIEH | NA/NA/25-G01 | ROUMYN | \$10,789.00 | \$10,680.45 | \$10,680.45 | NS | Post | 270 days | 30 days | 100% | | | | | | | |
| 51 | NABATIEH | NA/NA/01-G01 | AIN KANA | \$50,733.00 | \$49,571.13 | \$43,571.13 | NS | Post | 150 days | 90 days | 100% | | | | | | | |
| 62 | NABATIEH | NA/NA/21-G01 | MAYFADOUN | \$36,316.00 | \$35,584.29 | \$35,584.29 | NS | Post | 270 days | 60 days | 100% | | | | | | | |
| 85 | NABATIEH | NA/NA/36-G01 | ARNOUN | \$55,572.50 | \$38,233.88 | \$38,233.88 | NCB | Post | 270 days | 60 days | 10% | | | | | | | |
| 88 | NABATIEH | NA/NA/28-G01 | ZAOUTAR EL CHARKIET | \$74,031.00 | \$74,006.57 | \$85,097.30 | NCB | Post | 270 days | 60 days | 100% | | | | | | | |
| 90 | NABATIEH | NA/NA/12-G01 | JBAA | \$63,367.00 | \$55,097.50 | \$55,097.50 | NS | Post | 270 days | 90 days | 100% | | | | | | | |
| 141 | NABATIEH | NA/NA/08-G01 | HAROUF | \$12,004.67 | \$11,968.65 | \$13,752.62 | NS | Post | 225 days | 30 days | 100% | | | | | | | |
| 142 | NABATIEH | NA/NA/13-G01 | JEBCHIT | \$23,611.00 | \$23,598.86 | \$23,598.86 | NS | Post | 225 days | 60 days | 100% | | | | | | | |
| 143 | NABATIEH | NA/NA/26-G01 | SARBA | \$35,881.00 | \$35,522.90 | \$35,522.19 | NS | Post | 225 days | 60 days | 100% | | | | | | | |
| 155 | NABATIEH | NA/NA/23-G01 | NABATIEH TAHTA | \$29,390.00 | \$29,242.39 | \$29,242.39 | NS | Post | 225 days | 60 days | 100% | | | | | | | |
| 25 | SAIDA | SL/SA/19-G01 | KHARAYEB | \$120,130.00 | \$118,928.04 | \$118,928.04 | NS | Post | 270 days | 90 days | 100% | | | | | | | |
| 44 | SAIDA | SL/SA/30-G01 | KAWSARIET EL SAYAD | \$10,002.00 | \$9,996.67 | \$9,978.34 | NS | Post | 270 days | 30 days | 100% | | | | | | | |

4/1

6/23

Project: Procurement Plan
Updated: Fri 5/28/10

EXECUTION PHASE 
WORK STOPPING DUE TO THE RAIN SEASON 

Summary 
PROCUREMENT PHASE 


PROCUREMENT PLAN
COMPONENT 1 : Reconstruction of Public Infrastructure

| ID | CAZA | ID PROJECT | MUNICIPALITY / VILLAGE | Bid Package Cost Estimate | Original Contract Amount \$ | contract after variation order | Proc. Method | WB Review | Forecasted Proc. Duration | Project Duration | % Work Complete | | | | | | | |
|-----|-------|--------------|------------------------|---------------------------|-----------------------------|--------------------------------|--------------|-----------|---------------------------|------------------|-----------------|---|---|---|---|---|---|------|
| | | | | | | | | | | | | 3 | 4 | 5 | 6 | 7 | 8 | 9 |
| 55 | SAIDA | SL/SA/13-G01 | GHESSANIET | \$12,761.00 | \$12,633.06 | \$12,633.06 | NS | Post | 270 days | 60 days | 100% | | | | | | | |
| 67 | SAIDA | SL/SA/25-G01 | SAKSAKIEH | \$61,077.00 | \$61,076.33 | \$61,076.33 | NS | Post | 270 days | 60 days | 100% | 5 | | | | | | |
| 78 | SAIDA | SL/SA/22-G01 | MEAAAMARIEH | \$21,955.00 | \$21,889.14 | \$21,889.14 | NS | Post | 270 days | 60 days | 100% | | | | | | | |
| 81 | SAIDA | SL/SA/31-G01 | ANSARIET | \$30,767.00 | \$29,623.80 | \$29,623.80 | NS | Post | 270 days | 60 days | 100% | | | | | | | |
| 160 | SAIDA | SL/SA/12-G01 | GHAZIYEH | \$36,766.00 | \$36,582.17 | \$36,582.17 | NS | Post | 225 days | 60 days | 100% | | | | | | | |
| 163 | SAIDA | SL/SA/32-G01 | ARKI | \$17,171.00 | \$17,085.15 | \$17,085.15 | NS | Post | 225 days | 60 days | 100% | | | | | | | |
| 10 | SOUR | SL/SO/02-G01 | AIN BAAL | \$21,657.00 | \$21,519.58 | \$21,519.58 | NS | Post | 270 days | 60 days | 100% | | | | | | | |
| 11 | SOUR | SL/SO/22-G01 | RAMADIET | \$31,076.00 | \$30,766.00 | \$30,766.00 | NS | Post | 150 days | 60 days | 100% | | | | | | | |
| 12 | SOUR | SL/SO/26-G01 | SALAA | \$16,100.00 | \$16,003.40 | \$16,003.40 | NS | Post | 270 days | 30 days | 100% | | | | | | | |
| 13 | SOUR | SL/SO/24-G01 | TOURA | \$27,133.00 | \$26,726.30 | \$26,726.30 | NS | Post | 270 days | 60 days | 100% | | | | | | | |
| 20 | SOUR | SL/SO/25-G01 | BAFLIEH | \$93,875.00 | \$44,486.45 | \$44,486.45 | NS | Post | 270 days | 90 days | 100% | | | | | | | |
| 21 | SOUR | SL/SO/21-G01 | BOURJRAHAL | \$70,325.00 | \$70,078.36 | \$68,648.77 | NS | Post | 270 days | 90 days | 100% | | | | | | | |
| 32 | SOUR | SL/SO/31-G01 | YANOUH | \$33,732.00 | \$33,630.47 | \$33,630.47 | NS | Post | 270 days | 60 days | 100% | | | | | | | |
| 34 | SOUR | SL/SO/33-G01 | CHAMEA | \$62,870.00 | \$62,241.30 | \$62,241.30 | NS | Post | 270 days | 90 days | 100% | | | | | | | |
| 35 | SOUR | SL/SO/34-G01 | ALBOUSTAN | \$76,810.00 | \$74,785.00 | \$74,766.63 | NS | Post | 270 days | 90 days | 100% | | | | | | | |
| 36 | SOUR | SL/SO/08-G01 | CHAHOUR | \$94,304.00 | \$90,352.60 | \$90,352.60 | NS | Post | 270 days | 90 days | 100% | | | | | | | |
| 37 | SOUR | SL/SO/37-G01 | TAIR HARFA | \$97,936.00 | \$97,690.50 | \$97,661.60 | NS | Post | 270 days | 120 days | 100% | | | | | | | |
| 47 | SOUR | SL/SO/32-G01 | DEIR AAMES | \$37,934.00 | \$37,733.30 | \$37,673.08 | NS | Post | 270 days | 60 days | 100% | | | | | | | |
| 48 | SOUR | SL/SO/30-G01 | HALOUSSIET | \$47,324.00 | \$47,230.00 | \$46,429.29 | NS | Post | 270 days | 60 days | 100% | | | | | | | |
| 53 | SOUR | SL/SO/35-G01 | CHIHIN | \$82,162.00 | \$81,909.50 | \$79,958.50 | NS | Post | 150 days | 90 days | 100% | | | | | | | |
| 54 | SOUR | SL/SO/36-G01 | JANATA | \$4,817.00 | \$4,720.33 | \$4,720.33 | NS | Post | 270 days | 30 days | 100% | | | | | | | |
| 63 | SOUR | SL/SO/38-G01 | DORDGHAYA | \$43,936.00 | \$43,716.32 | \$43,716.32 | NS | Post | 270 days | 60 days | 100% | | | | | | | |
| 65 | SOUR | SL/SO/41-G01 | BORGLIET | \$43,480.00 | \$33,991.70 | \$35,991.00 | NS | Post | 270 days | 60 days | 100% | | | | | | | |
| 83 | SOUR | SL/SO/39-G01 | DEIR KIFA | \$42,204.00 | \$42,077.00 | \$42,077.00 | NS | Post | 270 days | 60 days | 100% | | | | | | | |
| 92 | SOUR | SL/SO/40-G01 | DBAAL | \$78,735.00 | \$78,499.13 | \$78,499.13 | NS | Post | 270 days | 90 days | 100% | | | | | | | |
| 93 | SOUR | SL/SO/46-G01 | JEBBINE | \$223,923.00 | \$223,312.12 | \$223,312.12 | NCB | Prior | 270 days | 120 days | 100% | | | | | | | |
| 107 | SOUR | SL/SO/15-G01 | MAAROUB | \$17,660.00 | \$17,624.68 | \$17,624.68 | NS | Post | 225 days | 60 days | 0% | | | | | | | 6/23 |
| 108 | | | | | | | | | | | | | | | | | | |
| 111 | SOUR | SL/SO/05-G01 | BATOULEH | \$24,180.00 | \$24,143.06 | \$24,143.06 | NS | Post | 225 days | 60 days | 100% | | | | | | | |
| 112 | SOUR | SL/SO/18-G01 | SRIFA | \$105,909.00 | \$99,904.42 | \$99,904.42 | NCB | Post | 240 days | 120 days | 100% | | | | | | | |
| 113 | SOUR | SL/SO/12-G01 | QANA | \$69,372.00 | \$66,064.75 | \$66,064.75 | NCB | Post | 240 days | 60 days | 100% | | | | | | | |
| 121 | SOUR | SL/SO/47-G01 | MAHROUNA | \$15,884.00 | \$15,836.35 | \$15,836.35 | NS | Post | 225 days | 60 days | 100% | | | | | | | |
| 122 | SOUR | SL/SO/01-G01 | AABASIYEH | \$30,182.00 | \$30,120.97 | \$30,120.97 | NS | Post | 225 days | 60 days | 100% | | | | | | | |
| 123 | SOUR | SL/SO/10-G01 | DEIR QANOUN ELNAHR | \$48,690.33 | \$48,592.95 | \$48,592.95 | NS | Post | 225 days | 60 days | 50% | | | | | | | 5-17 |
| 132 | SOUR | SL/SO/03-G01 | AITIT | \$49,097.00 | \$49,072.45 | \$56,432.84 | NS | Post | 240 days | 60 days | 100% | | | | | | | |
| 133 | SOUR | SL/SO/50-G01 | MAJDELZOUN | \$73,647.00 | \$73,600.00 | \$84,639.17 | NCB | Post | 240 days | 60 days | 100% | | | | | | | |
| 145 | SOUR | SL/SO/51-G01 | JBAL ELBOTOM | \$83,995.00 | \$83,785.01 | \$83,785.01 | NCB | Post | 240 days | 90 days | 100% | | | | | | | |
| 146 | SOUR | SL/SO/13-G01 | KLALILI | \$56,059.00 | \$55,890.49 | \$55,890.49 | NCB | Post | 240 days | 60 days | 100% | | | | | | | |

Project: Procurement Plan
Updated: Fri 5/28/10

EXECUTION PHASE

WORK STOPPING DUE TO THE RAIN SEASON







Summary

PROCUREMENT PHASE



PROCUREMENT PLAN
COMPONENT 1 : Reconstruction of Public Infrastructure

| ID | CAZA | ID PROJECT | MUNICIPALITY / VILLAGE | Bid Package Cost Estimate | Original Contract Amount \$ | contract after variation order | Proc. Method | WB Review | Forecasted Proc. Duration | Project Duration | % Work Complete | | | | | | | |
|-----|----------------|--------------|------------------------|---------------------------|-----------------------------|--------------------------------|--------------|-----------|---------------------------|------------------|-----------------|------|---|---|---|---|---|------|
| | | | | | | | | | | | | 3 | 4 | 5 | 6 | 7 | 8 | 9 |
| 147 | SOUR | SL/SO/42-G01 | SIDIKIN | \$176,347.00 | \$176,000.00 | \$176,000.00 | NCB | Post | 240 days | 60 days | 100% | | | | | | | |
| 148 | SOUR | SL/SO/49-G01 | BAYAD | \$7,707.00 | \$7,553.20 | \$7,553.20 | NS | Post | 225 days | 30 days | 100% | | | | | | | |
| 149 | SOUR | SL/SO/52-G01 | ZIBKIN | \$94,753.00 | \$94,563.83 | \$108,738.94 | NCB | Post | 240 days | 60 days | 100% | | | | | | | |
| 150 | SOUR | SL/SO/07-G01 | BORJ CHMALI | \$12,142.00 | \$12,123.12 | \$12,123.12 | NCB | Post | 240 days | 60 days | 100% | | | | | | | |
| 156 | SOUR | SL/SO/43-G01 | MARWAHIN | \$199,680.00 | \$165,734.40 | \$190,594.56 | NCB | Post | 240 days | 90 days | 100% | | | | | | | |
| 161 | SOUR | SL/SO/53-G01 | MANSOURI | \$49,070.66 | \$49,021.59 | \$49,021.59 | NS | Post | 225 days | 60 days | 100% | | | | | | | |
| 162 | SOUR | SL/SO/06-G01 | BAZOURIET | \$90,527.00 | \$90,254.00 | \$115,847.74 | NS | Post | 225 days | 60 days | 100% | | | | | | | |
| 165 | SOUR | SL/SO/19-G01 | TAIR FELSSIEH | \$17,545.00 | \$17,510.24 | \$17,510.24 | NS | Post | 225 days | 30 days | 100% | | | | | | | |
| 166 | SOUR | SL/SO/16-G01 | NAQOURA | \$173,450.00 | \$172,322.58 | \$198,153.57 | NCB | Post | 225 days | 90 days | 100% | | | | | | | |
| 168 | SOUR | SL/SO/45-G01 | DEIR QANOUN RASS AIN | \$34,583.00 | \$34,530.80 | \$34,530.80 | NS | Post | 225 days | 60 days | 100% | | | | | | | |
| 14 | ZAHLE | BK/ZA/26-G01 | AIN KFARZABAD | \$12,860.00 | \$12,731.40 | \$12,731.40 | NS | Post | 150 days | 30 days | 100% | | | | | | | |
| 15 | ZAHLE | BK/ZA/14-G01 | KOUSSAYA | \$28,780.00 | \$28,492.20 | \$26,802.60 | NS | Post | 150 days | 60 days | 100% | | | | | | | |
| 33 | ZAHLE | BK/ZA/25-G01 | TERBOUL | \$56,933.00 | \$56,364.00 | \$56,364.00 | NS | Post | 150 days | 90 days | 100% | | | | | | | |
| 40 | ZAHLE | BK/ZA/20-G01 | REIT | \$6,854.00 | \$6,732.00 | \$6,732.00 | NS | Post | 270 days | 30 days | 100% | | | | | | | |
| 41 | | | | | | | | | | | | | | | | | | |
| 42 | | | | | | | | | | | | | | | | | | |
| 181 | BATCH 2 | | | \$1,519,557.45 | \$1,366,614.09 | \$1,366,601.91 | | | | | | | | | | | | 8/30 |
| 182 | BINT JBEIL | NA/BJ/06-G02 | BARAACHIT | \$59,742.33 | \$59,682.59 | \$59,682.59 | NCB | Post | 240 days | 90 days | 0% | 3/22 | | | | | | 7/23 |
| 187 | BINT JBEIL | NA/BJ/24-G02 | SRIBBINE | \$91,768.66 | \$91,722.78 | \$91,722.78 | NCB | Post | 240 days | 90 days | 90% | | | | | | | 6/18 |
| 194 | BINT JBEIL | NA/BJ/31-G02 | BEIT YAHOUN | \$65,942.00 | \$65,876.06 | \$65,876.06 | NCB | Post | 240 days | 60 days | 100% | | | | | | | 5/20 |
| 195 | BINT JBEIL | NA/BJ/34-G02 | KOUNINE | \$158,877.33 | \$158,717.12 | \$158,717.12 | NCB | Post | 240 days | 90 days | 100% | | | | | | | 4/2 |
| 196 | BINT JBEIL | NA/BJ/22-G02 | YATER | \$88,103.33 | \$88,000.00 | \$88,000.00 | NCB | Post | 240 days | 60 days | 100% | | | | | | | 4/3 |
| 197 | BINT JBEIL | NA/BJ/04-G02 | AYTAROUN | \$43,280.00 | \$43,063.60 | \$43,063.60 | NS | Post | 240 days | 60 days | 0% | | | | | | | 5/3 |
| 209 | BINT JBEIL | NA/BJ/09-G03 | DEBBEL | \$100,996.70 | \$100,693.67 | \$100,693.67 | NCB | Post | 240 days | 90 days | 5% | | | | | | | 6/18 |
| 210 | BINT JBEIL | NA/BJ/16-G02 | RMEICH | \$34,179.33 | \$34,162.24 | \$34,162.24 | NS | Post | 225 days | 60 days | 100% | | | | | | | 4/30 |
| 211 | BINT JBEIL | NA/BJ/23-G02 | RAMIA | \$50,000.00 | \$0.00 | \$0.00 | NS | Post | 225 days | 60 days | 0% | | | | | | | 7/30 |
| 214 | BINT JBEIL | NA/BJ/13-G02 | KAFRA | \$56,450.00 | \$56,390.89 | \$56,390.89 | NCB | Post | 240 days | 60 days | 0% | | | | | | | 6/30 |
| 215 | BINT JBEIL | NA/BJ/33-G02 | RCHAF | \$54,733.00 | \$54,666.67 | \$54,666.67 | NCB | Post | 240 days | 60 days | 0% | | | | | | | 7/4 |
| 218 | BINT JBEIL | NA/BJ/35-G02 | JMEYJMEH | \$21,510.00 | \$21,472.59 | \$21,472.59 | NS | Post | 225 days | 30 days | 100% | | | | | | | 4/9 |
| 185 | MARJOYOUN | NA/MA/09-G02 | KFARKILA | \$51,718.00 | \$35,735.76 | \$35,731.84 | NCB | Post | 240 days | 60 days | 100% | | | | | | | |
| 186 | MARJOYOUN | NA/MA/06-G02 | HOULA | \$49,844.00 | \$49,794.16 | \$49,785.90 | NS | Post | 225 days | 60 days | 100% | | | | | | | |
| 200 | MARJOYOUN | NA/MA/23-G02 | MAJDEL SELEM | \$147,242.67 | \$146,208.66 | \$146,208.66 | NCB | Post | 240 days | 90 days | 100% | | | | | | | 6/16 |
| 202 | MARJOYOUN | NA/MA/08-G02 | KABRIKHA | \$22,494.00 | \$22,282.75 | \$22,282.75 | NS | Post | 225 days | 30 days | 100% | | | | | | | 5/1 |
| 203 | MARJOYOUN | NA/MA/20-G02 | RUB TLATINE | \$25,373.33 | \$25,322.59 | \$25,322.59 | NS | Post | 225 days | 30 days | 0% | | | | | | | 4/15 |
| 206 | MARJOYOUN | NA/MA/13-G02 | TAYBEH | \$181,778.67 | \$181,413.79 | \$181,413.79 | NCB | Post | 240 days | 90 days | 0% | | | | | | | 6/1 |
| 201 | NABATIEH | NA/NA/20-G02 | KSAYBEH | \$10,652.77 | \$10,614.06 | \$10,614.06 | NS | Post | 225 days | 30 days | 100% | | | | | | | |
| 188 | SOUR | SL/SO/42-G02 | SIDDIKINE | \$44,300.00 | \$44,276.71 | \$44,276.71 | NS | Post | 225 days | 60 days | 100% | | | | | | | 4/29 |
| 189 | SOUR | SL/SO/52-G02 | ZIBKINE | \$76,563.33 | \$76,517.40 | \$76,517.40 | NCB | Post | 240 days | 60 days | 100% | | | | | | | 4/20 |

| | | |
|---|--|---|
| Project: Procurement Plan Updated: Fri 5/28/10 | EXECUTION PHASE  | Summary  |
| | WORK STOPPING DUE TO THE RAIN SEASON  | PROCUREMENT PHASE  |

PROCUREMENT PLAN
COMPONENT 1 : Reconstruction of Public Infrastructure

| ID | CAZA | ID PROJECT | MUNICIPALITY / VILLAGE | Bid Package Cost Estimate | Original Contract Amount \$ | contract after variation order | Proc. Method | WB Review | Forecasted Proc. Duration | Project Duration | % Work Complete | | | | | | | | |
|-----|-------------------------|---------------------|------------------------|---------------------------|-----------------------------|--------------------------------|--------------|-------------|---------------------------|------------------|-----------------|---|------|-----|---|-----|---|---|------|
| | | | | | | | | | | | | 3 | 4 | 5 | 6 | 7 | 8 | 9 | |
| 190 | SOUR | SL/SO/16-G02 | NAQUOURA | \$84,008.00 | \$0.00 | \$0.00 | NCB | Post | 240 days | 60 days | 0% | | | | | 7/2 | | | 8/30 |
| 193 | | | | | | | | | | | | | | | | | | | |
| 219 | | | | | | | | | | | | | | | | | | | |
| 220 | BATCH 3 | | | \$813,823.65 | \$793,128.84 | \$793,128.84 | | | | | | | | | | | | | 8/28 |
| 248 | BAALBECK | BK/BA/30-G02 | NABI CHIT | \$15,533.00 | \$15,378.00 | \$15,378.00 | NS | Post | 225 days | 30 days | 0% | | 4/15 | | | | | | 6/16 |
| 241 | BENT JBEIL | NA/BJ/05-G02 | BEIT LIF | \$196,696.67 | \$196,106.58 | \$196,106.58 | NCB | Post | 240 days | 90 days | 100% | | | | | | | | 5/20 |
| 242 | BENT JBEIL | NA/BJ/01-G02 | AIN EBEL | \$29,704.67 | \$29,541.55 | \$29,541.55 | NS | Post | 225 days | 60 days | 0% | | | 5/3 | | | | | 7/23 |
| 247 | BENT JBEIL | NA/BJ/11-G03 | HARYSS | \$25,668.00 | \$25,537.01 | \$25,537.01 | NS | Post | 225 days | 60 days | 100% | | | | | | | | 5/20 |
| 240 | JEZZINE | SL/JE/21-G02 | RIHAN | \$24,013.33 | \$23,941.29 | \$23,941.29 | NS | Post | 225 days | 30 days | 50% | | | | | | | | 5/30 |
| 221 | MARJOYOUN | NA/MA/04-G02 | DEIR MIMASS | \$29,998.00 | \$29,933.33 | \$29,933.33 | NS | Post | 225 days | 60 days | 0% | | | 5/2 | | | | | 6/30 |
| 224 | MARJOYOUN | NA/MA/11-G02 | KLAYAAT | \$38,626.67 | \$38,530.10 | \$38,530.10 | NS | Post | 225 days | 60 days | 0% | | 4/1 | | | | | | 7/23 |
| 227 | MARJOYOUN | NA/MA/24-G02 | MARKABA | \$25,281.33 | \$25,568.69 | \$25,568.69 | NS | Post | 225 days | 60 days | 100% | | | | | | | | 5/20 |
| 251 | MARJOYOUN | NA/MA/21-G02 | KANTARA | \$16,610.67 | \$16,527.61 | \$16,527.61 | NS | Post | 225 days | 30 days | 0% | | | | | | | | 6/9 |
| 239 | NABATIEH | NA/NA/28-G02 | ZAWTAR EL CHARKIEH | \$39,010.66 | \$38,932.65 | \$38,932.65 | NS | Post | 225 days | 60 days | 15% | | | | | | | | 6/21 |
| 245 | NABATIEH | NA/NA/37-G01 | YOHMOR | \$22,710.66 | \$22,699.31 | \$22,699.31 | NS | Post | 225 days | 60 days | 0% | | | | | | | | 7/23 |
| 255 | NABATIEH | NA/NA/35-G02 | CHOUKINE | \$28,308.67 | \$28,293.85 | \$28,293.85 | NS | Post | 225 days | 60 days | 100% | | | | | | | | |
| 228 | SOUR | SL/SO/08-G02 | CHHOUR | \$13,926.00 | \$13,193.04 | \$13,193.04 | NS | Post | 225 days | 30 days | 100% | | | | | | | | 4/28 |
| 229 | SOUR | SL/SO/33-G02 | CHAMAA | \$20,543.33 | \$20,440.62 | \$20,440.62 | NS | Post | 225 days | 30 days | 100% | | | | | | | | 4/28 |
| 230 | SOUR | SL/SO/02-G02 | AIN BAAL | \$17,524.66 | \$0.00 | \$0.00 | NS | Post | 225 days | 30 days | 0% | | | 5/3 | | | | | 8/6 |
| 233 | SOUR | SL/SO/41-G02 | BORGHILIEH | \$59,533.33 | \$58,938.00 | \$58,938.00 | NCB | Post | 240 days | 60 days | 0% | | | | | | | | 7/10 |
| 236 | SOUR | SL/SO/03-G02 | AYTIT | \$30,688.67 | \$30,673.22 | \$30,673.22 | NS | Post | 225 days | 60 days | 0% | | | 5/3 | | | | | 7/6 |
| 246 | SOUR | SL/SO/50-G02 | MAJDELZOUN | \$48,880.67 | \$48,861.11 | \$48,861.11 | NS | Post | 225 days | 60 days | 30% | | | | | | | | 7/20 |
| 252 | SOUR | SL/SO/45-G02 | DEIR KANOUN RAS EL AYN | \$10,862.66 | \$10,808.35 | \$10,808.35 | NS | Post | 225 days | 30 days | 100% | | | | | | | | 3/25 |
| 253 | SOUR | SL/SO/18-G02 | SRIFA | \$33,851.33 | \$33,833.08 | \$33,833.08 | NS | Post | 225 days | 60 days | 100% | | | | | | | | 4/29 |
| 254 | SOUR | SL/SO/34-G02 | BOUSTAN | \$49,910.67 | \$49,810.85 | \$49,810.85 | NCB | Post | 240 days | 60 days | 100% | | | | | | | | 5/20 |
| 256 | AKKAR | NL/AK/50-G01 | KOBET CHAMRA | \$35,940.00 | \$35,580.60 | \$35,580.60 | NS | Post | 225 days | 60 days | 0% | | | | | | | | 8/28 |
| 169 | | | | | | | | | | | | | | | | | | | |
| 170 | Mun. surrounding | NBC | | \$3,500,000.00 | \$2,945,314.80 | \$3,216,859.58 | | | 0 days | 0 days | 0% | | | | | | | | |
| 171 | AKKAR | NL/AK/06-G01 | BEBNINE | \$933,514.00 | \$783,970.88 | \$783,970.88 | NCB | Prior | 180 days | 180 days | 30% | | | | | | | | |
| 180 | AKKAR | NL/AK/54-G01 | ALMOHAMMARA | \$104,146.00 | \$103,050.42 | \$103,050.42 | NCB | Post | 180 days | 60 days | 100% | | | | | | | | |
| 172 | MOUNIEH DONIEH | NL/MD/13-G01 | MOUNIEH | \$1,220,835.00 | \$1,062,585.54 | \$1,220,597.00 | NCB | Prior | 180 days | 210 days | 100% | | | | | | | | 7/23 |
| 173 | MOUNIEH DONIEH | NL/MD/05-G01 | BHANINE | \$302,042.00 | \$257,201.03 | \$294,532.99 | NCB | Prior | 180 days | 150 days | 100% | | | | | | | | |
| 174 | MOUNIEH DONIEH | NL/MD/08-G01 | DEIR AMMAR | \$356,494.00 | \$320,788.20 | \$356,121.53 | NCB | Prior | 180 days | 150 days | 100% | | | | | | | | |
| 175 | MOUNIEH DONIEH | NL/MD/02-G01 | BADDAWI | \$458,908.00 | \$417,718.73 | \$458,586.76 | NCB | Prior | 180 days | 180 days | 100% | | | | | | | | |
| 176 | MOUNIEH DONIEH | NL/MD/13-G01 | MOUNIEH(G02) | \$124,061.00 | \$0.00 | \$0.00 | NCB | Post | 180 days | 60 days | 0% | | | | | | | | |
| 179 | | | | | | | | | | | | | | | | | | | |

Project: Procurement Plan
Updated: Fri 5/28/10

EXECUTION PHASE

WORK STOPPING DUE TO THE RAIN SEASON



Summary

PROCUREMENT PHASE

