

Social Monitoring Report

Project Number: 47235-001
February 2017

Pakistan: Trimmu and Panjnad Barrages Improvement Project Loans 3159/3160

Internal Resettlement Monitoring Report

Prepared by the Project Management Office (PMO) for Punjab Barrages, Irrigation Department, Punjab for the Asian Development Bank (ADB).


The social monitoring report is a document of the borrower. The views expressed herein do not necessarily represent those of ADB's Board of Directors, Management, or staff, and may be preliminary in nature.

In preparing any country program or strategy, financing any project, or by making any designation of or reference to a particular territory or geographic area in this document, the Asian Development Bank does not intend to make any judgments as to the legal or other status of any territory or area.

GOVERNMENT OF THE PUNJAB, IRRIGATION DEPARTMENT



Trimmu-Panjnad Barrages Improvement Project (TPBIP)

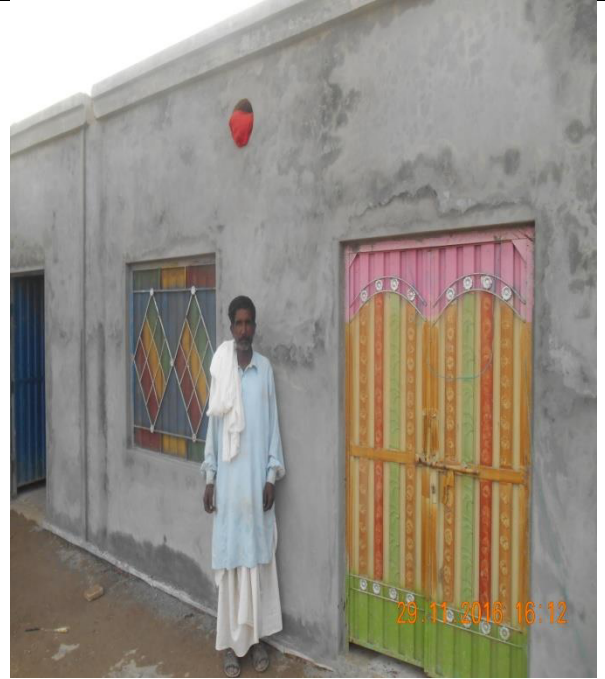

INTERNAL RESETTLEMENT MONITORING REPORT
Quarter Oct-Dec. 2016



NATIONAL ENGINEERING SERVICES
PAKISTAN (PVT.) LIMITED
1-C, Block-N, Model Town Ext.
Lahore-Pakistan

TABLE OF CONTENTS

| | |
|--|----------|
| 1. BACKGROUND | 1 |
| 2. RESETTLEMENT IMPACTS..... | 1 |
| 3. STATUS OF LARP IMPLEMENTATION..... | 1 |
| 3.1 Compensation to the Affected Persons..... | 1 |
| 3.2 Unpaid Compensation Cases | 1 |
| 3.3 Relocation of Affected Persons (APs) | 2 |
| 4. ACTIVITIES CARRIED OUT DURING THE QUARTER PERIOD | 2 |
| 4.1 Relocation of Residential Structures | 2 |
| 4.2 Cases of Widows of Compensation | 3 |
| 4.3 Relocation of Commercial Structures:..... | 3 |
| 4.4 Relocation of Community Mosque | 3 |
| 4.5 AFs losing Agriculture/Crops..... | 4 |
| 5. CONSULTATION | 4 |
| 5.1 Consultation after Displacement | 4 |
| 6. EMPLOYMENT TO THE APS | 4 |
| 7. COMPARISON OF APS RESIDENTIAL STRUCTURES (BEFORE-PROJECT AND AFTER PROJECT)..... | 4 |
| 8. CONCLUSIONS..... | 4 |
| Annexure-I&II A Sample Showing Receipt of Compensation..... | 7 |
| Annexure-III. Compensation Unpaid Female APs | 9 |
| Annexure-IV Comparison of Before Displacement and After Displacement of APs..... | 11 |
| Residential Structures | |

Abbreviation

| | |
|--------|---|
| ADB | Asian Development Bank |
| AP | Affected Person |
| DP | Displaced Person |
| LARP | Land Acquisition & Resettlement Plan |
| NESPAK | National Engineering Services, Pakistan |
| PID | Punjab Irrigation Department |
| PIU | Project Implementation Unit |
| PMO | Project Management Office |
| SDO | Sub Divisional Officer |
| SPS | Safeguard Policy Statement |
| TPB | Trimmu-Panjnad Barrages |

Trimmu-Panjnad Barrages Improvement Project (TPBIP)

1. BACKGROUND

The Government of Punjab is intended to improve and rehabilitate the barrages through Punjab Irrigation Department with the financial assistance of Asian Development Bank (ADB). The main objective of the rehabilitation and upgrading program is to enhance the water supply for sustainable irrigated agriculture. The TPBIP is the part of this rehabilitation and up-dation program. Apart from other project tasks, the rehabilitation of the barrage involved the land acquisition and resettlement impact of the project. Hence, a Land Acquisition and Resettlement Plan (LARP) was prepared by the Project Management Office (PMO) and approved by the ADB in 2014.

2. RESETTLEMENT IMPACTS

The construction work is limited to Government owned land and no impact was reported on the private land. In term of resettlement impact, there were total 112 households, impacted through structure, crop, small businesses and trees. In addition, one community structure (Mosque) is also impacted. These included affectees of 62 household's structures, 09 APs were small business operators/fish sellers etc., 12 APs were agriculturists and remaining 29 affectees were involved in fishing occupation (boatmen). Except fishermen and small business operators, other APs are under project impacts permanently.

3. STATUS OF LARP IMPLEMENTATION

3.1 Compensation to the Affected Persons

The LARP is being implemented successfully as per ADB, s Safeguard Policy Statement (SPS) 2009 and National Laws. The compensation payment has been paid to 93 percent of the total affected households till the end of September 2016. The compensation was paid in two phases mentioned as below:

Phase-I Compensation paid to 35 APs in June 2016.

Phase-II Compensation paid to 70 APs in July 2016.

Thus total 105 APs have been received compensation. The details of the APs were provided in the previous report of July-Sep. 2016. A sample of receipt of compensation showing the total amount of all lost structures and assets is provided in the Annexure-I & II.

3.2 Unpaid Compensation Cases

Now there are 07 Affected Persons, who are not yet paid. Six are females (Widows), because their husbands are died and the 7th AP has also died in April 2016 and waiting for his legal inherent papers. The details of these cases are provided in the following Table-1.

| Type of AFs | Total AFs | Compensated AFs (Nos) | Remaining AFs To be compensated | Remarks |
|----------------|-----------|-----------------------|---------------------------------|---------|
| Small Business | 09 | 07 | 02 | |
| Agri. crops | 12 | 12 | - | |

| Type of AFs | Total AFs | Compensated AFs (Nos) | Remaining AFs To be compensated | Remarks |
|--------------|------------|-----------------------|---------------------------------|---------|
| Boatmen | 29 | 27 | 02 | |
| Total | 112 | 105 | 07 | |

- Total 65 residential AFs (Trimmu 62 and Panjand 3)

Their spouses are eligible to receive compensation, but the Director finance PMO Barrages did not agree and demanded succession letter from the court. The affected structures are not registered in the Revenue department and do not fall under judicial procedure for inheritance. The compensation is assistance for rehabilitation of the displaced persons. The next family person (preferably wife) who is also entered in the Proforma of census survey of DPs is the real rightful and beneficiary of the compensation.

3.3 Relocation of Affected Persons (APs)

Before payment of compensation to the APs, there was a concern that after receiving compensation, the APs may take long time to vacate the site. The Project Authority had opinion that some APs may refuse to vacate the site with unexpected new demand causing delay to start the project activities. But due to close coordination, fair measurements of their affected structures, frequent meetings and consultation with them and timely payment to arrange alternate place, the site eviction process completed very shortly and smoothly without any issue. At the end of September 2016, 100 percent APs were moved from the project site and were busy in new construction of their houses. They are relocating near by the project area as they desired to intact with their businesses and relationship with the other peoples and communities in the surroundings.

4. ACTIVITIES CARRIED OUT DURING THE QUARTER PERIOD

4.1 Relocation of Residential Structures

Different locations of APs for their relocation of residential structures were visited to assess the situation. The purpose of the visit was to provide morally support and encourage them in their resettlement process.

During the month of November, meetings with the displaced persons at various sites were conducted. The status of their houses under construction was observed. It was noted that about 40 percent of their compensation amount is being spent on account of purchase of residential plot. The project provided them a fixed amount of Rs.120000 for relocation that proved in-sufficient to purchase a plot with reasonable size (10 marla). Because about every household have small numbers of livestock units as a economic asset to utilize during severe needs or hard time. Therefore, they have to buy a plot of medium size. They showed deep concern that construction of the same number of rooms as before project seem too difficult because financial constraints, while few of them showed their satisfaction that they have constructed new houses with in the limit of project compensation amount. The distribution of relocation of 62 DPs losing residential structures is shown in the following Table-2.

Table-2 Showing Relocation Sites of 62 DPs Losing Residential Structures

| No. of DPs | Relocation Site | Remarks |
|------------|---|---|
| 40 | New basti Muhammad Bukhsh, near the existing place | To intact with their earnings and community. |
| 07 | About one 3kilometre from the existing place | Same reason |
| 11 | On Jhang road, near kauray (fish farm and market) about 4 kilometresr from the existing place | They also continued their previous occupations. |
| 04 | Moved to near City Jhang (Sargodha Road). | Started work as labourer in the city. |

4.2 Cases of Widows of Compensation

The pending cases were completed and submitted to PMO. The matter of pending cases of widows regarding compensation was discussed and explained the policy of ADB to the Deputy Director Procurement to release the payment. But the Director Procurement, PMO did not agree and demanded succession letter from the court which is against the ADB safeguard IR policy. Now these widows are still deprived from their compensation, although they have vacated the site in the interest of the project. Due to winter, the widows with their families are living with their relatives and facing severe social problems etc.

These female APs are as follow:

| | |
|----------------|-------|
| Zafra Bibi | T-018 |
| Shahzadan Bibi | T-072 |
| Safya Bibi | T-073 |
| Sughran Bibi | T-057 |
| NooranBibi | T-107 |
| Siddiqa Begum | T-108 |

The above-mentioned cases are under process and hopefully be completed soon.

4.3 Relocation of Commercial Structures:

All APs have been shifted on main Jhang road about one kilometer away from the existing place. They have established their selling points with the improved condition for more attraction of the customers. Their relocation of business structures/points were shown in the previous report.

4.4 Relocation of Community Mosque

The community structure of Mosque has been demolished and material is shifted to the new site. The Mosque committee is waiting for the compensation to re-construct the mosque in the Basti Muhammad Bukhsh. The case is in the process with the PMO for award of compensation. The Director procurement demanded certificate showing that the mosque has been registered in the Auqaf department. The Community was contacted to produce the required document to release the compensation.

4.5 AFs losing Agriculture/Crops

All the Government agricultural lands fall in the project area were occupied by different farmers (squatters). There was not one AFs losing entire land. There were 12 AFs losing agriculture land and crops. Out of 12 AFs, 05 AFs lost entire land under cultivation falling upstream and downstream of the Trimmu barrage. These AFs also own private land in their respective villages. Although, they are losing their income, but they were cultivating government land without any payment etc. Due to Project intervention, they had to vacated state land and the project compensated them reasonably as per ADB IR Policy 4.12 under SPS-2009.

5. CONSULTATION

5.1 Consultation after Displacement

The Consultants Social team as well as PMO Social and Environment unit is persistently in coordination with the affected persons. All APs are satisfied with the cooperation and positive attitude of the social staff regarding compensation and moral support after displacement.

6. EMPLOYMENT TO THE APS

A Contract Clause 6.1 "Particular Condition of the Contract" bound the Contractor to provide jobs to skilled / unskilled persons, particular Affected Persons to restore their livelihoods. In this regard, APs were updated to apply, if they need jobs at project site. Total 43 applications were received from the willing APs and list of these APs was handed over to the Contractor at site. It is very encouraging that during the month of November and December. 2016, jobs are provided to six APs (4 jobs in November and 2 jobs in December). With the increase of project activities, more jobs will be provided to the APs.

7. COMPARISON OF APS RESIDENTIAL STRUCTURES (BEFORE-PROJECT AND AFTER PROJECT)

During the field visit, newly constructed house to house survey was conducted and photographs with APs were taken. The purpose was to make comparison, what was the residential condition of the APs before shifting and after receiving compensation, what is the condition of their newly constructed houses. After completion, all houses of the APs, a detailed report will be prepared showing the comparison and difference. However, few snaps of the APs are being provided as Annexure-IV.

8. CONCLUSIONS

The implementation of the LARP is being carried out by the Client and Consultant and consequently progressing satisfactorily. PMO and Consultants have made all necessary good faith efforts to make disbursement of compensation to the entitled APs. The report confirms that no issue or any payment related encumbrance found in the Project.

ANNEXURES

**Annexure- I & II
A Sample Showing receipt of Compensation**

تریموں - پنجنڈ بیراجز امپروومنٹ پراجیکٹ

Annex - L

اقرار نامہ

تاریخ اجراء 27/10/20

میں مسمیٰ مسٹر احمد ولد اللہ دے شناختی کارڈ نمبر 33202-32967610-9
پراجیکٹ شناختی نمبر 027-1- تحصیل و ضلع جھنگ جو کہ تریوں بیراج کے دائیں
جانب 13 عدد توسیعی گیلوں کی تعمیر کی سرکاری جگہ سے ملحقہ واقع بستی محمد بخش میں رہائش پذیر تھا تھی۔ اب چونکہ مذکورہ بیراج
کی توسیعی کاموں کی تعمیر شروع ہو چکی ہے اور بحوالہ دیئے گئے اقرار نامہ (انضمام) نمبر 454 تاریخ 20-12-10
میں یہ اقرار کرتا کرتی ہوں کہ متاثرہ گھرا کاروبار کاروبار کشتی ازراعت کا کل تخمینہ بیج الاؤنسز جو کہ 4,84,520 روپے
بنتے تھے اور ہمیں مختلف مشاوری میٹنگز کے دوران بتایا گیا تھا۔ آج مورخہ 27/10/20 بذریعہ چیک نمبر 684555
بینک NBP مسٹر برانچ منیجر کو 30 لاکھ روپے دے دیا گیا ہے۔ اور دیئے گئے انضمام پر اقرار نامہ کے تحت میں آج سے
30 دنوں کے اندر اندر یہاں سے شفٹ ہو جاؤں گا گی۔ اور یہ جگہ خالی کرنے کا پابند ہوں گا گی تاکہ تریوں بیراج کی
مرمت و بحالی کا کام بروقت اور احسن طریقے سے ہو سکے۔ اور میں یہ بھی اقرار کرتا کرتی ہوں کہ اگر میں نے مقررہ وقت
کے اندر یہ جگہ خالی نہ کی تو محکمہ کو میرے خلاف قانونی کارروائی کرنے کا حق حاصل ہوگا۔

گواہ
نام محمد حسین عہدہ منسٹر
دستخط محمد حسین
نمائندہ پی ایم او بیراج
چیرمین سائمن کمیٹی
نام مسٹر حسین عہدہ ڈپٹی ڈائریکٹر ایم او
دستخط مسٹر حسین
نام محمد اسلم عہدہ SDO
دستخط محمد اسلم
نام مسٹر حسین عہدہ SDO
دستخط مسٹر حسین
نام مسٹر حسین عہدہ SDO
دستخط مسٹر حسین

تربیلوں و پنجنڈہ ہزار اجیر امیر و منٹ پر اجیکٹ

اداسکی کلیمز برائے متاثرین مضروبہ

T-027

بیتا ملکاتہ قرآن

MC

5050

رجسٹریشن فیرو مقام

2

بیت کا نام

ہائیکو کڈو شہر

فتبر عام و اول الله و

33202-329761-8

1007287

1007287

تاثیر فرد کا نام بعد ولادت:

تلفیظی کارڈ نمبر:

لاؤٹ ہولڈر کا نام:

کائنات نمبر:

طیروز کی تفصیل:

10

| رقم | تفصیل نقصان (مبادئی) | تفصیل اضرار |
|----------------|----------------------|-------------------------------|
| روپے 166320 ✓ | مکرہ کی | |
| روپے 121200 ✓ | مکرہ سیسے کے | |
| روپے - | | |
| روپے - | | |
| روپے - | | |
| روپے - | | |
| روپے 287520 ✓ | گن رقم | |
| روپے 120,000 ✓ | | الاکٹریسیٹ |
| روپے 500 ✓ | | تور آؤڈیکریٹ الائنس |
| روپے 36000 ✓ | | بہار ملریٹ الائنس |
| روپے 36000 ✓ | | ڈسٹریکٹ الائنس |
| روپے - | | کارڈریٹ الائنس |
| روپے - | | زری مکملیٹ الائنس |
| روپے - | | سٹریٹ الائنس |
| روپے - | | ماریٹیٹ نقصان / روزگار کا زخم |
| روپے 197000 ✓ | گن رقم | |
| روپے 484520 ✓ | کل میزبان (الف + ب) | |

جـ

✓ 9. 11

نہ کہنے گا، نہ کہنے گا،

حکمت کا ستارہ و تقسیم:

نقصان دکن

۱. ۲. ۳. ۴. ۵. ۶. ۷. ۸. ۹. ۱۰. ۱۱. ۱۲. ۱۳. ۱۴. ۱۵. ۱۶. ۱۷. ۱۸. ۱۹. ۲۰. ۲۱. ۲۲. ۲۳. ۲۴. ۲۵. ۲۶. ۲۷. ۲۸. ۲۹. ۳۰. ۳۱. ۳۲. ۳۳. ۳۴. ۳۵. ۳۶. ۳۷. ۳۸. ۳۹. ۴۰. ۴۱. ۴۲. ۴۳. ۴۴. ۴۵. ۴۶. ۴۷. ۴۸. ۴۹. ۵۰. ۵۱. ۵۲. ۵۳. ۵۴. ۵۵. ۵۶. ۵۷. ۵۸. ۵۹. ۶۰. ۶۱. ۶۲. ۶۳. ۶۴. ۶۵. ۶۶. ۶۷. ۶۸. ۶۹. ۷۰. ۷۱. ۷۲. ۷۳. ۷۴. ۷۵. ۷۶. ۷۷. ۷۸. ۷۹. ۸۰. ۸۱. ۸۲. ۸۳. ۸۴. ۸۵. ۸۶. ۸۷. ۸۸. ۸۹. ۹۰. ۹۱. ۹۲. ۹۳. ۹۴. ۹۵. ۹۶. ۹۷. ۹۸. ۹۹. ۱۰۰.

اکاؤٹ نمبر:

شماره: _____

0.000 0.000 0.000

۱۵۲۱

Annexure-III
Compensation Unpaid Female APs






Annexure-IV
Comparison of Before Displacement and After
Displacement of APs Residential Structures

Before Displacement



Case No.62 Muhammad Akhter

After Displacement

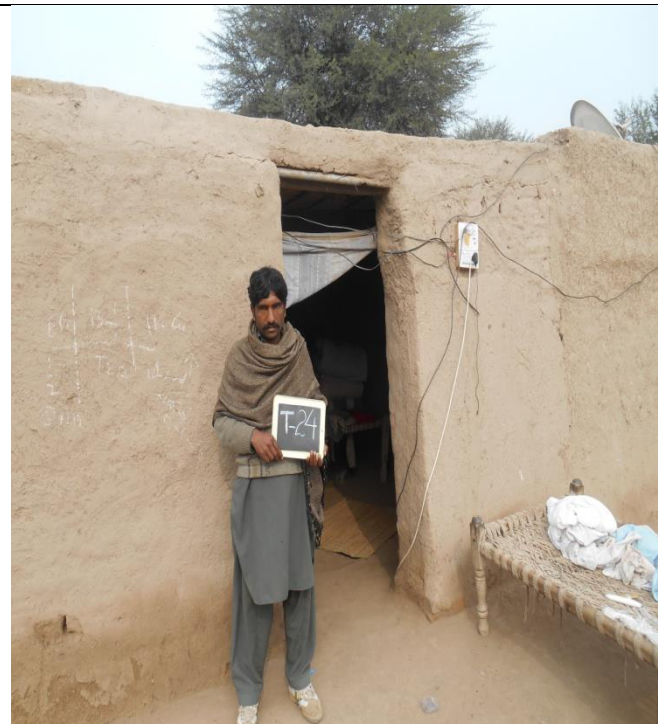

Case No.24 Manzoor Hussain





Before Displacement



Case No. 46 Hasna Bibi

After Displacement

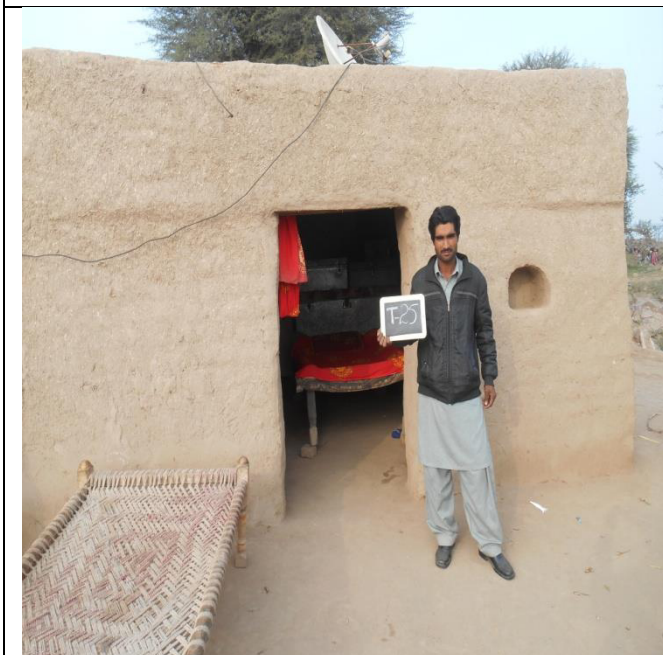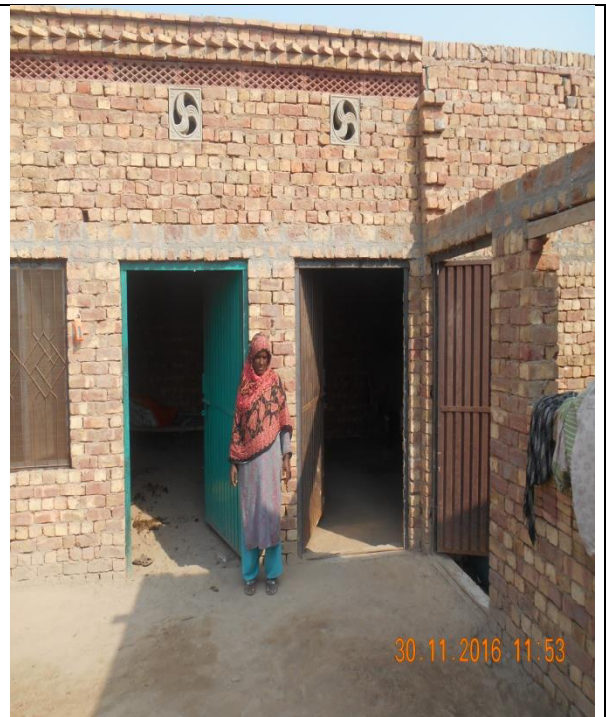

Case No.25 Muhammad Saleem

