

Social Monitoring Report

1st Internal Monitoring Report (N-70 - Qila Saifullah-Loralai-Waigum Rud Road Project)
(Jan – March 2017)

PAK: National Highway Development Network in Balochistan

NOTES

- (i) The fiscal year (FY) of the Government of the Islamic Republic of Pakistan and its agencies ends on 30 June.
- (ii) In this report, "\$" refers to US dollars.

This social monitoring report is a document of the borrower. The views expressed herein do not necessarily represent those of ADB's Board of Directors, Management, or staff, and may be preliminary in nature.

In preparing any country program or strategy, financing any project, or by making any designation of or reference to a particular territory or geographic area in this document, the Asian Development Bank does not intend to make any judgments as to the legal or other status of any territory or area.

NATIONAL HIGHWAY AUTHORITY



(N-70)

Qila Saifullah - Loralai - WaigumRud (120 km)

Road Project

Internal Monitoring Report

Of RP Implementation

05th April 2017

1st Quarterly Report (January – March, 2017)

Quarterly Internal Monitoring Report of Qila Saifullah – Loralai – WaigumRud Section (N-70)

1. Introduction

1. Through ADB financial support, National Highway Authority (NHA), Pakistan is upgrading Qila Saifullah-Loralai-WaigumRud Section of N-70 under National Highway Network Development in Baluchistan Project (NHNDP) through loan Pak 3134. The designated NHA owned ROW of project road section is 110 feet in urban areas and 220 feet in rural areas and project did not entail acquisition of land. However, to address the resettlement issues in sections wherever ROW was encroached near settlements and agricultural land along the project road, NHA endorsed updated resettlement plan was cleared by ADB in January 2017. Immediate after clearance of updated resettlement plan, implementation activities were started for compensating impacted before clearing the encroached sections of ROW and to ensure implementation of project is consistent with ADB's IR requirements. The RP implementation require day to day monitoring of implementation progress and compile quarterly monitoring reports for ADB's review and acceptance. Accordingly this first monitoring report is prepared that covers the implementation progress achieved between January to March 2017.

1.1. Objectives of the IMR

2. The objective of this internal monitoring report is to:

- Review and assess progress on payment of compensation for assets and entitled allowances to the DPs;
- Review progress on efforts implemented and ccoordination activities/actions performed to outreach affected communities for information dissemination and facilitate them in compensation processing and payment.
- Consultations, recording, tracking and handling of grievances at local and GRC levels.
- Recommend actions for improved RP implementation and execution of project works.

1.2. MONITORING METHODOLOGY

3. Methodolgy for this monitoring report includes a review of LARP implementation progress data and consultations with key informants and the displaced persons. The monitoring instruments included review of progress on the a) institutional set-up placed for RP implementation, b) RP disclosue and community outreach efforts implementd, c) compensation payment progress achieved for impacted assets, d) consultations progress and meeting proceedings by DPC and project GRC etc. Based on the review the results are summarized in the sections below explaining the achieved progress and actions required to improve the progress.

2. Updated Resettlement Plan and RP implementation process.

2.1. Project Description

4. Existing Qila Saifullah-Loralai-WaigumRud section of N-70 is single lane carriageway that is located in territorial jurisdiction of two districts i.e district Qila Saifullah and district Loralai of Balochistan. In District Qila Saifullah area the road section traverses through barren hilly tract and rolling landscape with no settlements along the road corridor, while in District Loralai the landscape is mostly even with scattered settlements and agricultural land along the road. The designated ROW of project road section is 110 feet in urban areas and 220 feet in rural areas.

5. The Project road sections are the part of the National Highway N-70 in Northern Baluchistan and it starts at Qila Saifullah on N-50, and terminates at WaigumRud with a total length of 120 km. For rehabilitation and improvement works the project road has been divided into two sections: Lot-I is from RD 0+000 to RD 67+900 (before entering into Loralai city), and Lot-II starts after crossing Loralai city at RD 78+500 to RD 128+375.

6. The project works include rehabilitation and upgrading of existing single lane Qila Saifullah-Loralai-WaigumRud Section of N-70 road into 7.3 meter wide carriageway with 2.5 meter shoulders on each side. As per design the total pavement width of the road is 13.3 meters (44 ft.). The National Highway Authority is the Executing Agency (EA) for the project. The Project will rehabilitate and improve project section of National Highway N-70 to provide a dependable road network for local communities and interprovincial connectivity with reduced transportation time and costs.

2.2. Updated Resettlement Plan

7. During detailed design and subsequent design review efforts are ensured to avoid and minimize the adverse impacts on privately owned land and properties along the road. Accordingly, the road alignment is adjusted within the available ROW limits to avoid land acquisition and by adjustments in vertical and horizontal alignment resettlement impacts on the private assets encroached in the ROW limits have been minimized to the best possible extent. The draft Resettlement Plan (RP) for Qila Saifullah-Loralai-WaigumRud Section of N-70 project was prepared based on the detailed design of 2011 which is updated in 2016 as final RP after design review by the Design and Construction supervision consultants.

8. NHA endorsed draft resettlement plan was updated after completing design review in 2016 which is cleared by ADB in January 2017. The project resettlement impacts were scattered in small portions of the road, hence to facilitate implementation of project works, ADB allowed the works in LAR free areas based on due diligence reports cleared in October 2016 and the identified LAR section were kept on hold to update the RP in parallel. Nonetheless, the project works will not be allowed until confirmation of full implementation of ADB cleared updated resettlement plan. As per updated RP a summary of DPs entitled for compensation by category of impact due to clearance of COI is presented in table 2.1 below.

Table 2.1 Impact type with number of displaced households

S#	Assets to be compensated as per updated RP	Entitled Displaced Persons
1	Agricultural infrastructure (farm boundary walls, main hole, water ponds/channels, gate pillars, pipelines (Concrete & Plastic), water tanks, well, dry well, service station)	125
2	Shops and veranda	24
3	Other miscellaneous structures (kiosks, huts, cabins, electric pole sign board and dispensing units of petrol pumps requiring shifting	29

S#	Assets to be compensated as per updated RP	Entitled Displaced Persons
4	Rental business operators	23
5	Trees	177
6	Community structures/mosques	3
7	Public / government structures	14
9	Households facing loss of rented in commercial structures	23
Total Displaced Households/DPs		294*
* Seven Public/government Institutions facing loss of assets located at different locations and 3 community structures (mosques) are not counted in total. The DHs lose different categories of assets. Total entitled Households/DPs to be paid for different loss types is 294 (without double-counting).		

9. In total 294 DPs will face loss of their assets and livelihood source established within the ROW limits in different LAR sections of the project road. The number of DPs entitled for compensation in withheld LAR sections on both contract packages (Lot-1 and Lot-2) are presented in table 2.2 below.

Table 2.2 LAR sections as of updated RP with number of DPs.

Contract Package Lot-1 RD (0+500 to 69+200) LAR sections.				Contract Package Lot-2 RD (78+500 to 128+375) LAR sections			
S#	Chainage (km)	LAR Area	DPs	S#	Chainage (km)	LAR Area	DPs
1	29+450 to 34+550	5.0 km	10	1	78+500 to 82+700	4.2 km	26
2	36+500 to 36+750	0.2 km	8	2	83+700 to 101+700	18.0 km	50
3	40+250 to 40+400	0.1 km	6	3	105+000 to 105+400	0.4 km	9
4	41+100 to 41+200	0.1 km	8	4	106+350 to 110+500	4.15 km	81
5	41+350 to 42+825	1.4 km	22	5	112+200 to 112+500	0.3 km	7
6	44+250 to 44+700	0.4 km	9	6	115+050 to 116+475	1.42 km	11
7	47+750 to 47+850	0.1 km	3	7	119+900 to 120+150	0.25 km	9
8	48+825 to 50+800	1.9 km	13	8	121+175 to 121+225	0.05 km	7
9	51+950 to 52+200	0.2 km	6	9	122+100 to 122+150	0.05 km	2
10	53+450 to 65+200	11.7 km	4	-	-	-	-
11	66+150 to 69+200	3.0 km	3	-	-	-	-
Total in Lot - 1		24.1 km	92	Total in Lot - 2		28.82 km	202

2.3. RP costs and availability of Funds

10. Based on draft RP budget, a demand for release and deposit of funds (as per draft RP budget) in project account was processed by the PMU on which NHA HQ released draft RP

cost partially and an amount of Rs. 39.74 Million was deposited in project account to start implementation of updated resettlement plan as and when it is updated. However, as per updated RP total RP cost is Rs. 109.39 million which include Rs.-98.356 million for delivery of compensation costs against affected assets and entitled allowances and Rs.11.036 million as RP implementation support cost. Upon ADB's clearance of updated RP, the RP implementation process was started with available funds and a request for release of remaining RP cost Rs.66.65 million was tendered to NHA HQ in March 2017 and it is expected that the requested LAR cost can be released by 30 April 2017.

2.4. LAR institutional Set-up and RP implementation process.

11. The LAR unit including Resettlement Specialist mobilized by the DCSC is established and project grievance redress committee is operationalized during the monitoring period. Besides, a team of two social mobilizers (one male and one female) is engaged through RP implementation support costs to assist the Resettlement Specialist and LARU in community coordination and consultations. The project grievance redress committee is notified and operational and the GRM is functioning to record and redress the grievances timely and the DPs have been explained on the GRM system available. For improved coordination, consultations and DPs participation in the GRM, 06 Displaced Persons Committees are constituted and functional at village level. Through DPC meetings, the DPs representatives and local notables are being coordinate and engaged in the grievance redress process.

12. The updated RP provisions are disclosed to the DPs and a scheduled action plan has been prepared to ensure timely disbursement of compensation. During the reporting months, disclosure efforts were continued by serving notices for compensation claims and DPs were facilitated to approach the project team for timely delivery of their compensation. A solution for small compensation amounts, like making payment through cross cheques in the name of DPs nominated Special Attorney were worked out and the DPs were informed about the process and documents to be prepared and submitted for nominating Special Attorney to collect their compensation accordingly.

3. RP Implementation Progress

9. During the reporting months, considering available RP cost (39.47 million) in the project account, instead of processing compensation claims for all 294 DPs, the payment process was started in selected sections of both contract packages (Lot-1 and Lot-2). The staggered implementation facilitated to ensure full payment of compensation in selected sections with available LAR costs and to clear these sections for construction activity.

10. A weekly plan was prepared to disburse compensation to DPs in selected LAR sections of Lot-I and Lot-II and the compensation payment was processed in two batches to ensure full implementation of RP in a speedy manner and keep a track of implementation progress and make adjustments if required. The DPs were informed accordingly through Notices to submit their claims and receive their compensation amount. The DPs who were served with notices were contacted and assisted to prepare and submit their claims and receive the compensation amount. After due scrutiny, the compensation claims were processed in two batches i.e in batch one the compensation cases of 105 DPs in Lot –II were processed while in batch-2 compensation cases for 29 DPs in Lot-1 were processed. The paras below reflect compensation payment progress achieved so far and subsequent section show DP wise payment status for each section in selected reaches.

11. Out of total 294 DPs compensation cases were processed for 134 DPs in two batches for selected sections. Accordingly 98 compensation cheques for an amount of **Rs. 18,588,401/-** were issued on 16.02.2017 to compensate **105** DPs in lot-2, whereas in Lot-I, 27 cheques for compensating **29** DPs were issued for an amount of **Rs. 14,010,188/-** on 28.02.2017. By end of monitoring period (March-2017) the cheques were distributed to the 126 DPs at their door step and the DPs were advised to remove their impacted assets and take the salvage. While the compensation cheques amounting to Rs 2,042,348/- for 8 entitled DPs remained undelivered due to unavailability of DPs in project area and some other administrative issues. The efforts are in progress to ensure the DPs having administrative issues are those went out of project area are paid in April or as and when they are available to receive compensation.

12. By close of monitoring period (March 2017), total cumulative amount of **Rs. 32,598,589/-** has been disbursed in persons and through attorneys to **134** DPs out of 294 DPs in the selected LAR section. On payment of compensation the DPs were advised to clear the ROW by removing their assets to facilitate execution of project works. The lists of compensation disbursement of Batch – 1 and 2 having signatures and thumb impressions of DPs and Pictures are attached as **Annex I**. The breakup of payment disbursement detail is shown in table 3.1 below.

Table 3.1 Compensation Payment Status

S #	Batches	Date	Total # of DPs	No of Paid DPs	Unpaid DPs	Total Amount Rs.	Disbursed Amount Rs.	Remaining Amount Rs.
1	Batch # 1	16.02.17	294	105	189	39,740,810	18,588,401	21,152,409
2	Batch # 2	28.02.17	189	29	160	21,152,409	14,010,188	7,142,221
Total Up till Now				134		43. 3 %	32,598,589	Awaiting for Remaining Amount

13. Implementation of RP and delivery of compensation in other LAR sections will continue when additional funds are available for which the NHA HQ is being coordinated closely to release and deposit demanded RP cost Rs.69,650,450/- in project account. Nonetheless, the LAR sections where compensation is not paid will remain at hold until the LARP implementation is confirmed after delivery of compensation. The compensation payment process for remaining 160 DPs in left over LAR sections will be started immediate after release and deposit of demanded RP cost **Rs. 69,650,450/-** by NHA Head Quarter in N-70 Project Resettlement Account. The sections below represent the LAR areas where compensation is fully paid and those LAR areas where compensation is yet to be paid.

3.1. Sections where Compensation is fully paid:

14. Based on available LAR funds, instead of starting delivery of compensation in all LAR sections throughout project corridor, a structured payment plan was devised to limit the payment process in selected sections in both contract packages (Lot-1 and Lot-2) for ensuring full implementation of RP is achieved to that extent and sections where RP implementation is confirmed could be cleared for construction activity. The table below represents the sections for which LAR implementation is achieved satisfactorily and 126 DPs have been paid their entitled compensation and allowances while the efforts are in progress to outreach and deliver compensation cheques to 8 DPs. The issues that restricted payment to 8 DPs by close of monitoring period included unavailability of DPs in the project area (6 DPs) and DPs having internal disputes (2 DPs). The relatives of the DPs living in project area and local notables are being coordinated to approach and deliver the compensation cheques to unpaid DPs. The Sections where RP implementation is completed are shown in linear plans attached as **Annexure – II**.

Table. 3.2: Shows below the Area Cleared by Cheques.

LOT - 1					LOT - 2				
S #	Compensation paid LAR sections	KMs	DPs Status		S#	Compensation paid LAR sections	Kms	DPs Status	
			Paid	Unpaid				Paid	Unpaid
1	29+400 - 34+600	5.2	8	Nil	1	92+600 - 92+775	0.18	7	Nil
2	44+250 - 44+700	0.45	2	Nil	2	92+825 - 94+675	1.9	9	Nil
3	48+825 - 50+800	2	3	Nil	3	95+000 - 96+750	1.75	13	Nil
4	51+950 - 53+450	1.5	4	Nil	4	97+000 - 99+400	2.4	24	Nil
5	53+480 - 56+000	2.5	5	Nil	5	99+450 - 99+750	0.3	6	Nil
6	56+100 - 60+000	3.9	7	Nil	6	99+800 - 101+150	1.35	11	Nil
					7	101+155 - 101+160	0.005	2	Nil
					8	101+165 - 101+425	0.26	6	Nil
					9	101+450 - 112+500	11	9	Nil
					10	115+000 - 116+475	1.5	5	Nil
					11	119+900 - 120+150	0.25	1	Nil
					12	121+175 - 121+225	0.05	7	Nil
					13	122+100 - 122+150	0.05	5	Nil
Total		15.6 Km	29			Total	21 Km	105	

15. As the RP has been implemented in 15.6 Km and 21 km of withheld LAR sections as mentioned in table above for both contract packages (Lot-1 and Lot-2) and could be considered to allow construction activity. Based on achieved progress a linear plan is attached as Annex-II showing sections where LAR implementation is completed (green), the sections where RP implementation is still ongoing (red) LAR free sections (white) where project works were

allowed and progressing. The ADB may consider to allow construction in 15.56 KM in Lot-1 and 21 KM in Lot-2 (areas shown in green in attached linear plan) so the said sections could be handed over to contractor for construction.

3.2. Sections where Compensation Payment is under process:

16. Based on achieved progress for payment of compensation in selected sections in both contract packages (Lot-1 and Lot-2) as presented above, the remaining sections with LAR impacts where compensation is still ongoing were reviewed and reassessed in both contract packages. The identified areas where RP implementation is still ongoing and the sections (9.38 km in (Lot-1) and 14.9 km in (Lot-2)) which are not clear yet for construction are presented in table below and shown as red in linear plan attached to the report as Annex-II. Although efforts are in progress to deliver notices for submission of compensation claims and DPs are being coordinated for facilitating them in preparation and submission of claims, however, the payment process will start immediate after receipt of requested LAR funds (Rs 66.65 million) from NHA, HQ. The Finance wing in NHA, HQ is being coordinated on daily bases for early release of funds and it is expected that the funds could be made available by close of April and accordingly disbursement of compensation to the DPs could start in May 2017 and will be completed by the time next monitoring period is due.

Table. 3.3: Shows the Area under LARP.

LOT - 1					LOT - 2				
S#	Unpaid LAR sections	KMs	DPs Status		S #	Unpaid LAR sections	Kms	DPs Status	
			Paid	Unpaid				Paid	Unpaid
1	36+500 - 36+750	0.25	Nil	2	1	78+500 - 92+600	14	Nil	68
2	40+250 - 41+200	1.0	Nil	6	2	92+775 - 92+825	0.05	Nil	1
3	42+300 - 42+850	0.55	Nil	3	3	94+675 - 95+000	0.3	Nil	9
4	47+700 - 47+850	0.15	Nil	4	4	96+750 - 97+000	0.3	Nil	7
5	53+450 - 53+480	0.03	Nil	9	5	99+400 - 99+450	0.05	Nil	2
6	56+000 - 56+100	0.1	Nil	18	6	99+750 - 99+800	0.05	Nil	3
7	60+000 - 67+300	7.3	Nil	21	7	101+150 - 101+155	0.005	Nil	1
					8	101.160 - 101+165	0.005	Nil	1
					9	101+425 - 101+450	0.2	Nil	5
Total		9.38 Km		63	Total		21 km		97

4. RP disclosure, Consultations, and Grievance Redress.

17. Immediate after clearance of RP by ADB, the DPs were coordinated to disclose RP provisions and compensation claim notices (**Annex-III**) were delivered at their door steps. Meanwhile, the DPs were clarified on compensation payment mechanism, grievance redress system available to them and were mobilized and supported to submit their compensation claims. For effective coordination the DPS were guided and supported to constitute the displaced persons committee by nominate their representatives. Accordingly the 06 DPCs were constituted (**Annex-IV**) and notified by the PMU during the monitoring period for improved consultations, coordination and participation of DPs in the RP implementation and grievance redress processes. Efforts were ensured to constitute a DPC for each moza, however, in cases where number of DPs was less a DPC for two mozas is notified throughout project area to promote public interest and involvement for problem identification regarding resettlement. The Sections below explain community consultations and grievance redress progress achieved through participation of the DPCs.

4.1. Public Consultations/Meetings

18. Besides approaching DPs individually to deliver notices for claiming compensation, structured public consultations were arranged through the DPCs at different locations of the project to ensure the involvement and participation of project DPs. During the consultation process, resettlement specialist and his team discussed the issues by community and documented the same and provided information to the DPs regarding resettlement impacts, compensation payment process and mechanism for recording and redress of grievances and explained them the ADB social safeguard policy. During consultation process in reported period, 4 meetings of male DPCs has been conducted (2 in Lot-I and 2 in Lot-II) and 2 meetings of female DPCs were conducted (1 in Lot-1 and 1 in Lot-2). Minutes of DPC meetings were recorded and are attached as **Annex VI**.

4.2. Grievance Recording and Redress

19. Immediate after start of RP implementation, the DPs started approaching the project GRM for raising their concerns about impacts assessment, compensation payment and construction related issues. During the reporting months, 67 applications were received to GRC regarding assessment of irrigation pipelines, shops, tube wells, trees and land etc. All applications were properly registered in Grievance register. Out of total 67 applications, 5 were related to construction and pertained to PD office and 10 were related to land compensation, while the remaining were about assessment of affected assets. The GRC reviewed the complaints/applications and conducted consultations with the complainants and the local notables to address the concerns raised by the aggrieved DPs. The GRC proceedings and consultation meetings were recorded. In land compensation cases, the DPs has been informed that 110 ft ROW is available with NHA as per decision of Government of Balochistan and confirmed by Commissioner Zhob division and SMBR. Whereas 6 complaints about payment of compensation were disposed of by making the payment as per RP entitlements.

20. Thus during reporting period, 16 applications (10 related to land compensation and 6 related to compensation of LAR) were disposed of through two GRC meetings and 5 application related to construction issues were referred to the project construction office for redressal of their grievances. The remaining 46 applications are still under scrutiny and process of verification in GRC for which the concerned DPs are being coordinated through Resettlement Specialist and Social mobilizers. Tables below shows the overall status of grievances recorded and redressed during the reporting months. Copies of Minutes of GRC meetings are attached as **Annex-V**.

Table. 6.1: GRC Complaints Recorded

Complaints Received/Registered During Reporting Months.						Over All Status			
S.N	District	No. of Complaints Received			Type of Grievance	Total Comp laints	Resolved	Out Stand ing	Remarks
		Jan 2017	Feb 2017	Mar 2017					
1	Loralai	Nil	23	44	Assets Identification and Compensation Payment Regarding Land, Trees, and Structure etc.	67	6= Resol ved. 10= DPs informed about RoW. 5= Referr ed to PD pertai ned to const issue	46	

Table. 6.2: GRC Meeting Details during reporting months




Grievances Redressed Committee meetings detail.				
S.N	GRC Meeting Date, Time and Venue	Type of Grievances Discussed and DPs Concerns.	Remedial Actions Proposed/Taken	Remarks
1	9.3.2017 9.30 am	6 complaints pertains to compensation issues	Assured that payment will be made within a week time.	
2	27.2.2017 10.00 am	10 complaints pertains to Land issues	DPs have been informed regarding status of RoW & confirmed by Commissioner Zhob & SMBR.	

5. Conclusion and Recommendations

Based on achieved progress it is concluded that the RP implementation with partially released RP budget progressed smoothly in selected LAR sections and the LAR implementation in left over sections can start immediate after release of funds by NHA HQ and could be completed by next quarterly monitoring report. In total compensation payment process for 130 DPs were started to clear selected LAR section presented in Table 3.2 out of which full compensation amount through crossed cheques has been paid to 122 DPs, whereas, the for 8 DPs compensation could not be disbursed because the DPs have some administrative impediments including temporarily moved outside of project area for their needs or some other domestic issues. DPs are participating in consultations and grievance redress mechanism regularly and are clarified on the RP provisions and compensation entitlements. Based on RP implementation progress achieved actions are recommended for consideration by NHA and ADB.

- The NHA HQ should immediately release the required 69.65 million rupees for payment of compensation to leftover DPs for Unpaid LAR sections presented in table 3.3 under section 3.2 of the report.
- The DPs who did not have their bank accounts or those who could not approach the project team in person for processing and payment of compensation should be facilitated to receive compensation in the name of their nominated attorneys after fulfilling proper documentation including special power of attorney on Stamp Paper of Rs.100/- duly attested by the Tehsildar, Advocate or Notary Public.
- Reported ROW reaches in table 3.2 of section 3.1 and highlighted green in linear plan (Annex-II) with the report, in which RP implementation is reported as completed and construction limits are cleared by DPs after receipt of compensation, should be considered for allowing the constructions activity. While the unpaid LAR reaches presented in in table 3.3 of Section 3.2 and shown as red on linear plan (Annex-II) in the report will remain on hold till RP implementation is confirmed.
- It is therefore, suggested to approach the ADB for allowing the construction activity requested in bullet above after conducting required due diligence in this regards so the construction work in cleared section could start.

Batch No. 1 (Lot - 2)
 Qila Saifullah - Loralai - Waigum Rud Section
Detailed Summary of Compensation Disbursement to Project Affectees
 RD# 78+500 - 128+350

S#	Mouza	Name & F/Name of AF	S# As Per RP Census	Amount	Name of Attorney	Amount Received	Cheque No	Date	Sign/Thurr
1	Chamoze Kotki	Abdul Jabbar s/o H. Mohhbat Khan	277	21,094	Abdul Jabbar s/o H. Mohhbat Khan	435,968	28348378	16.02.2017	
2		Murad Khan s/o Hazrat Khan	273	149,320					
3		Abdul Hameed s/o Jan Mohammad	274/1	45,782					
4		Asmatullah s/o Akhtar Mohammad	276	28,594					
5		Niaz Mohammad s/o Yar Mohammad	278	28,594					
6		Sahib Jan s/o Ghazi Khan	279	23,594					
7		Lal Jan s/o Khaliqdad	271	95,532					
8		Alam Khan s/o Ghazi Khan	272	43,458					
9		Jamaluddin s/o Abdul Rehman	281	23,594	Jamaluddin s/o Abdul Rehman	23,594	28348379	16.02.2017	
10	Chamoze Kotki	Azizullah s/o Sarwar Jan (< 18 Yrs)	280	23,594	Sarwar Jan s/o Mohammadi	23,594	28348380	16.02.2017	

✓ 11	Chamoze Kotki	Kaleemullah s/o Mola Dad	275	285,600	Kaleemullah s/o Mola Dad	285,600	28348410	16.02.2017	110
✓ 12	Chamoze Kotki	Rafo Jan (Alias Janan) s/o M. Karim (Alias Mohammadi)	274	154,440	Rafo Jan (Alias Janan) s/o M. Karim (Alias Mohammadi)	154,440	28348381	16.02.2017	نوبان
✓ 13	Maewaal	Mirza Khan s/o Shadi Khan	264	88,476	Mirza Khan s/o Shadi Khan	88,476	28348382	16.02.2017	
✓ 14	Maewaal	Sher Mohammad s/o Bismillah	267	62,160	Sher Mohammad s/o Bismillah	62,160	28348383	16.02.2017	شعر
✓ 15	Konak	Juma Khan s/o Faiz Mohammad	270	301,000	Sado Khan s/o Juma Khan	301,000	28348384	16.02.2017	سادی/سادی
✓ 16	Saghrat	Malik M. Aslam s/o Abdul Qadir	251	167,500	Malik M. Aslam s/o Abdul Qadir	167,500	28348385	16.02.2017	مالک/مالک
✓ 17	Khanra Kala	Baran Khan s/o Rodi Khan (Heritor, Sunatullah) + Khanan s/o Noorudin (Heritor, Hasamuddin, Akhtar, M)	252 + 253	65,944	Akhtar Mohammad s/o Khanan	65,944	28348386	16.02.2017	
✓ 18	Khanra Kala	Kamaludin s/o Haji Tor Khan	254	541,600	Jalauddin s/o Kamaluddin	541,600	28348387	16.02.2017	جلال الدین
✓ 19	Saghrat	Jamal Abdul Nasir s/o Sahib jan	249	854,976	Jamal Abdul Nasir s/o Sahib jan	854,976	28348388	16.02.2017	جمال
✓ 20	Bori Viyala	Fazal Mohammad s/o Nazar Mohammad Achakzai	247	438,040	Fazal Mohammad s/o Nazar Mohammad Achakzai	438,040	28348389	16.02.2017	فک - 19.2
✓ 21	Bori Viyala	Rahmatullah s/o M. Akram	247 A	128,304	Rahmatullah s/o M. Akram	128,304	28348390	16.02.2017	
✓ 22	Bori Viyala	M. Ayaz Khan s/o Pasta Khan	246/1 A	215,622	M. Ayaz Khan s/o Pasta Khan	215,622	28348391	16.02.2017	ایاز

23	Bori Viyala	Abdul Razzaq s/o M. Gul	245	104,544	Abdul Razzaq s/o M. Gul	104,544	28348392	16.02.2017	محمد رزاق
24	Bori Viyala	Abdul Razzaq s/o M. Gul	245/1	240,470	Abdul Razzaq s/o M. Gul	240,470	28348393	16.02.2017	محمد رزاق
25	Bori Viyala	Sheikh Ibrahim s/o Akhtar .M	246	38,458	Sheikh Ibrahim s/o Akhtar .M	38,458	28348394	16.02.2017	اچھا
26	Bori Viyala	M. Roedar s/o Abdul Razaq	244/2	18,594	M. Roedar s/o Abdul Razaq	18,594	28348395	16.02.2017	
27	Bori Viyala	M. Tahir s/o M. Ismaeel	244/1	18,594	M. Tahir s/o M. Ismaeel	18,594	28348396	16.02.2017	
28	Bori Viyala	Mula Saadudin s/o Mula Khan . M	244	337,986	Mula Saadudin s/o Mula Khan . M	337,986	28348397	16.02.2017	سجادہ علی
29	Bori Viyala	M. Ibrahim s/o M. Umar	243/10	45,782	M. Ibrahim s/o M. Umar	45,782	28348398	16.02.2017	28
30	Bori Viyala	Noor . M s/o Tanak	243/8	18,594	Noor . M s/o Tanak	18,594	28348399	16.02.2017	درجہ
31	Bori Viyala	Bilal s/o Murtaza	243/6	45,782	Bilal s/o Murtaza	45,782	28348400	16.02.2017	
32	Bori Viyala	Naoroz Khan s/o Meera Jan	243/5	45,782	Naoroz Khan s/o Meera Jan	45,782	28348401	16.02.2017	ناوروز
33	Dargai Shabozai	M. Shareef s/o M. Hassan	239/1	130,680	M. Shareef s/o M. Hassan	130,680	28348402	16.02.2017	میرزا
34	Dargai Shabozai	H. Shareef s/o M. Hassan	239	218,940	H. Shareef s/o M. Hassan	218,940	28348403	16.02.2017	میرزا
35	Bori Viyala	Riaz Khan s/o Qadar	243/7	45,782	Riaz Khan s/o Qadar	45,782	28348404	16.02.2017	ریاض خان
36	Bori Viyala	Lal Jan s/o Niaz Mohammad (< 18 Yrs)	243/3	45,782	All s/o Niaz .M	45,782	28348405	16.02.2017	علی
37	Bori Viyala	Naseer Khan s/o Niaz. M	243/4	45,782	Naseer Khan s/o Niaz. M	45,782	28348406	16.02.2017	نیر خان


38	Bori Viyala	Abdul Manan s/o Qalam	243/2	716,540	Abdul Manan s/o Qalam	716,540	28348407	16.02.2017	A
39	Dargai Shabozai	Ramzan s/o Nazar. M	241	406,686	Ramzan s/o Nazar. M	406,686	28348408	16.02.2017	وفا
40	Bori Viyala	Abdul Hakeem s/o Abdul Jalil	233	310,464	Abdul Hakeem s/o Abdul Jalil	310,464	28348409	16.02.2017	MA
41	Dargai Shabozai	Ghulam Sarwar s/o Karam Khan	238	154,440	Kaleemullah s/o Mola Dad	999,468	28348448	16.02.2017	وفا
42		Tahir s/o Abdul Haq	211	149,688				16.02.2017	
43		Bashir Ahmed s/o Ikhlās	237	132,660				16.02.2017	
44		Zainullah s/o Saifuddin	257	122,760				16.02.2017	
45		M. Shafi s/o Bashir Ahmed	255	142,560				16.02.2017	
46		Naseer Ahmed s/o Ikhlās	256	110,880				16.02.2017	
47		Abdul Khaliq s/o M. Rafiq	260	186,480				16.02.2017	
48	Dargai Shabozai	Ahsanullah s/o Mehmood	235	99,000	Ahsanullah s/o Mehmood	99,000	28348421	16.02.2017	احسان
49	Dargai Shabozai	M. Naeem s/o Essa Khan	234	256,605	M. Naeem s/o Essa Khan	256,605	28348422	16.02.2017	
50	Dargai Shabozai	Fazal. M s/o Wazir	231/1	45,782	Fazal. M s/o Wazir	45,782	28348423	16.02.2017	فکر
51	Dargai Shabozai	Nasrullah s/o Nazar. M	232	566,430	Nasrullah s/o Nazar. M	566,430	28348424	16.02.2017	
52	Dargai Shabozai	Malak Yameen s/o Shado	230	19,810	Malak Yameen s/o Shado	19,810	28348425	16.02.2017	مبین

53	Dargai Shabozai	Abdullah s/o Aman	229	44,674	Abdullah s/o Aman	44,674	28348426	16.02.2017	
54	Dargai Shabozai	H. M. Rafiq s/o Mula M. Akbar	228	87,120	H. M. Rafiq s/o Mula M. Akbar	87,120	28348427	16.02.2017	حرفی
	Dargai Shabozai	Pashuk s/o M. Jan	226	207,960	Rasoolddad s/o Pashuk	207,960	28348411	16.02.2017	رسل
55	Dargai Shabozai	Gul. M s/o Bakhtiar Mohammad	222	32,242	Gul. M s/o Bakhtiar Mohammad	32,242	28348428	16.02.2017	
56	Dargai Shabozai	Musa Gul s/o Barkhurdaar	221	200,800	Musa Gul s/o Barkhurdaar	200,800	28348429	16.02.2017	
57	Dargai Shabozai	Nazar. M s/o Taj. Mohammad	220	194,558	Nazar. M s/o Taj. Mohammad	194,558	28348430	16.02.2017	
58	Dargai Shabozai	Gul. M (Alias Katali) s/o Paindi	219	362,062	Gul. M (Alias Katali) s/o Paindi	362,062	28348431	16.02.2017	طپا
59	Dargai Shabozai	Khangai s/o H. Bazak	218	342,128	Khangai s/o H. Bazak	342,128	28348432	16.02.2017	
60	Dargai Shabozai	Kala Khan s/o Iqbal (Kala Khans are Heritor) 1. Zafullah Khan, 2. Jaron, 3. Qian, 4. Bakhtiar Khan, 5. Shah Shaid	214	577,980	Jonejo Khan s/o Zafullah Khan	577,980	28348433	16.02.2017	
61	Dargai Shabozai	Dusmaal s/o Zharal (Heritor Saifullah s/o Dusmaal)	?	310,200	Mir Wali s/o Saifullah	310,200	28348434	16.02.2017	بی
62	Dargai Shabozai	Yar. M s/o Faidi (Heritor, 1. Abdul Karim, 2. Rotti Khan, 3. M. Ali, 4. Abdul Rahman, 5. Daulat Khan s/o Yar. M)	216	318,726	Daulat Khan s/o Yar. M	318,726	28348435	16.02.2017	دولت
63	Dargai Shabozai	Daulat Khan s/o Yar. M (Alias Yaro)	215	162,560	Daulat Khan s/o Yar. M (Alias Yaro)	162,560	28348436	16.02.2017	دولت
64	Dargai Shabozai	H. M. Yaqoob s/o Shehzada	212	315,916	H. M. Yaqoob s/o Shehzada	315,916	28348437	16.02.2017	م
65	Dargai Shabozai	H. M. Yaqoob s/o Shehzada	212/1	92,928	H. M. Yaqoob s/o Shehzada	92,928	28348438	16.02.2017	م
66	Dargai Shabozai	Malik s/o H. Bashir (Heritor, Najeebullah)	210	191,664	Najeebullah s/o Malik	191,664	28348439	16.02.2017	ن
67	Dargai Shabozai	Saifullah s/o Shaikh	209	237,600	Saifullah s/o Shaikh	237,600	28348440	16.02.2017	س
68	Dalli	Baitullah s/o Karam Khan	206	356,400	Baitullah s/o Karam Khan	356,400	28348441	16.02.2017	ب
69	Dalli	Habibullah s/o Juma Khan Jogezai	205	646,728	Habibullah s/o Juma Khan Jogezai	646,728	28348442	16.02.2017	ح
70	Dalli	Habibullah s/o Juma Khan Jogezai	200	26,026	Habibullah s/o Juma Khan Jogezai	26,026	28348443	16.02.2017	ح

71	Orad Shabozai	Abdullah Khan s/o Malay	204	47,520	Abdullah Khan s/o Malay	47,520	28348444	16.02.2017	عبدالله خان
72	Orad Shabozai	Haji Fazli s/o Lal. M	203	32,242	Abdul Haq s/o Raz Gul	32,242	28348445	16.02.2017	حاجی فاضل
73	Orad Shabozai	Nawab Khan s/o Abdul Rasheed	202	115,348	Nawab Khan s/o Abdul Rasheed	115,348	28348446	16.02.2017	نواب خان
74	Dalli	Sharafudin s/o Fazli Khan	208	264,000	Sharafudin s/o Fazli Khan	264,000	28348447	16.02.2017	شرف الدین
75	Orad Shabozai	Baz Gul s/o Dad Gul	197	63,444	Baz Gul s/o Dad Gul	63,444	28348448	16.02.2017	باز گل
76	Lahore	Fazal. M s/o M. Sadeeq	196	261,360	Fazal. M s/o M. Sadeeq	261,360	28348450	16.02.2017	فضل
77	Lahore	Dad. M s/o M. Sadeeq	198	32,242	Dad. M s/o M. Sadeeq	32,242	28348451	16.02.2017	داد
78	Lahore	Nazar. M s/o M. Shafeeq	195	259,380	Nazar. M s/o M. Shafeeq	259,380	28348452	16.02.2017	ناظر
79	Lahore	Abdul Wadood s/o Ghulam.M	194	213,312	Abdul Wadood s/o Ghulam.M	213,312	28348453	16.02.2017	عبد الوہود
80	Lahore	M. Nawaz s/o Lal. M	193	230,232	M. Nawaz s/o Lal. M	230,232	28348454	16.02.2017	محمد نواز
81	Lahore	Abdul Hakeem s/o Usman Ghani	188/1	88,756	Abdul Hakeem s/o Usman Ghani	88,756	28348455	16.02.2017	عبد الحکیم
82	Lahore	Abdul Hakeem s/o Usman Ghani	188	22,310	Abdul Hakeem s/o Usman Ghani	22,310	28348456	16.02.2017	عبد الحکیم
83	Lahore	M. Zareef Khan s/o Abdul Latif	187	411,686	M. Zareef Khan s/o Abdul Latif	411,686	28348457	16.02.2017	مظفر خان
84	Lahore	Sardar Khan s/o Hashim	186	90,204	Sardar Khan s/o Hashim	90,204	28348458	16.02.2017	سردار
85	Lahore	Sardar Khan s/o Hashim	186/1	100,368	Sardar Khan s/o Hashim	100,368	28348459	16.02.2017	سردار
86	Lahore	Abdul Latif s/o Usman Ghani	185/2	38,458	Abdul Latif s/o Usman Ghani	38,458	28348460	16.02.2017	عبد اللطیف
87	Dalli	Malik Sharbat, Musa/Essa s/o Sahibjan	207	792,000	Wazir Khan s/o Malik Sharbat	792,000	28348462	16.02.2017	ملک شربت
88	Dalezai Shabozai	Nasrullah s/o Haji Aleem	223	173,028	Sahibjan s/o Nasrullah	173,028	28348463	16.02.2017	ناصر اللہ
89	Orad Shabozai	H. Zarghun s/o Haji Zharai	201	99,456	Santullah s/o H. Zarghun	99,456	28348464	16.02.2017	حسن
90				Total		16,652,773			

90	Shabozai	Hassan s/o Baron	233	271,920	Asmatullah s/o Hassan Khan	310,924	28348412	16.02.2017	 
91	Shabozai	Musa Khan, Hassan Khan s/o Baron	227, 227/1	39,004					
92	Shabozai	Abdul Rehman (Alias DAD) s/o M. Ibrahim	224	93,288	Fazal. M s/o Abdul Rehman	553,000	28348413	16.02.2017	 
93	Shabozai	Abdul Rehman (Alias DAD) s/o M. Ibrahim	224/1	459,712					
94	Shabozai	Allah dad s/o Abdulah Jan	236	152,136	Hashim Khan s/o Allah Dad	152,136	28348414	16.02.2017	 
95	Shabozai	Rahim Khan s/o M. Jan	213	62,160	Noorullah s/o Rahim Khan	62,160	28348415	16.02.2017	 
96	Saghrail	Ziaul Haq s/o Abdul Haq	259	335,664	Ibrahim Shah s/o Ghaffar Shah	335,664	28348416	16.02.2017	 

97	Saghrat	Abdul Aleem s/o Taj. M	250	173,528	Abdul Aleem s/o Taj. M	173,528	28348417	16.02.2017	
98	Dalli	Naseebullah s/o Juma Khan Jogezai	199	440,796	Naseebullah s/o Juma Khan Jogezai	440,796	28348418	16.02.2017	
99	Maewaaf	Taj. M s/o Musa (Malak Alam)	261, 261/1 to 7, 265, 265/1	115,256	Taj. M s/o Musa	115,256	28348419	16.02.2017	
100	Maewaaf	Hassan Khan s/o Sher Khan	261, 261/1 to 7, 265, 265/1	145,884	Hassan Khan s/o Sher Khan	145,884	28348420	16.02.2017	
101	Maewaaf	Ibrahim s/o Alam Khan	261, 261/1 to 7, 265, 265/1	190,480	Ibrahim s/o Alam Khan	190,480	28348461	16.02.2017	
102	Maewaaf	Allah Yar s/o Samad Khan	261, 261/1 to 7, 265, 265/1	244,160	Habibullah s/o Allah Yar	244,160	28348465	16.02.2017	




103	Maewaal	Khudat Rahim s/o Far Khan	260	32,242	Abdul Aziz s/o M. Gul	104,484	28348466	16.02.2018	
104	Maewaal	Abdul Mateen (Lando) s/o Kamul Khan	268	38,648					
105	Maewaal	Kamool Khan Marro s/o Dumaal	269	33,594					
89									19,481,245

Batch - 2

Qila Saifullah - Loralai - Waigum Rud Section (LOT - 1)

Detailed Summary of Compensation Disbursement to Project Affectees

RD# 0+000 - 67+300

S#	Moza	Name & F/Name of AF	SR As Per RP Census List	Amount	Name of Attorney	Amount Received	Cheque No	Date	Sign/Thumb
1	Kach Amaqzai	Abdul Qadir, Abdul Hadi, Abdul Wasey, Abdul Ghafoor, Abdul Wateoor, Abdul Qam s/o Khaliqdad	QLW 4	178,170	Abdul Qadir s/o Khaliqdad	178,170	28348467	28.2.17	56302-0824851-5 
2	Drazinda	M. Shah, Daulat Khan s/o Karimdad	QLW 5	1,079,400	M. Shah s/o Karimdad	1,149,100	28348468	28.2.17	56302-0825665-5 
3	Drazinda	Abdul Matin s/o Ali M (Alias Baloch Marri)	QLW 7	69,700					
4	Kach Amaqzai	Akhtar, M s/o Dad, M	QLW 2	297,000	Naseer Ahmed Khan s/o Jahan Khan	685,892	28348469	28.2.2017	
5	Drazinda	Ameer s/o M. Azeem	QLW 8	388,892					
6	Drazinda	M. Khan, Saifullah s/o Juma Khan	QLW 6	165,876	M. Khan s/o Juma Khan	165,876	28348470	28.2.2017	56302-9983956-5 

 (RS)



2

7	Drazinda	M. Din s/o Malik Habibullah	QLW 10	42,686	M. Din s/o Malik Habibullah	42,686	28348471	28.2.2017	56302-0845392-7
8	Drazinda	M. Salim s/o Shaheen	QLW 11	136,108	M. Salim s/o Shaheen	136,108	28348472	28.2.2017	56302-0825721-7
9	Kunwarabad	Molvi, M Yusuf s/o Noor. M	QLW 13	31,504	M. Yaqoob s/o Noor .M	31,504	28348473	28.2.2017	12101-8203936-3
10	Dalli	Ali Hyder s/o Pir Zainuddin	QLW 17	1,587,552	Ali Hyder s/o Pir Zainuddin	1,587,552	28348474	28.2.2017	54400-6995433-7
11	Nigahang	Abdullah s/o Jalo	QLW 21	1,498,752	Abdullah s/o Jalo	1,498,752	28348475	28.2.2017	56302-7423182-7
12	Nigahang	Sardar Ali s/o Wazir	QLW 22	1,495,212	Sardar Ali s/o Wazir	1,495,212	28913126	28.2.2017	56302-4707587-9
13	Nigahang	Ahmed Shah s/o Haji Khan	QLW 25	1,250,974	Ahmed Shah s/o Haji Khan	1,250,974	28913127	28.2.2017	56302-3978911-9

Abdullah Shah (RS)

8/10/17

3

✓ 14	Nigahang	Haji Gula Khan s/o Jan	QLW 24	46,080	Haji Gula Khan s/o Jan	46,080	289/3/28	28.2.2017	56302-0845047-5 عبدالغنی خان
✓ 15	Nigahang	Abdul Ghafoor s/o Shin Gul	QLW 27	140,782	Abdul Ghafoor s/o Shin Gul	140,782	289/3/29	28.2.2017	56302-8172137-5 عبدالغفور
✓ 16	Zar Karez	Nasrullah s/o Nazar. M	QLW 23	352,596	Nasrullah s/o Nazar. M	352,596	289/3/30	28.2.2017	56302-9716701-9 نسر اللہ
✓ 17	Zar Karez	Abdul Majeed, Naseebullah s/o Meeran	QLW 29	213,446	Naseebullah s/o Meeran	213,446	289/3/31	28.2.2017	56302-2933778-1 عاجی نصیب خان
✓ 18	Zar Karez	Abdul Baqi s/o Abdul Haleem	QLW 33	1,985,056	Abdul Baqi s/o Abdul Haleem	1,985,056	289/3/32	28.2.2017	عبدالباقی
✓ 19	Zar Karez	Surat Khan s/o Sher Khan	QLW 34/1	1,451,196	Surat Khan s/o Sher Khan	1,451,196	289/3/33	28.2.2017	56302-4530476-7 سورٹ خان
✓ 20	Zar Karez	Nematullah s/o Azizur Rehman	QLW 43	837,736	Nematullah s/o Azizur Rehman	837,736	289/3/34	28.2.2017	56302-1667268-7 نematullah

Abdul Wahid Syed (RS)

ME

✓ 21	Zar Karez	Abdul Rehman, Abdul Haleem s/o Haji Hassan	QLW 46	485,372	Abdul Haleem s/o Haji Hassan	485,372	28/3/35	28.2.2017	56302-0851644-9
✓ 22	Zar Karez	Mula Saifur Rehman s/o Habibullah	QLW 49	87,024	Mula Saifur Rehman s/o Habibullah	87,024	28/3/36	28.2.2017	56302-0825930-7
23	Zar Karez	Fateh Khan s/o Ramzan	QLW 51	130,536	Fateh Khan s/o Ramzan	130,536	28/3/37	28.2.2017	56302-6281033-9
24	Zar Karez	Haji Raz. M s/o Ramzan	QLW 52	118,104	Haji Raz. M s/o Ramzan	118,104	28/3/38	28.2.2017	56302-0620231-5
✓ 25	Zar Karez	Abdul Majeed s/o Malik Nemat	QLW 53	71,256	Abdul Majeed s/o Malik Nemat	71,256	28/3/39	28.2.2017	56302-1031666-1
✓ 26	Zar Karez	Abdul Qadir s/o Malik Nemat	QLW 54	136,752	Abdul Qadir s/o Malik Nemat	136,752	28/3/40	28.2.2017	56302-7190630-5
✓ 27	Zar Karez	Kala Khan s/o Hayat	QLW 57	499,728	Kala Khan s/o Hayat	499,728	28/3/41	28.2.2017	56302-3017057-1

Attaullah Saigga (RS)

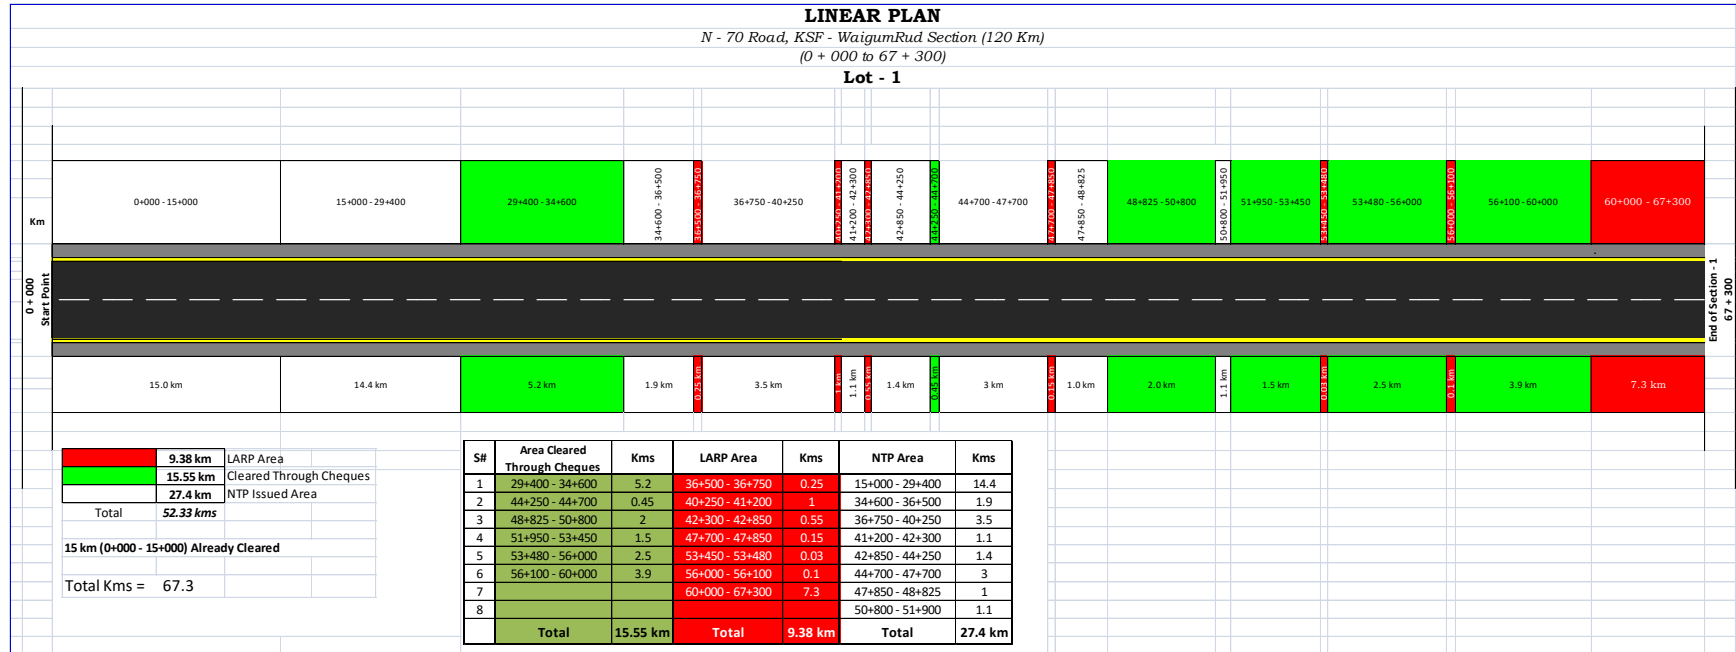
5

28	Zar Karez	Hyder s/o Sahibjan	Q.W 56	49,126	Hyder s/o Sahibjan	49,126	289/3/42	28.2.2017	56302-1820788-7 @ 10/10/17
29	Zar Karez	H. M. Zareef s/o Abdul Hakeem	Q.W 59	333,076	H. M. Zareef s/o Abdul Hakeem	333,076	289/3/43	28.2.2017	
			29		27				15,159,692

Abdul Saifullah (RS)

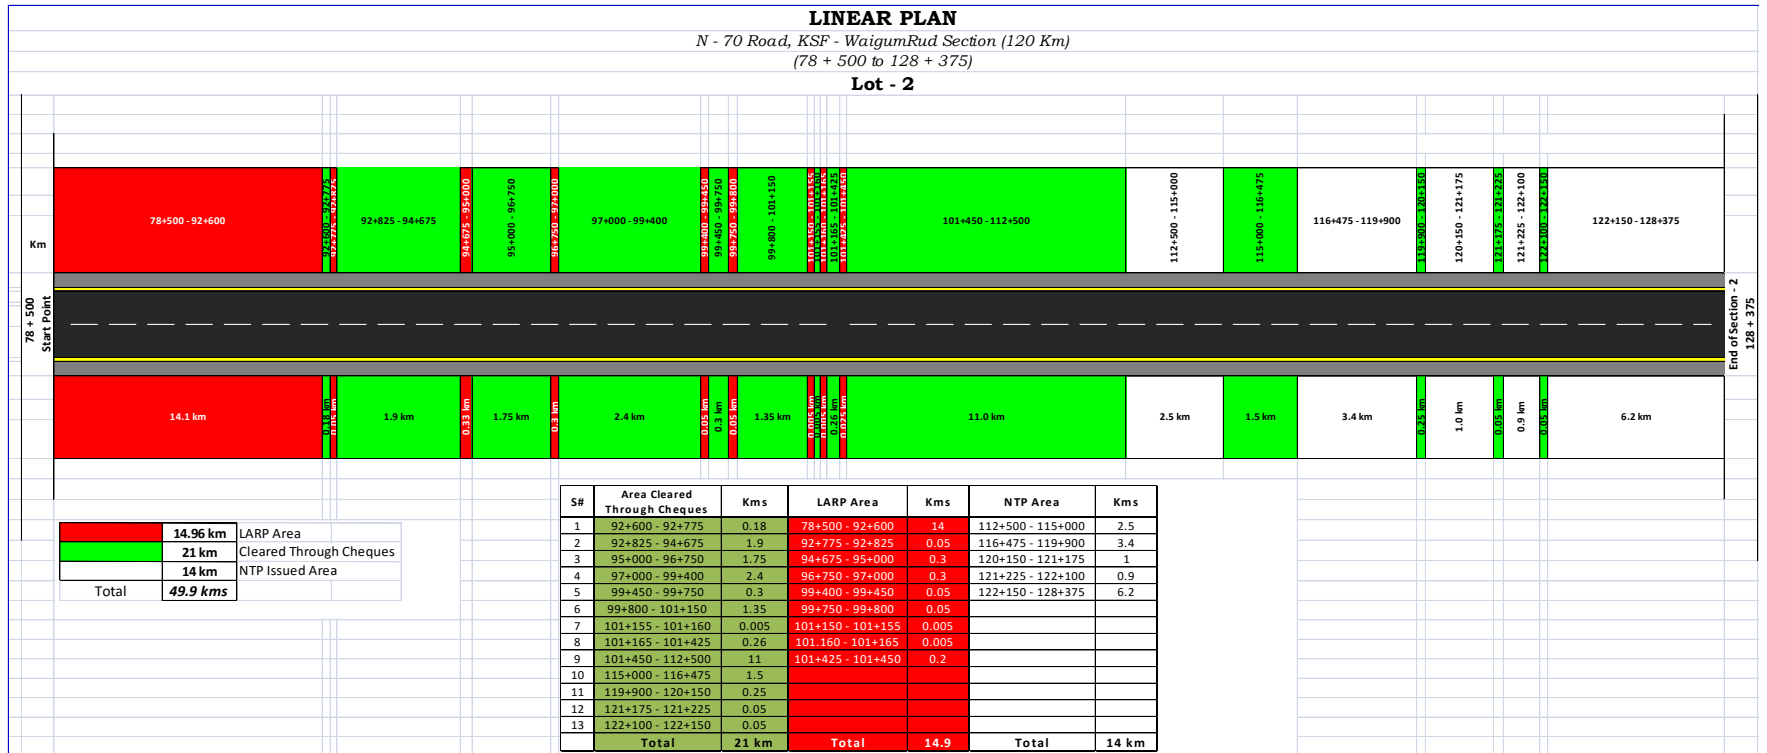
[Signature]





LINEAR PLAN

N - 70 Road, KSF - WaigumRud Section (120 Km)
(78 + 500 to 128 + 375)

Lot - 2

Copy of compensation Notice Delivered.

نوٹس برائے ادا کی گئی رقم

ریسٹلمنٹ پوائنٹ N-70 نام --- تعمیراتی محکمہ، قومی شاہراہ پاکستان، قلعہ سیف اللہ، تالورالائی، تالیم

روڈ N-70 کی تعمیر نو و بہتری کا کام کر رہا ہے۔ تعمیر نو و بہتری کے کام کی وجہ سے آپ کے جو اثاثہ جات دھکا شکاری سڑک کی زمین پر واقع ہے، ان کے نقصان کے ازالہ کیلئے ایک جزوی انتقال آبادی منصوبہ تیار کیا گیا جس کی رو سے آپ کے اثاثہ جات یا دھکا شکاری کے نقصانات کا تخمینہ و ملے شدہ رقم کا ازالہ درج ذیل ہے۔

اثاثہ جات	تفصیل نقصان	تخمینہ ازالہ
تعمیرات بشمول کمرہ جات بشمول دو بوار	-----	-----
ذریعہ آب رسانی وغیرہ	-----	-----
پھلدار درخت	-----	-----
غیر پھلدار درخت	-----	-----
نقصان متصل زیر کاشت رقبہ	-----	29900
آباد کاری الاؤنسز	-----	-----
الاؤنسز برائے نقصان کاروبار	-----	-----
الاؤنسز برائے نقل سامان	-----	-----
تاداری الاؤنس	-----	-----
کل میزان	-----	29900

آپ کی رقم کی ادائیگی بذریعہ کراس چیک کی جائے گی جو کہ آپ کے بینک اکاؤنٹ میں جمع ہوگا۔ اس لئے آپ سے التماس ہے کہ آپ اندریں 15 یوم وصولی نوٹس بذراپنا اکاؤنٹ نمبر پر اجیکٹ منجھٹ پوائنٹ N-70 کے دفتر واقع --- --- میں جمع کرا دیں تاکہ آپ کو جلد از جلد معاوضہ کی ادائیگی کر کے جگہ خالی کروائی جاسکے۔

ڈپٹی ڈائریکٹر LM&IS (ریسٹلمنٹ)

ہراجوگٹ مڈویچ مڈویچ پوائنٹ (N-70)

Detail of representatives from the Male & Female DPCs constituted

S#	DPC Moza/Village	DPC Representatives
1	Zar Karez & Nigahang	1. Mr. Abdul Majeed 2. Mr. Nasibullah 3. Mr. Zareef 4. Mr. Abdul Khalaq
2	Shabozai	1. Mr. Daulat Khan 2. Mr. Musa Gul. 3. Mr. Sharafuddin 4. Mr. Nazar Mohammad
3	Chamoze + Saghrail	1. Mr. Abdul Manan, 2. Mr. Sadadin, 3. Mr. M. Baseer, 4. Mr.M. Ayaz, 5. Mr. Fazal. Muhammad, 6. Mr. Muhammad Aslam
4	Maewaal + Boriviyala	1. Mr. Haji Muhammad Zareef 2. Mr. Adam Khan, 3. Mr. Mehrab Khan, 4. Mr.. Bahadur Khan, 5. Mr. Sher. Muhammad.
5	Shah Karez (Female DPC)	1. Ms. Saira, 2. Ms. Noor Bakhta, 3. Ms. Bibi gul, 4. Ms. Parveen 5. 5. Ms. Sughra bibi.
6	Shabozai (Female DPC)	1. Ms Rukhsana, 2. Ms Zarlasta, 3. Ms Zulekha, 4. Ms. Balanasta, 5. Ms.. Khadija, 6. Ms. Zar Khatoon, 7. Ms. Rukayya.

GRC Meeting Proceedings.

جی۔ آر۔ بی۔ ٹینک قلعہ سیف اللہ کورڈل ویلیم روڈ 70-75 قلعہ کورڈل

تاریخ 2017-02-07 وقت 10:00 AM تا 3:30 PM
 ① حوضہ کنور آباد
 ② مٹی والی
 ③ بوری والی
 ④ ٹولی
 ⑤ سانگری
 ⑥ جھوز

تفصیل ارکان جی۔ آر۔ بی۔ ٹینک و شہر کارمزداران
 ذیل: عبدالرحمان غلام علی ڈیڑھ لاکھ روپے
 جبریل جی۔ آر۔ بی۔ ٹینک

1۔ محمد احمد
 2۔ محمد خالد
 3۔ نصیب اللہ وید فضل اللہ ساکن کنور آباد کورڈل
 4۔ ملک شیر محمد ولد لہجہ اللہ ساکن مٹی والی
 5۔ تاج محمد ولد موسیٰ خان
 6۔ ضیاء ملک ولد تورک ساکن بوری والی
 7۔ ملک حاکم خان ولد شیر خان لاکھ ساکن جھوز

کہ بوقت جو کل ہے سے سرپرست 3:30 بجے تک مختلف مواقع میں
 مذکورہ شہر کارمزداران کے ساتھ مذکورہ حوضہ کے میں۔ انفرادی و اجتماعی
 ٹینک کی گئی ہے۔ مذکورہ زمرداران نے اپنی درخواست کے روڈ کی
 تعمیر و ترمیم میں اپنی اراضیات متاثر ہونے کا دعویٰ کیا ہے۔ مزید
 زبانی دورانی جنرل بھی مذکورہ مطالبہ دیا گیا۔ مزید بتایا کہ درخت ہٹے

ملک کے جاری اراضی کے نقصانات کا ازالہ صورت معاوضہ کیا جائے
 ضروری زمینداران کا مطالبہ برسر در خواست و زیانی سنا گیا ہے
 دریں زمینداران میں بتایا گیا ہے اور واضح کیا گیا ہے کہ حکم ۷۱۴۴
 ایچ۔یو۔ کی لغو توہید کے لئے ۱۹۵۵ء کے انڈیا ایکٹ کے تحت ہے۔

کیونکہ ٹوٹنٹ آف بلوچستان کے فیصلہ کے مطابق ۱۱۵ خورانی میں ۱۹۵۵ء
 حکم ۷۱۴۴ کی ملکیت ہے۔ اس کی اقدار دفتر عسکر چار شرب ڈوٹیشن
 و دفتر عسکر چار لوڈ آف ایویو کی جا سکتی ہے۔

مزید ڈاکٹر عطاء اللہ نے سرکار کا زمینداران نے زمینداران کے لئے متعلق
 سوال کیا۔ تو اسے بھی بتایا گیا ہے کہ جب روڈ کی لغو توہید میں آنے
 والی اراضی حکم ۷۱۴۴ کی اپنی ہے۔ تو زمینداران کے لئے کاتوال میا
 پور میں ہوا۔

اس طرح سرکار زمینداران دھن ہوئے۔ بعد ازاں زمینداران نے خواہش
 کی تھی کہ

عبدالغفار خیر منجی اسی ملی
 محمد احمد ری سٹنٹ سینیٹ
 محمد طاہر شکر خاں
 حاکم شیر خور ولیم اسد
 تاج محمد ولد حوسی مانلی
 ضیاء خلوک ولد نورک
 نصیب اللہ ولد مصغر محمد
 حاکم خان کاکر
 ضیاء خلوک

جی۔ آر۔ سی ڈیزینک فلو سیف ایئر ٹور ایئر ویلیم روڈ 70-71 قلعہ لورالائی

تاریخ 09-03-2017 وقت 09:30 AM تا 03:45 PM 05 مونس - لگانگ
 ② کنٹرول ملڈن
 ③ بوری ویالہ
 4 - می وال
 تفصیل ارکان جی۔ آر۔ سی ڈیزینک فلو سیف ایئر ٹور ایئر ویلیم روڈ 70-71 قلعہ لورالائی
 1 - عبدالحق صاحب ڈیپٹی ڈائریکٹر ایئر ٹور ایئر ویلیم روڈ 70-71 قلعہ لورالائی
 2 - محمد احمد ڈیپٹی سیکرٹری ایئر ٹور ایئر ویلیم روڈ 70-71 قلعہ لورالائی
 3 - محمد زاہر سٹیشن ہولڈنگز
 4 - ابرار احمد خان ولد عالم خان ساکن می وال
 5 - عبد المجہد ولد میر علی ساکن لگانگ
 6 - کمال الدین ولد حاجی نور خان ساکن کنٹرول ملڈن
 7 - عبد الرزاق ولد محمد علی ساکن بوری ویالہ
 8 - نوروز خان ولد میر علی خان
 آئندہ درخواست کے سے متعلق ریکارڈ متاثرین ARP کے ہیں ہیں ہیں
 متاثرین نے اپنی درخواست کے جس روڈ کی تعمیر و توسیع میں متاثر ہونے
 والے ملکہ اور درخت کے معاوضہ کی ادائیگی کا مطالبہ کیا ہے۔ خیر
 اس سے متعلق ذکورہ زمینداران کے مطالبہ کو ان کی قربانی بنا
 بعد ازاں ذکورہ زمینداران کو اطمینان دلایا گیا ہے کہ ان کی متاثرہ چیزوں
 کی رقم معاوضہ ان کے نام بنائی جا چکی ہے۔ انشاء اللہ ان کو نفع و صلہ ملے

کے اندر اندر معاوضہ کی ادائیگی کر دی جائے گی۔ اس سے وہ حطل
 ہوئے۔ اور انہوں نے روڈ کی کھدائی و نو تعمیر سے متعلق مزید سوا دت
 کیے۔ اس بابت ال کے رہنمائی کی گئی اور بیان کیا۔ مزید چیک کی
 وصولی سے متعلق بھی مزید سوا دت کیے۔ مثلاً بذات خود معاوضہ
 وصول کرنا۔ اکاؤنٹ کا سونا۔ معاوضہ کی وصولی بذریعہ نمائندہ
 بعد ازاں سٹیک برخواست کی گئی

دستخط درکاران محکمہ جی۔ آر۔ سی
 محمد ناصر محمد ناصر
 محمد ناصر محمد ناصر
 محمد ناصر محمد ناصر

دستخط شریکاء درخواست گزار

ابراہیم خاں ولد عالم خاں عبد المجہد ولد حمیرا علی
 محمد ناصر محمد ناصر محمد ناصر
 محمد ناصر محمد ناصر محمد ناصر

عبد الرزاق ولد محمد گل نوروز خاں ولد محمد خاں

DPC meeting and Public Consultation Proceedings

DPC میٹنگ: قلعہ سیف اللہ - وایگم روڈ سوڈ پراجیکٹ (N-70)

موضوع: چھوڑ + ساغرٹی

تاریخ: 2/3/2017

آج مورچہ 3 کو DPC کی میٹنگ منعقد ہوئی۔ میٹنگ میں درج ذیل
الینور پر بات ہوئی۔ اور کمیٹی ممبران کے بیانات کو تسلی سے سنا گیا۔ اور انہیں
ان کے بیانات کی مد میں تسلی سے سنا گیا اور مطمئن کیا۔

1۔ زرعی اراضی سے متعلق کمیٹی نے بتایا کہ روڑ کے کنارے عرصہ دراز سے آبپاشی کے لئے
ناہیاں بنائیں گئیں ہیں۔ روڑ کی تعمیر تو کسب میں آئے خوب اور متاثر نہ ہونے کے بہت
امکانات ہیں۔ اس سلسلے میں اگر ہمیں عارضی طور پر بندوبست کروایا جائے تاکہ
ہم اپنے باغات اور فصلات کو پانی بہم پہنچا سکیں۔ اسے جواب میں انہیں
بتایا گیا کہ آپ کی ناہیاں کا متبادل بندوبست ضرور ہوگا۔ اس مد میں ہم نے PD
میں کو پہلے ہی آگاہ کیا ہوا ہے۔ اور اس حوالے سے آپ کو کوئی تکلیف نہیں
ہوگی۔

2۔ بینک اکاؤنٹ سے متعلق کمیٹی نے درپیش مسائل سے آگاہ کرتے ہوئے لگا بتایا، کہ کچھ
متاثرین کے بینک اکاؤنٹ نہ ہونے کی وجہ سے (ریشن ہیں)۔ اسے جواب میں کمیٹی کو
بتایا گیا، کہ وہ اپنا اکاؤنٹ کبھی بھی بینک میں کھول سکتے ہیں۔ اور انہیں اس امر پر
جیک جمع کروا سکتے ہیں۔ جو متاثر بینک اکاؤنٹ کھولنا نہیں چاہتے تو وہ اپنے کبھی
عزیز، رشتہ دار کو بذریعہ سٹامپ بمبر فتیلہ خاں مقرر کر کے بذریعہ سٹامپ بمبر اپنا
جیک وصول کر سکتا ہے۔ بعد ازاں میٹنگ کو اختتامی کلمات کے ساتھ ختم کیا۔
ممبر سٹامپ بمبر لفظ ہذا ہے۔


02/3/17

Attendance Sheet of DPC Meeting

N-70 Qila Saifullah - Loralai - WaigumRud Section (1.29 km)

Date: 2-3-2017 Moza: ہجومز + ساغرٹی LOT: 2

Signature/Thumb

Name & F/Name

1. _____
2.  (RS) احمد خان
3.  محمد خالد (SM)
4.  عبد الرحمن ولد قلم
5.  سادہ سولوی سعید الدین ولد ملہ خان محمد
6.  محمد بصیر ولد خان محمد
7.  محمد ایزعان ولد لیستہ خان
8.  منضل محمد ولد نذر محمد
9.  ملک محمد اسلم ولد عبد القادر

DPC میٹنگ: قلعہ سیف اللہ - دیگر روڈ سڈ برا جیٹ (N-70)

موضوع: 2/3/2017

موضوع: آڈٹ کارپوریشن کے ممبران

آج مورچہ 3/17 کو DPC کی میٹنگ منعقد ہوئی۔ جس میں اس کے
(RS) اراکین اور (SM) ممبران نے شرکت کی۔ میٹنگ میں کمیٹی ممبران نے درج ذیل امور
پر بات کی اور ان کے بیانات کو تسلسل سے سنا گیا۔ اور انہیں اس میں مد میں پیش کیا۔

1:- کمیٹی ممبران نے بتایا کہ کچھ ممبران / ممبران برادری کے درختوں کے نقصان کی
مد میں کم معاوضہ ملا ہے۔ اس حوالے سے کمیٹی ممبران کو بتایا گیا کہ ADB کی
پالیسی کے مطابق درختوں کی تقسیم بلحاظ درجہ بندی میں درجوں میں کی ہے۔
ممبران کو پورا پورا معاوضہ مل سکے۔ اس درجہ بندی کو انگریزوں نے دیا تھا
سے بذریعہ لیٹر تصدیق کیا ہے۔ کمیٹی کو بتایا گیا کہ جو ممبران کم معاوضہ ملنے کی
مشکات کر رہے ہیں ان کے درخت کیے گئے سروے کے مطابق درمیانے اندے چھوٹے
درجے کے ہونے کی وجہ سے معاوضہ بتایا گیا ہے۔ اور پورا پورا معاوضہ ادا کیا
ہے۔ اگر کمیٹی کے چند ممبران نے اس بات کی تصدیق کرتے ہوئے کہا کہ یہ بات
بالکل درست ہے۔ کہ چند ممبران کے درخت بلحاظ عمر چھوٹے اور درمیانے درجے
کے تھے۔ اس حساب سے انہیں معاوضہ صحیح اندے پورا ملا ہے۔
اس کے ساتھ ہی کمیٹی کو سطحیں رستہ پورے میٹنگ کو اختتامی حکمت کے ساتھ
پر حاضرت کیا۔

2/3/17

فہرست حذا شرکا، لفظ ہے۔

Attendance Sheet of DPC Meeting

N-70 Qila Saifullah - Loralai - WaigumRud Section (120 km)

Date: 2. 3. 2017 Moza: شیر کا پتہ + 1/2 LOT: 1

Signature/Thumb

Name & F/Name

	1.
	2. محمد صاف (RS)
	3. محمد صاف (SM)
	4. عبد المجید ولد ولد محمد صاف
	5. نصیب اللہ ولد میران
	6. عبد المظفر ولد فتح محمد
	7. حاجی محمد ظریف ولد عبد المجید

DPC ٹینٹ: قلعہ سیف اللہ - وایگم روڈ موڈ پراجیکٹ (N-70)

موضوع: تیسوری

موسم: 12-03-2017

آج مورخہ 13/3 کو DPC کی ٹینٹ منعقد ہوئی۔ جسکی
ممبران ایس ایم ڈی خان (RS) اور محمد خالد (SM) نے کی ٹینٹ میں کمیٹی ممبران نے درج
ذیل امور پر بات کی اور انکے بیانات کو نقل سے سنایا۔ اور انہیں اس
مد میں مطلع کیا۔

1:- کمیٹی ممبران نے ایسی زرعی زمین کی رہنمائی کے حوالے سے اپنے تحفظات سے آگاہ
کرتے ہوئے بتایا کہ روڈ کے کنارے اور کہیں کہیں پائپ لائن چھائی گئی ہیں
جس کے ذریعے وہ ایسی زمین اور فصلات کو باقی بنچا رہے ہیں۔ انکے متاثر
ہونے کا حذر ہے۔ اس حوالے سے انکو یہ بتایا کہ جہاں جہاں زرعی زمین کو
باقی فراہم کرنے کیلئے روڈ کے کنارے ٹالیاں بنائی گئی ہیں اور پائپ لائن چھائی گئی ہیں۔
وطن کی بیماریاں پکڑنے کے لئے ایک درخواست بنام PD (N-70) کو ملے کر جمع کرادے۔
تاکہ روڈ کاروائی عمل میں لائی جاسکے۔ اور انکے فصلات/معاوضات کو نقصان سے
بچایا جاسکے۔

2:- زمین کی مد میں کمیٹی نے بتایا کہ روڈ کی زرعی پورے قوم کی ترقی ہے۔ اور اس ترقی سے
ہونے والی زمینوں کے نقصانات کی مد میں حکومتیں معاوضہ ادا کرے گی؟ اس سے متعلق
کمیٹی کو بتایا گیا کہ گورنمنٹ آف پنجاب نے NHA کو زمین کی روڈ کیلئے زمین کی
حوزائی 110 فٹ دی ہے۔ اور NHA ایسی روڈ کی زمین میں روڈ تعمیر کر رہی ہے۔
اور جن لوگوں نے NHA کی حدود یعنی سرکاری زمین میں درخت، فصل یا تعمیرات کیے
ہیں۔ انکو ADB کی پالیسی کے مطابق معاوضہ دیا جائے گا۔
اسکے ساتھ ہی ٹینٹ کو اختتامی کلمات کے ساتھ اختتام تک پہنچایا۔
منیر سید شرماء لغت ہذا ہے۔

13/3/17







Attendance Sheet of DPC Meeting

N-70 Qila Saifullah - Loralai - Waigum Rud Section (120 km)

Date: 12. 3. 2017 Moza: ستون LOT: 2

Signature/Thumb

Name & F/Name

_____	_____ 1
	_____ 2 محمد خان (RS)
	_____ 3 محمد خالد (SM)
 <u>Muhammad Khan</u>	_____ 4 دولت خان ولد بار محمد
 <u>Mullah</u>	_____ 5 موسوی گل ولد / خوددار
 <u>Sherafuddin</u>	_____ 6 شرف الدین ولد ناصیل خان
 <u>Nazir</u>	_____ 7 نظر محمد ولد تاج محمد

DPC میٹنگ: تلعام سیف اللہ - دیگم روڈ موڈ پراجیکٹ (N-70) ۱

موضوع: مواصلات و لوری ویاہ

15/3/2017

۲۔ ع. موافق 15/3/2017 کو DPC کی میٹنگ منعقد ہوئی۔ میٹنگ میں پراجیکٹ متاثرین کے ساتھ درج ذیل البتوز پر بات ہوئی اور ان کے بیانات کی تسلی سے سنا گیا اور ان بیانات کی مد میں اہلین مطمئن کیا۔

۱۔ - کمپنی ممبران نے زمین کی مد میں ریسٹوئراے نقصان / روڈ تجاوزات پر معاوضہ ادا کرے گی۔ اس سے متعلق کمپنی کو بتایا گیا کہ گورنمنٹ آف بلوچستان نے NHA کو روڈ سٹیٹ زمین کی چوڑائی 110 فٹ دی ہے۔ اور NHA اسی زمین میں روڈ تعمیر کر رہی ہے۔ اور جن لوگوں نے NHA کی حدود یعنی سرکاری زمین میں درخت، فصل یا تعمیرات کی ہیں۔ تو انکی ADB کی پالیسی کے مطابق معاوضہ دیا جائے گا۔

۵۔ - کمپنی نے بتایا کہ کچھ مقامات پر زرعی زمین کی آبپاشی کیلئے کچی ٹالیاں اور جگہ جگہ ڈیمپ لائین بچھائی ہیں۔ روڈ کی تعمیر سے ان کے متاثر ہونے کا اندیشہ ہے۔ اس پر اہلین یہ بتایا گیا کہ آبپاشی زرعی زمینوں کی آبپاشی لائین جو کچی ٹالیاں اور ڈیمپ لائین بچھائی ہیں۔ ان سے متبادل بندوبست چلیا ہی کر دیا جائے گا۔ تاکہ زرعی زمین، فصل و باغات کو آبپاشی کا سلسلہ متاثر نہ ہو سکے۔ اس پر کمپنی نے بتایا خوشامیاد اظہار کیا۔ اور میٹنگ کو اختتامی کلمات کے ساتھ ختم کیا۔

فہم سٹ شرماء، میٹنگ لف عذا عہ

15/3/17







Attendance Sheet of DPC Meeting

N-70 Qila Saifullah - Loralai - WaigumRud Section (120 km)

Date: 15. 3. 2017 Moza: ميوال + نورى ميوال LOT: 2

Signature/Thumb

Name & F/Name

- | | | |
|---|-------|----|
| _____ | _____ | 1. |
|  | _____ | 2. |
| _____ | _____ | 3. |
|  | _____ | 4. |
|  | _____ | 5. |
|  | _____ | 6. |
|  | _____ | 7. |
|  | _____ | 8. |

DPC میٹنگ: قلعہ سیف اللہ - وایگم روڈ پراجیکٹ (N-70)

موضوع: 3 مارچ 2017

موضوع: شاہ کاریز

خواتین سے رابطے کے لیے موضعہ شاہ کاریز کے

علاقے میں خواتین سے میٹنگ ہوئی میٹنگ میں جوہ (14) خواتین موجود تھیں جن کی نمبر لسٹ لکھی گئی ہے۔

دوران میٹنگ خواتین کو روڈ پروجیکٹ قلعہ سیف اللہ لورالائی وایگم روڈ

N 70 کے متعلق معلومات دی گئی ان کو بتایا گیا کہ ایسٹائی ٹر قیاتی

بینک (ADB) کی مدد اور مالی تعاون سے بنایا جا رہا ہے۔ پروجیکٹ

کے متعلق خواتین کو روڈ کی تعمیر کے متعلق معلومات دی گئی کہ انسانی

ترقیاتی بینک (ADB) کے تعاون سے جو روڈ بنایا جا رہا ہے اس سے

علاقے میں ترقی ہوگی اور کہیں بھی آئے جانے میں آسانی ہوگی

لورالائی کی خواتین کی ذمہ داری ٹھریلوں کا کام کی انجام دہی ہوتی

ہے گھر کے باہر اور معاشرے میں ان کا کردار بہت کم ہے اس لیے زیادہ

تر خواتین نے علاج معالجے کے متعلق سوالات پوچھے۔ (دوران

میٹنگ خواتین کو یہ بھی بتایا گیا کہ اس منصوبے کی تعمیر سے علاقے

میں تعلیم اور صحت کی سہولتیں مسیر آئیں گی اور کسی بھی بیماری کی

صورت میں ہسپتال بروقت پہنچنے میں آسانی ہوگی مزید خواتین کو

ایسٹائی ٹر قیاتی بینک (ADB) کی پالیسی بابت معاوضہ درخت اور

تعمیرات کے متعلق تفصیل سے معلومات بھی پہنچائی گئی۔

Umea


Attendance Sheet of DPC Meeting

N-70 Qila Saifullah – Loralai / WaigumRud Section (1.20 km)

Date: 3.3.2017 Moza: شاه کاپڑ LOT: 1

Signature/Thumb

Name & F/Name

- | | |
|---|--------------------------|
|  | 1. غفاری منیر عباسی (SN) |
|  | 2. حاجی گل دلہ رفیقہ |
|  | 3. حاجرہ دلہ حاجی منیر |
|  | 4. صفراہی دلہ شیر محمد |
|  | 5. حاجی نازیہ دلہ سکندر |
|  | 6. رامتہ دلہ خان محمد |
|  | 7. گل مینہ دلہ گل بابر |

Attendance Sheet of DPC Meeting

N-70 Qila Saifullah - Loralai - WaigumRud Section (120 km)

Date:

Moza:

LOT:

Signature/ThumbName & F/Name

مفتوحه ولد شاه ولي 8

تاجوره ولد اختر محمد 9

سائره بي بي ولد زردلي 10

توره ولد خانك 11

سپينه ولد عبدالرحيم 12

خرد مختد ولد كاشف 13

بي بي گكي ولد رفیق 14

15

DPC میٹنگ، قلعہ سیف اللہ - وایگم روڈ سوڈ پراجیکٹ (N-70)

موضوع: 16 مارچ 2017

موضوع: شہورٹی

خواتین سے رابطے کیلئے موضوع شہورٹی کے علاقے میں خواتین سے میٹنگ ہوئی، میٹنگ میں تقریباً (13) خواتین موجود تھیں جن کی ضرورت لف ہذا ہے۔

دورانِ میٹنگ خواتین کو روڈ پروجیکٹ قلعہ سیف اللہ لورالائی وایگم روڈ N70 کے متعلق معلومات دی گئی ان کو بتایا گیا کہ ایڈیٹری ترقیاتی بینک (ADB) کی مدد اور مالی تعاون سے بنایا جا رہا ہے پروجیکٹ کے متعلق خواتین کو روڈ کی تعمیر کے متعلق معلومات دی گئی کہ ایڈیٹری ترقیاتی بینک (ADB) کے تعاون سے جو روڈ بنایا جا رہا ہے اس سے علاقے میں ترقی ہوگی اور آگے جانے میں آسانی ہوگی دورانِ میٹنگ ایک خاتون جو کہ متاثرین میں شامل ہے ان کے اس سوال ~~میں~~ کہ مجھے معاوضہ کیسے ملے گا کہ جواب میں یہ بتایا گیا کہ وہ بینک میں اپنا اکاؤنٹ کھول سکتی ہیں یا اپنے کسی بھائی یا رشتہ دار کو اختیار نامہ دے کر معاوضہ وصول کر سکتی ہیں۔

لورالائی کی خواتین کی ذمہ داری ٹمبرلو ٹاؤن کالج کی انجام رہی ہوئی ہے گھر کے باہر اور معاشرے میں ان کا کردار بہت کم ہے اسلئے زیادہ تر خواتین نے علاج معالجے کے متعلق سوالات کیے، خواتین کو بتایا گیا کہ اس منصوبے کی تعمیر سے علاقے میں تعلیم اور صحت کی سہولتیں مسیر آئیں گی، مزید خواتین کو ADB یا ایسی کے متعلق بتایا گیا۔

Amir

Attendance Sheet of DPC Meeting

N-70 Qila Saifullah - Loralai - WaigumRud Section (120 km)

Date: 16. 3. 2017 Moza: شعورنی LOT: 2

Signature/Thumb

Name & F/Name

	1. غلام نبي ولد عباسي (Sed)
	2. خير بي بي ولد حاجي عثمان
	3. شبانه گل ولد محمد گل
	4. خديجه ولد نذر محمد
	5. ذرخا تون ولد جان نظر
	6. شبانه ولد نظر جان
	7. بي بي زينبا ولد حسن







Attendance Sheet of DPC Meeting

N-70 Qila Saifullah - Loralai - WaigumRud Section (120 km)

Date: _____ Moza: _____ LOT: _____

Signature/Thumb

Name & F/Name

	8. محمد جبین ولد محمد انور .
	9. گل بی بی ولد مسفر محمد .
	10. صالحہ ولد شین گل .
	11. حفصہ ولد نور محمد .
	12. بلہ شستہ ولد شاہ محمد .
	13. ذر شستہ ولد مسرود خان .
	14. _____
	15. _____
