Land Acquisition and Resettlement



PAK: National Trade Corridor Highway Investment Program (NTCHIP) – Tranche 2 (Package I)

Prepared by National Highways Authority for the Asian Development Bank.

NOTES

- (i) The fiscal year (FY) of the Government of the Islamic Republic of Pakistan and its agencies ends on 30 June.
- (ii) In this report, "\$" refers to US dollars.

This social monitoring report is a document of the borrower. The views expressed herein do not necessarily represent those of ADB's Board of Directors, Management, or staff, and may be preliminary in nature.

In preparing any country program or strategy, financing any project, or by making any designation of or reference to a particular territory or geographic area in this document, the Asian Development Bank does not intend to make any judgments as to the legal or other status of any territory or area.



NATIONAL HIGHWAY AUTHORITY



Ministry of Communications Government of Pakistan

National Trade Corridor Highway Investment Program

(ADB Loan No. 3121: Pak NTCHIP Tranche 2)

Consultancy Services for Social Safeguard Management Consultant (SSMC) of Hassanabdal-Havelian (E-35) Expressway Project

2nd Quarterly Internal Monitoring Report

for the

Implementaion of Land Acquisition and Resettlement Plan (Package I)

(0+000 - 20+300) (Nov. - Jan 2016)

Social Safeguard Management Consultant

Project Implemenation Unit NHA Office, Burhan

(February 29, 2016)

NATIONAL HIGHWAY AUTHORITY

Ministry of Communications Government of Pakistan

National Trade Corridor Highway Investment Program

(ADB Loan No. 3121: Pak NTCHIP Tranche 2)

Consultancy Services for Social Safeguard Management Consultant (SSMC) of Hassanabdal-Havelian (E-35) Expressway Project

2nd Quarterly Internal Monitoring Report

for the
Implementaion of Land Acquisition and Resettlement Plan
(Package I)
(0+000 - 20+300)
(Nov. - Jan 2016)

Social Safeguard Management Consultant

Project Implemenation Unit NHA Office, Burhan (February 29, 2016)

TABLE OF CONTENTS

TABL	E OF CC	ONTENTS	1
LIST	OF TABL	_ES	2
LIST	OF ANN	EXES	2
	1.	INTRODUCTION	3
	1.1	Background	3
•	1.2	Internal Monitoring Report and its Objectives	4
2	2.	STATUS OF IMPLEMENTATION OF LARP	4
2	2.1	No. of Displaced Persons (DPs)	5
2	2.2	Land Acquisition	5
2	2.3	Compensation Disbursement	
2	2.3.1	Disbursement of land Compensation	6
2	2.4.2	Payment of Affected Structures	6
2	2.4.3	Payment of Affected Trees	6
2	2.4.4	Payment of Affected Crops	
2	2.4.5	Payment for Allowances	6
2	2.5	Categorized Land Payments Requiring Special Effrots to Enable	
[Disburser	ment to DPs	7
3	3.1	NHA's Efforts Made/ Being Made to Facilitate Pending Payments	8
3	3.1.1	Efforts Made and actions taken to Address Pending Payments	8
3	3.1.2	Efforts Exhausted by NHA with Way Forward	
3	3.2	Institutional Arrangements	12
3	3.3	Resolution of DPs Grievances	
3	3.3.1	Formation of Displaced Persons Committees (DPCs)	13
3	3.4	Social Safeguards Management Consultant (SSMC)	13
3	3.5	Process for Disbursement of Compensation	13
3	3.6	Receipt of Payment U/S 18 of LAA 1894	14
3	3.7 Ache	vid Progress Shown Linear Plan	
4	4	CONCLUSIONS	16

Table 2.1: Phase 1 of E-35 Packageand its Sections	5 7
LIST OF ANNEXES	
Annex A: Updated Linear Plan - Section-wise status of Payment of Compensation Annex 1: Village-wise summary of Awarded Land	17 17 18 18 26 28 29 30 31

1. INTRODUCTION

1.1 Background

1. The National Highway Authority (NHA) is implementing the National Trade Corridor Highway Investment Program (NTCHIP) financed by Asian Development Bank (ADB) through a Multitranche Financing Facility (MFF). National Highway Authrotiy (NHA, the project executing agency) identified several road projects for construction under different trahcnes of the MFF. Tranche 1 of MFF included the construction of section 1 (loan no. 2400) Faisalabad-Khanewal Motorway Project (M-4) in the province of Punajb. Construction of section 1 of M-4 and implementation of LARP has been confirmed by the external monitoring agent. Tranche 2 of MFF includes sections I and II of the Hassanabdal-Havelian Expressway Project (E-35). The expressway project is a green field project and involves a completely new alignment in the province of Khyber Pakhtunkhaw (KPK (Figure 1 below shows the project location).



2. NHA plans to implement the expressway in 2 phases. Phase-1 consists of a 58.6km long road from Hassanabdal to Havelian which is financed by ADB. Phase-2 of expressway includes 51.4km long road from Havelian-Mansehra, which is currently outside ADB's financing. Total length of phase-1¹ is 58.6 km which is divided into three different sections as shown in the table 2.1 below:

Table 2.1: Phase 1 of E-35 Packageand its Sections

Sections/Package	Sub-	Location	Chainage
	sections		
I	1a	Punjab Province	000+000 - 007+000
I	1b	KPK Province	007+000 - 020+300
II	2	KPK Province	020+300 - 039+500
III	3	KPK Province	039+500 - 058+600

¹ The Package –I: 000+000 - 007+000 km in Punjab & 000+007 - 020+300 (KPK), the Package-II: 020+300 - 039+500 km & Package-III: 039+500 - 058+600. The package II & III is located in the province of Khyber Pakhtunkhwa

- 3. Phase 1 of E-35 Expressway Project starts from Islamabad-Lahore Motorway (M-1) near Burhan interchange and ends at Havellian. The package-I of E-35 has a total length of 20.3km starting from Burhan Interchange (village Kholian) in District Attock (Punjab) and ending at village Dingi Tubewell (chainage 20+300 km) in tehsil and district of Harripur in KPK.
- 4. The road design of package-I includes construction of new 7.3 meter dual carriageway with New Jersey barrier as median, In addition, it also has 2 interchanges, 3 flyovers and 10 underpasses which will be constructed during implementation.. The Expressway will be fenced from both sides and six (15) feet service road will also be provided on both sides for use by local people. Total width of Right of Way (ROW) is 80m, which has been full acquired using the Land Acquisition Act (LAA) of 1894.
- 5. The Land Acquisition and Resettlement (LAR) impacts of the project (package I) were assessed as significant and a Land Acquisition and Resettlement Plan (LARP) was prepared in accordance with ADB's Safeguard Policy Statement of 2009 (SPS), Pakistan's Land Acquisition Act of 1894 (LAA) and the updated Land Acquisition and Resettlement Framework of MFF. In addition to the LARP, NHA also undertook a detailed land valuation study by the valuation experts to ensure that land compensation provided to the displaced perosns (DPs) meets/approximates full replacement cost as required under ADB's SPS 2009.

1.2 Internal Monitoring Report and its Objectives

6. This internal monitoring has been prepared by NHA with assistance of Social Safeguard Management Consultant (SSMC) of the project. The objective of report is to present an up to date status of progress of LARP and disbursement of payments to DPs and illustrate the payments made on a linear map of the road to confirm that construction activities fully comply with the requirements of LARP and SPS 2009 that no construction activities are taking place in any area (under package I road) where full payments of compensation have not been achieved and verified/validated by an external monitoring agent.

2. STATUS OF IMPLEMENTATION OF LARP

- 7. NHA is implementing the LARP of package I with assistance of SSMC based at Project Implementation Unit (PIU based in the field at Burhan) and Project Management Unit (based at NHA headquarters in Islamabad). This internal monitoring report, prepared by NHA with assistance of SSMC, provides an update status of LARP implementation and payments made to the DPs covering the following:
 - i) No. of displaced persons (DPs) paid, unpaid and being paid;
 - ii) Status of land acquistion;
 - iii) Loss of structures and status of payments and income restoration;
 - iv) Affected fruit and timber/ wood trees and status of their payments;
 - v) Affected crops and payments;
 - vi) Payment of allowances including rehabilitation, livelihood restoration and vulnerability allowances;
 - vii) Categorized payment of land compensation including payments to the DPs (a) not living in the project area, (b) have meager amounts of compensation, (c) do not have bank accounts and national ID cards, (d) and have issues with land titles/ownership or inheritance matters;
 - viii) Efforts urderway to complete all categorized payments:
 - ix) Complaints/redress management;

- x) Institutional arrangements put in place for LARP implementation and monitoring;
- xi) Linear map of the road indicating status of land compensation and construction works; and
- xii) Conclusions and recommendations.

2.1 No. of Displaced Persons (DPs)

8. Total number of DPs of land and non-land assets including those eligible for different allowances comes to be 3,797 DPs. The status of their payment is as aunder:

2.2 Land Acquisition

9. A total of 3859.6 kanals (482.45 acres) land was needed for the construction of road, which has been fully acquired.

10. This land was located in 15 villages which were affected by the project. These villages included Jabar, Padarah, Kala Katha, Khoi Dara, Dar Chitti, Motian, Jar, Dingi, Aamgah, Kohlian, Kanwan, Ballar Jogi, Mohri, Bedian, Barwal). Figures 2.1 provide a village-wise status of land acquisition in package I of the project.




Figure 2.1: Village-wise Land Acquisition of Hassanabdal - Havelian Expressway

11. Further details showing number of affected land owners in all 15 villages with the land acquired are provided below in table 2.2.

Table 2.2: Mouza-wise Land Acquisition and Owners of Land/ DPs

Affected villages	Village	Affected Land with RoW	hin 80m	
		(Kanal)	(Acres)	No. of DPs
1	Jabar (KPk)	381.55	47.69	175
2	Padarah (KPk)	244.85	30.61	226
3	Kala Katha (KPk)	192.65	24.08	143
4	Khoi Dara (KPk)	202.05	25.26	320
5	Dar Chitti (KPk)	117.8	14.73	535
6	Motian (KPk)	465.45	58.18	645
7	Jar (KPk)	145.1	18.14	71
8	Dingi (KPk)	145.2	18.15	52
9	Aamgah (KPk)	209.05	26.13	449
10	▶ Kohlian (Punjab)	964.35	120.54	258
11	Kanwan (Punjab)	258.95	32.37	320
12	Ballar Jogi (Pun)	262.45	32.81	314
13	Bedian (Punjab)	59.75	7.47	75
14	Mohree (Punjab)	140.45	17.56	168
15	Barwal (Punjab)	69.95	8.74	46
	Total (affected land owners)	3859.6	482.45	3,797
DPs of Non	-land Assets			
	uctures owners			98
	ees owners (fruit trees)			222
Affected no	on-fruit trees			289
Affected Cr	ops			3143*

^{*}multiple count. Already included in affected land owners.

2.3 Compensation Disbursement

12. Procedures of LAA 1894 are being followed in disbursement of land compensation to the affected land owners. Details of payments disbursed so far is as under:

2.3.1 Disbursement of land Compensation

13. A total amount of land compensation was Rs.476.047 million was to be paid to 3797 DPs². Out of which, Rs.457.55 million (96.1%) have been paid to 2,733 DPs (72.0%). The remaining amount of Rs. 18.50 million (3.9%) to remaining 1,064 DPs (28.0%) is under process. More details about land compensation to the DPs are provided in table 2.3 below.

2.4.2 Payment of Affected Structures

14. Internal monitoring results show that total amount of compensation for loss of residential/ commercial structures was Rs. 85.679 million payable to 102 DPs. Out of which payment of Rs. 85.638 million (99.95%) have been paid to 101 DPs (99.0%), while the remaining amount of Rs. 0.04 million (0.05%) to 1 DP (1.0%) is under process. Further details are in table 2.3 below.

2.4.3 Payment of Affected Trees

15. In case of fruit and wood trees, a total of 511 DPs³ had to be paid an amount of Rs.8.54 million. To date, 307 DPs (60.1%) have been paid an amount of Rs. 6.05 million (70.8%). The remaining 204 DPs (39.9%) are yet to be paid an amount of Rs. 2.49 million (29.2%). Further details are in table 2.3 below.

2.4.4 Payment of Affected Crops

16. In case of crops a total number of 2,164 DPs⁴ had to be paid an amount of Rs. 14.22 million. To date 1,033 DPs (47.7%) have been paid an amount of Rs. 11.62 million (81.7%). The remaining 1,131DPs (52.3%) are yet to be paid an amount of Rs. 2.61 million (18.4%). More details are in table 2.3 below.

2.4.5 Payment for Allowances

17. In case of allowances (rehabilitation/ livelihood restoration) payments, 141 DPs⁵ had to be paid an amount of Rs. 12.40 million. Out of total, 139 DPs (99.0%) have been paid an amount of Rs. 12.147 million (98.0%) on account of allowances/ livelihood restoration. More details are in table 2.3 below.

Annexes 1, 2, 3 & 4 provide additional details about DPs and their payments for affected land, structures, trees and crops.

²Differnce of 132 DPs is due to to compensation apportionment, i.e. the number of DPs payable is 3,797, while the LARP reported 3,929 landowners.

³DPs already include in land owner.

⁴DPs already include in land owner.

⁵DPs already include in land owner.

Table 2.3: Status of Implementation of LARP

Type of Payment	Payable	Total	Progress till			Progress during			Todate Total		
				Pec 2015	5 · ·		an. 2016				5
	Payment	DPs	Paid	Unpaid	Paid	Paid	Unpaid		Paid	Unpaid	Paid
			Amount	Amount	DPs			DPs	Amount	Amount	DPs
	(Rs. M)	(No)	(Rs. M.)	(Rs. M.)	(No.)	(Rs. M.)	(Rs. M.)	(No.)	(Rs. M.)	(Rs. M.)	(No.)
Land Compensation	476.05	3797	457.55	18.5	2733	-	-	-	457.55	18.5	2733
Crops Compensation	14.22	2164	11.62	2.61	1033	-	-	1	11.62	2.61	1033
Affected Structures	85.68	102	85.64	0.04	101	-	-	-	85.64	0.04	101
Affected Trees	8.54	511	6.03	2.52	306	0.017	2.49	1	6.05	2.49	307
Allowances – rehabilitation/ livelihood restoration	12.40	141	12.15	0.25	139	-	•		12.15	0.25	139

2.5 Categorized Land Payments Requiring Special Effrots to Enable Disbursement to DPs

- 18. As mentioned ealirer in the report, a total remaining 1,064 DPs are yet to be compensated for land. Their payments are slow due to the following reasons:.,
 - Transfer Record of Rights: a total of 95 land owners have unfortunately passed away which requires transfer of land to the inheritors. Payments to inheritors will be made after transfer of land to the inheritors by the district revenue authority. .The process of transfer of land to the inheritors is under progress already.
 - DPs under Verification (i.e. title/ ownership disputed): 120 DPs of family ownership disputes i.e. having no proof of ownership.
 - Untraceable DPs: There are 16 DPs not traceable. The compensation of their land will remain with the LAC. They will be paid under LAA procedures when they come forward and approach NHA/LAC for payments.
 - DPs Who Moved Out of Project Area: There are 94 DPs who have been reportedly moved out of the project area without leaving a clue or address to with fellow villagers. They will be paid under LAA procedures when they come forward and approach NHA/LAC for payments
 - DPs Unwilling to Receive Payments: There are 668 DPs who are unwilling to receive compensation because of share of compensation being meager amount. Under LAA procedures they are required open their bank accounts for disbursement of payments of their bank accounts.
 - Mortgaged Land: There is 1 DP who'se land is mortgaged. He cannot receive payment unless the mortgaged land is freed by a commercial bank form where the DP received a loan against the mortgaged land.
 - Land Litigation: About 6 land owners DPs, are in litigation and did not agree to get the compensation announced by the revenue department. These Dps are demanding higher compensation and their cases are in the courts of law.
 - Miscellenaous Issues: About 15 DPs are also difficulty in receiving payments due to different issues such as DPs who don't have CNIC or whom bank accounts / Land Owners under other reasons:

Table 2.4: Categorized Land Payments Requiring Special Effrots to Enable Disbursement to DPs

Total un Paid DPs	Transfer Record of Rights (Death Cases)	Absent DPs (Not Traceable)	DPs under Verification (i.e. title/ ownership disputed)	Out of City	Out of Country	Meager Amount	Mortgage land with DPs	Land Owner/ DPs under court cases	Other reason
(Nos.)	(Nos.)	(Nos.)	(Nos.)	(Nos.)	(Nos.)	(Nos.)	(Nos.)	(Nos.)	(Nos.)
1064	95	16	120	94	49	668	1	6	15

3.1 NHA's Efforts Made/ Being Made to Facilitate Pending Payments

3.1.1 Efforts Made and actions taken to Address Pending Payments

- 19. For delivery of pending payment, the LAC and his team retained a close liaison with the displaced persons during the reporting period. Sites visits for compensation delivery, consultative and information dissemination sessions/ meetings and DPs follow-up has been carried out by the LAC and NHA Land staff. In this regard a comprehensive field visit plan was implemented and the LAC and his team repeatedly visited the affected villages to process compensation claims and deliver compensation to displaced persons at their door steps.
- 20. During visits, meetings were held with available displaced persons and their relatives in presence of village DPCs and headman; written notices were distributed to available DPs by LAC/ land staff and DPs were motivated to submit their claims in all affected villages; and the list of unpaid DPs was disclosed to the village headmen, DPC members and local community to seek assistance for locating and informing unpaid DPs for receipt of their compensation. In the notices, DPs were informed to receive their compensation for acquired assets (land, structure, houses, trees and crops) and allowances etc. During consultative process, LAC and NHA land staff clarified the DPs that the compensation is deposited in treasury and can be collected after submission of claims and if not claimed in timely manner, the compensation could be deposited in the court under section 31 of LAA 1894 and no excuses will be accepted. Deposit of funds in treasury is presented in Annex 5.
- 21. Since mobilization of SSMC, its team developed a rapport with the LARU team in PIU, DPCs in each village and displaced persons. During reporting period total 12 consultations were made by the male and female social mobilizers, wherein 76 DPs/members of DPCs as well as local community participated. During such consultations with DPs and DPCs, the information disclosed include project LAR impacts, compensation eligibility and entitlements as per LARP provisions, submission of compensation claim for acquired assets (land, crops, trees and structures etc) and other compensation entitlements under LARP provisions including resettlement, income/livelihood restoration allowances and land price gap differential etc. List of 12 Nos. consultations and participants belonging to the category of DPs/ members of DPCs and representative of local community is given in Annex 6.
- 22. Also delivery of notices, consultative meetings with the DPs in each village, for information disclosure, the following additional activities were also undertaken to inform unpaid DPs to come-up and collect compensation:
 - Information regarding early collection of compensation was also displayed through "Banners" at conspicuous places in all concerned villages. During displaying process, the SSMC team informed the DPs and local people about objective and information contained on banners. A photograph of displayed Banner in different villages (Annex 7)

- The DPs who were not available, NHA issued public notices to receive their payments. Copy of a public notice is given in Annex 8.
- Unpaid compensation amount/ funds have been put in project account and DPs with their whereabouts unknown informed through a local (the daily newspaper "Shamal" to come and receive their compensation). A copy of notice published in newspaper is given in Annex 9.
- Consultative process with DPs continued to ensure that payments to be made as and when the DPs come forward to claim the payments;
- Information disclosure was completed by disclosing the LARP related information to all DPs. A copy of information brochure is given in Annex 10

3.1.2 Efforts Exhausted by NHA with Way Forward

23. The Matrix below provide a summary on efforts exhausted for each unpaid land category and proposed actions with responsibility as way forward to ensure compensation is delivered to all identified unpaid DP as and when their issues are resolved:

24. Proposed Action Plan for the implementation of LARP

Imapct	Un-paid	Action Taken by NHA	Action to address	Responsib
A) Land Compensation	Cases 95 - Transfer Record of Rights(land owners passed away)	 Meetings were held with available displaced persons and their relatives in presence of village DPCs and headman; written notices were delivered to available DPs by LAC/ land staff and DPs were motivated to submit their claims in all affected villages; NHA has informed to all unpaid DPs publically (the daily "Shamal" local newspapers) to come, submit their claims and collect their entitled compensation without delay. Issued notices for early collection of compensation. Displayed banners at prominent places in concerned villages. NHA confirmed that the land cost is already deposited in the treasury. 	pending payments - The available decedents of the DP living in village will be approached through social mobilizers; - DPs will be assisted to approach land revenue authorities and get inheritance mutations recorded; - a close liaison will be maintained with local land revenue people for early mutation in record, and DPs will be mobilized for submission of compensation claims with requisite support documents and delivery of compensation accordingly	PIU (LAC, NHA/ Local revenue authority)/ SSMC will ensure the payment to the DPs
	16 DPs-Absent DPs (NotTraceable)	 NHA deposited funds in District Treasuary DPs with their whereabouts unknown informed through local print media (the daily 'Shamal') newspapers to come and receive their compensation. Issued notices for early collection of compensation. Placed banners at prominent places in concerned villages. For delivery of pending compensation, the LAC and his team retained a close 	The village notables and the DPCs will be coordinated continuously to identify the where about of the DPs living in other cities in Pakistan efforts will be made to approach the DPs at their current places; and DPs will be mobilized to collect compensation through telephonic contacts and by delivering	PIU (LAC, NHA/ Local revenue authority)/ SSMC will ensure the payment to the DPs

Imapct	Un-paid Cases	Action Taken by NHA	Action to address pending payments	Responsib ility
		liaison with the affected people during the reporting period Sites visits for compensation delivery, consultative and information dissemination sessions/ meetings and DPs follow-up has been carried out by the LAC and NHA Land staff. Comprehensive field visit plan was implemented and the LAC and his team repeatedly visited the affected villages	notices through post and any other plausible mean.	
	120 DPs under Verification (i.e. title/ ownership disputed)	 NHA maintained a close liaison between the DPs and the local revenue authorities for early payment as documents are completed. NHA confirmed that the land cost is already deposited in 	- LAC (PIU) will help the DPs to expedite the process of transfer of ownership	PIU (LAC, NHA/ Local revenue authority)/ SSMC will ensure the payment to the DPs
	94 DPs Who Moved Out of Project Area (out of village)	the district treasury. For delivery of pending compensation, the LAC and his team retained a close liaison with the displaced persons during the reporting period Sites visits for compensation delivery, consultative and information dissemination sessions/ meetings and DPs follow-up has been carried out by the LAC and NHA Land staff. Comprehensive field visit plan was implemented and the LAC and his team repeatedly visited the affected villages NHA deposited funds in District Treasury and DPs with their whereabout unknown informed through local press media (the daily "Shamal" local newspapers) to come and receive their entitled compensation. Displayed banners at conspicuous places in concerned villages.	The village notables and the DPCs will be coordinated continuously to identify the where about of the DPs living in other cities in Pakistan efforts will be made to approach the DPs at their current places; and DPs will be mobilized to collect compensation through telephonic contacts and by delivering notices through post and any other plausible mean.	PIU (LAC, NHA/ Local revenue authority)/ SSMC will ensure the payment to the DPs
	668 – Meager amount of compensation	 ➢ For delivery of pending compensation, the LAC and his team retained a close liaison with the displaced persons during the reporting period ➢ Sites visits for compensation delivery, consultative and information dissemination sessions/ meetings and DPs follow-up has been carried out by the LAC and NHA Land staff. ➢ Meetings were held with 	Close liaison will be maintained with DPs to motivate them for submitting of claims with requisite support documents; opportunities to open joint bank accounts will be explored; the efforts will be continued to support DPs in opening of bank	PIU (LAC, NHA/ Local revenue authority)/ SSMC will ensure the payment to the DPs

Imapct	Un-paid Cases	Action Taken by NHA	Action to address pending payments	Responsib ility
		available displaced persons and their relatives in presence of village DPCs and headman; written notices were delivered to available DPs by LAC/land staff and DPs were motivated to submit their claims in all affected villages; The land compensation is already deposited in the treasury.	accounts, submission of claims and deliver their compensation	
	49 DPs out of country (abroad)	For delivery of pending compensation, the LAC and his team retained a close liaison with the displaced persons during the reporting period Sites visits for compensation delivery, consultative and information dissemination sessions/ meetings and DPs follow-up has been carried out by the LAC and NHA Land staff. NHA deposited funds in District Treasury and DPs with their where about unknown informed through local press media (the daily "Shamal" local newspapers) to come and receive their entitled compensation. Displayed banners at prominent places in concerned villages.	The village notables and the DPCs will be coordinated continuously to identify the where about of the DPs living in other cities in Pakistan efforts will be made to approach the DPs at their current places; and DPs will be mobilized to collect compensation through telephonic contacts and by delivering notices through post and any other plausible mean.	PIU (LAC, NHA/ Local revenue authority)/ SSMC will ensure the payment to the DPs
	6 - Court cases – price enhancement	 NHA maintained a close liaison between the DPs and the local revenue authorities to ensure timely disbursement of compensation as court decides. NHA confirmed that the land cost is already deposited in the treasury. 	- NHA maintained a close liaison between DP and local revenue authorities to ensure timely payment of compensation as court decides.	PIU (LAC, NHA/ Local revenue authority)/ SSMC will ensure the payment to the DPs
	1 DP under mortgage with local bank	NHA confirmed that the land cost is already deposited in the treasury and can be paid to PAPs only as per law and subject to decision of the mortgaged property.	 DP will get compensation on paying back the bank loan. Revenue Department is unable to pay the cost of land to these DPs until they get back their land or otherwise decided by the banks. Compensation of land as their land is under mortgage with local bank. 	PIU (LAC, NHA/ Local revenue authority)/ SSMC will ensure the payment to the DPs
	15 DPs are deficient in requisite documentation including lack of CNIC, bank account	 Compensation cost is already deposited in the district treasury. For delivery of pending compensation, the LAC and his team retained a close liaison with the displaced persons during the reporting period 	- Close liaison will be maintained with DHs to motivate them for submitting of claims with requisite support documents; - opportunities to open joint bank accounts will be	PIU (LAC, NHA/ Local revenue authority)/ SSMC will ensure the payment to the DPs

Imapct	Un-paid Cases	Action Taken by NHA	Action to address pending payments	Responsib ility
		 Sites visits for compensation delivery, consultative and information dissemination sessions/ meetings and DPs follow-up has been carried out by the LAC and NHA Land staff. Meetings were held with available displaced persons and their relatives in presence of village DPCs and headman; Written notices were delivered to available DPs by LAC/land staff and DPs were motivated to submit their claims in all affected villages. 	explored; - the efforts will be continued to support DHs in opening of bank accounts, submission of claims and deliver their compensation - LAC (PIU) will help the DPs to expedite the requisite documentation	

3.2 Institutional Arrangements

25. NHA has established a Project Implementation Unit (PIU) under the General Manager E-35 at Abbottabad. The PIU presently comprises of a Project Director, Assistant Director (Engineering), Deputy Director (Land) and Land Acquisition Collector (LAC)with support land staff.NHA and ADB have agreed to acquire the services of Social Safeguard and Management Consultant to plug the capacity gap and assist NHA in the preparation and implementation of LARP.

3.3 Resolution of DPs Grievances

- Presently, a grievance redress mechanism has been established. The grievance redress mechanism in Package-I is following one informal and two formal tier processes to address grievances. The first informal level is existence of DPC at village level. This level includes the DPC representatives and members (both male and female) and social mobilizer. SM often visits the DPC to hear and record their grievances. The grievances that are not resolved by social mobilizer in the field are then share with First level GRC. A Grievance Redress Committee headed by the PD is functioning. Project Director, DD (land) and LAC and In order to provide support to GRC and strengthen its functioning, members from SSMC are included in GRC (RS, GRS, SM) grievances are received and responded to by the members of the GRC. The DPCs⁶ at village level (Informal) are kept involved in the complaint redressal process. Notification of GRC is presented in Annex 11.
- 27. The details of status of community compliance are given in Table 2.5. According to this table, out of the total 220 complaints entered, the issues were resolvel for 213 (96.8%) complaints, while the appropriate addressal is under process for 7 complaints (3.2%)
- 28. Most of the complaints received pertain to the assessment of prices by the Provincial Revenue Departments. The complainants have been informed that the prices ware assessed/fixed on the basis of average of the transactions carried out during the last one year and including an independent land valuation study that they were allowed an opportunity by the Land Collector to record the grievances prior to announcement of award. The complainant still can approach the Referee courts for revision of prices.

⁶Each village already has been assigned 2 social mobilizers to maintain regular contact with the DPs/ DPCs being the first line of contact on issues related to Land Acquisition Resettlement matters.

29. A total of 220 complaints were received from DPs of package-I. A summary of community complaints by type has been prepared and presented in Table 2.5.

Table 2.5: Number of Complaints Entered by Type

Category of Issues	Total No. of Complaint Reported	Total issues resolved (Nos.)	Remaining Issue to be Resolved (Nos.)	Remarks
▶ Price Enhancement	200	200	-	Compensation assessment was based on the valuation study and unit rate estimated is equal to the replacement cost of lost item/ asset.
Court Cases	6	-	6	Court hearings are in process
Passageway	8	8	-	-
Protection Wall	1	-	1	NHA protection wall to construction is in process
► Compensation issue	1	1	-	Already been assessed as well as included in the award and compensation has also been paid. Therefore the complaint is baseless may be closed without further action.
 Calculation errors in revenue record 	4	4	-	-
Total	220	213	7	

3.3.1 Formation of Displaced Persons Committees (DPCs)

30. DPCs in all the 15 mouzas have been established⁷. These committees are taken on-board by the project staff in addressing the grievances of the DPs. These committees are taken on-board by the project staff in addressing the grievances of the DPs at village level.

3.4 Social Safeguards Management Consultant (SSMC)

- 31. In order to effectively implement the LARP and address the social safeguard issues, NHA employed SSMC in April 8, 2015. SSMC is staffed by Resettlement Specialist, Grievance Rredress Specialist, Gender Specialist and Social Mobilizers and is assisting NHA/ PIU in the LARP implementation and monitoring and capacity building in LAR.
- 32. Since its mobilization, the SSMC team deputed for E-35 project is assisting the LARU and PIU in LARP implementation process as per TORs. The specific LAR activities performed up-till January 31, 2016 is given as under.
 - Updating of LARP data base and implementation progress data;
 - Community consultation and information dissemination meetings for LARP disclosure and to provide guidance to the DPs for submission of claims;
 - Assistance of DPs and LARU in processing of compensation claims and delivery of compensation:
 - Developments of templates for grievances recording and maintaining grievance registers and operationalizing the GRM with all key members.
 - Assistance of PIU in monitoring of LARP implementation progress and preparation of LARP monitoring reports.

3.5 Process for Disbursement of Compensation

33. The disbursement of compensation to the DPs is in progress for Package I of E-35. The amount is disbursed to the DPs by the LAC. No other Project functionary participates in the payment process. The progress of payment by the LAC is reported to

⁷ Office letter No. LAC.E-35/NHA/Atd/12/1358, dated 25th April, 2012.

the higher offices of NHA and Revenue Department in the form of monthly report. The following disbursement arrangements are in place at the Project Office.

- A team comprising LAC, Quanoogo and 02 Patwaris is carrying out the compensation disbursement task. As a first step, as per requirements of the LAA, announcements are made in the relevant village/ area before one day of the scheduled visit of the disbursement team. People are asked to come to a specified place (generally prominent place in the village) along with their CNICs and land ownership documents to receive their compensation.
- On the specified date, the LAC with his staff holds a meeting. The Patwari identifies the DP as per his CNIC and fard-e-malkiat issued by revenue office and takes his signatures on the acquaintance roll and affixes his thumb impression, which is mandatory.
- After this activity, the voucher is prepared by Quanoogo. The voucher includes
 the details about affected land with land types and the compensation costs as per
 acquaintance roll. DP signs the voucher. The thumb impression of the DP and his
 CNIC number on the voucher is mandatory. Two witnesses also sign the voucher
 with their CNIC number. Then LAC signs the voucher. The voucher is handed
 over to the DP and a copy is kept in the record.
- The DP brings this voucher to the District Account Office. This office after confirming the identity of the voucher bearer with two witnesses, issues a cross cheque to the DP/ AP of his amount payable from National Bank of Pakistan, Haripur/ Attock.
- The DP deposits this cheque in his account in a bank and the amount is transferred to his account its generaly 15 days process.
- The vouchers for trees and assets are issued separately by the LAC.

3.6 Receipt of Payment U/S 18 of LAA 1894

34. The LAA provides that if a person, in spite of proceedings under sections8 5a, 9 and 10 is not satisfied with the Award in any way, he is allowed to go the court of law for the rectification of his grievances. For this purpose, he is required to receive the Award amount under protest. He records his protest on the acquittance roll at the time preparation of payment voucher. According to information from the LAC, about 6 land owners have gone to the court of law u/s⁹ 18. The LAC facilitates the DPs by providing them the documents related to their compensation amounts and calculation of average vear (owsat vaksala) for different categories of land.

⁹LAA 1894: Section 18: The award of compensation for the owners for acquired land is determined at its market value plus 15% premium in view of the compulsory nature of the acquisition for public purposes.

⁸LAA 1894: i) Section 5a covering the need for enquiry of the concerns or grievances of the affected people related to land prices, ii) Section 9: The LAC gives notice to all APs that the Government intends to take possession of the land and if they have any claims for compensation then these claims are to be made to him at an appointed time and iii) Section 10: Delegates power to the LAC to record statements of the APs in the area of land to be acquired or any part thereof as co-proprietor, sub-proprietor, mortgage, and tenant or otherwise.

3.7 Achevid Progress Shown Linear Plan

- 35. As per ADB SPS 2009 and LAR conditions of the project. 100% payments are to be completed before start up of construction work in the acquired right of way (ROW). The land for ROW has been fully acquired but the process of payments of the DPs is still going on although 96% payment has already been made to 72% DPs. Remaining payments are slow or stuck due to LAA's procedural requirements of compensation disbursement and other factors not in control of NHA. These factors are DPs not living in village or are out of country, meager amount of compensation which connot be disbursed to DPs who do not have bank accounts and CNICs and those DPs who are contesting the land award or awarded prices in the court or those who have issues of land ownership/ inheritance.
- 36. In view of the above issues impeding the compensation disbursement. NHA prepared a linear map of the package-I roadin which NHA illustrated the sections or different stretches of the road where 100% payments have been completed and some small sections where payments are yet to be made or are in the process of making. Based on the linear map, as cleared by ADB, NHA is undertaking construction in only those sections where 100% payments have been completed. This is further illustrated in the linear map as Annex-A. Construction the remaining sections/areas will be undertaken after completing 100% payments. Verification by external monitor and approval by ADB.
- 37. So far 100% payments have been achived in an area of 19.0 Kms (of the total lenth of 20.3 Kms). The EMA has verified the payments and the report has been cleared by ADB, based on which NHA is undertaking the construction work. The remaiing area of 1.3 Km is put on hold and will continue to be on hold unless all payments are completed by 100% and are verified by EMA. The EMA report and linear map will be provided to ADB for approval after all payments are completed in the remaining section of 1.3 Km.


4 CONCLUSIONS

- 38. As mentioned earlier, the land for the project has already been acquired under the LAA in the 15 villages of Package-I. The disbursement of compensation for land and land based assets, acceptable under the LAA is in progress.
- 39. Significant progress has been achieved in the process of payment of land and land based asserts compensation. The final LARP has been approved, hopefully payment of allowances as per ADB Policy will be completed in due course of time, as per provisions of the LARP. The procurement of Social Safeguards and Management Consultant (SSMC) is also a critical action to ensure the effective implementation of LARP.
- 40. On the whole, total amount of compensation of land, non land based and crops (Rs. 596.9 million) was to be paid to 3,797 DPs¹⁰, out of which, an amount of Rs. 573.010 million has been paid to 2,733 DPs on account of payment for the loss of land, structures, community structures and crops. Balance amount of Rs. 23.890 million is yet to be paid to 1,064 DPs, which is under process. The break-up of leftover payments is as under:
 - i) Payment of land Rs.18.5 million to 1064 DPs on account of compensation for the loss of land.
 - ii) Payment of Rs.0.04 million to one DP on account of compensation for the loss of permanent structures.
 - iii) Payment of Rs. 2.49 million to 206 DPs on account of compensation for the loss of trees.
 - iv) Payment of Rs. 2.61 million to 1,131 DPs on account of compensation for the loss of crops.
 - v) Payment of Rs. 0.25 million to 2 DPs on account of compensation for allowances.

¹⁰Differnce of 132 DPs is due to to compensation apportionment, i.e. the number of DPs payable is 3,797, while the LARP reported 3,929 landowners.

ANNEXES

Annex A: Updated Linear Plan - Section-wise status of Payment of Compensation in Package I

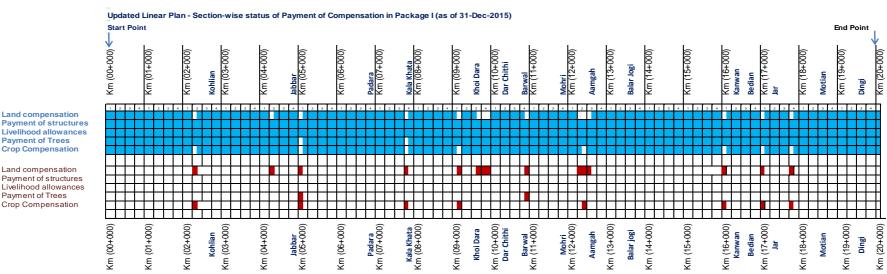

Scale: 1 square equals 250 meters, and 4 squares equal 1 kilometer

Payment has been made to DPs Payments are in process

Land compensation

Livelihood allowances **Payment of Trees Crop Compensation** Land compensation Payment of structures Livelihood allowances Payment of Trees Crop Compensation

	Part A: All type	es of compen	sation fully	paid	Part I	B: Payments o	on-going		
Sr. No.	Affected Villages	_	Chainage-wise sub- sections/reaches		Affected Villages	Chainage-wise sub- section/reaches		Length (KM)	Remarks
		From	То			From	То		
1	Kohlian	0.000	2.250	2.250	Kohlian	2.250	2.375	0.125	Total length of package I road is 20.3 km. Part A, all types
2	Jabbar	2.375	4.250	1.875	Jabbar	4.250	4.375		payments payable to the DPs as per LARP have been fully
3	Padara	4.375	5.125	0.750	Padara	5.125	5.200		completed in different subsections totaling about 19.000
4	Kala Khata	5.200	7.750	2.550	Kala Khata	7.750	7.850	0.100	kms. In other subsections/ reaches as identified part B of
5	Khoi Dara	7.850	9.125	1.275	Khoi Dara	9.125	9.250	0.125	this table totaling about 1.350 km, where the payments are
6	Dar Chithi	9.250	9.625	0.375	Dar Chithi	9.625	9.875	0.250	under process. Payments in these subsections are slow
7	Barwal	9.875	10.750	0.875	Barwal	10.750	10.875	0.125	due to the reasons of land ownership disputes, inheritand
8	Mohri	10.875	12.250	1.375	Mohri	12.250	12.450	0.200	and compensation apportionment cases. Amounts payab will be known after the revenue department makes the
9	Amgah	12.450	16.000	3.550	Amgah	16.000	16.100	0.100	apportionment. Other issues delaying the payments are
10	Kanwan	16.100	17.000	0.900	Kanwan	17.000	17.075	0.075	meager amount of compensation awaiting opening up of
11	Jar	17.075	17.750	0.675	Jar	17.750	17.800	0.050	bank accounts by DPs and some DPs not available at the
12	Motian	17.750	18.625	0.875	Motian	18.625	•		given addresses.
13	Digni	18.625	20.300	1.675					
			Total	19.000			Total	1.350	

Annex 1: Village-wise summary of Awarded Land

Sr. No.	Village	Affected Land (Kanal)	No of DPs Total	Total Amount (Rs.)	Amount Disbursed (Rs.)	Balance Amount (Rs.)
1	Jabar	381.55	175	10,366,901	9,000,762	1,366,139
2	Padarah	244.85	226	17,862,233	16,251,639	1,610,594
3	Kala Katha	192.65	143	4,641,096	3,797,804	843,292
4	Khoi Dara	202.05	320	5,514,341	4,928,347	585,994
5	Dar Chitti	117.8	535	1,197,616	321,483	876,133
6	Motian	465.45	645	161,522,078	155,536,572	5,985,506
8	Jar	145.1	71	22,412,693	21,547,351	865,342
7	Dingi	145.2	52	34,128,479	34,086,276	42,203
9	Aam ghah	209.05	449	15,003,372	13,446,706	1,556,666
10	Kohlian	964.35	258	94,147,050	92,919,848	1,227,202
11	Kanwan	258.95	320	38,283,500	38,184,478	99,022
12	Ballar Jogi	262.45	314	42,392,220	41,016,833	1,375,387
13	Bedian	59.75	75	6,835,025	6,395,340	439,685
14	Mohree	140.45	168	14,584,300	13,784,906	799,394
15	Barwal	69.95	46	7,155,875	6,331,655	824,220
	Total	3859.6	3797	476,046,779	457,550,000	18,496,779

Source: PD office, Abbottabad.

Annex 2: Mouza-wise summary of Payment for Affected Structures

Sr. No	Name of Mouza	DP Nos.	Total Amount (Rs)	Amount Disbursed (Rs)	Balance Amount (Rs)
1	Jabar	6	1,408,640	1,408,640	-
2	Padarah	19	9,699,009	9,699,009	•
3	Kala Katha	2	218,608	218,608	•
4	Khoi Dara	10	12,787,741	12,787,741	•
5	Dar Chitti	6	4,126,413	4,126,413	-
6	Motian	15	17,131,416	17,131,416	-
7	Jar	5	5,049,715	5,049,715	•
8	Dingi	1	192,473	192,473	ı
9	Aam ghah	2	2,188,775	2,188,775	•
10	Kohlian	2	447,274	447,274	•
11	Kanwan	16	17,296,946	17,296,946	•
12	Ballar Jogi	4	2,172,554	2,172,554	•
13	Bedian	4	3,802,446	3,802,446	-
14	Mohree	7	7,926,866	7,926,866	-
15	Barwal	3	1,230,367	1,188,772	41,595
	Total	102	85,679,243	85,637,648	41,595

^{*}Recovery of amount Rs.1,474,550 has to be made in Moza Dar-Chithi by LAC (KPK) E-35 Source: PD office, Abbotabad

Annex 3: Mouza-wise summary of Payment for Affected Trees

Sr. No.	Name of Mouza	No. of DPs	No. of DPs paid	No. of DPs Unpaid	Compensation Amount (Rs)	Disbursed Amount (Rs)
1	Jabar	22	13	9	437,316	341,182
2	Padarah	28	16	12	412,977	288,018
3	Kala Katha	19	15	4	787,646	544,582
4	Khoi Dara	20	15	5	827,051	714,666
5	Dar Chitti	20	6	14	461,152	189,892
6	Motian	38	7	31	624,167	220,799
7	Jar	4	0	4	64,554	43,505
8	Dingi	2	0	2	14,448	1,072
9	Aam ghah	15	8	7	317,090	205,665
10	Kohlian	65	18	47	767,681	721,350
11	Kanwan	99	81	18	1,433,833	1,407,725
12	Ballar Jogi	99	76	23	1,288,107	608,850
13	Bedian	26	15	11	607,068	474,970
14	Mohree	46	32	14	300,121	274,414
15	Barwal	8	4	4	198,875	10,295
Total		511	306	205	8,542,086	6,046,985

Annex 4: Payment for Crops

Sr. No.	Name of Mouza	Compensation Amount (Rs)	Disbursed Amount (Rs)
1	Jabar	1,197,120	1,071,086
2	Padarah	1,032,480	570,348
3	Kala Katha	1,031,520	405,410
4	Khoi Dara	978,720	919,335
5	Dar Chitti	197,760	10,727
6	Motian	4,310,400	4,133,150
7	Jar	1,323,840	1,196,003
8	Dingi	1,386,240	1,289,453
9	Aam gah	558,150	276,309
10	Kohlian	400,023	357,257
11	Kanwan	556,393	455,059
12	Ballar Jogi	925,911	701,369
13	Bedian	91,646	65,022
14	Mohree	198,798	159,549
15	Barwal	33,737	9,923
	Total	14,222,738	11,620,000

Annex 5: Deposit of Fund in Treasury

District Treasury Haripur and Abbottabad



National Highway Authority Land Acquisition Collector (E-35) House No. 79, Street No. 11, Jinnahabad Abbottabad

No: 1()/LAC/(E-35)/NHA/Atd/15/2230-3

Abbottabad, 13th July, 2015

To

District Accounts officers

Abbottabad

District Accounts officers

Haripur

Subject:

VERIFICATION OF ADVANCES FOR PROJECT E-35

With reference to the subject noted above and to state that the detail of status of land acquisition advances of E-35 laying in the Govt treasury is required to be reconciled and verified by the District Account Officer/ treasury.

It is therefore requested to provide this office the detail reconciled statement of amount deposited under Account G-11215 and dispersed so far, so the same may be sent to NHA HQ Islamabad please.

e/c

Land Acquisition Collector (E-35) NHA, Abbottabad

C. C:

• GM (E-35) NHA, Burhan

• PD (E-35) NHA Abbottabad

• Director (LM&IS) NHA HQ, Islamabad

• DD (LM&IS) E-35 NHA, Abbottabad

Land Acquisition.Collector (E-35) NHA, Abbottabad

19

DETAIL OF AMOUNT RECIVED FOR LAND ACQUISITION OF EXPRESSWAY (E-35)(UPDATED 13-07-2015)

S.NO	Cheque No.	Date and From	Amount (IN PKR)	District Treasury	Date of Clearance and Submission in Treasury including Voucher No.	Verification by District Accounts Officer/ Treasury Incharge Concerned
1	(1)No 705993 (2)No 5567078	(1)2-6-2010 (2)3-7-2013 From Director Accounts NHA Islamabad	(1)Rs 700000000.00 (Seven Hundred Million Rupees Only) And (2)Rs339911843.00	Abbottabad	(1)Submitted in District Treasury Abbottabad Vide Voucher No.44 in the Revenue Head Account G-11213 on 8-6-2010. (2) Submitted in District Treasury Abbottabad cheque No 5567078 Dated 03-07-2013 Challan No.24, Rs 420 Million, have been transferred to District Treasury Haripur Vide Challan No 02 in the Revenue Head Account G-11215 on 24-12-2011. Rs 225 Million, have been transferred to District Treasury Haripur Vide Cheque No.2241350 Dated 14-09-2012 Rs 289911843 have been transferred to District Treasury Haripur Vide challan No.07 Dated 09-06-2014	

Land Acquisition Collector Hassanabdal - Havelian Manschra Expressway (E-35) NHA ABBOTTABAH

	No 3307105	4-06-014 From Abbottabad Treasury to Haripur Treasury	Rs.289911843 (Twenty Eight Crore, Ninety Nine Lac, Eleven Thousand Eight Hundred Forty Three Rupees Only)	Hariour	Submitted in the District Treasury Haripur Vide Clique No 3307105/Dated 04-06-2014 Challan No 07 Dated 09-06- 2014
9	No 20605257	12-05-2014 Director Accounts NHA Islamabad	Rs 35930341 (Three crore, Firty Nine Lac, Thirty Thousand Three Hundrey and Forty One Rupees Only)	Haribur	Submitted in the District Treasury Hripur Vide Chque No 20605257 Dated 02-05-2014 Challan No 3 Dated 2-6- 2014 In Revenue Head Account G-11215.

- 1. BALANCE IN HARIPUR TREASURY (Rd) = A//
- 2. BALANCE IN ABBOTTABAD TREASURY (Rd) = 50,000,009.

3. BALANCE IN ABBOTTABAD TREASURY (Lapsed)

LAND ACQUISITION COLLECTOR (E-35) NHA ABBOTTABAD

/AIL OF AMOUNT RECIVED FOR LAND ACQUISITION OF EXPRESSWAY (E-35)(UPDATED 13-07-2015)

S.NO	Cheque No.	Date and From	Amount (IN PKR)	District Treasury	Date of Clearance and Submission in Treasury including Voucher No.	Verification by District Accounts Officer/ Treasury Incharge Concerned
1	Tot	al Expe 6 30-6-1 Ba Ason 3	(1)Rs 700000000.00 (Seven Hundred Million Rupees Only) cl Amount = 32 ichture = 27 SS2S652/ Signamus = 27 SS2S652/ SS2S62/ SS2S62/ SS2S62/ SS2S62/ SS2S62/ SS2S62/ SS2S62/ SS2S62/	83986 25652/	(1)Submitted in District Treasury Abbottabad Vide Voucher No.44 in the Revenue Head Account G-11215 on 8-6-2010. (2) Submitted in District Treasury Abbottabad cheque No 5567078 Dated 03-07-2013 Challan No 24, Rs 420 Million, have been transferred to District Treasury Haripur Vide Challan No 02 in the Revenue Head Account G-11215 on 24-12-2011. Rs 225 Million, have been transferred to District Treasury Haripur Vide Cheque No 24-1350 Dated 14-09-2012. Lapsed Amount (32709638) Dated 30-06-2013	Concerned

BALANCE IN ABBOTTABAD TREASURY (Lapsed)

LAND ACQUISITION COLLECTOR (E-35)

NHA ABBOTTABAD

DETAIL OF AMOUNT RECIVED FOR LAND ACQUISITION OF EXPRESSWAY (E-35) (UPDATED 19-08-2015)

S.NO	Cheque No.	Date and From	Amount (IN PKR)	District Treasury	Date of Clearance and Submission in Treasury including Voucher No.	Verification by District Accounts Officer/ Treasury Incharge Concerned
1	(1)No 705993 (2) No 5567078	(1)2-6-2010 (2)3-7-2013 From Director Accounts NHA Islamabad	(1)Rs 70000000.00 (Seven Hundred Million Rupees Only) & 2(Rs) 339911843	Abbottabad	(1)Submitted in District Treasury Abbottabad Vide Voucher No.44 in the Revenue Head Account G-11215 on 8-6-2010. (2) Submitted in District Treasury Abbottabad cheque No 5567078 Dated 03-07-2013 Challan No 24, Rs 420 Million, have been transferred to District Treasury Haripur Vide Challan No 02 in the Revenue Head Account G-11215 on 24-12-2011. Rs 225 Million, have been transferred to District Treasury Haripur Vide Cheque No2241350 Dated 14-09-2012 Rs 289911843 have been transferred to District Treasury Haripur Vide Cheque No2241350 Dated 14-09-2012 Rs 289911843 have been transferred to District Treasury Haripur Vide challan No 07 Dated 09-06-2014	

Land Acquisition Concetor Hassanabdal - Havelian Janschra Expressway (E-35) NHA ABBO FTABAD

	o 240289	15-12-2011 From Abbottabad Treasury to Haripur Treasury	Rs.42000000.00 (Four Hundred and Twenty Million Rupees Only)	Haripur	Submitted in District Treasury Haripur Vide Voucher No 3 Account office Chque No 2240289 Dated 15-12-2011 in Revenue Head G-11215	
3	lo 23573	14-06-2011 From Director Accounts, NHA, Islamabad	Rs 35000000.00 (Three Hundred And Fifty Million Rupees Only)	Haripur	Submitted in District Treasury Haripur Vide Voucher No)4 in Revenue Head Account G-11215 On 18-06-2011	
4	lo 9788600	15-12-2011 From NHA Project Account	Rs 18400000.00 (One Hundred and Eighty Four Million Rupees Only)	Haripur	Submitted in District Tresury Haripur Vide Voucher No 02 In Revenue Head Account G-11215	
5	002597	11-01-2012 From NHA Project Account	Rs. 41024440 (Four Crore, Ten Lac, Twenty Four Thousand, Four Hundred And Forty Rupees Only	Haripur	Submitted in District Treasury Haripur Vide Voucher No 01 In Revenue Head Account G-11215 on 03-04-2012	
6	lo 6849378	09-03-2012 From NHA	Rs 10000000.00 (One Hundred Million Rupees Only)	Haripur	Submitted in District Treasury Haripur Vide Voucher No 01 in Revenue Head Account G-11215	
7	lo 241350	14-09-2012 From Abbottabad Treasury to Haripur Treasury	Rs 225000000.00 (Two Hundred and Twenty Five Million Rupees Only)	Haripur	Submitted in the District Treasury Haripur Vide Voucher No 04 in Revenue Head Account G-11215	

and Aequisition Conector Hassanabdal - Havelian Mansehra Expressway (E-35) NHA ABBOTT / BAD

8	No 3307105	4-06-014 From Abbottabad Treasury to Haripur Treasury	Rs.289911843 (Twenty Eight Crore, Ninety Nine Lac, Eleven Thousand Eight Hundred Forty Three Rupees Only)	Haripur	Submitted in the District Treasury Haripur Vide Chque No 3307105 Dated 04-06-2014 Challan No 07 Dated 09- 06-2014
9	No 20605257	12-05-2014 Director Accounts NHA Islamabad	Rs 35930341 (Three crore, Fifty Nine Lac, Thirty Thousand, Three Hundred and Forty One Rupees Only)	Haripur	Submitted in the District Treasury Hripur Vide Chque No 20605257 Dated 02-05-2014 Challan No 3 Dated 2-6- 2014 In Revenue Head Account G-11215.

1. BALANCE IN HARIPUR TREASURY (Rd) = 153983730/= wef-19-08-2012 Herigm.

LAND ACQUISITION COLLECTOR (E-35)

NHA ABBOTTABAD

Annex 6: List of Consultations with DPCs/ DPs

A) Consultations matrix with Male DPCs/ DPs

Sr. No	Date	Village	No of participant	Name of participant
1	November 02, 2015	Bhallar Jogi	01	- Malik Rashid Manzoor s/o Malik Manzoor Huaaain
2	November 18, 2015	Amgah	12	 Mr. Khani Zaman s/o Mirza Khan Mr. Awrangzaib s/o Muhammad Ashraf Mr. Zardad Khan s/o Golab Khan Mr. Muhammad Yousaf s/o Muhammad Ismail Mr. Khan Afsar s/o Muhammad Ismail Mr. Ejaz s/o Abdul Rehman Mr. Kamran Khan s/o Ameen Khan Mr. Haji Akhater Zaman Khan s/o Amir Khan (DPC) Mr. Safdar Zaman S/o Muhammad Nazeer Khan (DPC) Mr. Haji Misqeen s/o Muhammad Akber (DPC) Ms. Rasheeda Bibi w/o Maqbool Ali Ms. Rashida Bibi D/o Muhammad Ismai
3	November 18, 2015	Dar Chitti	06	 Mr. Zardad Khan s/o Karam shair Mr. Raheemdad s/o Jandad Khan Mr. Jandad s/o Zardad Khan Mr. Nadir s/o Ghulam Qadir Ms. Parveen Akhter D/o Shair Rehman Ms. Raffat Bibi D/o Ghulam Qadir
4	November 19, 2015	Dar Chitti	02	 Mr. Shair Afzal s/o Sultan Muhammad Mr. Abdul Waqar s/o Nusrat Ali
5	December 07, 2015	Koi Dara	12	 Mr. Muhammad Alyas s/o Jabbar Mr. Noor Alam s/o Sayed Alam Mr. Muhammad Mazhar s/o Munawer Mr. Wali Ahmad s/o Mian dad Mr. Muhammad Akhtar s/o Miskeen Mr. Gulam Sarwer s/o Noor Ahmad Namberdar Muhammad Iqbal s/o Mirza Khan Mr. Gulab s/o Abdul Gafar Mr. Khan Muhammad s/o Allahdad Mr. Haaider Zaman s/o Gulab Mr. Salman s/o Sultan Mr. Lal Baz s/o Sher Baz
6	December 07, 2015	Dar Chitti	06	 Mr. Muhammad Irfan s/o Sher Rehman Mr. Zaheer Ahmad s/o Kamer Zaman Mr. Liaqat Ali s/o Noor Muhammad Mr. Fakhar Zaman Mr. Muhammad Zaman s/o Nawab Mr. Naseer
7	December 07, 2015	Kala Katta	01	- Mr. Pirvez Akhter s/o Misree khan (DPC)

B) Consultations matrix with Female DPCs/ DPs

Sr. No.	Date	Village	No of participant	Name of participant
1	November 19, 2015	Dar Chitti	04	- Ms. Sherazi W/o Shair Afzal D/o Sayed Ahmad - Mr. Abdul Waqar s/o Nusrat Ali
2	December 07, 2015	Kohi Dara	08	 Ms. Shameem Akhter w/o Ghulam Sarwer Ms. Arfana Bibi w/o Abrar Ali Ms. Naseem Akhter w/o Khalid Ali Ms. Maida Bibi w/o Haji Muhammad Ishaq Ms. Noreen Akhter w/o Riayasat Ali Ms. Sodan Jan w/o Sher Bahadur Ms. Rafaqatan Jan w/o Mumtaz Ali Ms. Somia Bibi D/o Mumtaz Ali

Sr. No.	Date	Village	No of participant	Name of participant
3	December 07, 2015	Dar Chitti	09	- Ms. Hameeda w/o Farman Ali - Ms. Rukhsana Bibi w/o Zaheer Ahmad - Ms. Asma Bibi D/o Qamer Zaman - Ms. Abshana Bibi W/o Amjid Ali - Ms. Farzana Bibi w/o Javaid - Ms. Mehwish w/o Muhammad Irfan - Ms. Shehzadi Bibi w/o Sher Afzal - Ms. Shabana Bibi w/o Ibrar khan - Ms. Nazana Bibi w/o Qamer Zaman
4	December 07, 2015	Kala Katta	08	- Ms. Maqsooda Negum w/o Anwer Sher - Ms. Yasmeen w/o Misri khan - Ms. Nabia Bibi w/o Rafaqat - Ms. Chanzib Bibi w/o Muhammad Khursheed - Ms. Farnaz Begum w/o Shehroz khan - Ms. Eiden Bibi w/o Shamrez khan - Ms. Farmeen D/o Sher Rehman - Ms. Raheela Jan D/o Zaheer
5	December 22, 2015	Kala Khatta	07	- MsMaqsooda Jan wd/o Anwer Sher - MsLubna d/o Rafaqat - MsTazeem Bibi w/o Daud - MsMaliya Bibi w/o Rafaqat - MsKaram Jan Bibi Yousaf - Ms Saima w/o Rezwan - Ms. Shazia w/o Zahoor

Annex 7: Information Banner Displayed in the Village





Annex 8: Copy of a Public Notice for Payment

ربان کیمیة فن وسترکت انگ	برصاحب نیشتل مائی و سے اتھار ئی :	از وفتر لينذا يكوزيش كك							
من الله على الله الله الله الله الله الله الله ال									
20-12-014									
.1894	زيرة فعد 1/9/10) يكت جحصول اراشتى سال <u>189</u> 4 ،								
	ينام: ما لكان ، قا بنشين ، مزارعين								
ته ا حدیدال		T .							
مقدم مندرج عنوان بالآقلي ب كدارافني زير حصول حرضيع كالخوال منتصيل حسن ومدال ضلع انك ما كان كوهب ضابط نوش ويا جاتا ب كدهب في باشتبار سركار فيري 946/LAC-2Attock مورد									
ل المل ماهان و مسب صابعه و 10 و کا با ما ہے کہ مسب ویں اسبار مردار بیری <u>946/LAC-ZAttock</u> موریدی 4.32-2013 مندرجہ گورنمنٹ ہنچا یہ مطبوعہ 2013-03-03 مظلم یہ سرای المزقرام اشکام جقراری میں ایک رکد									
<u>4-2-2013 مندرجہ گورنمنٹ ہن</u> جا <u>مطبو</u> ہو <u>. 2013-03-0</u> 0 مطلوب ہے اس کیلئے قمام اشخاص حقداران زمین ندگورو کو معاملات کی جاتی ہے کہ بہتا م ہاری مکولئ پیائش کی اطلاع کی جاتی ہے کہ بہتا م ہارور ندیق بتار ی الامدے اور ب وت <u>9:00 ہ</u> یج بستی اساقا یا مختیارہ حاضر ہوگر									
ا بينا البين القول واقتل أن من مي كيفيت اورمعا وفسه ذكور وكي تعدادا ورتفسيل بيان كرين - البينا البين القول واقتل أن من كي كيفيت اورمعا وفسه ذكور وكي تعدادا ورتفسيل بيان كرين -									
لمزخره متاتره بثير	<i>مو</i> د	اللوج الكوق الماسان							
4—08 96	768	فراس افر سوء قدر فان							
	14/68	عظمت عنى در الحديث خان							
	"	हिम्म्। १५ हर्ट्यं ए							
110	7/168	المسعين دفتر وري فان							
Mosn	,	تسرمني مي وفر تعديان							
	,	لتغطيم بيما فعر فعبت غان							
	56 168	اه و از ور حور مان							
		לעט קעט ועריני							
	168	القال الهروروطور							
1	9/188	المجان في دنفز							
	,	हिर्या प्रांचे वर्ष							
ليندا يكوز يشن كلفر فيشق بالك و القارقي	,	العلم مين نو نظو							
じりょうがよりは、E-35									

Annex 9: Advertisement in Local Newspaper



Annex 10: Information Disclosure Brochure

3-8 103: 104: 104: 105: 105: 105: 105: 105: 105: 105: 105	1 - જેને દેવ તે કે મુશ્કિક મુખ્ય જ - છે : મેં મુખ્ય મારે કે મારે કે માને કે મ		بشر بالروع اقدار في (اين الكال) حكومت باكستان
interpretation heldstore to the registers - Lessen of the restricted description of the contract of the contra	plu:	2 المورك الإنتان 2 المامان +	ميخش زيدكور فيصافى وساؤهن بدكرام
તમે કે મિલ્ક નિર્વા હતા તમે કે ફિંગ નિર્ધા હતા પાનિક હતા તે હોલા હતા હતા હતા હતા હતા હતા હતા હતા હતા હત	X31.8: (46) X10.9: X10.9: X3.65: X7.3:	द्याचार्यात्राहर्यक्षः कः रिक्ट्रिक्ट्याद्याद्वर्षः कः वेद्याच्याद्याद्वर्षः कः (५००) व्यव्यक्तिकः कः वेद्याचीद्वर्णः कः	حسن ابدال-حويليان
-cittingstandigationists Shi A	X385 : Alexandrus :	(qua) वर्रास्त्री के राज्यक्षीर्यं, के के	ایکسپریس ویے پراجیکٹ (ای-35)
4. Lander of section of the state of a -	142 : 1485 :	1-8 8p ± 18 ±	حسول الماضي آباد كالرئيالة ما الولياتي الثرات بارك
- of the standard of the stand	1418 : 140 : 141 :	कार्या के कार्या के	
- esichien Bestelle de la commentation de la commen	₩2 :	2-8	معلوماتی کتابچه
when the word and the course of	: Dos : Dos : Dos	Spr to US to U to Description	
	at :	ه فارس	

Annex 11: Constitution of Grievance Redress Committee under PIU

National Highway Authority Deputy Director (LM&IS) I-35 House No.79, Street No.11, Jinnahabad Abbottabad

213+ Sep. 2015

No. 1() DD (LM & IS)/ (E-35)/NHA/ATD 15

Hassanabdal-Havelian Expressway (E-35) Subject:

Constitution of "Grievance Redress Cell" under PIU LARP

In continuation of AD (L&S)-III NHA HQ LETTER NO. Reference:

1(1)/EALS/NHA/2010/HQ/09 dated 05/03/2011 and approval of Member (N-

Z) vide para-19-24 of office note No.1(1)PD/HAM/E-35/NHA/Atd11/819 para

26 to 30.

Member (North-Zone) has been pleased to accord approval for the constitution of "Grievance Redress Cell" under PIU for LARP on E-35. Accordingly the following Officers/Officials will be responsible for aforementioned cell.

- PD (E-35) NHA i.
- DD/AD (LM&IS) E-35 NHA
- DD/AD (Const) E-35 NHA
- LAC (E-35) KPK/Punjab, NHA
- Qanoongo/Patwari (E-35) NHA V.
- Grievances Redress Specialist/Resettlement Specialist vi.
- Social Mobilizer (Male and Female member) vii.

Deputy Director (LM&IS) (E-35) NHA, Abbottabad

Distribution:

All above concerned officers/officials

- GM (EALS) NHA HQ, Islamabad
- GM (E-35) NHA, Burhan
- · Director (L&S) NHA HQ. Islamabad
- PS to Member (North-Zone)NHA, Peshwar
