



Metro Manila Flood Management Project (P145237)

EAST ASIA AND PACIFIC | Philippines | Water Global Practice |
 Recipient Executed Activities | Specific Investment Loan | FY 2015 | Seq No: 1 | ARCHIVED on 09-Dec-2015 | ISR21878 |

Implementing Agencies: Department of Public Works and Highways

Key Dates

Key Project Dates

Bank Approval Date:16-Sep-2014

Effectiveness Date:19-Jun-2015

Original Closing Date:31-Jan-2017

Revised Closing Date:31-Jan-2017

Project Development Objectives

Project Development Objective (from Project Appraisal Document)

The objective is to prepare priority projects, identified by the flood management master plan, that aim to improve flood management and resilience in and around Metro Manila.

Has the Project Development Objective been changed since Board Approval of the Project Objective?

No

Components

Name

Overall Ratings

Name	Previous Rating	Current Rating
Progress towards achievement of PDO	--	● Moderately Satisfactory
Overall Implementation Progress (IP)	--	● Moderately Satisfactory

Implementation Status and Key Decisions

The Department of Public Works and Highways is currently in the preparation stage for the recruitment of consultants for the various activities to be financed from the grant funds. It is expected that consultants will mobilize within the first half of 2016.



Risks

Overall Risk Rating

Risk Category	Rating at Approval	Previous Rating	Current Rating
Overall	● Moderate	--	● Moderate

Comments

The project is a high priority of the current administration, which is committed to improve the flood management situation in the Greater Metro Manila Area. The implementing agency, DPWH, has experience working with the Bank and its current capacity and governance to implement the studies with the assistance of consulting firms is good. Resettlement of affected people in the flood plain of the Marikina River may potentially be a substantial risk to the eventual implementation of the Upper Marikina River flood management improvements that will be designed through this PHRD grant. It will be tried to keep as many people in place where they are now by designing appropriate infrastructure, but some resettlement cannot be excluded. Resettlement issues will receive detailed attention during the studies. There will be much emphasis on consultations with key stakeholders, including civil society. It has to be stressed that the grant relates to studies only and not to implementation of any works. Considering all this leads to an overall moderate risk.

Results

Project Development Objective Indicators

►Proposals for Upper Marikina structural measures fully designed that are technically, economically, socially, and environmentally sound and that are ready for appraisal. (Number, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	--	0.00	1.00
Date	22-Dec-2014	--	07-Dec-2015	31-Jan-2017

►Proposals for an integrated flood forecasting and early warnign system fully designed and ready for appraisal. (Number, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	--	0.00	1.00
Date	22-Dec-2014	--	07-Dec-2015	31-Jan-2017



►Proposals for institutional arrangements for sustainable flood management in the Greater Metro Manila Area acceptable to the Government of the Philippines and key stakeholders and ready for implementa (Number, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	--	0.00	1.00
Date	22-Dec-2014	--	07-Dec-2015	31-Jan-2017

Overall Comments

Intermediate Results Indicators

►Feasibility study for the proposed interventions in Upper Marikina River completed. (Number, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	--	0.00	1.00
Date	22-Dec-2014	--	07-Dec-2015	31-Jan-2017

►Mid-term report with draft proposals for institutional arrangements for sustianable flood management completed. (Number, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	--	0.00	1.00
Date	22-Dec-2014	--	07-Dec-2015	31-Oct-2016

Overall Comments

Data on Financial Performance

Disbursements (by loan)


Project	Loan/Credit/TF	Status	Currency	Original	Revised	Cancelled	Disbursed	Undisbursed	Disbursed
P145237	TF-18611	Effective	USD	2.73	2.73	0.00	0.00	2.73	0%



Key Dates (by loan)

Project	Loan/Credit/TF	Status	Approval Date	Signing Date	Effectiveness Date	Orig. Closing Date	Rev. Closing Date
P145237	TF-18611	Effective	04-Jun-2015	19-Jun-2015	19-Jun-2015	31-Jan-2017	31-Jan-2017

Cumulative Disbursements

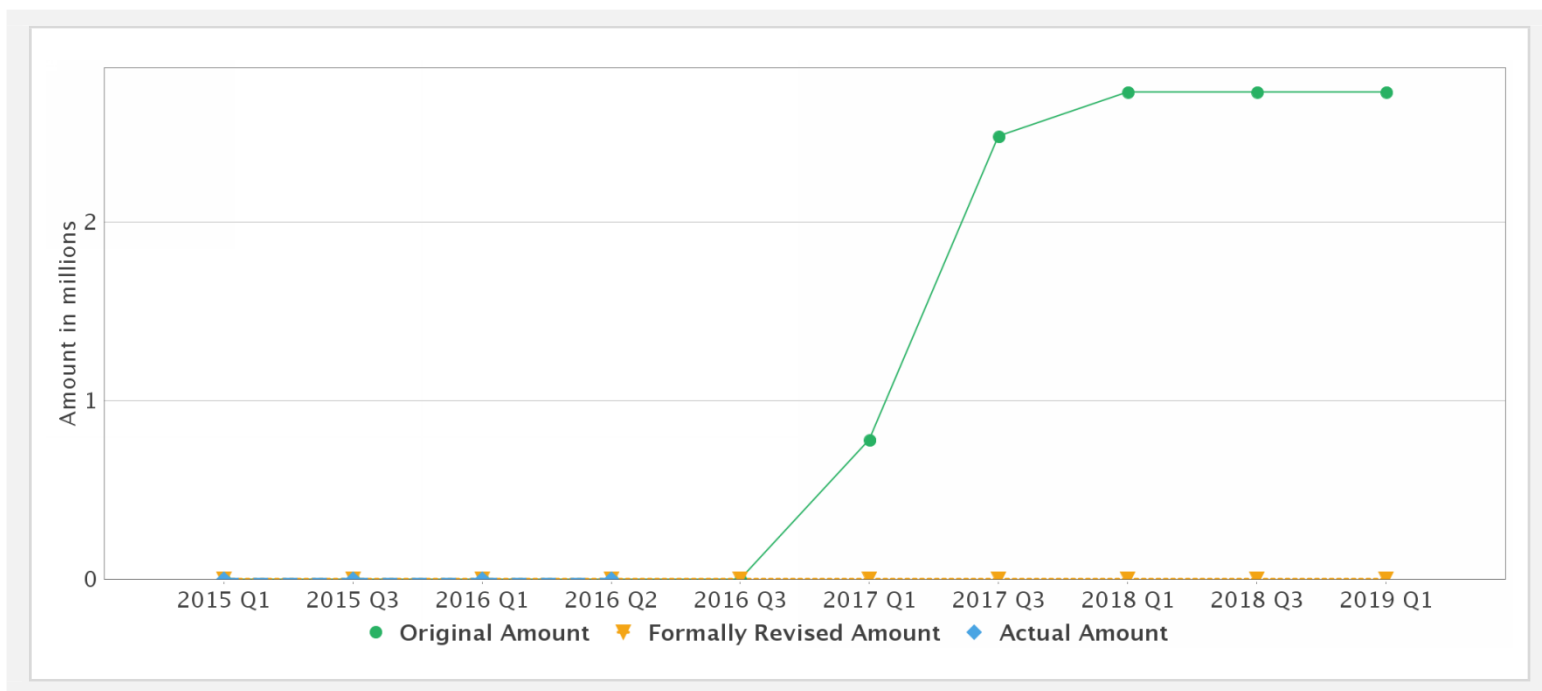

Restructuring History

There has been no restructuring to date.

Related Project(s)

There are no related projects.
