



## Preparation of a Program Towards Sustainable Flood Management in the Greater Metro Manila Area Project (P145237)

EAST ASIA AND PACIFIC | Philippines | Water Global Practice | Recipient Executed Activities | Specific Investment Loan | FY 2015 | Seq No: 3 | ARCHIVED on 27-Jun-2017 | ISR28507 |

Implementing Agencies: Department of Public Works and Highways, Department of Finance

### Key Dates

#### Key Project Dates

Bank Approval Date:16-Sep-2014

Effectiveness Date:19-Jun-2015

Original Closing Date:31-Jan-2017

Revised Closing Date:31-Jan-2018

### Project Development Objectives

Project Development Objective (from Project Appraisal Document)

The objective is to prepare priority projects, identified by the flood management master plan, that aim to improve flood management and resilience in and around Metro Manila.

Has the Project Development Objective been changed since Board Approval of the Project Objective?

No

### Components

Name

### Overall Ratings

Name	Previous Rating	Current Rating
Progress towards achievement of PDO	● Unsatisfactory	● Unsatisfactory
Overall Implementation Progress (IP)	● Unsatisfactory	● Unsatisfactory

### Implementation Status and Key Decisions

The Department of Public Works and Highways is currently in the process of recruiting consulting services for the implementation of the agreed grant activities. It is expected that a contract can be awarded around the end of October 2017.

## Risks

### Overall Risk Rating

Risk Category	Rating at Approval	Previous Rating	Current Rating
Overall	● Moderate	● Moderate	● Moderate

## Results

### Project Development Objective Indicators

►Proposals for Upper Marikina River structural measures fully designed that are technically, economically, socially, and environmentally sound and that are ready for appraisal. (Number, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	1.00
Date	22-Dec-2014	16-Jan-2017	15-Jun-2017	31-Jan-2018

►Proposals for an integrated flood forecasting and early warning system fully designed and ready for appraisal. (Number, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	1.00
Date	22-Dec-2014	16-Jan-2017	15-Jun-2017	31-Jan-2018

►Proposals for institutional arrangements for sustainable flood management in the Greater Metro Manila Area acceptable to the Government of the Philippines and key stakeholders and ready for implementa (Number, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	1.00
Date	22-Dec-2014	16-Jan-2017	15-Jun-2017	31-Jan-2018

## Overall Comments

End targets will be updated if and when a second closing date extension is granted.

## Intermediate Results Indicators

► Feasibility study for the proposed interventions in Upper Marikina River completed. (Number, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	1.00
Date	22-Dec-2014	16-Jan-2017	15-Jun-2017	31-Jan-2018

► Mid-term report with draft proposals for institutional arrangements for sustainable flood management completed. (Number, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	1.00
Date	22-Dec-2014	16-Jan-2017	15-Jun-2017	31-Jan-2018

## Overall Comments

## Data on Financial Performance

## Disbursements (by loan)


Project	Loan/Credit/TF	Status	Currency	Original	Revised	Cancelled	Disbursed	Undisbursed	Disbursed
P145237	TF-18611	Effective	USD	2.73	2.73	0.00	0.00	2.73	0%

## Key Dates (by loan)

Project	Loan/Credit/TF	Status	Approval Date	Signing Date	Effectiveness Date	Orig. Closing Date	Rev. Closing Date
P145237	TF-18611	Effective	04-Jun-2015	19-Jun-2015	19-Jun-2015	31-Jan-2017	31-Jan-2018



### Cumulative Disbursements

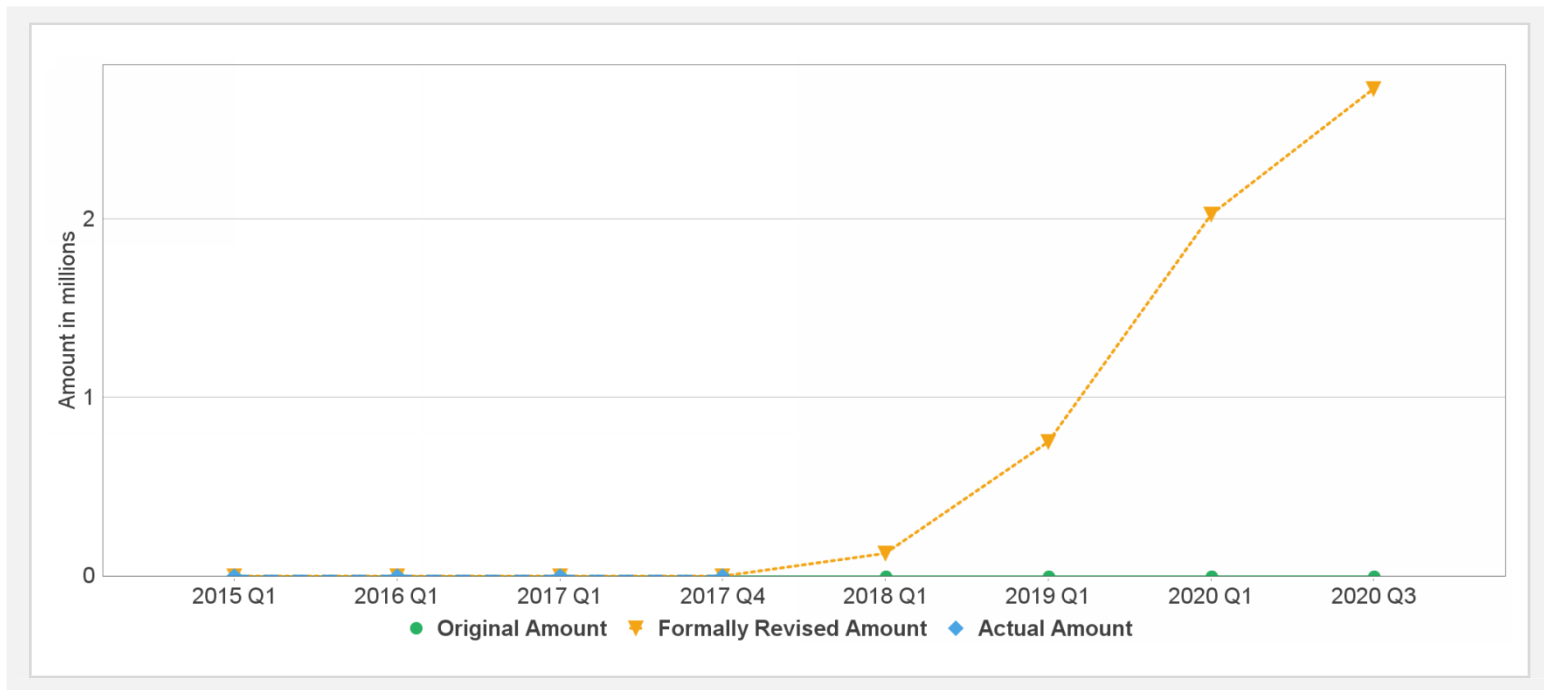

### Restructuring History

Level 2 Approved on 24-Jan-2017

### Related Project(s)

There are no related projects.
