

# Land Acquisition and Resettlement

---

Internal Monitoring Report (E-35, Hassanabdal – Havelian Expressway)  
(November 2015 – January 2016)

**PAK: National Trade Corridor Highway Investment  
Program (NTCHIP) – Tranche 3 (Package III)**

Prepared by National Highways Authority for the Asian Development Bank.

## **NOTES**

- (i) The fiscal year (FY) of the Government of the Islamic Republic of Pakistan and its agencies ends on 30 June.
- (ii) In this report, "\$" refers to US dollars.

This social monitoring report is a document of the borrower. The views expressed herein do not necessarily represent those of ADB's Board of Directors, Management, or staff, and may be preliminary in nature.

In preparing any country program or strategy, financing any project, or by making any designation of or reference to a particular territory or geographic area in this document, the Asian Development Bank does not intend to make any judgments as to the legal or other status of any territory or area.



NATIONAL HIGHWAY AUTHORITY  
Ministry of Communications  
Government of Pakistan



**National Trade Corridor Highway Investment Program**

(ADB Loan No. 3197: Pak NTCHIP Tranche 3)

**Consultancy Services for  
Social Safeguard Management Consultant (SSMC) of  
Hassanabdal-Havelian (E-35) Expressway Project**

**2<sup>nd</sup> Quarterly Internal Monitoring Report**  
for the  
**Implementaion of Land Acquisition and Resettlement Plan  
(Package III)**  
(39+500 – 58+600)  
(Nov. – Jan 2016)

**Social Safeguard Management Consultant**  
Project Implemenation Unit  
NHA Office, Burhan  
(February 29, 2016)

NATIONAL HIGHWAY AUTHORITY

Ministry of Communications  
Government of Pakistan

**National Trade Corridor Highway Investment Program**

(ADB Loan No. 3197: Pak NTCHIP Tranche 3)

**Consultancy Services for  
Social Safeguard Management Consultant (SSMC) of  
Hassanabdal-Havelian (E-35) Expressway Project**

**2<sup>nd</sup> Quarterly Internal Monitoring Report**  
for the  
Implementaion of Land Acquisition and Resettlement Plan  
(Package III)  
(39+500 – 58+600 )  
(Nov. – Jan 2016)

**Social Safeguard Management Consultant**  
Project Implemenation Unit  
NHA Office, Burhan

(February 29, 2016)

## TABLE OF CONTENTS

TABLE OF CONTENTS .....	1
LIST OF TABLES .....	2
LIST OF ANNEXES.....	2
1. INTRODUCTION.....	3
1.1 Background.....	3
1.2 Internal Monitoring Report and its Objectives .....	4
2. STATUS OF IMPLEMENTATION OF LARP .....	4
2.1 No. of Displaced Persons (DPs).....	5
2.2 Land Acquisition.....	5
2.3 Compensation Disbursement .....	6
2.3.1 Disbursement of land Compensation.....	6
2.4.2 Payment of Affected Structures.....	6
2.4.3 Payment of Affected Trees .....	6
2.4.4 Payment of Affected Crops .....	6
2.4.5 Payment for Allowances.....	6
2.5 Categorized Land Payments Requiring Special Efforts to Enable Disbursement to DPs.....	7
<b>3.1 NHA's Efforts Made/ Being Made to Facilitate Pending Payments .....</b>	<b>8</b>
<b>3.1.1 Efforts Made and actions taken to Address Pending Payments.....</b>	<b>8</b>
<b>3.1.2 Efforts Exhausted by NHA with Way Forward .....</b>	<b>9</b>
3.2 Institutional Arrangements.....	10
3.3 <b>Resolution of DPs Grievances.....</b>	<b>10</b>
3.3.1 Formation of Displaced Persons Committees (DPCs) .....	11
3.4 Social Safeguards Management Consultant (SSMC) .....	11
3.5 Process for Disbursement of Compensation .....	12
3.6 Receipt of Payment U/S 18 of LAA 1894.....	12
3.7 Achevid Progress Shown Linear Plan .....	14
4 CONCLUSIONS.....	15

## **LIST OF TABLES**

Table 2.1: Phase 1 of E-35 Package and its Sections .....	3
Table 2.2: Mouza-wise Land Acquisition and Owners of Land/ DPs .....	5
Table 2.3: Status of Implementation of LARP .....	7
Table 2.4: Categorized Land Payments Requiring Special Efforts to Enable Disbursement to DPs .....	7
Table 2.5: Number of Complaints Entered by Type .....	11

## **LIST OF ANNEXES**

Annex A: Updated Linear Plan - Section-wise status of Payment of Compensation .....	16
Annex 1: Village-wise summary of Awarded Land .....	19
Annex 2: Village -wise Status of Payment for Affected Fruit & Non-Fruit Trees .....	19
Annex-3: Payment for Crops .....	20
Annex-4: Village -wise Status of Payment of Allowances .....	20
Annex 6: List of Consultations with DPCs/ DPs .....	28
Annex 7: Information Banner Displayed in the Village .....	31
Annex 8: Advertisement in Local Newspaper .....	32
Annex 9: Information Disclosure Brochure .....	33
Annex 10: Constitution of Grievance Redress Committee under PIU .....	34

Internal Monitoring Report of E-35 Project  
(Package III: 39+500 – 58+600)

**1. INTRODUCTION**

**1.1 Background**

1. The National Highway Authority (NHA) is implementing the National Trade Corridor Highway Investment Program (NTCHIP) financed by Asian Development Bank (ADB) through a Multitranchise Financing Facility (MFF). National Highway Authority (NHA, the project executing agency) identified several road projects for construction under different tranches of the MFF. Tranche 1 of MFF included the construction of section 1 (loan no. 2400) Faisalabad-Khanewal Motorway Project (M-4) in the province of Punjab. Construction of section 1 of M-4 and implementation of LARP has been confirmed by the external monitoring agent. Tranche 2 of MFF includes sections I and II of the Hassanabdal-Havelian Expressway Project (E-35). The expressway project is a green field project and involves a completely new alignment in the province of Khyber Pakhtunkhwa (KPK). Figure 1 below shows the project location.



2. NHA plans to implement the expressway in 2 phases. Phase-1 consists of a 58.6km long road from Hassanabdal to Havelian which is financed by ADB. Phase-2 of expressway includes 51.4km long road from Havelian-Mansehra, which is currently outside ADB’s financing. Total length of phase-1<sup>1</sup> is 58.6 km which is divided into three different sections as shown in the table 2.1 below:

**Table 2.1: Phase 1 of E-35 Package and its Sections**

Sections/Package	Sub-sections	Location	Chainage
I	1a	Punjab Province	000+000 - 007+000
I	1b	KPK Province	007+000 - 020+300
II	2	KPK Province	020+300 - 039+500
III	3	KPK Province	039+500 - 058+600

<sup>1</sup> The Package –I: 000+000 - 007+000 km in Punjab & 000+007 - 020+300 (KPK), the Package-II: 020+300 - 039+500 km & Package-III: 039+500 - 058+600. The package II & III is located in the province of Khyber Pakhtunkhwa

3. Phase 1 of E-35 Expressway Project starts from Islamabad-Lahore Motorway (M-1) near Burhan interchange and ends at Havellian. The package-II of E-35 has a total length of 19.1 km starting from Maqsooda interchange near Sarai Saleh (chainage 39+500 km) and ends at Langra (chainage 58+600) km tehsil Haripur and Havelian and district of Haripur Abbottabad in KPK.

4. The road design of package-III includes construction of new 7.3 meter dual carriageway with New Jersey barrier as median, In addition, it also has 2 interchanges, 2 flyovers and 5 underpasses, one bridge over railway crossing and service area at one location which will be constructed during implementation. The Expressway will be fenced from both sides and six (15) feet service road will also be provided on both sides for use by local people. Total width of Right of Way (ROW) is 60m, which has been full acquired using the Land Acquisition Act (LAA) of 1894.

5. The Land Acquisition and Resettlement (LAR) impacts of the project (package III) were assessed as significant and a Land Acquisition and Resettlement Plan (LARP) was prepared in accordance with ADB's Safeguard Policy Statement of 2009 (SPS), Pakistan's Land Acquisition Act of 1894 (LAA) and the updated Land Acquisition and Resettlement Framework of MFF. In addition to the LARP, NHA also undertook a detailed land valuation study by the valuation experts to ensure that land compensation provided to the displaced persons (DPs) meets/ approximates full replacement cost as required under ADB's SPS 2009.

## **1.2 Internal Monitoring Report and its Objectives**

6. This internal monitoring has been prepared by NHA with assistance of Social Safeguard Management Consultant (SSMC) of the project. The objective of report is to present an up to date status of progress of LARP and disbursement of payments to DPs and illustrate the payments made on a linear map of the road to confirm that construction activities fully comply with the requirements of LARP and SPS 2009 that no construction activities are taking place in any area (under package III road) where full payments of compensation have not been achieved and verified/ validated by an external monitoring agent.

## **2. STATUS OF IMPLEMENTATION OF LARP**

7. NHA is implementing the LARP of package III with assistance of SSMC based at Project Implementation Unit (PIU based in the field at Burhan) and Project Management Unit (based at NHA headquarters in Islamabad). This internal monitoring report, prepared by NHA with assistance of SSMC, provides an update status of LARP implementation and payments made to the DPs covering the following:

- i) No. of displaced persons (DPs) paid, unpaid and being paid;
- ii) Status of land acquisition;
- iii) Loss of structures and status of payments and income restoration;
- iv) Affected fruit and timber/ wood trees and status of their payments;
- v) Affected crops and payments;
- vi) Payment of allowances including rehabilitation, livelihood restoration and vulnerability allowances;
- vii) Categorized payment of land compensation including payments to the DPs (a) not living in the project area, (b) have meager amounts of compensation, (c) do not have bank accounts and national ID cards, (d) and have issues with land titles/ ownership or inheritance matters;
- viii) Efforts underway to complete all categorized payments;
- ix) Complaints/ redress management;



- x) Institutional arrangements put in place for LARP implementation and monitoring;
- xi) Linear map of the road indicating status of land compensation and construction works; and
- xii) Conclusions and recommendations.

## 2.1 No. of Displaced Persons (DPs)

8. Total number of DPs of land and non-land assets including those eligible for different allowances comes to be 6,632 DPs. The status of their payment is as under:

## 2.2 Land Acquisition

9. A total of 2,066.75 kanals (258.34 acres) land was needed for the construction of road, which has been fully acquired.

10. This land was located in 15 villages which were affected by the project. These villages included Nowshehra, Mallah, Kalu Maira, Droni Maira, Maqsooda, Dobandi, Akhon Bandi, Mairatoot, Mohri, Changi Bandi, Bagra, Gheba,

Langra, Wazeera, Kholiyan Bala and Langra. Figure 2.1: provides a village-wise status of land acquisition in package III of the project.

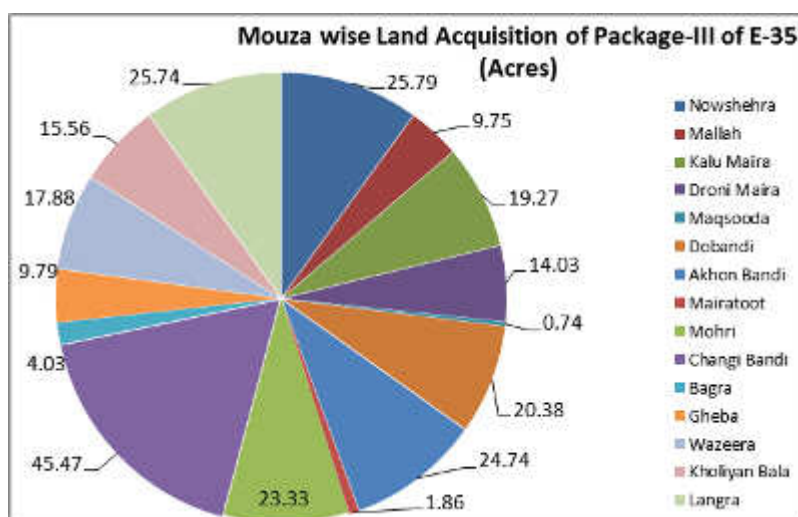


Figure 2.1: Village- wise Land Acquisition of Hassanabdal - Havelian Expressway

11. Further details showing number of affected land owners in all 15 villages with the land acquired are provided below in table 2.2.

Table 2.2: Mouza-wise Land Acquisition and Owners of Land/ DPs

Affected villages	Village	Affected Land within 60m RoW		No. of DPs
		(Kanal)	(Acres)	
1	➤ Nowshehra	206.30	25.79	512
2	➤ Mallah	78.00	9.75	232
3	➤ Kalu Maira	154.15	19.27	583
4	➤ Droni Maira	112.20	14.03	272
5	➤ Maqsooda	5.90	0.74	3
6	➤ Dobandi	163	20.38	203
7	➤ Akhon Bandi	197.95	24.74	452
8	➤ Mairatoot	14.9	1.86	167
9	➤ Mohri	186.60	23.33	1541
10	➤ Changi Bandi	363.75	45.47	1270
11	➤ Bagra	32.25	4.03	54
12	➤ Gheba	78.35	9.79	231
13	➤ Wazeera	143.00	17.88	179
14	➤ Kholiyan Bala	124.50	15.56	277
15	➤ Langra	205.90	25.74	656
Total (affected land owners)		<b>2066.75</b>	<b>258.34</b>	<b>6,632</b>

<b>DPs of Non-land Assets</b>			
Affected structures owners			<b>40</b>
<b>Affected trees owners (fruit trees)</b>			<b>195</b>
<b>Affected non-fruit trees</b>			<b>100</b>
<b>Affected Crops</b>			<b>1,877*</b>

*\*multiple count. Already included in affected land owners.*

## **2.3 Compensation Disbursement**

12. Procedures of LAA 1894 are being followed in disbursement of land compensation to the affected land owners. Details of payments disbursed so far is as under:

### **2.3.1 Disbursement of land Compensation**

13. A total amount of land compensation was Rs. 359.26 million was to be paid to 6,632 DPs<sup>2</sup>. Out of which, Rs.308.20 million (85.8%) have been paid to 3,639 DPs (54.9%). The remaining amount of Rs. 51.06 million (14.2 %) to remaining 2,993 DPs (45.21%) is under process. More details about land compensation to the DPs are provided in table 2.3 below.

### **2.4.2 Payment of Affected Structures**

14. Internal monitoring results show that total amount of compensation for loss of residential/ commercial structures was Rs. 22.13 million payable to 5 DPs. Out of which payment of Rs. 17.36 million (78.4%) have been paid to 3DPs (60.0%). The remaining amount of Rs. 4.77 million (21.6 %) to remaining 2 DPs is under process. Further details are in table 2.3 below.

### **2.4.3 Payment of Affected Trees**

15. In case of fruit and wood trees, a total of 635 DPs<sup>3</sup> had to be paid an amount of Rs. 11.01 million. To date, 459 DPs (72.3 %) have been paid an amount of Rs. 8.75 million (79.5%). The remaining 176 DPs (27.7%) are yet to be paid an amount of Rs. 2.26 million (20.5%). Further details are in table 2.3 below.

### **2.4.4 Payment of Affected Crops**

16. In case of crops a total number of 1,877 DPs<sup>4</sup> had to be paid an amount of Rs. 4.48 million. To date 220 DPs (11.7%) have been paid an amount of Rs. 1.33 million (29.7%). The remaining 1,657 DPs (88.3%) are yet to be paid an amount of Rs. 3.15 million (70.3%). More details are in table 2.3 below.

### **2.4.5 Payment for Allowances**

17. In case of allowances (rehabilitation/ livelihood restoration) payments, 208 DPs<sup>5</sup> had to be paid an amount of Rs. 10.37 million. Out of total, 157 DPs (75.5%) have been paid an amount of Rs. 8.11 million (78.2%) on account of allowances/ livelihood restoration. More details are in table 2.3 below.

<sup>2</sup> The number of DPs increased to 6,632 due to inheritance cases as compared with the LARP figure of 5,028 Nos.

<sup>3</sup>DPs already include in land owner.

<sup>4</sup>DPs already include in land owner.

<sup>5</sup>DPs already include in land owner.

Annexes 1, 2, 3 & 4 provide additional details about DPs and their payments for affected land, structures, trees and crops.

**Table 2.3: Status of Implementation of LARP**

Type of Payment	Payable	Total	Progress till December 2015			Progress during January 2016			Total (as of 31 <sup>st</sup> January, 2016)		
	Payment	DPs	Paid Amount	Unpaid Amount	Paid DPs	Paid Amount	Unpaid Amount	Paid DPs	Paid Amount	Unpaid Amount	Paid DPs
	(Rs. M)	(No)	(Rs. M.)	(Rs. M.)	(No.)	(Rs. M.)	(Rs. M.)	(No.)	(Rs. M.)	(Rs. M.)	(No.)
Land Compensation	359.26	6632	308.19	51.07	3637	0.015	51.06	2	308.20	51.06	3639
Crops Compensation	4.48	1877	1.32	3.16	218	0.01	3.15	2	1.33	3.15	220
Affected Structures	22.13	5	17.36	4.77	3	0.00	4.77	0	17.36	4.77	3
Affected Trees	11.01	635	8.67	2.34	456	0.08	10.93	3	8.75	2.26	459
Allowances – rehabilitation/ livelihood restoration	10.37	208	8.11	2.26	157	0.00	2.26	0	8.11	2.26	157

## 2.5 Categorized Land Payments Requiring Special Efforts to Enable Disbursement to DPs

18. As mentioned earlier in the report, a total remaining 2,993 DPs are yet to be compensated for land. Their payments are slow due to the following reasons: . ,

- **Transfer Record of Rights:** a total of 439 land owners have unfortunately passed away which requires transfer of land to the inheritors. Payments to inheritors will be made after transfer of land to the inheritors by the district revenue authority. The process of transfer of land to the inheritors is under progress already.
- **DPs under Verification** (i.e. title/ ownership disputed): 199 DPs of family ownership disputes i.e. having no proof of ownership.
- **DPs Unwilling to Receive Payments:** There are 1790 DPs who are unwilling to receive compensation because of share of compensation being meager amount. Under LAA procedures they are required open their bank accounts for disbursement of payments of their bank accounts.
- **Land Litigation:** About 13 land owners DPs, are in litigation and did not agree to get the compensation announced by the revenue department. These Dps are demanding higher compensation and their cases are in the courts of law. .
- **Miscellaneous Issues:** About 552 DPs are also difficulty in receiving payments due to different issues such as DPs who don't have CNIC or whom bank accounts, correction of name / Land Owners under other reasons;

**Table 2.4: Categorized Land Payments Requiring Special Efforts to Enable Disbursement to DPs**

Total un Paid DPs	Transfer Record of Rights (Death Cases)	DPs under Verification (i.e. title/ ownership disputed)	Meager Amount	Land Owner/ DPs under court cases	Other reason
(Nos.)	(Nos.)	(Nos.)	(Nos.)	(Nos.)	(Nos.)
2993	439	199	1790	13	552

### 3.1 NHA's Efforts Made/ Being Made to Facilitate Pending Payments

#### 3.1.1 Efforts Made and actions taken to Address Pending Payments

19. For delivery of pending payment, the LAC and his team retained a close liaison with the displaced persons during the reporting period. Sites visits for compensation delivery, consultative and information dissemination sessions/ meetings and DPs follow-up has been carried out by the LAC and NHA Land staff. In this regard a comprehensive field visit plan was implemented and the LAC and his team repeatedly visited the affected villages to process compensation claims and deliver compensation to displaced persons at their door steps.

20. During visits, meetings were held with available displaced persons and their relatives in presence of village DPCs and headman; written notices were distributed to available DPs by LAC/ land staff and DPs were motivated to submit their claims in all affected villages; and the list of unpaid DPs was disclosed to the village headmen, DPC members and local community to seek assistance for locating and informing unpaid DPs for receipt of their compensation. In the notices, DPs were informed to receive their compensation for acquired assets (land, structure, houses, trees and crops) and allowances etc. During consultative process, LAC and NHA land staff clarified the DPs that the compensation is deposited in treasury and can be collected after submission of claims and if not claimed in timely manner, the compensation could be deposited in the court under section 31 of LAA 1894 and no excuses will be accepted. Deposit of funds in treasury is presented in Annex 5.

21. Since mobilization of SSMC, its team developed a rapport with the LARU team in PIU, DPCs in each village and displaced persons. During reporting period total 13 consultations were made by the male and female social mobilizers, wherein 138 DPs/ members of DPCs as well as local community participated. During such consultations with DPs and DPCs, the information disclosed include project LAR impacts, compensation eligibility and entitlements as per LARP provisions, submission of compensation claim for acquired assets (land, crops, trees and structures etc) and other compensation entitlements under LARP provisions including resettlement, income/ livelihood restoration allowances and land price gap differential etc. List of 13 Nos. consultations and participants belonging to the category of DPs/ members of DPCs and representative of local community is given in Annex 6.

22. Also delivery of notices, consultative meetings with the DPs in each village, for information disclosure, the following additional activities were also undertaken to inform unpaid DPs to come-up and collect compensation:

- Information regarding early collection of compensation was also displayed through "Banners" at conspicuous places in all concerned villages. During displaying process, the SSMC team informed the DPs and local people about objective and information contained on banners. A photograph of displayed Banner in different villages (Annex 7)
- The DPs who were not available, NHA issued public notices to receive their payments.
- Unpaid compensation amount/ funds have been put in project account and DPs with their whereabouts unknown informed through a local (the daily newspaper "Shamal" to come and receive their compensation). A copy of notice published in newspaper is given in Annex 8.

- Consultative process with DPs continued to ensure that payments to be made as and when the DPs come forward to claim the payments;
- Information disclosure was completed by disclosing the LARP related information to all DPs. A copy of information brochure is given in Annex 9

### 3.1.2 Efforts Exhausted by NHA with Way Forward

23. The Matrix below provide a summary on efforts exhausted for each unpaid land category and proposed actions with responsibility as way forward to ensure compensation is delivered to all identified unpaid DP as and when their issues are resolved:

### 24. Proposed Action Plan for the implementation of LARP

Impact	Un-paid Cases	Action Taken by NHA	Action to address pending payments	Responsibility
A) Land Compensation	439 – Transfer Record of Rights (land owners passed away)	<ul style="list-style-type: none"> <li>➤ Meetings were held with available displaced persons and their relatives in presence of village DPCs and headman;</li> <li>➤ written notices were delivered to available DPs by LAC/ land staff and DPs were motivated to submit their claims in all affected villages;</li> <li>➤ NHA has informed to all unpaid DPs publically (the daily “Shamal” local newspapers) to come, submit their claims and collect their entitled compensation without delay.</li> <li>➤ Issued notices for early collection of compensation.</li> <li>➤ Displayed banners at prominent places in concerned villages.</li> <li>➤ NHA confirmed that the land cost is already deposited in the treasury.</li> </ul>	<ul style="list-style-type: none"> <li>- The available decedents of the DP living in village will be approached through social mobilizers;</li> <li>- DPs will be assisted to approach land revenue authorities and get inheritance mutations recorded;</li> <li>- a close liaison will be maintained with local land revenue people for early mutation in record, and DPs will be mobilized for submission of compensation claims with requisite support documents and delivery of compensation accordingly</li> </ul>	PIU (LAC, NHA/ Local revenue authority)/ SSMC will ensure the payment to the DPs
	199 DPs under Verification (i.e. title/ ownership disputed)	<ul style="list-style-type: none"> <li>➤ NHA maintained a close liaison between the DPs and the local revenue authorities for early payment as documents are completed.</li> <li>➤ NHA confirmed that the land cost is already deposited in the district treasury.</li> </ul>	<ul style="list-style-type: none"> <li>- LAC (PIU) will help the DPs to expedite the process of transfer of ownership</li> </ul>	PIU (LAC, NHA/ Local revenue authority)/ SSMC will ensure the payment to the DPs
	1790 – Meager amount of compensation	<ul style="list-style-type: none"> <li>➤ For delivery of pending compensation, the LAC and his team retained a close liaison with the displaced persons during the reporting period</li> <li>➤ Sites visits for compensation delivery, consultative and information dissemination sessions/ meetings and DPs follow-up has been carried out by the LAC and NHA Land staff.</li> <li>➤ Meetings were held with available displaced persons</li> </ul>	<ul style="list-style-type: none"> <li>- Close liaison will be maintained with DPs to motivate them for submitting of claims with requisite support documents;</li> <li>- opportunities to open joint bank accounts will be explored;</li> <li>- the efforts will be continued to support DPs in opening of bank accounts, submission of</li> </ul>	PIU (LAC, NHA/ Local revenue authority)/ SSMC will ensure the payment to the DPs

Impact	Un-paid Cases	Action Taken by NHA	Action to address pending payments	Responsibility
		<ul style="list-style-type: none"> <li>and their relatives in presence of village DPCs and headman;</li> <li>&gt; written notices were delivered to available DPs by LAC/land staff and DPs were motivated to submit their claims in all affected villages;</li> <li>&gt; The land compensation is already deposited in the treasury.</li> </ul>	claims and deliver their compensation	
	13- Court cases – price enhancement	<ul style="list-style-type: none"> <li>&gt; NHA maintained a close liaison between the DPs and the local revenue authorities to ensure timely disbursement of compensation as court decides.</li> <li>&gt; NHA confirmed that the land cost is already deposited in the treasury.</li> </ul>	- NHA maintained a close liaison between DP and local revenue authorities to ensure timely payment of compensation as court decides.	PIU (LAC, NHA/ Local revenue authority)/ SSMC will ensure the payment to the DPs
	552 DPs are deficient in requisite documentation including lack of CNIC, bank account	<ul style="list-style-type: none"> <li>&gt; Compensation cost is already deposited in the district treasury.</li> <li>&gt; For delivery of pending compensation, the LAC and his team retained a close liaison with the displaced persons during the reporting period</li> <li>&gt; Sites visits for compensation delivery, consultative and information dissemination sessions/ meetings and DPs follow-up has been carried out by the LAC and NHA Land staff.</li> <li>&gt; Meetings were held with available displaced persons and their relatives in presence of village DPCs and headman;</li> <li>&gt; Written notices were delivered to available DPs by LAC/land staff and DPs were motivated to submit their claims in all affected villages.</li> </ul>	<ul style="list-style-type: none"> <li>- Close liaison will be maintained with DHs to motivate them for submitting of claims with requisite support documents;</li> <li>- opportunities to open joint bank accounts will be explored;</li> <li>- the efforts will be continued to support DHs in opening of bank accounts, submission of claims and deliver their compensation</li> <li>- LAC (PIU) will help the DPs to expedite the requisite documentation</li> </ul>	PIU (LAC, NHA/ Local revenue authority)/ SSMC will ensure the payment to the DPs

### 3.2 Institutional Arrangements

25. NHA has established a Project Implementation Unit (PIU) under the General Manager E-35 at Abbottabad. The PIU presently comprises of a Project Director, Assistant Director (Engineering), Deputy Director (Land) and Land Acquisition Collector (LAC) with support land staff. NHA and ADB have agreed to acquire the services of Social Safeguard and Management Consultant to plug the capacity gap and assist NHA in the preparation and implementation of LARP.

### 3.3 Resolution of DPs Grievances

26. Presently, a grievance redress mechanism has been established. The grievance redress mechanism in Package-III is following one informal and two formal tier processes to address grievances. The first informal level is existence of DPC at village

level. This level includes the DPC representatives and members (both male and female) and social mobilizer. SM often visits the DPC to hear and record their grievances. The grievances that are not resolved by social mobilizer in the field are then share with first level GRC. A Grievance Redress Committee headed by the PD is functioning. Project Director, DD (land) and LAC and In order to provide support to GRC and strengthen its functioning, members from SSMC are included in GRC (RS, GRS, SM) grievances are received and responded to by the members of the GRC. The DPCs<sup>6</sup> at village level (Informal) are kept involved in the complaint redressal process. Notification of GRC is presented in Annex 10.

27. The details of status of community compliance are given in Table 2.5. According to this table, out of the total 19 complaints entered, the issues were resolved for 6 (31.6 %) complaints, while the 13 complaints (68.4%) will be redressed after the decision of court.

28. Most of the complaints received pertain to the assessment of prices by the Provincial Revenue Departments. The complainants have been informed that the prices were assessed/ fixed on the basis of average of the transactions carried out during the last one year and including an independent land valuation study that they were allowed an opportunity by the Land Collector to record the grievances prior to announcement of award. The complainant still can approach the Referee courts for revision of prices.

29. A total of 19 complaints were received from DPs of package-III. A summary of community complaints by type has been prepared and presented in Table 2.5.

**Table 2.5: Number of Complaints Entered by Type**

Category of Issues	Total No. of Complaint Reported	Total issues resolved (Nos.)	Remaining Issue to be Resolved (Nos.)	Remarks
▶ Price Enhancement	5	5	-	Compensation assessment was based on the valuation study and unit rate estimated is equal to the replacement cost of lost item/ asset.
▶ Court Cases	13	-	13	Court hearings are in process
▶ Calculation errors in revenue record	1	1	-	
<b>Total</b>	<b>19</b>	<b>6</b>	<b>13</b>	

### 3.3.1 Formation of Displaced Persons Committees (DPCs)

30. DPCs in all the 15 villages have been established<sup>7</sup>. These committees are taken on-board by the project staff in addressing the grievances of the DPs. These committees are taken on-board by the project staff in addressing the grievances of the DPs at village level.

### 3.4 Social Safeguards Management Consultant (SSMC)

31. In order to effectively implement the LARP and address the social safeguard issues, NHA employed SSMC in April 8, 2015. SSMC is staffed by Resettlement Specialist, Grievance Redress Specialist, Gender Specialist and Social Mobilizers and is assisting NHA/ PIU in the LARP implementation and monitoring and capacity building in LAR.

<sup>6</sup>Each village already has been assigned 2 social mobilizers to maintain regular contact with the DPs/ DPCs being the first line of contact on issues related to Land Acquisition Resettlement matters.

<sup>7</sup>Office letter No. LAC.E-35/NHA/Atd/12/1358, dated 25<sup>th</sup> April, 2012.

32. Since its mobilization, the SSMC team deputed for E-35 project is assisting the LARU and PIU in LARP implementation process as per TORs. The specific LAR activities performed up-till January 31, 2016 is given as under.

- Updating of LARP data base and implementation progress data;
- Community consultation and information dissemination meetings for LARP disclosure and to provide guidance to the DPs for submission of claims;
- Assistance of DPs and LARU in processing of compensation claims and delivery of compensation;
- Developments of templates for grievances recording and maintaining grievance registers and operationalizing the GRM with all key members.
- Assistance of PIU in monitoring of LARP implementation progress and preparation of LARP monitoring reports.

### **3.5 Process for Disbursement of Compensation**

33. The disbursement of compensation to the DPs is in progress for Package III of E-35. The amount is disbursed to the DPs by the LAC. No other Project functionary participates in the payment process. The progress of payment by the LAC is reported to the higher offices of NHA and Revenue Department in the form of monthly report. The following disbursement arrangements are in place at the Project Office.

- A team comprising LAC, Quanoogo and 02 Patwaris is carrying out the compensation disbursement task. As a first step, as per requirements of the LAA, announcements are made in the relevant village/ area before one day of the scheduled visit of the disbursement team. People are asked to come to a specified place (generally prominent place in the village) along with their CNICs and land ownership documents to receive their compensation.
- On the specified date, the LAC with his staff holds a meeting. The Patwari identifies the DP as per his CNIC and fard-e-malkiat issued by revenue office and takes his signatures on the acquaintance roll and affixes his thumb impression, which is mandatory.
- After this activity, the voucher is prepared by Quanoogo. The voucher includes the details about affected land with land types and the compensation costs as per acquaintance roll. DP signs the voucher. The thumb impression of the DP and his CNIC number on the voucher is mandatory. Two witnesses also sign the voucher with their CNIC number. Then LAC signs the voucher. The voucher is handed over to the DP and a copy is kept in the record.
- The DP brings this voucher to the District Account Office. This office after confirming the identity of the voucher bearer with two witnesses, issues a cross cheque to the DP/ AP of his amount payable from National Bank of Pakistan, Haripur/ Attock.
- The DP deposits this cheque in his account in a bank and the amount is transferred to his account its generally 15 days process.
- The vouchers for trees and assets are issued separately by the LAC.

### **3.6 Receipt of Payment U/S 18 of LAA 1894**

34. The LAA provides that if a person, in spite of proceedings under sections 8 5a, 9 and 10 is not satisfied with the Award in any way, he is allowed to go the court of law for

---

<sup>8</sup>LAA 1894: i) Section 5a covering the need for enquiry of the concerns or grievances of the affected people related to land prices, ii) Section 9: The LAC gives notice to all APs that the Government intends to take possession of the land and if they have any claims for compensation then these claims are to be made to him at an appointed time and iii) Section 10: Delegates power to the LAC to record statements of the APs in the area of land to be acquired or any part thereof as co-proprietor, sub-proprietor, mortgage, and tenant or otherwise.



the rectification of his grievances. For this purpose, he is required to receive the Award amount under protest. He records his protest on the acquittance roll at the time preparation of payment voucher. According to information from the LAC, about 6 land owners have gone to the court of law u/s<sup>9</sup> 18. The LAC facilitates the DPs by providing them the documents related to their compensation amounts and calculation of average year (owsat yaksala) for different categories of land.

---

<sup>9</sup>LAA 1894: Section 18: The award of compensation for the owners for acquired land is determined at its market value plus 15% premium in view of the compulsory nature of the acquisition for public purposes.

### 3.7 Achevid Progress Shown Linear Plan

35. As per ADB SPS 2009 and LAR conditions of the project. 100% payments are to be completed before start up of construction work in the acquired right of way (ROW). The land for ROW has been fully acquired but the process of payments of the DPs is still going on although 84.4% payment has already been made to 54.9% DPs. Remaining payments are slow or stuck due to LAA's procedural requirements of compensation disbursement and other factors not in control of NHA. These factors are meager amount of compensation which cannot be disbursed to DPs who do not have bank accounts and CNICs and those DPs who are contesting the land award or awarded prices in the court or those who have issues of land ownership/ inheritance.

36. In view of the above issues impeding the compensation disbursement. NHA prepared a linear map of the package-III road in which NHA illustrated the sections or different stretches of the road where 100% payments have been completed and some small sections where payments are yet to be made or are in the process of making. Based on the linear map, as cleared by ADB, NHA is undertaking construction in only those sections where 100% payments have been completed. This is further illustrated in the linear map as Annex-A. Construction the remaining sections/ areas will be undertaken after completing 100% payments. Verification by external monitor and approval by ADB.

37. So far 100% payments have been achieved in an area of 15.415 Kms (of the total length of 19.04 Kms). The EMA has verified the payments and the report has been cleared by ADB, based on which NHA is undertaking the construction work. The remaining area of 3.625 Km is put on hold and will continue to be on hold unless all payments are completed by 100% and are verified by EMA. The EMA report and linear map will be provided to ADB for approval after all payments are completed in the remaining section of 3.625 Km.

#### 4 CONCLUSIONS

38. As mentioned earlier, the land for the project has already been acquired under the LAA in the 15 villages of Package-III. The disbursement of compensation for land and land based assets, acceptable under the LAA is in progress.

39. Significant progress has been achieved in the process of payment of land and land based asserts compensation. The final LARP has been approved, hopefully payment of allowances as per ADB Policy will be completed in due course of time, as per provisions of the LARP. The procurement of Social Safeguards and Management Consultant (SSMC) is also a critical action to ensure the effective implementation of LARP.

40. On the whole, total amount of compensation of land, non land based and crops (Rs. 407.25 million) was to be paid to 6,632 DPs<sup>10</sup>, out of which, an amount of Rs. 343.76 million has been paid to 3,639 DPs on account of payment for the loss of land, structures, community structures and crops. Balance amount of Rs.63.49 million is yet to be paid to 2,993 DPs, which is under process. The break-up of leftover payments is as under:


- (i) Payment of land Rs. 51.06 million to 2,993 DPs on account of compensation for the loss of land.
- (ii) Payment of 2 DPs on account of compensation for the loss of permanent structures.
- (iii) Payment of Rs. 2.26 million on account of compensation for the loss of trees.
- (iv) Payment of Rs. 3.15 million on account of compensation for the loss of crops.
- (v) Payment of 51 DPs on account of compensation for the allowances (rehabilitation/ livelihood restoration).

---

<sup>10</sup>The number of DPs payable is 6632, while the LARP reported 5184 landowners, the difference of 1448 DPs is due to Inheritance cases and shamlat (village's common land cases).

# **ANNEXES**

### Annex A: Updated Linear Plan - Section-wise status of Payment of Compensation in Package III

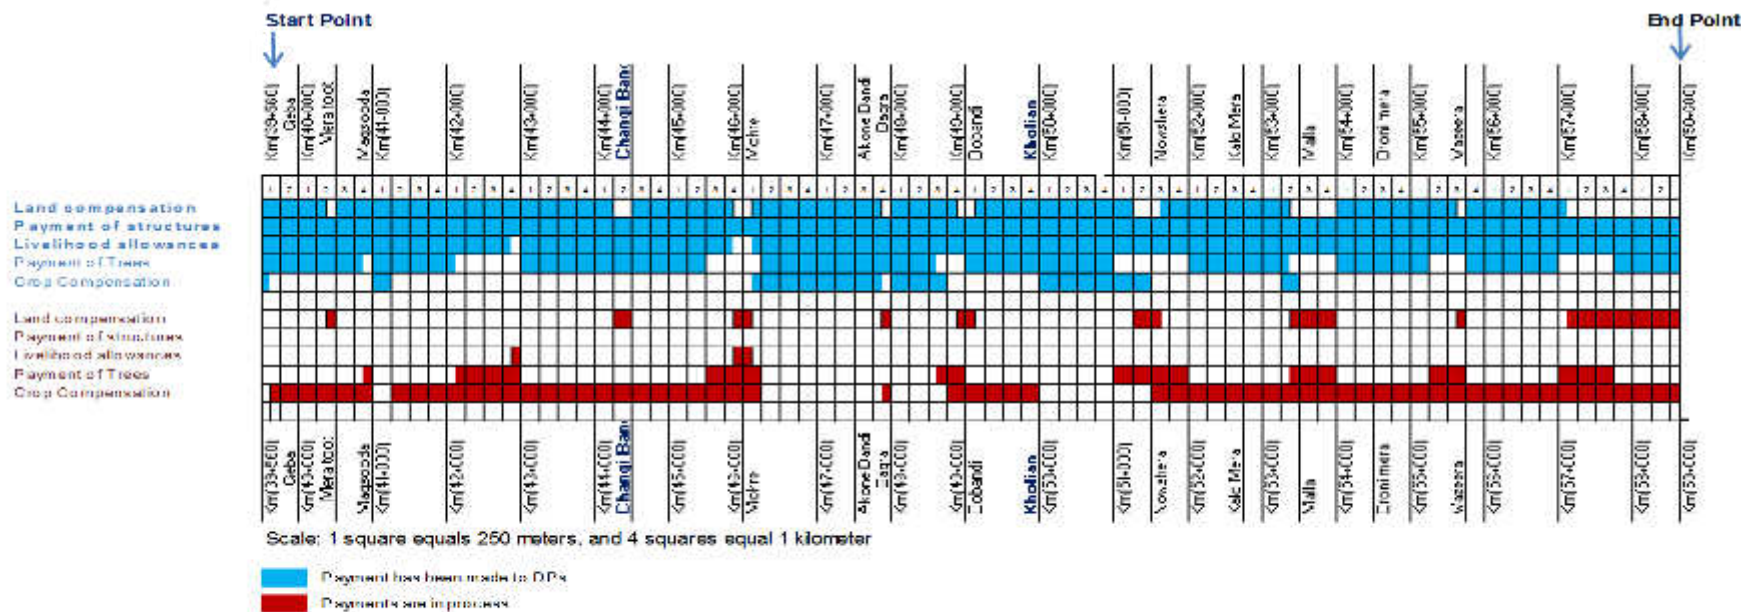

Status of Payment of Package-III

Sr. No.	Part A: All types of compensation fully paid				Part B: Payments on-going				Remarks
	Affected Villages	Chainage-wise subsections/reaches		Length (KM)	Affected Villages	Chainage-wise subsection/reaches		Length (KM)	
		From	To			From	To		
1	Geba	39.560	40.000	0.440	Geba				Total length of package III is 12.04 km. All types of payment payable to the DP/asset/LARP have been fully completed in different subsections taking about 17.710 km. The construction activities will be strictly limited to the specified reaches as identified in the part A of this table. In all other subsections/reaches awarded in the part B of this table (totaling about 3.405 km) will remain on hold until these payments are fully made and are validated by the external monitor. Payments in these subsections are slow due to the laxness of land clearing, delays in implementation and compensation procurement cases. Amount payable will be known after the received documents make the application. Other works awaiting the payments are merger amount of compensation on ongoing opening up of bank account by DP and some DP not available at their project sites.
2	Mera Toot	40.000	40.375	0.375	Mera Toot	40.375	40.500	0.125	
3	Maqsooda	40.500	41.000	0.500	Maqsooda	-	-	-	
4	Changi Bandi	41.000	44.350	3.350	Changi Bandi	40.250	40.500	0.250	
5	Mohree	44.500	45.875	1.375	Mohree	45.875	46.000	0.125	
6	Akhone Bandi	46.075	47.500	1.425	Akhone Bandi	46.000	46.075	0.075	
7	Bagra	47.500	47.875	0.375	Bagra	47.875	48.000	0.125	
8	Dobandi	48.000	48.875	0.875	Dobandi	48.875	49.000	0.125	
9	Kholian	49.125	50.000	0.875	Kholian	49.000	49.125	0.125	
10	Nowshera	50.000	51.250	1.250	Nowshera	51.675	51.750	0.075	
11	Kalu Mera	51.675	52.750	1.075	Kalu Mera	51.500	51.750	0.250	
12	Malla	52.750	53.375	0.625	Malla	53.375	53.500	0.125	
13	Dorani Mera	54.000	54.500	0.500	Dorani Mera	53.500	54.000	0.500	
14	Wazehra	54.500	55.625	1.125	Wazehra	55.625	55.750	0.125	
15	Langra	55.750	57.000	1.250	Langra	57.000	58.600	1.600	
			Total	15.415		Total	3.625		

### Annex 1: Village-wise summary of Awarded Land

Sr. No	Name of Mouza	Affected Land (Kanal)	Total DP (Nos.)	Paid DPs (Nos.)	Total Amount (Rs)	Amount Disbursed (Rs)	Balance amount (Rs)
1	Nowshehra	206.3	665	95	977,437	667,031	310,406
2	Mallah	78	232	74	5,911,845	4,365,704	1,546,141
3	Kalu Maira	154.15	583	359	8,052,544	6,649,056	1,403,488
4	Droni Maira	112.2	272	30	4,087,679	2,379,139	1,708,540
5	Maqsooda	5.9	3	3	6,067,285	6,067,285	-
6	Dobandi	163	203	141	12,019,309	10,472,874	1,546,435
7	Akhon Bandi	197.95	452	228	34,723,974	32,794,369	1,929,605
8	Mairatoot	14.9	167	129	4,962,962	3,198,328	1,764,634
9	Mohri	186.6	1388	880	176,366,541	164,795,368	11,571,173
10	Changi Bandi	363.75	1270	911	32,739,947	28,816,870	3,923,077
11	Bagra	32.25	54	48	17,394,745	15,750,095	1,644,650
12	Gheba	78.35	231	162	5,800,431	5,439,647	360,784
13	Wazeera	143	179	123	5,304,427	4,677,570	626,857
14	Kholiyan Bala	124.5	277	141	3,701,367	3,085,133	616,234
15	Langra	205.9	656	315	41,152,283	19,041,531	22,110,752
<b>Total</b>		2066.75	<b>6,632</b>	<b>3,639</b>	<b>359,262,776</b>	<b>308,200,000</b>	<b>51,062,776</b>

### Annex 2: Village -wise Status of Payment for Affected Fruit & Non-Fruit Trees

Sr. No.	Name of Mouza	Payment for Affected Fruit & Non-Fruit Trees			
		Total DP (Nos.)	Paid DP (Nos.)	Un-Paid DPs	Balance amount
				(Nos.)	(Rs)
1	Nowshehra	15	12	3	70
2	Mallah	24	12	12	70,315
3	Kalu Maira	48	40	8	183,235
4	Droni Maira	17	9	8	51,732
5	Maqsooda	3	2	1	61,352
6	Dobandi	28	16	12	80,273
7	Akhon Bandi	115	93	28	413,603
8	Mairatoot	11	10	1	3,701
9	Mohri	96	76	28	648,958
10	Changi Bandi	204	135	69	496,504
11	Bagra	5	4	1	5,000
12	Gheba	-	-	-	-
13	Wazeera	40	22	18	77,288
14	Kholiyan Bala	-	-	-	-
15	Langra	29	28	1	167,969
<b>Total</b>		<b>635</b>	<b>459</b>	<b>190</b>	<b>2,260,000</b>
					20.50%

**Annex-3: Payment for Crops**

Sr. No.	Village	Paid DPs (No.)	Total Amount (Rs.)	Amount paid (Rs.)	Balance Amount (Rs.)
1	Nowshehra	-	-	-	-
2	Mallah	23	222,425	139,065	90,360
3	Kalu Maira	18	232,366	33,706	198,660
4	Droni Maira	16	208,634	57,784	150,850
5	Maqsooda	-	19,425	-	19,425
6	Dobandi	16	166,657	106,725	59,932
7	Akhon Bandi	28	603,100	119,417	486,683
8	Mairatoot	10	54,760	10,777	43,983
9	Mohri	34	542,219	304,834	237,385
10	Changi Bandi	7	1,012,174	47,373	964,801
11	Bagra	27	467,106	267,106	200,000
12	Gheba	6	252,525	86,521	166,004
13	Wazeera	25	221,445	119,416	102,029
14	Kholiyan Bala	-	19,980	-	19,980
15	Langra	8	458,850	38,317	420,533
<b>Total</b>		<b>218</b>	<b>4,481,666</b>	<b>1,331,041</b>	<b>3,160,625</b>

**Annex-4: Village -wise Status of Payment of Allowances**

Sr. No.	Village	Total No of DPs	No of DPs PAID	% of DPs PAID	Remaing DPs	Total Amount (Rs)	Amount Disbursed (Rs.)
1	Nowshehra	10	10	100	-	437,169	437,169
2	Mallah	15	15	100	-	667,947	667,947
3	Kalu Maira	39	39	100	-	3,138,093	3,138,093
4	Droni Maira	11	11	100	-	605,097	605,097
6	Maqsooda	7	7	100	-	321,780	321,780
5	Dobandi	-	-	-	-	-	-
7	Akhon Bandi	23	-	0.00	23	884,649	0
8	Mairatoot	5	5	100	-	192,315	192,315
9	Mohri	29	1	34.5	28	1,206,429	129,465
10	Changi Bandi	18	18	100	-	692,334	692,334
11	Bagra	-	-	-	-	-	-
12	Gheba	2	2	100	-	76,926	76,926
13	Wazeera	13	13	100	-	500,019	500,019
14	Kholiyan Bala	10	10	100	-	384,630	384,630
15	Langra	26	26	100	-	961,575	961,575
	<b>Total</b>	<b>208</b>	<b>157</b>	<b>75.48</b>	<b>51</b>	<b>10,068,963</b>	<b>8,107,350</b>

**Annex5: Deposit of Fund in Treasury**  
District Treasury Haripur and Abbottabad



National Highway Authority  
Land Acquisition Collector (E-35)  
House No. 79, Street No. 11, Jinnahabad  
**Abbottabad**

No: R ( ) / LAC / (E-35) / NHA / Atd / 15 / 2230-35

Abbottabad, 13<sup>th</sup> July, 2015

To  
District Accounts officers  
**Abbottabad**

District Accounts officers  
**Haripur**

Subject: VERIFICATION OF ADVANCES FOR PROJECT E-35

With reference to the subject noted above and to state that the detail of status of land acquisition advances of E-35 laying in the Govt treasury is required to be reconciled and verified by the District Account Officer/ treasury.

It is therefore requested to provide this office the detail reconciled statement of amount deposited under Account G-11215 and dispersed so far, so the same may be sent to NHA HQ Islamabad please.

  
Land Acquisition Collector (E-35)  
NHA, Abbottabad

C.C:


- GM (E-35) NHA, Burhan
- ✓ • PD (E-35) NHA Abbottabad
- Director (LM&IS) NHA HQ, Islamabad
- DD (LM&IS) E-35 NHA, Abbottabad

  
Land Acquisition Collector (E-35)  
NHA, Abbottabad



DETAIL OF AMOUNT RECEIVED FOR LAND ACQUISITION OF EXPRESSWAY (E-35)(UPDATED 23-07-2015)

S.NO	Cheque No.	Date and From	Amount (IN PKR)	District Treasury	Date of Clearance and Submission in Treasury including Voucher No.	Verification by District Accounts Officer/ Treasury Incharge Concerned
1	(1)No 705993 (2)No 5567078	(1)2-6-2010 (2)3-7-2013 From Director Accounts NHA Islamabad	(1)Rs 70000000.00 (Seven Hundred Million Rupees Only) And (2)Rs339911843.00	Abbottabad	(1)Submitted in District Treasury Abbottabad Vide Voucher No.44 in the Revenue Head Account G-11215 on 8-6-2010. (2) Submitted in District Treasury Abbottabad cheque No 5567078 Dated 03-07-2013/ Challan No/24, Rs 420 Million, have been transferred to District Treasury Haripur Vide Challan No 02 in the Revenue Head Account G-11215 on 24-12-2011. Rs 225 Million, have been transferred to District Treasury Haripur Vide Cheque No2241350 Dated 14-09-2012. Rs 289911843 have been transferred to District Treasury Haripur Vide challan No 07 Dated 09-06-2014.	


  
 Land Acquisition Control  
 Hassanabad - Division  
 Manchara Expressway (E-35)  
 NHA ABBOTTABAD

	No 3307105	4-06-2014 From Abbottabad Treasury to Haripur Treasury	Rs. 289911843 (Twenty Eight Crore, Ninety Nine Lac, Eleven Thousand Eight Hundred Forty Three Rupees Only)	Haripur	Submitted in the District Treasury Haripur Vide Cheque No. 3307105 Dated 04-06-2014 Chaffan No. 07 Dated 04-06- 2014
9	No 20605257	12-05-2014 Director Accounts NHA Islamabad	Rs. 35830341 (Three crore, Fifty Nine Lac, Thirty Thousand, Three Hundred and Forty One Rupees Only)	Haripur	Submitted in the District Treasury Haripur Vide Cheque No. 20605257 Dated 02-05-2014 Chaffan No. 3 Dated 2-5- 2014 In Revenue Head Account G-112 I.F.

1. BALANCE IN HARIPUR TREASURY (Rd) = *nil*

2. BALANCE IN ABBOTTABAD TREASURY (Rd) = *50,000,000/-*

3. BALANCE IN ABBOTTABAD TREASURY (Lapsed) = *nil*


  
LAND ACQUISITION COLLECTOR (E-35)  
NHA ABBOTTABAD

  
ACCOUNTANT  
NHA ABBOTTABAD

TAIL OF AMOUNT RECEIVED FOR LAND ACQUISITION OF EXPRESSWAY (E-35)(UPDATED 13-07-2015)

S.NO	Cheque No.	Date and From	Amount (IN PKR)	District Treasury	Date of Clearance and Submission in Treasury including Voucher No.	Verification by District Accounts Officer/ Treasury Incharge Concerned
1	No 705993	2-6-2010 From Director Accounts NHA Islamabad	(1)Rs 70000000.00 (Seven Hundred Million Rupees Only)	Abbottabad	(1)Submitted in District Treasury Abbottabad Vide Voucher No.44 in the Revenue Head Account G-11215 on 8-6-2010. (2) Submitted in District Treasury Abbottabad cheque No 5567078 Dated 03-07-2013 Challan No 24. Rs 420 Million, have been transferred to District Treasury Haripur Vide Challan No 02 in the Revenue Head Account G-11215 on 24-12-2011. Rs 225 Million, have been transferred to District Treasury Haripur Vide Cheque No2241350 Dated 14-09-2012. Lapsed Amount (32709638) Dated 30-06-2013.	
<p><i>Total Lapsed Amount = 32709638</i></p> <p><i>Total expenditure = 2783986 upto 30-6-15</i></p> <p><i>Balance = 5525652/- as on 30/6/15</i></p> <p><i>Balance 5525652/- upto 30/6/15</i></p> <p><i>Balance 5525652/- upto 30/6/15</i></p>						

BALANCE IN ABBOTTABAD TREASURY (Lapsed)

  
LAND ACQUISITION COLLECTOR (E-35)  
NHA ABBOTTABAD

DETAIL OF AMOUNT RECEIVED FOR LAND ACQUISITION OF EXPRESSWAY (E-35)(UPDATED 19-08-2015)

S.NO	Cheque No.	Date and From	Amount (IN PKR)	District Treasury	Date of Clearance and Submission in Treasury including Voucher No.	Verification by District Accounts Officer/ Treasury Incharge Concerned
1	(1) No 705993 (2) No 5567078	(1) 2-6-2010 (2) 3-7-2013 From Director Accounts NHA Islamabad	(1) Rs 700000000.00 (Seven Hundred Million Rupees Only) & 2(Rs) 339911843	Abbottabad	(1) Submitted in District Treasury Abbottabad Vide Voucher No 44 in the Revenue Head Account G-11215 on 8-6-2010. (2) Submitted in District Treasury Abbottabad cheque No 5567078 Dated 03-07-2013 Challan No 24 Rs 420 Million, have been transferred to District Treasury Haripur Vide Challan No 02 in the Revenue Head Account G-11215 on 24-12-2011. Rs 225 Million, have been transferred to District Treasury Haripur Vide Cheque No 2241250 Dated 14-09-2012 Rs 189911843 have been transferred to District Treasury Haripur Vide challan No 07 Dated 09-06-2014	

  
 Land Acquisition Collector  
 Hassanabad - Haychan  
 Jinnah Expressway (E-35)  
 NHA ABBOTTABAD

	No 2240289	15-12-2011 From Abbottabad Treasury to Haripur Treasury	Rs.420000000.00 (Four Hundred and Twenty Million Rupees Only)	Haripur	Submitted in District Treasury Haripur Vide Voucher No 3 Account office Cheque No 2240289 Dated 15-12-2011 in Revenue Head G-11215
3	No 823573	14-06-2011 From Director Accounts, NHA, Islamabad	Rs.350000000.00 (Three Hundred And Fifty Million Rupees Only)	Haripur	Submitted in District Treasury Haripur Vide Voucher No 4 in Revenue Head Account G-11215 On 18-06-2011
4	No 09788600	15-12-2011 From NHA Project Account	Rs.184000000.00 (One Hundred and Eighty Four Million Rupees Only)	Haripur	Submitted in District Treasury Haripur Vide Voucher No 02 In Revenue Head Account G-11215
5	No 3002597	11-01-2012 From NHA Project Account	Rs. 41024440 (Four Crore, Ten Lac, Twenty Four Thousand, Four Hundred And Forty Rupees Only	Haripur	Submitted in District Treasury Haripur Vide Voucher No 01 In Revenue Head Account G-11215 on 03-04-2012
6	No 06849378	09-03-2012 From NHA	Rs.100000000.00 (One Hundred Million Rupees Only)	Haripur	Submitted in District Treasury Haripur Vide Voucher No 01 in Revenue Head Account G-11215
7	No 2241350	14-09-2012 From Abbottabad Treasury to Haripur Treasury	Rs.225000000.00 (Two Hundred and Twenty Five Million Rupees Only)	Haripur	Submitted in the District Treasury Haripur Vide Voucher No 04 in Revenue Head Account G-11215

  
 Mr. Acquisition Officer,  
 Hassanabad - District  
 Manshera Expressway (G-334)  
 NHA ABBOTTABAD

8	No 3307105	4-06-014 From Abbottabad Treasury to Haripur Treasury	Rs.289911843 (Twenty Eight Crore, Ninety Nine Lac, Eleven Thousand Eight Hundred Forty Three Rupees Only)	Haripur	Submitted in the District Treasury Haripur Vide Cheque No 3307105 Dated 04-06-2014 Challan No 07 Dated 09- 06-2014
9	No 20605257	12-05-2014 Director Accounts NHA Islamabad	Rs 35930341 (Three crore, Fifty Nine Lac, Thirty Thousand, Three Hundred and Forty One Rupees Only)	Haripur	Submitted in the District Treasury Haripur Vide Cheque No 20605257 Dated 02-05-2014 Challan No 3 Dated 2-6- 2014 In Revenue Head Account G-11215.

1. BALANCE IN HARIPUR TREASURY (Rd) = 153953730/= wdf. 19-08-2015 Haripur.

*Handwritten signature and date*  
19/8/15  
District Treasury Haripur

*Handwritten signature*  
LAND ACQUISITION COLLECTOR (E-35)  
NHA ABBOTTABAD

## Annex 6: List of Consultations with DPCs/ DPs

### A) Consultations matrix with Male DPCs/ DPs

1	November 09, 2015	Changi Bandi	09	<ul style="list-style-type: none"> <li>- Haji Ghulam Sarwer s/o Haji Shah Zaman</li> <li>- Mr Muhabat Khan</li> <li>- Mr Haji Latif</li> <li>- Mr Muhammad Rafiq Sr, Server (ZKB)</li> <li>- Mr Zaffar Assist Server</li> <li>- Mr Wajahat Assistant Server</li> <li>- Mr Gazafar</li> <li>- Mr Abu al Hussan</li> <li>- Mr Tasawer Zia Server</li> </ul>
2	November 12, 2015	Changi Bandi	14	<ul style="list-style-type: none"> <li>- Mr Abdul Akeem (DPC)</li> <li>- Mr Zahid Hussain</li> <li>- Mr Khan Afsar</li> <li>- Mr Muhammad Safdar</li> <li>- Mr Gulzar</li> <li>- Mr Abdul Ghafoor</li> <li>- Mr Ghulam Hassan</li> <li>- Mr Muhammad Irshad</li> <li>- Mr Arshad</li> <li>- Mr Javed Iqbal</li> <li>- Mr Ahmed</li> <li>- Mr Rab Nawaz</li> <li>- Mr Muhammad Sadiq</li> <li>- Mr Muhammad Sarwer</li> </ul>
3	December 09, 2015	Changi Bandi	12	<ul style="list-style-type: none"> <li>- Mr Latif s/o Hayat Muhammad(DPC)</li> <li>- Mr Adil Hayat s/o Abdul Rashid</li> <li>- Mr Haji Gulam Sarwer</li> <li>- Mr Abdul Hakeem Tanoli s/o Mr Muhammad Hussain Tanoli (DPC)</li> <li>- Mr Muhammad Arshad</li> <li>- Mr Muhammad Suleman</li> <li>- Mr Roshan din</li> <li>- Mr Goher Sultan</li> <li>- Mr Muhammad Ashraf</li> <li>- Mr Muhammad Sadiq</li> <li>- Mr Abdul Qayum</li> <li>- Mr Muhammad Rafiq</li> </ul>
4	December 09, 2015	Mohri	01	<ul style="list-style-type: none"> <li>- Muslim din Anwer s/o Muhammad Din(DPC)</li> </ul>
5	December 09, 2015	Changi Bandi	27	<ul style="list-style-type: none"> <li>- Mr Coi (R) Mussadiq Hussain Awan PC</li> <li>- Mr Muhammad Akram DD(LM&amp;IS)</li> <li>- Mr Raffaqat Ali DD(Cons)</li> <li>- Mr FatehUllah AD(Con)</li> <li>- Mr Farooq Shah ARE (St Con)</li> <li>- Mr Noman ARE (Highway Con)</li> <li>- Mr Mai( R) Saleem Khattak PM(ZKB)</li> <li>- Mr Anwar Fazal Ahmad Rs(SSMC)</li> <li>- Mr Muhammad Arif SM(SSMC)</li> <li>- Mr Rehan Khattak SM(SSMC)</li> <li>- Mr Jalil Shah (Cef Server Con)</li> <li>- Mr Farath Abbas (Said Eng)</li> <li>- Mr Amir Ali (Server)</li> <li>- Mr Raza (Girdawer)</li> <li>- Mr Gulfam (Patwari)</li> <li>- Mr Latie s/o Hayat Muhammad (Complainant)</li> <li>- Mr Adil Hayat s/o Abdul Rasheed</li> <li>- Mr Haji Ghulam Sarwer</li> <li>- Mr Abdul Hakeem</li> <li>- Mr Muhammad Arshad</li> </ul>

				<ul style="list-style-type: none"> <li>- Mr Muhammad Suleman</li> <li>- Mr Roshan din</li> <li>- Mr Gohar Sultan</li> <li>- Mr Muhammad Ashraf</li> <li>- Mr Muhammad Sadiq</li> <li>- Mr Abdul Qayum</li> <li>- Mr Rafiq</li> </ul>
6	December 10, 2015	Kalo Mira	08	<ul style="list-style-type: none"> <li>- Mr Rawaiz Khan</li> <li>- Mr Sarwar khan</li> <li>- Mr Nazo khan</li> <li>- Mr Ajab khan</li> <li>- Mr Sher Afzal</li> <li>- Mr Faqer khan</li> <li>- Mr Adalat khan</li> <li>- Mr Azram khan</li> </ul>
7	December 10, 2015	Nowshera	05	<ul style="list-style-type: none"> <li>- Mr Aksar khan s/o Muhammad Afsar</li> <li>- Mr Abdul Qayum khan s/o Rehan khan</li> <li>- Mr Javeid iqbal s/o Ajab khan</li> <li>- Mr Waseem Jaeid s/o Javeid Iqbal</li> <li>- Mr Gulestan khan s/o Muhammad Afser</li> </ul>
8	February 25,02, 2016	Mohri	08	<ul style="list-style-type: none"> <li>- Mr. Zia Ur-Rahman s/o Nisar Muhammad</li> <li>- Mr.Gulfriz S/o Gul Zaman</li> <li>- Mr.Sarfaz s/o Gulzaman</li> <li>- Mr. Muhammad Nadeem s/o Muhammad</li> <li>- Mr.Mumtaz Ali s/o Muhammad</li> <li>- Mr. Banaras Khan s/o Muhammad Ismael</li> <li>- Mr. Gull Khan s/o Haji Sher Muhammad</li> <li>- Mr. Muhammad Safdar s/o Muhammad Qasim</li> </ul>

#### Consultations matrix with Female DPCs/ DPs

1	November 12, 2015	Changi Bandi	12	<ul style="list-style-type: none"> <li>- Ms Bibi Jan w/o Gul Ahmed</li> <li>- Ms Gulzar Jan D/o Meer Afzal</li> <li>- Ms Rashida Bibi w/o Muhammad Shafeeq</li> <li>- Ms Maria Kausar D/o Haji Ghulam Haider</li> <li>- Ms Tahina Gul D/o o Haji Ghulam Haider</li> <li>- Ms Parveen Akhter D/o Ghulam Nabi</li> <li>- Ms Shereena Jan D/o Ghulam Nabi</li> <li>- Ms Khurshida Bibi wd/o Javed</li> <li>- Ms Mobarak Jan w/o Jumah Khan</li> <li>- Ms Ajhib Sultan w/o Muhammad Yousaf</li> <li>- Ms Nazeera Bibi D/o Gul Ahmed</li> <li>- Ms Shaeen Bibi D/o Gul Ahmed</li> </ul>
2	December 09, 2015	Mohri	13	<ul style="list-style-type: none"> <li>- Ms Ambreen Bibi</li> <li>- Ms Shahnaz Bibi</li> <li>- Ms Perveen Jan</li> <li>- Ms Zaveen Jan</li> <li>- Ms Rani Bibi</li> <li>- Ms Ghulam Fatima w/o Muhammad Ellahi</li> <li>- Ms Seva Bibi</li> <li>- Ms Perveen Akhter w/o Muhammad Dilber</li> <li>- Ms Sakeena Jan w/o Lal Muhammad</li> <li>- Ms Maryam Bibi</li> <li>- Ms Nazima Shaheen w/o Phalzeb</li> <li>- Ms Mehboob Akhter w/o Abdul Jalil</li> <li>- Ms Tahira Bibi w/o Imran</li> </ul>
3	December 09, 2015	Changi Bandi	08	<ul style="list-style-type: none"> <li>- Ms Perveen Akhter</li> <li>- Ms Asna Jan w/o Muhammad Yousaf</li> <li>- Ms Shameem Bibi D/o Muhammad Hussain</li> <li>- Ms Robina w/o Gulam Sarwer</li> <li>- Ms Rabia w/o Abdul Hakeem</li> <li>- Ms Khursheeda w/o Muhammad Javed</li> <li>- Ms Naseem Akhter w/o Ghulam Haider</li> <li>- Ms Shereena Bibi w/o Goher Rehman</li> </ul>



4	December 10, 2015	Kalo Mera	09	<ul style="list-style-type: none"> <li>- Ms Safeena Bibi w/o Qayum khan</li> <li>- Ms Farm Jan w/o Mehtab khan</li> <li>- Ms Sobia Bibi w/o Muneer khan</li> <li>- Ms Mumtaz Bibi w/o Pervez</li> <li>- Ms Sughran w/o Ravaiz khan</li> <li>- Ms Sohrish w/o Fared khan</li> <li>- Ms Khateena Bibi w/o Ghulam Saleem khan</li> <li>- Ms Aysa Bibi w/o Jabbar khan</li> <li>- Ms Faveedan w/o Muneer khan</li> </ul>
5	December 10, 2015	Nowshera	12	<ul style="list-style-type: none"> <li>- Ms Zardan Jan w/o Dedo khan</li> <li>- Ms Rasheeda Begum w/o Liyqat khan</li> <li>- Ms Khako Jan w/o Mir dad</li> <li>- Ms Khuban Nisa w/o Mir dad</li> <li>- Ms Mehfaz Begum w/o Sikandar</li> <li>- Ms Hasten Jan w/o Javed Iqbal</li> <li>- Ms Anam khan D/o Fared khan</li> <li>- Ms Safia Bibi w/o Riaz khan</li> <li>- Ms Waheeda Bibi w/o Fared khan</li> <li>- Ms Shunaila w/o Awranzaib</li> <li>- Ms Naheed Bibi w/o Nisar khan</li> <li>- Ms Nugat Bibi w/o Gulistan khan</li> </ul>

Annex 7: Information Banner Displayed in the Village



Annex 8: Advertisement in Local Newspaper



روزنامہ شمال ایف اے آباد۔۔۔ (8)۔۔۔ 2 دسمبر 2014ء

**فٹس برائے متاثرین ایکسپریس وی (E-35)**


حسن ابدال سے ہریپور ایکسپریس اس کے متاثرین کو مطلع کیا جاتا ہے کہ جن لوگوں نے ابھی تک ہارٹوٹس ویٹ کے باوجود اپنے معاوضات وصول نہیں کیے وہ یا تو ایکسپریس وی کے دفتر (House # 79, Street #11, Jinnahabad Abbottabad) سے رابطہ کریں یا اپنے گاڑوں میں ہائی گئی متاثرین ایکسپریس وی کے کیمپ کے نمبر ان سے رجوع کریں تاکہ حقداران کو ان کا باقی ماندہ معاوضہ دیا جائے۔ بہت دور دیکر آپ کا معاوضہ آپ کی طلبی عدالت میں جمع کروایا جائے گا۔

منجانب جنرل منیجر ایکسپریس وی (E-35) پیش ہائی وی اتھارٹی برہان

Annex 9: Information Disclosure Brochure

<p>3-1</p> <p>☆ اطلاع : ۱۰۲</p> <p>☆ بیان : ۱۰۳</p> <p>☆ راجہ کے متعلق : ۱۰۴</p> <p>☆ راجہ کی زندگی : ۱۰۵</p> <p>☆ دیگر : ۱۰۶</p>	<p>1. تہذیب</p> <p>سید اہل حلیوں انکسپریس سے پراچھارت اور ۱۹۳۰ء میں راجہ کی زندگی کے بارے میں ہندی کی زبان میں لکھی گئی تھی۔ اس کا اردو ترجمہ راجہ کی زندگی کے بارے میں ہے۔ اس کی ۱۰۲ اور ۱۰۳ کے صفحات پر بیان کیا گیا ہے۔ اس کی ۱۰۴ اور ۱۰۵ کے صفحات پر بیان کیا گیا ہے۔ اس کی ۱۰۶ کے صفحات پر بیان کیا گیا ہے۔</p>	<p>نیشنل ہائی وے اتھارٹی (این ایچ اے)</p> <p>حکومت پاکستان</p>
<p>3</p> <p>☆ اطلاع : ۱۰۲</p> <p>☆ بیان : ۱۰۳</p> <p>☆ راجہ کے متعلق : ۱۰۴</p> <p>☆ راجہ کی زندگی : ۱۰۵</p> <p>☆ دیگر : ۱۰۶</p>	<p>2. خصوصی تجربات</p> <p>☆ اطلاع : ۱۰۲</p> <p>☆ بیان : ۱۰۳</p> <p>☆ راجہ کے متعلق : ۱۰۴</p> <p>☆ راجہ کی زندگی : ۱۰۵</p> <p>☆ دیگر : ۱۰۶</p>	<p>نیشنل ٹریڈنگ ڈیپو ہائی وے اتھارٹی پر مگرام</p> <p>حسن ابدال - حویلیاں</p> <p>ایکسپریس ویلے پراجیکٹ</p> <p>(ای-35)</p>
<p>4</p> <p>☆ اطلاع : ۱۰۲</p> <p>☆ بیان : ۱۰۳</p> <p>☆ راجہ کے متعلق : ۱۰۴</p> <p>☆ راجہ کی زندگی : ۱۰۵</p> <p>☆ دیگر : ۱۰۶</p>	<p>☆ اطلاع : ۱۰۲</p> <p>☆ بیان : ۱۰۳</p> <p>☆ راجہ کے متعلق : ۱۰۴</p> <p>☆ راجہ کی زندگی : ۱۰۵</p> <p>☆ دیگر : ۱۰۶</p>	<p>حصول راجہ کی یادگار اور ماحولیاتی اثرات بارے</p> <p>معلوماتی کتابچہ</p>

## Annex 10: Constitution of Grievance Redress Committee under PIU

 National Highway Authority  
Deputy Director (LM&IS) E-35  
House No.79, Street No.11, Islamabad  
Abbottabad  
21<sup>st</sup> Sep. 2015


No. 11/ DD (LM&IS) (E-35) NHA/ATD/15

**Subject:** Hassanabdal-Havelian Expressway (E-35)  
Constitution of "Grievance Redress Cell" under PIU LARP

**Reference:** *In continuation of AD (L&S)-III NHA HQ LETTER NO 1(1)-EALS/NHA/2010/HQ/09 dated 05/03/2011 and approval of Member (N-Z) vide para-19-24 of office note No.1(1)PD/HAM/E-35 NHA/Aid/1/819 para 26 to 30.*

Member (North-Zone) has been pleased to accord approval for the constitution of "Grievance Redress Cell" under PIU for LARP on E-35. Accordingly the following Officers/Officials will be responsible for aforementioned cell.

- PD (E-35) NHA
- DD/AD (LM&IS) E-35 NHA
- DD/AD (Const) E-35 NHA
- LAC (E-35) KPK/Punjab, NHA
- Qanoongo/Patwari (E-35) NHA
- Grievances Redress Specialist/Resettlement Specialist
- Social Mobilizer (Male and Female member)

  
Deputy Director (LM&IS)  
(E-35) NHA, Abbottabad

**Distribution:**

- All above concerned officers/officials

**C.C**

- GM (EALS) NHA HQ, Islamabad
- GM (E-35) NHA, Burhan
- Director (L&S) NHA HQ, Islamabad
- PS to Member (North-Zone) NHA, Peshwar
