



Guizhou Tongren Rural Transport Project (P148071)

EAST ASIA AND PACIFIC | China | Transport & ICT Global Practice |
IBRD/IDA | Investment Project Financing | FY 2016 | Seq No: 1 | ARCHIVED on 07-Dec-2015 | ISR21789 |

Implementing Agencies: Tongren World Bank Project Management Office, Tongren Transport Bureau

Key Dates

Key Project Dates

Bank Approval Date:25-Sep-2015

Effectiveness Date:--

Planned Mid Term Review Date:01-Sep-2018

Actual Mid-Term Review Date:--

Original Closing Date:30-Jun-2021

Revised Closing Date:30-Jun-2021

Project Development Objectives

Project Development Objective (from Project Appraisal Document)

The project development objective is to improve rural transport connectivity in Dejiang and Sinan counties.

Has the Project Development Objective been changed since Board Approval of the Project Objective?

No

Components

Name

A. Dejiang Rural Transport:(Cost \$150.02 M)

B. Sinan Rural Transport:(Cost \$80.77 M)

C. Technical Assistance:(Cost \$1.00 M)

Overall Ratings

Name	Previous Rating	Current Rating
Progress towards achievement of PDO	--	● Satisfactory
Overall Implementation Progress (IP)	--	● Satisfactory
Overall Risk Rating	--	● Substantial

Implementation Status and Key Decisions



The Loan Agreement and Project Agreement were signed on October 29, 2015. The terminal date for effectiveness is January 27, 2016.

Risks

Systematic Operations Risk-rating Tool

Risk Category	Rating at Approval	Previous Rating	Current Rating
Political and Governance	--	--	● Low
Macroeconomic	--	--	● Low
Sector Strategies and Policies	--	--	● Moderate
Technical Design of Project or Program	--	--	● Moderate
Institutional Capacity for Implementation and Sustainability	--	--	● Substantial
Fiduciary	--	--	● Substantial
Environment and Social	--	--	● Substantial
Stakeholders	--	--	● Moderate
Other	--	--	--
Overall	--	--	● Substantial

Results

Project Development Objective Indicators

► Direct project beneficiaries (Number, Core)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	--	0.00	262000.00
Date	01-Apr-2015	--	02-Dec-2015	31-Dec-2020



▾ Female beneficiaries (Percentage, Core Supplement)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	--	0.00	48.00

▸ Travel Time Savings on Upgraded / Improved Roads (Percentage, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	--	0.00	30.00
Date	01-Apr-2015	--	02-Dec-2015	31-Dec-2020

Overall Comments

Intermediate Results Indicators

▸ Roads rehabilitated, Rural (Kilometers, Core)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	--	0.00	646.00
Date	01-Apr-2015	--	02-Dec-2015	31-Dec-2020

▸ Number of Bridges Improved / Constructed (Number, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	--	0.00	30.00
Date	01-Apr-2015	--	02-Dec-2015	31-Dec-2020



► Number of Villages with New Road Safety Measures (Number, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	--	0.00	147.00
Date	01-Apr-2015	--	02-Dec-2015	31-Dec-2020

► Number of Trainees who Attended Training and Study Tours (Number, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	--	0.00	300.00
Date	01-Apr-2015	--	02-Dec-2015	31-Dec-2020

► Technical Assistance: Studies and Plans Completed (Text, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	No	--	No	Yes
Date	01-Apr-2015	--	02-Dec-2015	31-Dec-2020

► Direct Project Consultations with Beneficiaries Undertaken (Text, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	Yes	--	Yes	Yes
Date	01-Apr-2015	--	02-Dec-2015	31-Dec-2020

Overall Comments

Data on Financial Performance




Disbursements (by loan)

Project	Loan/Credit/TF	Status	Currency	Original	Revised	Cancelled	Disbursed	Undisbursed	Disbursed
P148071	IBRD-85340	Not Effective	USD	150.00	150.00	0.00	0.00	150.00	0%

Key Dates (by loan)

Project	Loan/Credit/TF	Status	Approval Date	Signing Date	Effectiveness Date	Orig. Closing Date	Rev. Closing Date
P148071	IBRD-85340	Not Effective	25-Sep-2015	29-Oct-2015	--	30-Jun-2021	30-Jun-2021

Cumulative Disbursements

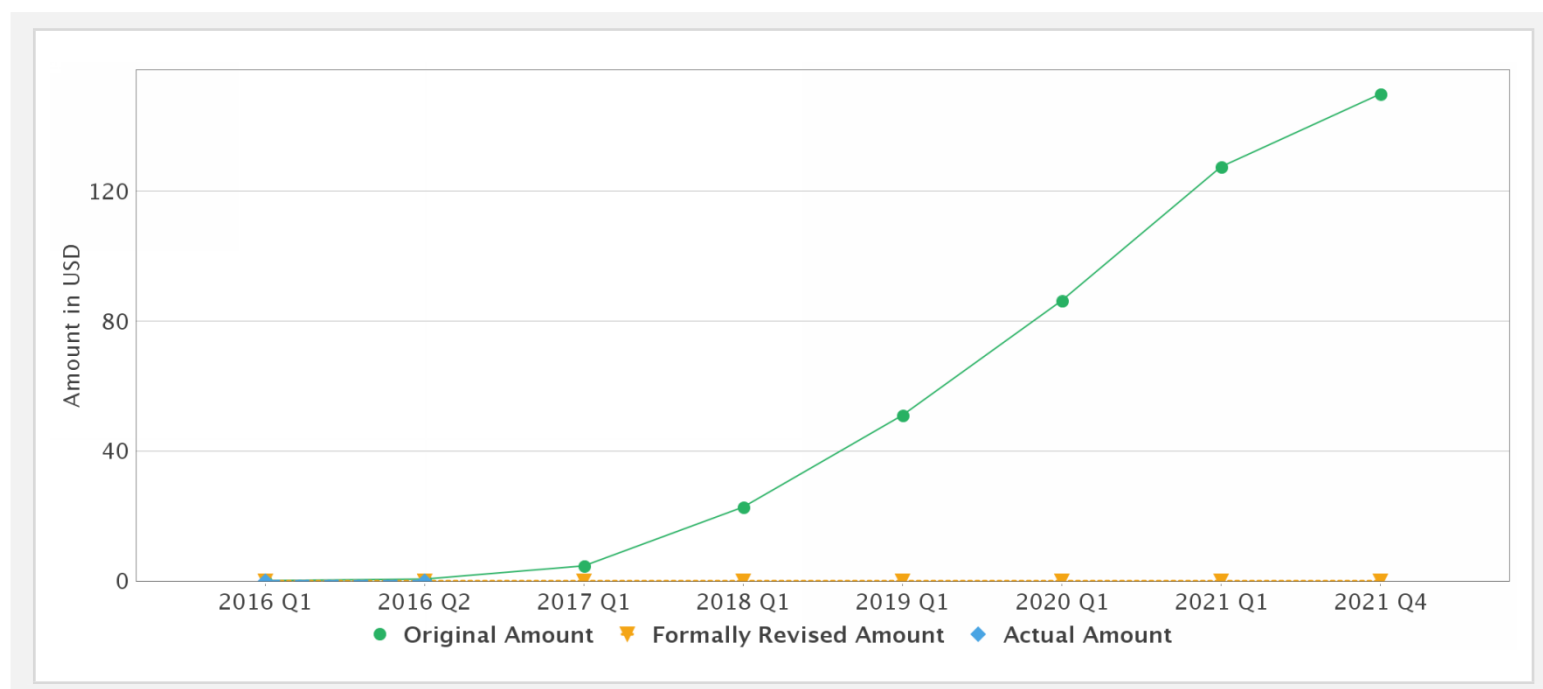

Restructuring History

There has been no restructuring to date.

Related Project(s)

There are no related projects.

