

# Internal Monitoring Report

---

March 2016

## PAK: National Motorway M-4 Gojra–Shorkot Section Project

Prepared by National Highway Authority of Ministry of Communications for the Islamic Republic of Pakistan and the Asian Development Bank.

This external monitoring report is a document of the borrower. The views expressed herein do not necessarily represent those of ADB's Board of Directors, Management, or staff, and may be preliminary in nature.

In preparing any country program or strategy, financing any project, or by making any designation of or reference to a particular territory or geographic area in this document, the Asian Development Bank does not intend to make any judgments as to the legal or other status of any territory or area.



**MINISTRY OF COMMUNICATIONS  
NATIONAL HIGHWAY AUTHORITY**



**PAK: National Motorway M-4 Gojra–Shorkot Section Project**

**Internal Monitoring Report (No.2)**  
for the  
Implementation of Land Acquisition & Resettlement Plan and  
Corrective Action Plan of Section II

Chainage 58+100 – 120+268 (62 km)

(Dec. – Feb 2016)

14<sup>th</sup> March 2016

**Social Safeguard Management Consultant**  
Office of the Project Director, NHA Complex,  
Faisalabad

**MINISTRY OF COMMUNICATIONS  
NATIONAL HIGHWAY AUTHORITY**

PAK: National Motorway M-4 Gojra–Shorkot Section Project

**Internal Monitoring Report (No.2)**  
for the  
Implementation of Land Acquisition & Resettlement Plan and  
Corrective Action Plan of Section II

Chainage 58+100 – 120+268 (62 km)

(Dec. – Feb 2016)

14<sup>th</sup> March 2016

**Social Safeguard Management Consultant**  
Office of the Project Director, NHA Complex,  
Faisalabad

## TABLE OF CONTENTS

<b>TABLE OF CONTENTS .....</b>	<b>i</b>
<b>LIST OF TABLES .....</b>	<b>ii</b>
<b>LIST OF ANNEXES .....</b>	<b>ii</b>
<b>ABBREVIATIONS .....</b>	<b>iii</b>
<b>1. INTRODUCTION .....</b>	<b>1</b>
1.1 Background .....	1
1.2 Objectives of the IMR .....	2
<b>2. LAR IMPLEMENTATION STATUS .....</b>	<b>3</b>
2.1 Project Impact as per LARP .....	3
2.1.1 Number of DHs .....	3
2.1.2 Land Acquisition .....	3
2.1.3 Structures and Farm Assets .....	3
2.1.4 Affected Crops .....	3
2.1.5 Affected Trees .....	4
2.2 LARP implementation as of 1 <sup>st</sup> Monitoring Report (November 2015): .....	4
2.3 LARP Implementation progress achieved till February 2016 .....	4
2.3.1 Payment of Land Compensation .....	5
2.3.2 Payment of Structures .....	5
2.3.3 Payment of Trees .....	5
2.3.4 Payment of Crop Compensation .....	5
2.3.5 Payment of Allowances .....	5
2.4. Achieved Progress Shown in Linear Plan .....	6
3 Reasons for On-going or Pending Payments with Way forward .....	8
3.1 Reasons for On-going or Pending Payments .....	8
3.2 NHA's efforts and actionstaken to Address Pending Payments .....	8
3.3 Efforts Exhausted by NHA with Way Forward. ....	9
4 Institutional Arrangements for LARP Implementation and monitoring. ....	13
4.2 Mobilization of Social Safeguards Management Consultant (SSMC) .....	13
4.3 Grievances Redress Committee at Project .....	14
4.3.1 Grievance Redress Mechanism followed .....	14
4.3.2 Grievances recorded and resolved .....	15
<b>5. CONCLUSIONS &amp; RECOMMENDATIONS .....</b>	<b>16</b>
5.1 Conclusions .....	16
5.2 Recommendations .....	16
<b>Pictorial Presentation .....</b>	<b>18</b>
<b>ANNEXES .....</b>	<b>23</b>

**LIST OF TABLES**

Table2.1: Land Acquisition by District and Number of DHs .....	3
Table 2.2: Summary of Project Impacts other than Land .....	4
Table 2.3: Status of Implementation of LARP .....	7
Table2.4: ReasonsforDelay in Payment of LandCompensation .....	8

**LIST OF ANNEXES**

AnnexA: Linear Plan - Payment of Compensation of M-4 (Section-II) .....	24
Annex1: Village-wise Summary of Awarded Land .....	26
Annex 2: Mouza-wise summary of Payment for Affected Structures .....	27
Annex3: Mouza-wise summary of Payment for Affected Trees.....	28
Annex4: Payment for Crops .....	29
Annex5: Mouza-wise summary of Payment for Allowances .....	31
Annex6: Schedule Visits of LAC M-4 Section-II Toba Tek Singh .....	40
Annex 7: Sample Site Visit Report of LAC M-4 Section-II Toba Tek Singh .....	43
Annex 8: Sample Notices for Payment of Compensation for unpaid DPs.....	46
Annex9: Deposit of Fund in Treasury.....	47
Annex10: List of Consultations with Unpaid DPs.....	49
Annex 11: Leftover DPs and Publication in Local Newspaper .....	54
Annex12: Notification of DPC/ GRC Constituted at village level .....	55

**ABBREVIATIONS**

AD	Assistant Director
ADB	Asian Development Bank
BOR	Board of Revenue
CAP	Corrective Action Plan
DD	Deputy Director
DHs	Displaced Households
DPs	Displaced Persons
GM	General Manager
GOP	Government of Pakistan
GRC	Grievances Redress Cell
IMR	Internal Monitoring Report
LAA	Land Acquisition Act 1894
LAC	Land Acquisition Collector
LARF	Land Acquisition & Resettlement Framework
LARP	Land Acquisition & Resettlement Plan
MFF	Multi-tranche Financing Facility
NHA	National Highway Authority
NTCHIP	National Trade Corridor Highway Investment Program
PIU	Project Implementation Unit
ROW	Right of Way
SPS	Safeguard Policy Statement
SSMC	Social Safeguards Management Consultant

**FAISALABAD – KHANEWAL MOTORWAY PROJECT (M4)**  
 2<sup>nd</sup> Internal Monitoring Report for the Implementation of LARP & CAP of  
 National Motorway M-4 Gojra–Shorkot Section Project  
 (58+100 – 120+268 = 62 km)


## 1. INTRODUCTION

### 1.1 Background

1. With financial assistance by ADB NHA is implementing National Motorway M-4 Gojra-Shorkot Section project. It starts at M-4 chainage 58+100 (end point of M-4 Faisalabad-Gojra Section at Gojra-Jhang road) and after crossing through various rural settlements, ends at chainage 120+268 km (near Shorkot city). The project works include construction of four lane dual carriage way with three (3) interchanges located at Chainage 80+000 km (Toba Tek Singh-Jhang Road), Chainage 94+000 Km (Toba Tek Singh- Waryamwala Road) and 120+000 km (Shorkot Cantt-Shorkot City Road). For award and execution of civil works the project road is divided into two parts i.e. Section A (Km 58+100 to 89+000) and Section B (Km 89+000 to 120+268). The project is located in the jurisdiction of two districts named Toba Tek Singh and Jhang. The location map of the proposed section is given in Figure 1.

2. The entire alignment of the project crosses through green fields and 100 meter ROW for 62 Km long carriageway and 40 meter ROW for interchanges loop carriageways at three locations has been acquired to execute the project civil works. The ROW land was acquired following the provisions of Land Acquisition Act 1984 and ADB's Safeguards Policy Principals as outlined in the SPS 2009. A Land Acquisition and Resettlement Plan including a Corrective Action Plan was prepared to ensure that the land acquisition and resettlement actions are consistent with ADB's safeguard requirements and the compensation for acquired assets is paid on full replacement cost basis. NHA endorsed LARP including CAP was cleared by ADB in July 2015 and its implementation and monitoring was started subsequently. The LARP for entire section was completed as a whole and overall implementation status is discussed accordingly in subsequent sections providing brief on the project LAR impacts, LARP implementation progress achieved, issues encountered and the recommended actions for facilitating execution of the project in a manner consistent with the SPS requirements.

**Figure 1: Location Map of M-4 (Section-II)**

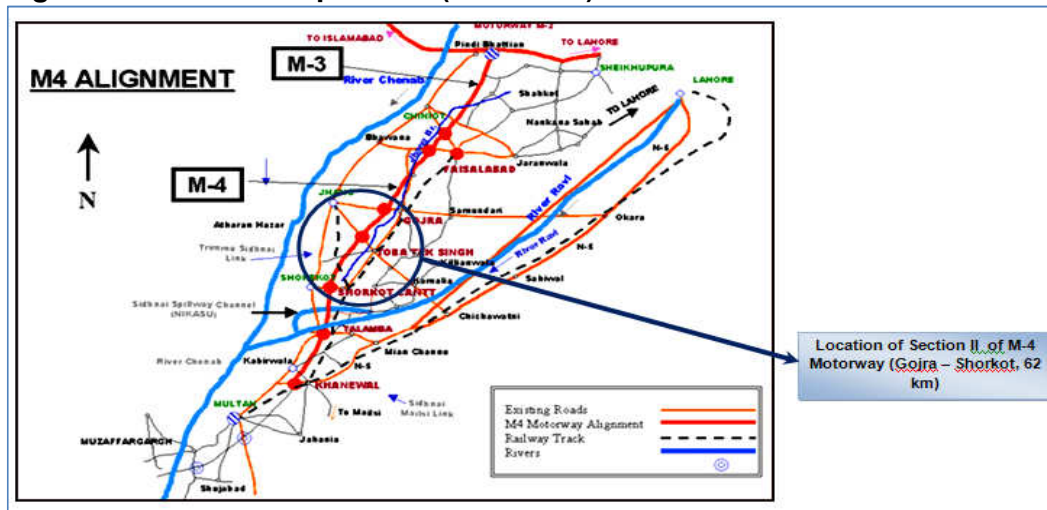

## 1.2 Objectives of the IMR

3. The approved LARP require monitoring of LARP implementation progress and submit quarterly internal monitoring reports for NHA and ADB review. Accordingly this quarterly internal monitoring report for a period from December 2015 to February 2016 is prepared. The objective of this internal monitoring report is to assess compensation payment progress achieved, document reasons for delayed payments and actions implemented to resolve problems faced; provide to date implementation status of land acquisition & resettlement plan (LARP) and corrective action plan (CAP) and status of compliance with the ADB social safeguard requirements for involuntary resettlement; and recommend actions for NHA or ADB consideration.

4. This IMR provides details of the following aspects:

- i) project LAR impacts and LARP implementation progress achieved covering delivery of compensation against acquired assets and allowances under LARP provisions;
- ii) reasons for pending/ongoing payments, and specific measures implemented for information dissemination and delivery of compensation to unpaid;
- iii) institutional arrangement for LARP implementation;
- iv) Grievance redress mechanism in place and progress on grievances received and redressed and
- v) Recommended actions for NHA and ADB's consideration.



## 2. LAR IMPLEMENTATION STATUS

### 2.1 Project Impact as per LARP

5. Impact on 1214.46 acres (491.1 ha) agriculture/barren/residential land, 22 residential structures (houses), 48 cattle yards/ farm yard, 2 brick kilns, 4 poultry farms, 1 mosque, 43 tubewells, 68 hand pumps, 7 miscellaneous structures, and 27,302 fruit trees and timber/ wood trees has been recorded, which will involve relocation of a large number of infrastructure assets resulting in social disruption and delayed project implementation. The project impacts as per approved LARP are discussed in the given below:

#### 2.1.1 Number of DHs

6. The number of displaced households (DHs) is 3,674 for land compensation, 450 for crop compensation, 162 for affected structures and 513 for trees compensation. Total 3,587 DHs are entitled for resettlement allowance, 21 livelihood allowance, 63 transport allowance, 43 business allowance, 22 vulnerability allowance, 6 employment allowance, 27 electricity allowance, 25 house rent (allowance) and 1,447 differential for replacement cost.

#### 2.1.2 Land Acquisition

7. In accordance with the approved LARP, total 1214.46 acres (491.1 ha) private land need to be acquired which is owned by 3674 DHs. This acreage of land belongs to 33 villages located in the jurisdiction 2 districts named as Toba Tek Singh and Jhang in Punjab province. A break-up of land needed for the project by districts is presented in Table 2.1 as below.

**Table 2.1: Land Acquisition by District and Number of DHs**

District	Land to be acquired (Acres)	No. of DHs
<b>A District TT Singh</b>		
i) Land Acquired for ROW	679.43	1,984
ii) Land Acquired for Interchanges ROW	44.09	131
<b>B District Jhang</b>		
i) Land Acquired for ROW	477.19	1,521
ii) Land Acquired for Interchanges ROW	13.75	38
<b>Total</b>	<b>1214.46</b> (491.1 ha)	<b>3,674</b>

#### 2.1.3 Structures and Farm Assets

8. As per LARP (2015), there are total of 195 affected structures, out of which 22 are residential structures (houses), 48 cattle yards/ farm yard, 2 brick kilns and 4 poultry farms, 1 mosque and 7 miscellaneous structures.

9. There are 43 tubewells and 68 hand pumps need to be relocated.

#### 2.1.4 Affected Crops

10. As a result of land acquisition, the crops grown on 793 acres will be affected as reflected in table below (Table 2.2).

### 2.1.5 Affected Trees

11. As a result of land acquisition, 27,302 fruit trees and timber/ wood trees will need to be cut down as given in Table 2.2.

**Table 2.2: Summary of Project Impacts other than Land**

Sr. No.	Type of Impact (As per LARP June 2015)	Unit	Quantity	No of DHs
<b>1</b>	<b>Structures</b>			
	Houses	No.	22	22
	Mosque	No.	1	-
	Brick Kilns	No.	2	2
	Poultry Farm	No.	4	4
	Farm Yard/ Cattle Yard	No.	48	48
	Miscellaneous	No.	7	7
<b>2</b>	<b>Farm Assets</b>			
	Tubewell	No.	43	43
	Hand Pump	No.	68	68
<b>3</b>	<b>Trees</b>			
	Fruit Trees/ Non-Fruit/ Firewood	No.	27302	513
<b>4</b>	<b>Crops</b>	Acres	793.09	446
<b>5</b>	<b>Vulnerable APs/ DPs</b>	No.	-	29

### 2.2 LARP implementation as of 1<sup>st</sup> Monitoring Report (November 2015):

12. The LARP implementation progress as reported in 1<sup>st</sup> internal monitoring report in November 2015 reflected following unpaid DHs for acquired assets (land, structures, trees and crops):

- 1146 Displaced Household entitled for land compensation amounting to Rs.47.703 million;
- 43 DHs entitled to compensation amount Rs. 1.800 million for crops loss and 329 DHs entitled for additional crop compensation amounting Rs. 15.605 million.
- 14 DHs entitled to compensation amount Rs.0.630 million against structure loss.
- 31 DHs entitled to compensation amount Rs. 2.766 million for tree losses.
- Payment of allowances Rs. 29.838 for rehabilitation/ livelihood restoration of 2786 entitled DHs<sup>1</sup>

### 2.3 LARP Implementation progress achieved till February 2016

13. During reporting period compensation amount Rs 12.675 million rupees is paid to the respective DHs against their acquired assets including land, structures, crops and trees. The compensation amount delivered against the resettlement allowances and land price differential include Rs. 11.528 million. The overall compensation payment progress is discussed in preceding paras and the payments made during reporting period against each category are summarized as under:

- Compensation amount Rs.5.185 million paid to 190 DHs for land;

<sup>1</sup>Unpaid DHs entitled for rehabilitation and livelihood restoration include: Resettlement Allowance (1466 DHs), Livelihood Allowance (6 DHs), Transport Allowance (15 DHs), Business Allowance (12 DHs), Vulnerable Allowance (9 DHs), employment loss (6 DHs), electricity (16 DHs), house rent (9 DHs) and Land cost deferrintail (1247 DHs).

- Compensation amount Rs. 0.618 million paid to 24 DHs for crop losses and 127 DHs are paid for additional crop compensation amounting Rs. 6.135 million.
- Compensation amount Rs.0.392 million paid to 9 DHs are against structure loss;
- Compensation amount Rs. 0.345 million paid to 18 DHs for tree losses; and
- Compensation amount Rs. 11.528 million for rehabilitation and livelihood resettlement allowances<sup>2</sup> paid to 560 DHs.

### 2.3.1 Payment of Land Compensation

14. The IMR results show that total amount of compensation assessed for the acquisition of 1,214.46 acres of private land is Rs. 647.925 million to be paid to 3,674 DHs. Out of which, the payment of Rs. 605.407 million (93.4%) have been paid to 2,718 DHs (74.0%) for 1,184.96 acres (97.6%), while the balance amount Rs. 42.518 million (6.6%) is to be paid to 956 DHs (26%) for 29.5 acres (2.4%) of land which is still under process.

### 2.3.2 Payment of Structures

15. The total amount of compensation for affected structures and other farm assets (tubewells & hand pumps) assessed was Rs. 31.935 million to be paid to 162 DHs. Out of which, the payment of Rs. 31.697 million (99.3%) have been paid to 157 DHs (97.0%). The remaining 5 DHs (3.0%) are yet to be paid an amount of Rs. 0.238 million (0.7%).

### 2.3.3 Payment of Trees

16. In case of fruit and timber/ wood trees, payments of Rs. 73.683 million had to be paid. As of 29-Feb-2016, the payment of Rs. 71.262 million (96.7%) has been made to 500 DHs (97.5%). The payment of Rs. 2.421 million (3.3%) is yet to be paid to 13 DHs (2.5%).

### 2.3.4 Payment of Crop Compensation

17. In case of crop compensation, 450 DH had to be paid an amount of Rs.56.814 million. To date 431 DHs (95.8%) have been paid an amount of Rs. 55.632 million (97.9%). The remaining 19 DH (4.2%) are yet to be paid an amount of Rs. 1.183 million (2.1%).

18. In addition, one additional crop compensation is also being made. In this context, 450 DH<sup>3</sup> had to be paid an amount of Rs. 19.974 million. To date 248 DHs (55.1%) have been paid an amount of Rs. 10.504 million (52.6%). The remaining 202 DH (44.9%) are yet to be paid an amount of Rs. 9.470 million (47.4%).

### 2.3.5 Payment of Allowances

19. The payment of various allowances including resettlement/ rehabilitation, livelihood, transportation, business, vulnerability, employment, replace cost differentials, electricity and house rent are to be paid to total 5041 DHs<sup>4</sup>. To date payment of allowances has been made to 2,814 DHs<sup>2</sup>. The leftover payment to entitled DHs is under process.

<sup>2</sup> DHs paid for entitled rehabilitation and livelihood restoration include: Resettlement Allowance (288 DHs), Transport Allowance (1 DHs, electricity (1 DHs), house rent (3 DHs) and Land cost deferral (267 DHs).

<sup>3</sup> DHs already included as land owners.

<sup>4</sup> 5041 DHs included the DHs having multiple allowances, i.e. entitled for more than 1 allowance.

20. The compensation payment status as described in above paragraphs is summarized for each impact in table 2.3 below. The village wise compensation payment status for acquired assets and entitled R&R allowances is given as Annexes 1, 2, 3, 4 and 5 for land, structures, trees, crops and allowances respectively.

#### **2.4. Achieved Progress Shown in Linear Plan**

21. Following LARP implementation progress achieved as discussed above, the Project road section showing sections with compensation paid and those where compensation payment is ongoing/pending due to reasons beyond NHA's control was updated according to the civil works contract packages i.e. Package A (Km 58+100 to Km 89+000, and Package B (Km 89+000 to Km120+268) of M-4 Gojra-Shorkot Project. The linear plan showing achieved progress for each contract package section is discussed below:

##### **M-4 Gojra-Shorkot Project Contract Package A**

22. Total length of Project road Section under Contract Package-A is 30.900 km. The LARP implementation progress achieved as of February 2016 reflect that applicable payments to the DPs have been paid in different subsections totaling about 30.25 kames and the said section is free for commencement of civil works. However, in 0.650 Km the land compensation is delayed due to different reasons and PIU with assistance from SSMC team mobilized on M-4 is making efforts to locate the DHs and deliver their entitled compensation. As per LAR conditions the construction activities will be limited to the specified reaches as identified in the part A of the table given in linear plan annexed A, while in other reaches as identified part B of said table a total of 0.650 km will remain on hold until these payments are fully made and are validated by the external monitor.

##### **M-4 Gojra-Shorkot Project Contract Package B**

23. Total length of Project road Section under Contract Package-B is 31.268 km. All types of payments payable to the DPs as per LARP have been completed in different subsections totaling about 29.508 kms. As per LAR conditions the construction activities could commence in the specified reaches as identified in the part A of the table included in linear Plan Annex-A while reaches totaling 1.760 km as identified part B of said table construction could remain on hold until these payments are fully made and are validated by the external monitor.

24. Having said above facts, it is clarified that the payments in remaining 0.650 Km in contract package A and 1.76 Km in Contract Package B are progressing very slow due to the reasons beyond NHA's control, including but not limited to, land ownership disputes, inheritance and compensation apportionment cases or meager compensation amounts and DPs not showing up to collect such meager compensations. In subsequent section-3 the reasons for nonpayment and NHA's efforts to deliver compensation are discussed in detail.

**Table 2.3: Status of Implementation of LARP**

Type of Payment	Payable	Total	Progress till 12 <sup>th</sup> November 2015				Progress (Nov 2015 to 29 <sup>th</sup> Feb 2016)				Total (as of 29 <sup>th</sup> Feb, 2016)			
	Payment	DHs	Paid	Unpaid	Paid	Unpaid	Paid	Unpaid	Paid	Unpaid	Paid	Unpaid	Paid	Unpaid
	(Rs. M)	(No.)	Amount (Rs. M.)	Amount (Rs. M.)	DHs (No.)	DHs (No.)	Amount (Rs. M.)	Amount (Rs. M.)	DHs (No.)	DHs (No.)	Amount (Rs. M.)	Amount (Rs. M.)	DHs (No.)	DHs (No.)
i) Land Compensation	647.925	3674	600.222	47.703	2,528	1,146	5.185	42.518	190	956	605.407	42.518	2,718	956
ii) Crop Compensation	56.814	450	55.014	1.800	407	43	0.618	1.182	24	19	55.632	1.183	431	19
iii) Additional Crop Compensation	19.974	450	4.369	15.605	121	329	6.135	9.47	127	202	10.504	9.470	248	202
iv) Affected Structures	31.935	162	31.305	0.630	148	14	0.392	0.238	9	5	31.697	0.238	157	5
v) Affected Trees	73.683	513	70.917	2.766	482	31	0.345	2.421	18	13	71.262	2.421	500	13
<b>Allowances – rehabilitation/ livelihood restoration</b>														
i) Resettlement Allowance	77.506	3587	63.972	12.630	2,121	1,466	6.779	6.755	288	1,178	70.751	6.755	2,409	1,178
ii) Livelihood Allowance	0.824	21	0.596	0.228	15	6	-	0.228	-1	7	0.590	0.235	14	7
iii) Transport Allowance	0.830	63	0.586	0.244	48	15	0.008	0.236	1	14	0.594	0.236	49	14
iv) Business Allowance	2.073	43	1.518	0.396	31	12	-	0.555	-	12	1.518	0.555	31	12
v) Vulnerable Allowance	0.872	22	0.594	0.277	13	9	-	0.278	-	9	0.594	0.277	13	9
vi) Employment losses allowance	0.238	6	-	0.238	-	6	-	0.238	-	6	-	0.238	-	6
vii) Replacement Cost	14.786	1,247	-	14.786	-	1,247	4.301	10.485	267	980	4.301	10.485	267	980
viii) Electricity	1.080	27	0.440	0.640	11	16	0.04	0.6	1	15	0.480	0.600	12	15
ix) House rent	0.952	25	0.552	0.399	16	9	0.4	-	3	6	0.952	0.289	19	6

### 3 Reasons for On-going or Pending Payments with Way forward

#### 3.1 Reasons for On-going or Pending Payments

25. Payment process for compensation against entitled rehabilitation and livelihood restoration allowances was started after approval of LARP which is in progress and on-going. In case of land compensation, 956 DHs (26%) are yet to be paid for acquired land measuring 29.5 acres (2.4% of acquired land). Although NHA is exhausting good faith efforts to ensure delivery of compensation to all unpaid APs against remaining 2.4% land acquired for ROW, but the payments are being delayed due to different reasons beyond NHA's control. The main reasons contributing towards the delay in payments are as below:

- Transfer Record of Rights: 142 land owners passed away but so far, the land has not been transferred to their inheritors.
- There are 243 DHs might have gone some other place/ not traceable
- 65 DHs are out of country.
- 313 DHs have meager amount of their entitlement share;
- 89 Land Owners/ DPs have title disputes pending before revenue authorities/ Courts. The court's decision is awaited and the PIU will follow the court decision;
- 104 DHs are deficient in requisite documentation including lack of CNIC, bank account, underage DPs.

Details of reasons are given in Table 2.4 as below.

**Table 2.4: Reasons for Delay in Payment of Land Compensation**

Reasons for delay in payments	Total unpaid DPs
1. Inheritance cases	142
2. Out of village	243
3. DPs out of country (abroad)	65
4. Meager amounts <sup>5</sup>	313
5. Mortgage cases	-
6. Court cases(e.g. internal ownership disputed & compensation enhancement)	89
7. Others with requisite documentation issues including CNIC, bank accounts etc	104
Total	956

#### 3.2 NHA's efforts and actions taken to Address Pending Payments

26. For delivery of pending compensation, the LAC and his team retained a close liaison with the affected people during the reporting period. Site visits for compensation delivery, consultative and information dissemination sessions/ meetings and DPs follow-up has been carried out by the LAC and NHA Land staff. In this regard a comprehensive field visit plan was implemented and the LAC and his team repeatedly visited the affected villages (LAC's visit schedule for months of November, December 2015 and January 2016 is added as annex 6) to process compensation claims and deliver compensation to affected persons at their door steps.

<sup>5</sup>Break up of 313 DPs of meager amount is as, 70 Inheritance cases, 209 Out of village, 17 DPs out of country (abroad), 14 Court cases(e.g. internal ownership disputed & compensation enhancement), 3 Others.

27. During scheduled visits, meetings were held with available affected persons and their relatives in presence of village DPCs and headman; written notices were delivered to available APs by LAC/land staff and DPs were motivated to submit their claims in all affected villages; and the list of unpaid DPs was disclosed to the village headmen, DPC members and local community to seek assistance for locating and informing unpaid DPs for receipt of their compensation.(See sample visit report in Annex7).In the notices, DPs were informed to receive their compensation for acquired assets (land, structure, houses, trees and crops) and allowances etc (Annex8 exhibits sample notice). During consultative process, LAC and NHA land staff clarified the DPs that the compensation is deposited in treasury and can be collected after submission of claims and if not claimed in timely manner, the compensation could be deposited in the court under section 31 of LAA 1894 and no excuses will be accepted. Deposit of funds in treasury is presented in Annex-9.

28. Since mobilization of SSMC, its team developed a rapport with the LARU team in PIU, DPCs in each village and affected persons. During reporting period total 20 consultations were made by the male and female social mobilizers, wherein 189 DPs/ members of DPCs as well as local community participated. During such consultations with DPs and DPCs, the information disclosed include project LAR impacts, compensation eligibility and entitlements as per LARP provisions, submission of compensation claim for acquired assets (land, crops, trees and structures etc) and other compensation entitlements under LARP provisions including resettlement, income/ livelihood restoration allowances and land price gap differential etc. List of 20 Nos. consultations and participants belonging to the category of DPs/ members of DPCs and representative of local community is given in Annex 10.

29. Besides delivery of notices, consultative meetings with the DPs in each village, for information disclosure, the following additional activities were also undertaken to inform unpaid DPs to come-up and collect compensation:

- Information bearing banners/Panaflexs were installed at conspicuous places like mosque and school walls near entrance gates and in markets/streets. During installation process, the SSMC team informed the DPs and local people about objective and information contained on panaflex. The activity was photographed which is presented as pictorial presentation at the end of the report.
- Advertisement of Unpaid DPs in Local Newspaper: After exhausting all good efforts to approach unpaid APs at village and project level, NHA as a last resort, published the name of unpaid cases (DPs) of each village in local newspaper (the Daily Dunya) to expand the canvas of its awareness campaign country wide and ensure the leftover over payment could be made to all DPs if they approach NHA. A copy of the advertisement is given in Annex 11.

### **3.3 Efforts Exhausted by NHA with Way Forward.**

30. The Matrix below provide a summary on efforts exhausted for each unpaid land category and proposed actions with responsibility as way forward to ensure compensation is delivered to all identified unpaid DP as and when their issues are resolved:

### 31. Proposed Action Plan for the implementation of LARP

Impact	Category of Un-paid Cases	NHA's Effort	Responsibility/ Action to address pending payments
<b>A) Land Compensation</b>	142 DPs- Transfer Record of Rights(land owners passed away)	<ul style="list-style-type: none"> <li>→ Meetings were held with available affected persons and their relatives in presence of village DPCs and headman;</li> <li>→ written notices were delivered to available APs by LAC/land staff and DPs were motivated to submit their claims in all affected villages;</li> <li>→ NHA has informed to all un-paid DPs through a local newspaper ("Dunya") to submit claims and collect entitled compensation.</li> <li>→ Information bearing banners/Panaflex were posted at conspicuous places like mosque and school walls near entrance gates and in markets/ streets</li> <li>→ NHA confirmed that the land compensation is already deposited in the treasury.</li> </ul>	<p><b>PIU (LAC, NHA), SSMC &amp;Local revenue authority</b></p> <ul style="list-style-type: none"> <li>- The available decedents of the DH living in village will be approached through social mobilizers;</li> <li>- DHs will be assisted to approach land revenue authorities and get inheritance mutations recorded;</li> <li>- a close liaison will be maintained with local land revenue people for early mutation in record, and DHs will be mobilized for submission of compensation claims with requisite support documents and delivery of compensation accordingly</li> </ul>
	243 DHs might have gone some other place(out of village)	<ul style="list-style-type: none"> <li>→ For delivery of pending compensation, the LAC and his team retained a close liaison with the affected people during the reporting period</li> <li>→ Sites visits for compensation delivery, consultative and information dissemination sessions/ meetings and DPs follow-up has been carried out by the LAC and NHA Land staff.</li> <li>→ NHA deposited funds in District Treasury and DPs with their whereabouts unknown informed through local press media (the daily'Dunya) newspapers to come and receive their entitled compensation.</li> <li>→ Information bearing banners/ Panaflex were posted at conspicuous places like mosque and school walls near entrance gates and in markets/ streets</li> </ul>	<p><b>PIU (LAC, NHA), SSMC &amp;Local revenue authority</b></p> <ul style="list-style-type: none"> <li>- The village notables and the DPCs will be coordinated continuously to identify the where about of the DHs living in other cities in Pakistan</li> <li>- ; efforts will be made to approach the DHs at their current places; and</li> <li>- DHs will be mobilized to collect compensation through telephonic contacts andby delivering notices through post and any other plausible mean.</li> </ul>
	65 DPs out of country (abroad)	<ul style="list-style-type: none"> <li>→ For delivery of pending compensation, the LAC and his team retained a close liaison with the affected people during the reporting period.</li> <li>→ Sites visits for compensation delivery, consultative and information dissemination sessions/ meetings and DPs follow-up has been carried out by the LAC and NHA Land staff.</li> <li>→ NHA deposited funds in District Treasury and DPs with their where about unknown informed through local press media</li> </ul>	<p><b>PIU (LAC, NHA), SSMC &amp;Local revenue authority</b></p> <ul style="list-style-type: none"> <li>- The village notables and the DPCs will be coordinated continuously to identify the where about of the DHs living in other cities in Pakistan</li> <li>- ; efforts will be made to approach the DHs at their current places; and</li> </ul>



Impact	Category of Un-paid Cases	NHA's Effort	Responsibility/ Action to address pending payments
		<p>(the daily' Dunya) newspapers to come and receive their entitled compensation.</p> <p>→ Information bearing banners/ Panaflex were posted at conspicuous places like mosque and school walls near entrance gates and in markets/ streets</p>	<p>- DHs will be mobilized to collect compensation through telephonic contacts and by delivering notices through post and any other plausible mean.</p>
	313 – Meager amount of compensation	<p>→ For delivery of pending compensation, the LAC and his team retained a close liaison with the affected people during the reporting period;</p> <p>→ Sites visits for compensation delivery, consultative and information dissemination sessions/ meetings and DPs follow-up has been carried out by the LAC and NHA Land staff;</p> <p>→ Meetings were held with available affected persons and their relatives in presence of village DPCs and headman; and written notices were delivered to available APs by LAC/land staff and DPs were motivated to submit their claims in all affected villages;</p> <p>→ NHA has informed to all un-paid DPs through a local newspaper ("Dunya") to submit claims and collect entitled compensation and information bearing banners/ Panaflex were posted at conspicuous places like mosque and school walls near entrance gates and in markets/ streets etc.</p> <p>→ The land compensation is already deposited in the treasury.</p>	<p><b>PIU (LAC, NHA), SSMC &amp;Local revenue authority</b></p> <p>- Close liaison will be maintained with DHs to motivate them for submitting of claims with requisite support documents;</p> <p>- opportunities to open joint bank accounts will be explored;</p> <p>- the efforts will be continued to support DHs in opening of bank accounts, submission of claims and deliver their compensation</p>
	89- Court cases – price enhancement/ Ownership/ Title Issues	<p>→ For delivery of pending compensation, the LAC and his team retained a close liaison with the affected people during the reporting period</p> <p>→ Sites visits for compensation delivery, consultative and information dissemination sessions/ meetings and DPs follow-up has been carried out by the LAC and NHA Land staff.</p> <p>→ NHA maintained a close liaison between the DPs and the local revenue authorities to ensure timely disbursement of compensation as court decides.</p> <p>→ The compensation cost is already deposited in the treasury.</p>	<p><b>PIU (LAC, NHA), SSMC &amp;Local revenue authority</b></p> <p>- Follow-up activities will be continued to approach the DHs to sensitize them for expeditious resolution of issues through courts and payment of compensation</p> <p>- NHA to maintain a close liaison between DP and local revenue authorities to ensure the timely payment of compensation as court decides.</p>
	104 DPs are deficient in requisite documentation including lack of CNIC, bank account and	<p>→ Compensation cost is already deposited in the district treasury.</p> <p>→ For delivery of pending compensation, the LAC and his team retained a close liaison with the affected people during the</p>	<p><b>PIU (LAC, NHA), SSMC &amp;Local revenue authority</b></p> <p>- Close liaison will be maintained with DHs to motivate them for submitting of claims with requisite support</p>

Impact	Category of Un-paid Cases	NHA's Effort	Responsibility/ Action to address pending payments
	underage	<p>reporting period</p> <p>→ Sites visits for compensation delivery, consultative and information dissemination sessions/ meetings and DPs follow-up has been carried out by the LAC and NHA Land staff.</p> <p>→ Meetings were held with available affected persons and their relatives in presence of village DPCs and headman; and written notices were delivered to available APs by LAC/land staff and DPs were motivated to submit their claims in all affected villages.</p>	<p>documents;</p> <ul style="list-style-type: none"> <li>- opportunities to open joint bank accounts will be explored;</li> <li>- the efforts will be continued to support DHs in opening of bank accounts, submission of claims and deliver their compensation</li> <li>- LAC (PIU) will help the DPs to expedite the requisite documentation</li> </ul>

## 4 Institutional Arrangements for LARP Implementation and monitoring.

### 4.1 Establishment of PIU with LARU

32. NHA has established a Project Implementation Unit (PIU) at Faisalabad under the overall supervision of General Manager (M-4). The PIU is being supported by two Project Directors covering Package A<sup>6</sup> by one Project Director, while the second Project Director is looking after the implementation of Package B<sup>7</sup> of Section II (Gojra – Shorkot). For Safeguards management, a Land Acquisition and Resettlement Unit headed by Director Land is in place in PIU M-4. The LARU team includes Director (L&S), Deputy Director (L&S), Assistant Directors (L&S), and Land Acquisition Collector (LAC) along with supporting staff including Land Acquisition Officer and Patwaries. Besides, the SSMC team including professional as resettlement specialist, grievances, LAR database management and M&E specialists with social mobilizers team is mobilized. In addition to formal institutional set-up for LARP implementation, village level DPCs are notified and made operational for keeping a close lesion with DPs to raise awareness and information dissemination about LARP implementation and compensation delivery process, provide them a forum and facilitate DPs to raise their concerns and get their issues resolved.

### 4.2 Mobilization of Social Safeguards Management Consultant (SSMC)

33. Upon approval of Addendum 1 for consultancy services for Social Safeguard Management at M-4 (Faisalabad – Khanewal 184 km Project) by the Executive Board of NHA, the Member (Central Zone), Lahore issued the commencement letter on 1 February, 2016. Accordingly, M/s *International Development Consultants (IDC)* has mobilized the Social Safeguard Management Consultant (SSMC) team with effect from 15 February, 2016 to Assist PIU LARU at M-4 and EALS in NHA Headquarter during LARP implementation and monitoring for M-4 Project. As per approved Addendum No. 1, SSMC team mobilized at PIU M-4 include total 7 key staff members (i.e. 1 RS, 4 SMs, 1 MIS & 1 M&E) and 2 non-key staff. The SSMC team is fully functional and assisting the LARU and PIU of M-4 in LARP implementation and monitoring process, *while the SSMC team in EALS is facilitating* NHA in review of LARP implementation progress and taking remedial measures on issues encountered at field level.

34. Since its mobilization, the SSMC team deputed for M-4 project is assisting the LARU and PIU in LARP implementation process as per TORs. The specific LAR activities performed up-till February 29, 2016 are given as under.

- Updating of LARP data base and implementation progress data.
- Community consultation and information dissemination meetings for LARP disclosure and to provide guidance to the DPs for submission of claims.
- Assistance of DPs and LARU in processing of compensation claims and delivery of compensation.
- Developments of templates for grievances recording and maintaining grievance registers and operationalizing the GRM with all key members including Resettlement Specialist on board.
- Assistance of PIU in monitoring of LARP implementation progress and preparation of LARP monitoring reports.

<sup>6</sup> Package A: 58+100 to 89+000 (30+900 km)

<sup>7</sup> Package B: 89+000 to 120+268 (31+268 km)

### 4.3 Grievances Redress Committee at Project

35. The GRC have been established at the project level (Faisalabad) with the primary objective of providing a mechanism to mediate conflict and cut down on lengthy litigation. Grievance Redress Committee at the project level have already been notified (office order no 1(1)/NHA/EALS/2009/26 dated 8-10-2009) and working for M-4 and is placed at Project Director's Office at Faisalabad. This provides a forum to raise awareness among the people especially DPs and facilitate to resolve their concerns/ issues or objections relating to the LAR activities. The project GRCs will be kept intact and functioning, for the benefit of the DPs, till complete implementation of LARP and during implementation of the project civil works..

36. The GRC is headed by the Director Land, M-4 and representatives from Project Management Unit, aggrieved DP/DPs and/or representatives of DPs, social mobilizers (male & female) and other interested groups (if any). The GRC meets at least once in a month. Other than issues/references relating to ownership rights and against award which are to be dealt under the court of law, GRC review grievances involving all resettlement benefits, compensation, relocation, and other rehabilitation and income restoration/ assistance, assist DPs to get their concerns resolved and facilitate project executors to implement the recommended actions. (Annex 12)

37. The GRC constituted the following members:

- |                                              |          |
|----------------------------------------------|----------|
| 1. Director (L&S) M-4                        | Convener |
| 2. Land Acquisition Collector                | Member   |
| 3. DD (L&S) M-4                              | Member   |
| 4. A.D (L&S) M-4                             | Member   |
| 5. Resettlement Specialist                   | Member   |
| 6. Social Mobilizer (s) of SSMC              | Member   |
| 7. Patwaris from Revenue Department (2 Nos.) | Members. |
| 8. Office Assistant (to maintain record)     |          |

#### 4.3.1 Grievance Redress Mechanism followed

38. The grievance redress mechanism in Section-II is following one informal and two formal tier processes to address grievances. The first informal level is existence of Affected People Committee APC at village level. This level includes the APC representatives and members (both male and female) and social mobilizer SM. SM keeps a close liaison with village level Affected Person Committees, regularly conduct field visits to convene meetings with the APC members for consultations and facilitate them to discuss/resolve their concerns at village level and record their grievances to elevate them to the project GRC. The grievances that are not resolved at village level by APC with assistance and guidance of social mobilizer in the field are then share with First level GRC at project level.

39. When the complaints and grievances are filed with Project's GRC, these are recorded in complaints register, acknowledged to the aggrieved persons/complaints, fact finding reports are prepared through PIU/SSMC field teams, reviewed by GRC in its monthly meetings and accordingly actions are recommended for implementation to resolve the grievances. The complainants are kept informed about the development on the grievance resolution process and about the actions recommended by the GRC. To keep a record on grievances the registers are prepared and maintained by the

Resettlement Specialist under overall supervision of the Director Land who is convener of the GRC. The registration of complaints includes the following three steps. (i) Complaint Register, (ii) Custodian of Register, (iii) Making Functional the Registry Process. The template below is prepared to keep a record of complaints and track progress about Grievance redress:

#### Sample Template for record management of community complaints

Sr. No.	Identification of Complainer						Description of Complaint	Location of Issue	Action Taken	Status of Action Taken		Time Taken in case of Issue Resolved (weeks)	If issue (s) not Resolved (Give Reasons)	Give details, in case the issue was forward to the project office	Remarks
	Date	Name of Complainer	Father's Name	Address	NIC #	Occupation				Issues Resolved	Not Resolved				
1															
2															

40. If the grievance not resolved at first formal level or the complainant being dissatisfied with the recommendations of project GRC seeks to elevate the grievance to next higher level, the grievances are elevated to the second formal level GRC established in EALs NHA HQ. It includes Resettlement expert, Environmentalist, Director Land and Assistant Director Land. The proceedings of the GRC are reviewed and fact findings are conducted by the second level of GRM and actions are recommended to address grievances and communicated to the project team and the aggrieved party. If grievances are not resolved here then the complainant may go to the court for further actions.

#### 4.3.2 Grievances recorded and resolved

41. The grievances are received and responded to by the members of the GRC. The DPCs are kept involved in the redress process. The complaints/ grievances received are briefly discussed below;

- During this month, PIU received only two complaints regarding cheques. Names of recipient DPs on cheques were written erroneous. One issue has been resolved, while other is under process with PIU.

#### 4.4 Hiring and Mobilization of EMA:

42. The Hiring of External Monitor is under process for the M-4 Project. The process for hiring was started in December 2015 and expression of interest was invited in January 2016 for potential candidates. The EOI received and reviewed, however, the evaluation reflected that the potential candidates are below mark; hence, the position of EMA is being re-advertised. It is expected that the EOI will be advertised in early March and after completing hiring process the EMA could be mobilized by June 2016.

## 5. CONCLUSIONS & RECOMMENDATIONS

### 5.1 Conclusions

43. The whole requisite land has been acquired in all 33 villages of Section II of M-4 (Package A& B). The disbursement of land and non-land based compensation is in progress, however, the payment of land compensation has been made to 2, 528 DHs (74%) out of total 3,674 DHs. The payment to remaining 956 DHs (26.0%) is delayed due to various reasons. However, the NHA is doing all efforts with true spirit to make the payment to 100% DHs to comply with ADB SPS 2009 requirements. The payment of non-land compensation to leftover DHs is also in progress.

44. All institutional arrangements are in place and operational. The SSMC is mobilized to facilitate in LARP implementation and monitoring and ensure delivery of compensation to all entitled DHs. Except for 29.5 acres (2.4%) of acquired land parcels; compensation for 1184.96 acres (97.6%) of acquired ROW land is delivered to the DHs. The ROW stretches with cumulative length of 30.25 Km in contract package A and 29.508 Km in contract package B are free for commencement of works while in ROW stretches 0.65 Km in Package-A and 1.760 Km in Package-B compensation payment is pending due to reasons beyond NHA's control. The break-up of leftover payments is as under:

- (a) Payment of land Rs.42.518 million to 956 DPs on account of compensation for the loss of land.
- (b) Payment of Rs. 1.183 million on account of compensation for the loss of crops.
- (c) Payment of Rs. 9.470 million on account of compensation for the loss of additional crops
- (d) Payment of structure Rs. 0.238 million to 5 DPs on account of compensation for the loss of structure.
- (e) Payment of Rs. 2.421 million to 13 DPs on account of compensation for the loss of trees.
- (f) Payment of allowances (rehabilitation/ livelihood restoration) Rs. 19.670 million to be paid.

### 4.2 Recommendations

45. Based on LARP implementation progress discussed in above sections, following actions are recommended for delivery of remaining unpaid compensating against 29.5 acres acquired land and entitled rehabilitation and livelihood restoration allowances:

- PIU LARU and SSMC will maintain a close liaison with the available Displaced Households for preparation and submission of compensation claims.
- For DHs out of country or shifted in other cities in Pakistan: The village notables and the DPCs will be coordinated continuously to identify the whereabouts of the DHs living abroad and in other cities in Pakistan; efforts will be made to approach the DHs at their current places; and DHs will be mobilized to collect compensation through telephonic contacts, by delivering notices through post and any other plausible mean.
- For DHs with Inheritance issues: The available decedents of the DH living in village will be approached through social mobilizers to assist and guide them to approach land revenue authorities and get inheritance mutations recorded; a close liaison will be maintained with DHs and local land revenue people for

early mutation in record, submission of compensation claims with requisite support documents and delivery of compensation accordingly.

- In case of meager compensation amounts, a close liaison will be maintained with DHs to motivate them for submitting of claims with requisite support documents; opportunities to open joint bank accounts will be explored; the efforts will be continued to support DHs in opening of bank accounts, submission of claims and deliver their compensation.
- DHs with title disputes: Follow-up activities will be continued to approach the DHs to sensitize them for expeditious resolution of issues through courts and payment of compensation;

46. Since, the LARP implementation is progressing satisfactorily and following validation by the External Monitor in his EMR submitted in December 2015, ADB already allowed Construction works in 52.02 Kms (28.55 Km in Contract Package-A and 23.47 Km in Contract Package-B) with 10.15 km (2.35 Km in Contract Package-A and 7.80 Km in Contract Package-B) is kept on hold till LARP implementation is confirmed. With compensation delivery progress achieved till February 2016, it is concluded that 97.6% acquired ROW land compensation is paid to respective 74% DHs and the left over pending payments for 2.4% acquired land are with reasons beyond NHA's control and it is likely that delivery of compensation to unpaid 26% DHs may take significant time.

47. Now, out of with held 10.15 km (2.35 Km in Contract Package-A and 7.80 Km in Contract Package-B), the remaining unpaid section is 2.41 Km (0.65 Km in Contract Package-A and 1.76 Km in Contract Package-B). NHA has already exhausted best efforts to approach unpaid DHs for delivery of compensation and is committed to continue its efforts to ensure full LARP implementation. The compensation amount is already deposited in treasury and full operational institutional set-up including SSMC team is in place to continue follow-up, coordinate with local communities to locate DPs new residential places, approach unpaid DPs and facilitate them in processing of claims and delivery of compensation to ensure LARP implementation objectives are fully met.

48. With above demonstrated efforts and action plan provided in section 3 of this Internal Monitoring Report, it is suggested that the ADB may be requested to review the progress and efforts exhausted by NHA for remaining unpaid cases and allow construction works in with held 10.15 Km section to facilitate in timely completion of the project. Meanwhile the PIU and SSMC will continue following-up the unpaid DPs to ensure disbursement of compensation to all payable pending cases.

## **Pictorial Presentation**



### Pictorial Presentation of Selected Events



A view of an Orientation Meeting to SSMC Team with the Project Director (M-4) at NHA Complex Faisalabad on February 15, 2016



Consultation with DPC/ DPs at village 307/ JB (Section - II)



Consultation with DPC/ DPs at village 304/ JB (Section - II)



Consultation with DPC/ DPs at village 400/ JB (Section - II)



Consultation with DPC/ DPs at village 310/ JB (Section - II)

### Pictorial Presentation of Selected Events



View of Disbursement Compensation at Village 390/ JB



View of Disbursement Compensation at Village 307/ JB



View of Disbursement Compensation at Village 307/ JB

### Information Banners installed on Prominent Places of Villages



Photograph: Pana flex Notice board adhesive at 305/ JB Mansoor Wali, TehGojra & Distt Toba Tek Singh



Photograph: Pana flex Notice board adhesive at 360/ JB, Teh Gojra & Distt Toba Tek Singh



Photograph: Pana flex Notice board adhesive at 385/ JB, Salehrian Teh Gojra & Distt TT Singh



Photograph: Pana flex Notice board adhesive at 304/ JB, TehGojra & Distt Toba Tek Singh



Photograph: Pana flex Notice board adhesive at 383/ JB




Photograph: Pana flex Notice board adhesive at 469/ JB, Distt TT Singh

## **ANNEXES**

**Annex A: Linear Plan - Payment of Compensation of M-4 (Section-II)**

**Annex A: Linear Plan - Section-wise status of Payment of Compensation in Package-II (A) M-4**

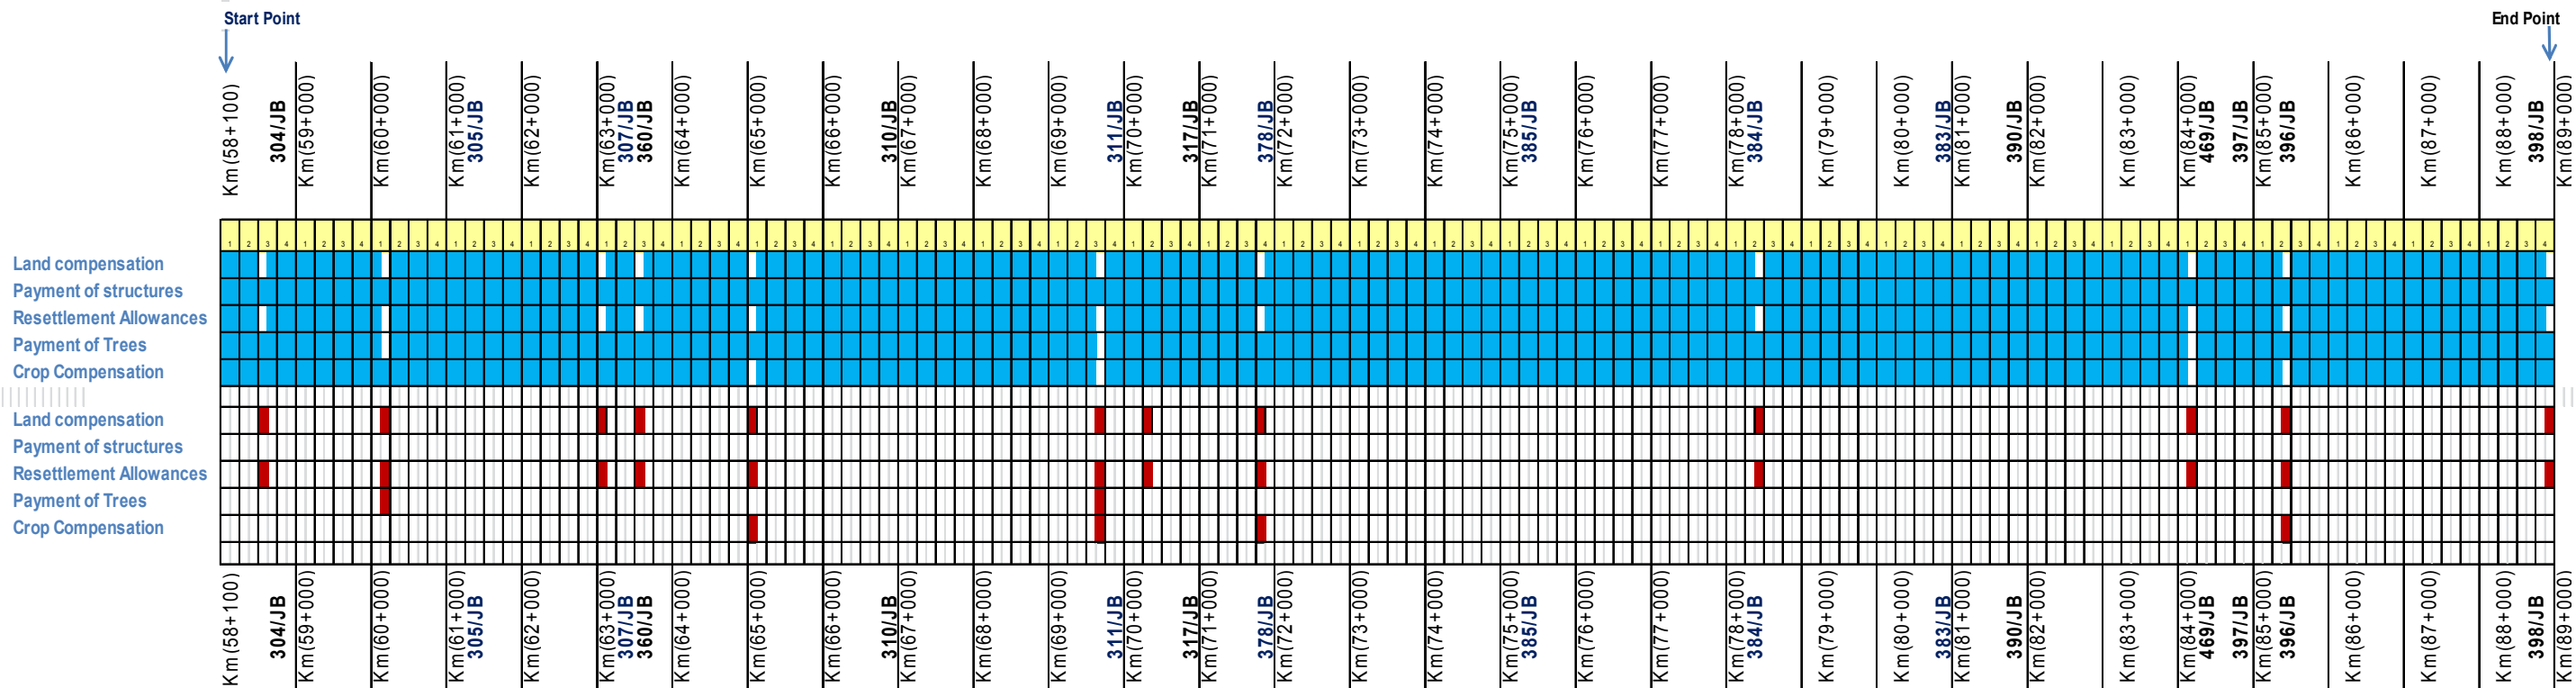

Scale: 1 square equals 250 meters, and 4 squares equal 1 kilometer

**Payment has been made to DPs** (Blue box)


**Payments are in process** (Red box)

**Status of Payment of Package-II (A)**

Sr. No.	Part A: All types of compensation fully paid				Part B: Payments on-going				Remarks
	Affected Villages	Chainage-wise subsections/reaches		Length (KM)	Affected Villages	Chainage-wise subsection/reaches		Length (KM)	
		From	To			From	To		
1	304/ JB	58.100	58.600	0.500	304/ JB	58.600	58.725	0.125	Total length of Section-II (Package-A) of Motorway Project (M4) is 30.900 km. All types of payments payable to the DPs as per LARP have been fully completed in different subsections totaling about 30.250 kms. The construction activities will be strictly limited to the specified reaches as identified in the part A of this table. In all other subsections/ reaches as identified part B of this table totaling about 0.650 km will remain on hold until these payments are fully made and are validated by the external monitor. Payments in these subsections are slow due to the reasons of land ownership disputes, inheritance and compensation apportionment cases. Other issues delaying the payments are meager amount of compensation awaiting opening up of bank accounts by DPs and some DPs not available at their given addresses.
2	305/ JB	58.725	60.125	1.400	305/ JB	60.125	60.200	0.075	
3	305/ JB	60.200	63.000	2.800	307/ JB	63.000	63.050	0.050	
4	307/ JB	63.050	63.500	0.450	360/ JB	63.500	63.600	0.100	
5	360/ JB	63.600	65.000	1.400	310/ JB	65.000	65.050	0.050	
6	310/ JB	65.050	66.750	1.700	311/ JB	69.625	69.675	0.050	
7	311/ JB	67.000	69.625	2.625	378/ JB	71.750	71.800	0.050	
8	317/ JB	69.675	71.750	2.075	469/ JB	84.125	84.175	0.050	
9	378/ JB	71.800	75.000	3.200	396/ JB	85.375	85.425	0.050	
10	385/ JB	75.000	78.375	3.375	398/ JB	88.875	89.000	0.050	
11	384/ JB	78.375	81.000	2.625	-	-	-	-	
12	383/ JB	81.000	84.125	3.125	-	-	-	-	
13	469/ JB	84.175	85.700	1.525	-	-	-	-	
14	397/ JB	85.425	88.875	3.450	-	-	-	-	
	<b>30.900</b>		Total	30.25		Total	0.65		

Annex A:

Linear Plan - Section-wise status of Payment of Compensation in Package-II (B) M-4

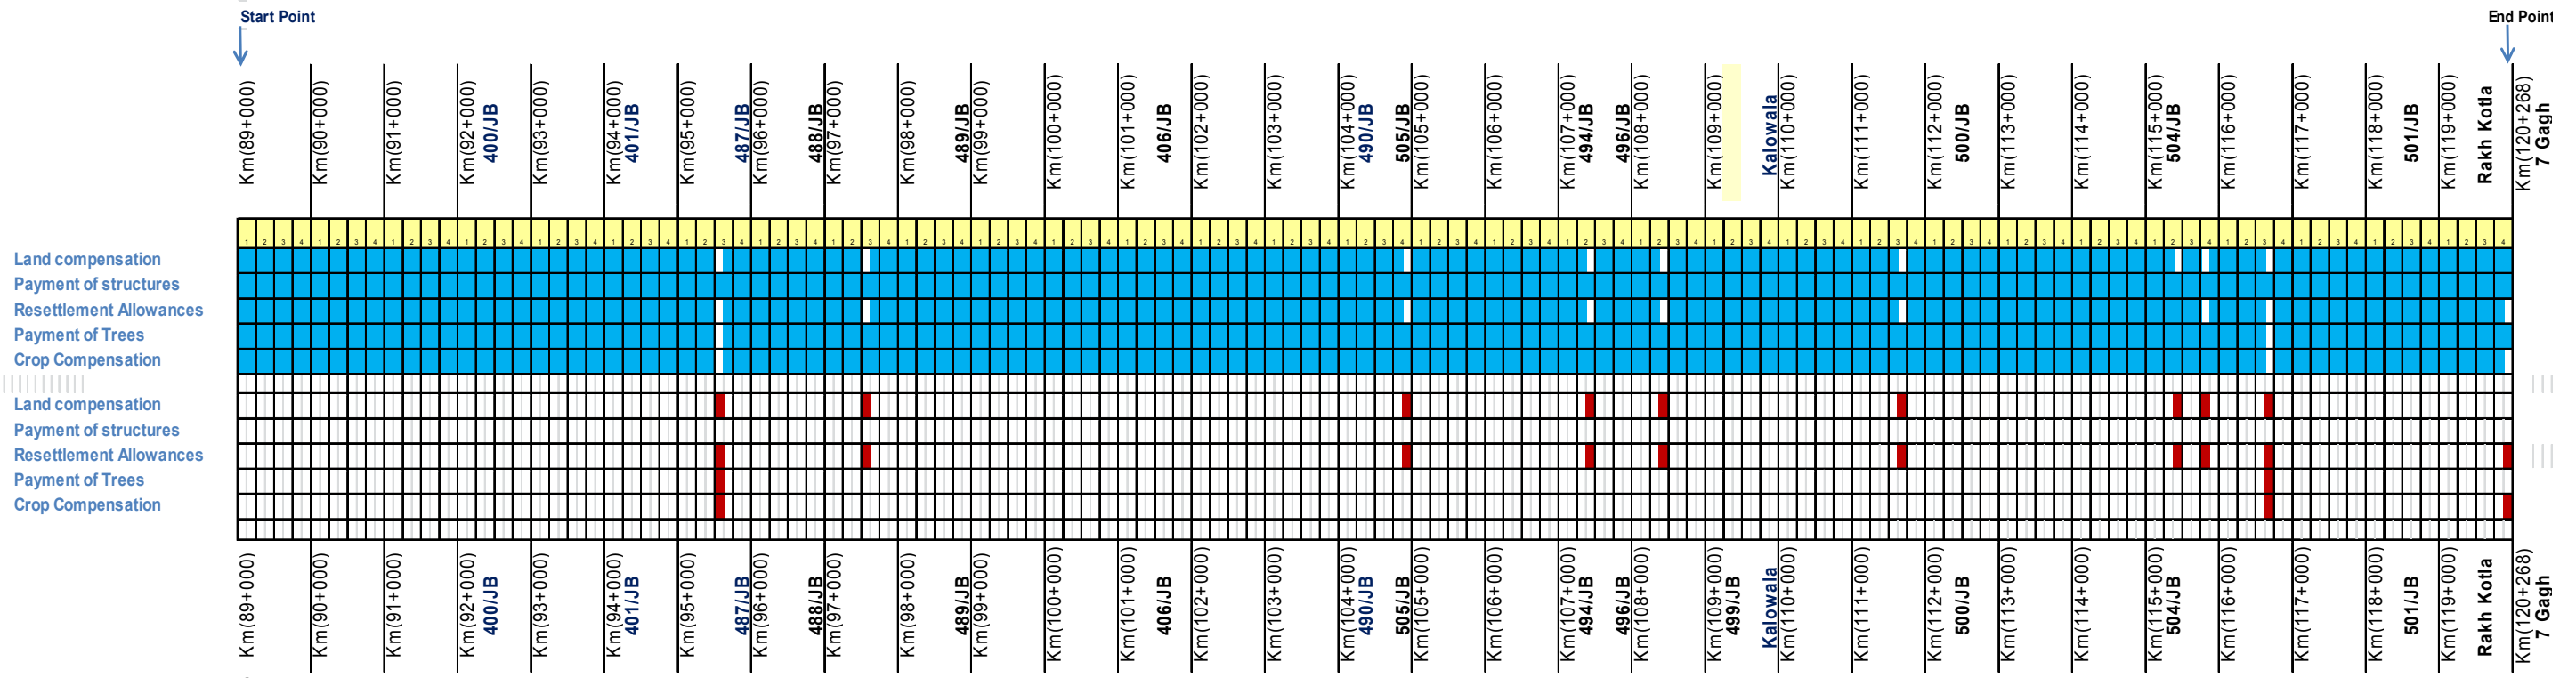

Payment has been made to DPs

Payments are in process

Status of Payment of Package-II (B)

Sr. No.	Part A: All types of compensation fully paid				Part B: Payments on-going				Section-II (Package-B)
	Affected Villages	Chainage-wise subsections/reaches		Length (KM)	Affected Villages	Chainage-wise subsection/reaches		Length (KM)	
		From	To			From	To		
1	400/JB	89.000	92.000	3.000	-	-	-	Total length of Section-II (Package-B) of Motorway Project (M4) is 31.268 km. All types of payments payable to the DPs as per LARP have been fully completed in different subsections totaling about 29.508 kms. The construction activities will be strictly limited to the specified reaches as identified in the part A of this table. In all other subsections/ reaches as identified part B of this table totaling about 1.760 km will remain on hold until these payments are fully made and are validated by the external monitor. Payments in these subsections are slow due to the reasons of land ownership disputes, inheritance and compensation apportionment cases. Other issues delaying the payments are meager amount of compensation awaiting opening up of bank accounts by DPs and some DPs not available at their given addresses.	
2	401/JB	92.000	94.000	2.000	-	-	-		
3	401/JB	94.000	95.500	1.500	401/ JB	95.500	95.625		0.125
4	487/JB	95.625	97.500	1.875	487/ JB	97.500	97.550		0.050
5	488/JB	97.550	99.000	1.450	-	-	-		
6	489/JB	99.000	101.500	2.500	-	-	-		
7	406/JB	101.500	104.000	2.500	-	-	-		
8	490/JB	104.000	104.375	0.375	490/ JB	104.375	104.425		0.050
9	490/ JB, 505/ JB	104.425	104.700	0.275	490/ JB	104.700	104.730		0.030
10	490/ JB, 505/ JB	104.730	107.375	2.645	494/ JB	107.375	107.425		0.050
11	494/JB	107.425	108.375	0.950	496/ JB	108.375	108.425		0.050
12	496/ JB	108.425	110.000	1.575	500/ JB	111.625	111.655		0.030
13	Kalowala	110.000	111.625	1.625	504/ JB	115.375	115.500		0.125
14	500/ JB	111.655	115.375	3.720	501/ JB	115.750	117.000		1.250
15	504/ JB	115.500	115.750	0.250	-	-	-		
16	501/ JB	117.000	120.268	3.268	-	-	-		
		31.268	Total	29.508		Total	1.760		

**Annex1: Village-wise Summary of Awarded Land**

Sr. No.	Village	Affected Land (Acre)	No of Displaced Household			Total Amount (Rs.)	Amount Disbursed (Rs.)	Balanced Amount (Rs.)
			Total	Paid	Un Paid			
A	District Toba	Tek Singh						
1	304/ JB	15.08	74	40	34	7,395,937	6,334,412	1,061,525
2	305 / JB	50.83	135	96	39	11,689,750	10,963,460	726,290
3	307 / JB	47.08	186	133	53	10,821,500	10,681,822	139,678
4	310 / JB	75.58	163	111	52	17,779,000	16,903,701	875,299
5	311 / JB	72.83	411	316	95	16,739,688	16,133,064	606,624
6	317/ JB	3.33	8	8	0	573,562	573,559	
8	360 / JB	10.45	100	52	48	2,988,203	2,573,458	414,745
7	378/ JB	37.7	113	94	19	15,179,281	14,612,714	566,567
9	383/ JB	57.58	193	174	19	58,018,219	57,582,942	435,277
10	384/ JB	67.08	112	102	10	46,309,063	45,335,538	973,525
11	385/ JB	46.95	108	86	22	32,412,750	32,256,401	156,349
12	390/ JB	28.33	32	23	9	19,557,187	19,548,565	8,622
13	396/ JB	55.58	36	34	2	12,769,313	12,174,365	594,948
14	398/ JB	6.83	95	42	53	1,169,766	786,957	382,809
15	400 / JB	13.83	25	23	2	3,100,687	3,078,348	22,339
16	401/ JB	37.7	107	101	6	20,888,313	20,829,096	59,217
17	438/ JB	0.08	8	6	2	34,500	20,401	14,099
18	469 / JB	52.83	83	49	34	18,261,281	17,387,718	873,563
	383/ JB Interchange	29.71	87	33	54	36,990,243	20,749,165	16,241,078
19	388 / JB Interchange	7.08	10	10	0	12,229,531	12,229,531	
	401/ JB Interchange	7.33	29	23	6	6,429,938	4,160,993	2,268,945
B	District Jhang							
20	487/ JB	46.24	118	86	32	8,703,244	8,079,393	623,851
21	488/ JB	22.58	49	39	10	6,801,848	6,748,047	53,801
22	489/ JB	44.38	212	178	34	14,392,839	13,702,704	690,135
23	490/ JB	85.37	222	189	33	46,338,157	44,424,069	1,914,088
24	406/ JB	26.74	75	69	6	13,839,890	13,591,753	248,137
25	505/ JB	21.57	26	20	6	4,960,813	4,797,043	163,770
25	494/ JB	32.69	88	83	5	31,018,196	30,943,861	74,335
27	496/ JB	10.3	65	43	22	6,318,475	5,943,841	374,634
28	Kalo Wala	55.77	224	129	95	48,741,887	45,991,921	2,749,966
29	500/ JB	26.85	92	76	16	20,626,386	19,919,863	706,523
30	504/ JB	42.18	180	136	44	48,508,437	45,413,297	3,095,140
31	501/ JB	28.69	104	37	67	13,196,250	9,551,218	3,645,032
32	Rakh Kotla	22.77	29	28	1	16,626,880	16,619,584	7,296
33	7 Gagh	10.99	37	34	3	10,518,820	10,182,071	336,749
	487/ JB Interchange	7.63	23	0	23	1,413,537	-	1,413,537
	Rakh Kotla Interchange	6.51	15	15	0	4,582,319	4,582,319	-
	<b>Total</b>	<b>1,214.46</b>	<b>3674</b>	<b>2718 (74.0%)</b>	<b>956 (26.0%)</b>	<b>647,925,690</b>	<b>605,407,194</b>	<b>42,518,496</b>



**Annex 2: Mouza-wise summary of Payment for Affected Structures**

Sr. No	Village	No of Displaced Household			Total Amount (Rs.)	Amount Disbursed (Rs.)	Balanced Amount (Rs.)
		Total	Paid	Un Paid			
<b>A</b>	<b>District TobaTek Singh</b>						
1	304/ JB	6	6	-	1,501,816	1,501,816	-
2	305/ JB	9	9	-	742,794	742,794	-
3	307/ JB	-	-	-	-	-	-
4	310/ JB	1	1	-	1,385,600	1,385,600	-
5	311/ JB	2	2	-	103,555	103,555	-
6	317/ JB	1	1	-	1,428,413	1,428,413	-
7	360/ JB	-	-	-	-	-	-
8	378/ JB	-	-	-	-	-	-
9	383/ JB	10	10	-	794,608	794,608	-
10	384/ JB	-	-	-	-	-	-
11	385/ JB	4	4	-	205,647	205,647	-
12	390/ JB	2	2	-	108,232	108,232	-
13	396/ JB	15	15	-	6,914,638	6,914,638	-
14	398/ JB	-	-	-	-	-	-
15	400/ JB	1	1	-	90,000	90,000	-
16	401/ JB	13	13	-	245,232	245,232	-
17	438/ JB	-	-	-	-	-	-
18	469/ JB	3	3	-	744,293	744,293	-
	383/ JB Interchange	9	4	5	403,577	165,735	237,842
19	388/ JB Interchange	1	1	-	39,768	39,768	-
	401/ JB Interchange	-	-	-	-	-	-
<b>B</b>	<b>District Jhang</b>						
22	487/ JB	3	3	-	631,447	631,447	-
23	488/ JB	3	3	-	175,420	175,420	-
24	489/ JB	10	10	-	1,190,099	1,190,099	-
25	490/ JB	1	1	-	1,078,654	1,078,654	-
26	406/ JB	7	7	-	148,140	148,140	-
27	505/ JB	-	-	-	-	-	-
28	494/ JB	6	6	-	433,605	433,605	-
29	496/ JB	5	5	-	459,600	459,600	-
30	Kalo Wala	12	12	-	3,500,359	3,500,359	-
31	500/ JB	4	4	-	673,006	673,006	-
32	504/ JB	8	8	-	2,259,584	2,259,584	-
33	501/ JB	13	13	-	1,368,883	1,368,883	-
34	Rakh Kotla	3	3	-	656,642	656,642	-
35	7 Gagh	9	9	-	4,390,939	4,390,939	-
36	487/ JB Interchange	-	-	-	-	-	-
37	Rakh Kotla Interchange	1	1	-	260,641	260,641	-
	<b>TOTAL</b>	<b>162</b>	<b>157</b> <b>96.9%</b>	<b>5</b> <b>3.1%</b>	<b>31,935,192</b>	<b>31,697,350</b>	<b>237,842</b>

### Annex3: Mouza-wise summary of Payment for Affected Trees (Fruit & Non-Fruit Trees)

Sr. No.	Village	No of Displaced Household			Total Amount (Rs.)	Amount Disbursed (Rs.)	Balanced Amount (Rs.)
		Total	Paid	Un Paid			
A	District Toba Tek	Singh					
1	304/ JB	3	3	0	132,058	132,058	0
2	305/ JB	22	21	1	2,374,755	2,357,206	17,549
3	307/ JB	24	24	0	1,676,245	1,676,245	0
4	310/ JB	16	16	0	604,744	604,744	0
5	311/ JB	29	28	1	1,667,197	1,619,437	47,760
6	317/ JB			0			0
8	360/ JB	3	3	0	215,944	215,944	0
7	378/ JB	18	18	0	2,673,532	2,673,532	0
9	383/ JB	38	38	0	13,263,563	13,263,563	0
10	384/ JB	19	19	0	5,408,735	5,408,735	0
11	385/ JB	20	20	0	8,372,389	8,372,389	0
12	390/ JB	16	16	0	5,172,608	5,172,608	0
13	396/ JB	14	14	0	2,745,610	2,745,610	0
14	398/ JB			0			0
15	400/ JB	5	5	0	498,676	498,676	0
16	401/ JB	38	38	0	4,336,742	4,336,742	0
17	438/ JB			0			0
18	469/ JB	11	11	0	437,869	411,394	26,475
	383/ JB Interchange	17	11	6	4,012,343	1,996,304	2,016,039
19	388/ JB Interchange	2	2	0	243,437	243,437	0
	401/ JB Interchange	6	5	1	610,231	358,943	251,288
B	District Jhang						
20	487/ JB	32	31	1	2,226,051	2,196,641	29,410
21	488/ JB	6	6	0	487,549	487,549	-
22	489/ JB	24	24	0	1,148,936	1,148,936	-
23	490/ JB	18	18	0	1,265,346	1,265,346	-
24	406/ JB	11	11	0	359,959	359,959	-
25	505/ JB	14	14	0	211,081	211,081	-
25	494/ JB	16	16	0	1,372,189	1,372,189	-
27	496/ JB	9	9	0	552,840	552,840	-
28	Kalo Wala	30	30	0	9,291,064	9,291,064	-
29	500/ JB	7	7	0	562,559	562,559	-
30	504/ JB	17	17	0	686,786	686,786	-
31	501/ JB	10	9	1	348,984	338,784	10,200
32	Rakh Kotla	8	8	0	385,744	385,744	-
33	7 Gagh	7	7	0	149,204	149,204	-
	487/ JB Interchange	2	0	2	22,338	-	22,338
	Rakh Kotla Interchange	1	1	0	165,911	165,911	-
	<b>TOTAL</b>	<b>513</b>	<b>500 (97.5%)</b>	<b>13 (2.5%)</b>	<b>73,683,219</b>	<b>71,262,160</b>	<b>2,421,059</b>

**Annex4: Payment for Crops**

Sr. No.	Village	No of Displaced Household			Total Amount (Rs.)	Amount Disbursed (Rs.)	Balanced Amount (Rs.)
		Total	Paid	Un Paid			
A	District Toba Tek Singh						
1	304/ JB	4	4	-	475,287	475,287	-
2	305/ JB	22	22	-	2,430,505	2,430,505	-
3	307/ JB	14	14	-	2,544,706	2,544,706	-
4	310/ JB	11	10	1	1,713,373	1,684,498	28,875
5	311/ JB	36	34	2	2,523,715	2,480,275	43,440
6	317/ JB	1	1	-	224,767	224,767	-
8	360/ JB	7	7	-	524,332	524,332	-
7	378/ JB	18	18	-	3,767,228	3,767,228	-
9	383/ JB	29	29	-	2,481,211	2,481,211	-
10	384/ JB	20	20	-	5,054,011	5,054,011	-
11	385/ JB	20	20	-	3,559,880	3,559,880	-
12	390/ JB	10	9	1	898,305	896,305	2,000
13	396/ JB	14	14	-	2,684,448	2,684,448	-
14	398/ JB	3	3	-	34,608	34,608	-
15	400/ JB	7	7	-	695,545	695,545	-
16	401/ JB	10	10	-	756,474	756,474	-
17	438/ JB			-			-
18	469/ JB	9	9	-	2,546,445	2,466,936	79,509
	383/ JB Interchange	20	12	8	1,431,218	842,748	588,470
19	388/ JB Interchange	3	3	-	469,475	469,475	0
	401/ JB Interchange	3	2	1	254,731	204,487	50,244
B	District Jhang						
20	487/ JB	21	20	1	1,558,245	1,508,520	49,725
21	488/ JB	7	7	-	695,845	695,845	-
22	489/ JB	22	22	-	1,342,520	1,342,520	-
23	490/ JB	17	17	-	2,037,140	2,037,140	-
24	406/ JB	12	12	-	516,044	516,044	-
25	505/ JB	5	5	-	496,056	496,056	-
25	494/ JB	9	9	-	790,696	790,696	-
27	496/ JB	9	9	-	959,807	959,807	-
28	Kalo Wala	29	29	-	3,779,146	3,779,146	-
29	500/ JB	12	12	-	1,689,031	1,689,031	-
30	504/ JB	17	17	-	2,516,116	2,516,116	-
31	501/ JB	8	7	1	1,392,407	1,126,758	265,649
32	Rakh Kotla	8	8	-	2,771,114	2,771,114	-
33	7 Gagh	8	6	2	693,450	686,700	6,750
	487/ JB Interchange	3	1	2	67,987	-	67,987
	Rakh Kotla Interchange	2	2	-	438,628	438,628	-
	<b>TOTAL</b>	<b>450</b>	<b>431 (95.8%)</b>	<b>19 (4.2%)</b>	<b>56,814,496</b>	<b>55,631,847</b>	<b>1,182,649</b>

**a) Additional Crop Compensation**

Sr. No	Village	No of Displaced Household			Total Amount (Rs.)	Amount Disbursed (Rs.)	Balanced Amount (Rs.)
		Total	Paid	UnPaid			
<b>A District TobaTek Singh</b>							
1	304/ JB	4	3	1	257,825	255,840	1,985
2	305/ JB	22	18	4	876,725	703,629	173,096
3	307/ JB	14	14	0	754,075	754,075	0
4	310/ JB	11		11	658,125		658,125
5	311/ JB	36		36	1,102,975		1,102,975
6	317/ JB	1	1	0	83,125	82,992	133
7	360/ JB	7		7	159,225		159,225
8	378/ JB	18		18	884,225		884,225
9	383/ JB	29		29	1,057,650		1,057,650
10	384/ JB	20	15	5	1,465,950	1,028,976	436,974
11	385/ JB	20	17	3	1,089,225	954,876	134,349
12	390/ JB	10	7	3	361,575	223,860	137,715
13	396/ JB	14	0	14	918,900		918,900
14	398/ JB	3	0	3	63,750		63,750
15	400/ JB	7	0	7	248,275		248,275
16	401/ JB	10	0	10	440,325		440,325
17	438/ JB		0	0	0		0
18	469/ JB	9	4	5	740,775	324,636	416,139
19	383/ JB Interchange	20	0	20	579,525		579,525
20	388/ JB Interchange	3	3	0	159,725	159,725	0
21	401/ JB Interchange	3	0	3	104,225		104,225
<b>B District Jhang</b>							
22	487/ JB	21	21	0	627,500	601068	26432
23	488/ JB	7	6	1	351,250	319176	32074
24	489/ JB	22	22	0	977,650	920088	57562
25	490/ JB	17	14	3	694,850	572052	122798
26	406/ JB	12	9	3	210,775	172224	38551
27	505/ JB	5	5	0	133,750	133,750	0
28	494/ JB	9	8	1	479,375	354120	125255
29	496/ JB	9	5	4	222,025	72384	149641
30	Kalo Wala	29	29	0	1,172,350	972036	200314
31	500/ JB	12	12	0	655,325	499044	156281
32	504/ JB	17	15	2	935,325	615108	320217
33	501/ JB	8	6	2	521,100	305448	215652
34	Rakh Kotla	8	6	2	560,475	284232	276243
35	7 Gagh	8	8	0	267,200	194688	72512
36	487/ JB Interchange	3		3	42,500		42500
37	Rakh Kotla Interchange	2		2	116,575		116575
	<b>TOTAL</b>	<b>450</b>	<b>248</b> <b>55.1%</b>	<b>202</b> <b>44.9%</b>	<b>19,974,225</b>	<b>10,504,027</b>	<b>9,470,198</b>

## Annex5: Mouza-wise summary of Payment for Allowances (Rehabilitation/ livelihood restoration)

### a) Resettlement Allowances

Sr. No	Village	No of Displaced Household			Total Amount (Rs.)	Amount Disbursed (Rs.)	Balanced Amount (Rs.)
		Total	Paid	Un Paid			
<b>A District TobaTek Singh</b>							
1	304/ JB	74	39	35	985,905	830,807	155,098
2	305/ JB	135	88	47	3,323,955	3,101,367	222,588
3	307/ JB	186	126	60	3,077,070	2,877,782	199,288
4	310/ JB	163	110	53	4,940,153	4,847,042	93,111
5	311/ JB	411	289	122	4,759,894	4,475,449	284,445
6	317/ JB	8	8	0	238,455	238,455	0
7	360/ JB	100	29	71	679,751	582,774	96,977
8	378/ JB	113	92	21	2,466,398	2,359,624	106,774
9	383/ JB	193	174	19	3,786,405	3,764,977	21,428
10	384/ JB	112	101	11	4,387,114	4,335,383	51,731
11	385/ JB	108	84	24	3,072,165	3,063,975	8,190
12	390/ JB	32	23	9	1,853,681	1,820,635	33,046
13	396/ JB	36	34	2	3,651,926	3,562,385	89,541
14	398/ JB	95	37	58	443,494	270,911	172,583
15	400/ JB	25	23	2	899,659	891,166	8,493
16	401/ JB	107	101	6	2,468,441	2,461,174	7,267
17	438/ JB	8	2	6	6,540	3,270	3,270
18	469/ JB	83	48	35	3,456,799	3,270,818	185,981
19	383/ JB Interchange						
20	388/ JB Interchange	10	10		461,476	461,476	
21	401/ JB Interchange	29	23	6	39,768	39,768	
<b>B District Jhang</b>							
22	487/ JB	118	76	42	3,024,750	2523650	501100
23	488/ JB	49	34	15	1,476,405	1458736	17669
24	489/ JB	212	153	59	2,902,534	2576975	325558.75
25	490/ JB	222	175	47	5,583,116	5157549	425567.25
26	406/ JB	75	55	20	1,749,041	1458037	291004.25
27	505/ JB	26	19	7	1,410,596	1296354	114242.25
28	494/ JB	88	73	15	2,138,171	1767814	370357.25
29	496/ JB	65	32	33	673,620	337291	336329
30	Kalo Wala	224	99	125	3,647,276	3355054	292222.25
31	500/ JB	92	52	40	1,755,990	1642381	113609
32	504/ JB	180	112	68	2,758,654	2046800	711853.75
33	501/ JB	104	34	70	1,876,163	1285954	590208.5
34	Rakh Kotla	29	29	0	1,892,307	1892307	0
35	7 Gagh	37	25	12	718,991	692996	25995.25
36	487/ JB Interchange	23		23	489,274		489273.75
37	Rakh Kotla Interchange	15		15	410,385		410385
	<b>TOTAL</b>	<b>3587</b>	<b>2409</b> <b>67.16%</b>	<b>1178</b> <b>32.84%</b>	<b>77,506,322</b>	<b>70,751,136</b>	<b>6,755,186</b>

**b) Livelihood Allowances**

Sr. No	Village	No of Displaced Household			Total Amount (Rs.)	Amount Disbursed (Rs.)	Balanced Amount (Rs.)
		Total	Paid	Un Paid			
<b>A District TobaTek Singh</b>							
1	304/ JB	4	1	3	158,520	39,630	118,890
2	305/ JB						
3	307/ JB						
4	310/ JB						
5	311/ JB						
6	317/ JB	1	0	1	39,630		39,630
7	360/ JB						
8	378/ JB						
9	383/ JB						
10	384/ JB						
11	385/ JB						
12	390/ JB						
13	396/ JB	4	3	1	158,520	128,108	30,412
14	398/ JB						
15	400/ JB						
16	401/ JB						
17	438/ JB						
18	469/ JB						
19	383/ JB Interchange						
20	388/ JB Interchange						
21	401/ JB Interchange						
<b>B District Jhang</b>							
22	487/ JB						
23	488/ JB						
24	489/ JB						
25	490/ JB						
26	406/ JB						
27	505/ JB						
28	494/ JB						
29	496/ JB						
30	Kalo Wala	3	2	1	118,080	79260	38820
31	500/ JB	1	1		39,630	39630	
32	504/ JB	1	1		39,630	39630	
33	501/ JB	4	3	1	151,582	144647	6935
34	Rakh Kotla	0					
35	7 Gagh	3	3		118,890	118890	
36	487/ JB Interchange						
37	Rakh Kotla Interchange						
	<b>TOTAL</b>	<b>21</b>	<b>14</b> 66.7%	<b>7</b> 33.3%	<b>824,482</b>	<b>589,795</b>	<b>234,687</b>

**c) Transport Allowances**

Sr. No	Village	No of Displaced Household			Total Amount (Rs.)	Amount Disbursed (Rs.)	Balanced Amount (Rs.)
		Total	Paid	Un Paid			
<b>A District TobaTek Singh</b>							
1	304/ JB	5	1	4	85,000	15,000	70,000
2	305/ JB	-	-	-	-	-	-
3	307/ JB	-	-	-	-	-	-
4	310/ JB	1	1	-	25,000	15,000	10,000
5	311/ JB	1	1	-	10,000	10,000	0
6	317/ JB	1	1	-	15,000	6,000	9,000
7	360/ JB	-	-	-	-	-	-
8	378/ JB	-	-	-	-	-	-
9	383/ JB	1	1	-	10,000	10,000	0
10	384/ JB	-	-	-	-	-	-
11	385/ JB	1	1	-	10,000	10,000	0
12	390/ JB	1	1	-	10,000	10,000	0
13	396/ JB	9	8	1	80,000	47,998	32,002
14	398/ JB	-	-	-	-	-	-
15	400/ JB	-	-	-	-	-	-
16	401/ JB	1	1	0	10,000	10,000	0
17	438/ JB	-	-	-	-	-	-
18	469/ JB	-	-	-	-	-	-
19	383/ JB Interchange	2	2	0	20,000	20,000	0
20	388/ JB Interchange	-	-	-	-	-	-
<b>B District Jhang</b>							
22	487/ JB	1	1	0	20,000	20000	0
23	488/ JB	-	-	-	-	-	-
24	489/ JB	1	-	1	10,000	-	10000
25	490/ JB	1	1	0	30,000	30000	0
26	406/ JB	-	-	-	-	-	-
27	505/ JB	-	-	-	-	-	-
28	494/ JB	3	2	1	40,000	20000	20000
29	496/ JB	5	0	5	65,000	-	65000
30	Kalo Wala	6	6	0	85,000	85000	-
31	500/ JB	3	3	0	45,000	45000	-
32	504/ JB	5	3	2	65,000	45000	20000
33	501/ JB	7	7	0	100,000	100000	-
34	Rakh Kotla	3	3	0	30,000	30,000	-
35	7 Gagh	4	4	0	55,000	55000	-
36	487/ JB Interchange	-	-	-	-	-	-
37	Rakh Kotla Interchange	1	1	0	10,000	10000	0
	<b>TOTAL</b>	<b>63</b>	<b>49</b>	<b>14</b>	<b>830,000</b>	<b>593,998</b>	<b>236,002</b>
			<b>77.8%</b>	<b>22.2%</b>			

**d) Business Allowances**

Sr. No	Village	No of Displaced Household			Total Amount (Rs.)	Amount Disbursed (Rs.)	Balanced Amount (Rs.)
		Total	Paid	Un Paid			
<b>A District TobaTek Singh</b>							
1	304/ JB	1		1	79,260		79,260
2	305/ JB						
3	307/ JB						
4	310/ JB	1	1		210,000	210,000	
5	311/ JB	1	1		39,630	39,630	
6	317/ JB						
7	360/ JB						
8	378/ JB						
9	383/ JB	1	1		39,630	39,630	
10	384/ JB						
11	385/ JB	3	2	1	118,890	79,260	39,630
12	390/ JB	1	1	0	39,630	39,630	0
13	396/ JB	2	1	1	79,260	39,630	39,630
14	398/ JB						
15	400/ JB						
16	401/ JB	1	1		39,630	39,630	
17	438/ JB						
18	469/ JB						
19	383/ JB Interchange	2		2	79,260	0	79,260
20	388/ JB Interchange			0			0
21	401/ JB Interchange			0			0
<b>B District Jhang</b>							
22	487/ JB	1	1	0	79,260	79260	0
23	488/ JB	0		0			0
24	489/ JB	1		1	39,630		39630
25	490/ JB	1	1	0	118,890	118890	0
26	406/ JB	0		0			0
27	505/ JB	0		0			0
28	494/ JB	2	2	0	79,260	79260	0
29	496/ JB	4		4	198,150		198150
30	Kalo Wala	4	4	0	158,520	158520	0
31	500/ JB	3	3	0	118,890	118890	0
32	504/ JB	5	3	2	198,150	118890	79260
33	501/ JB	4	4	0	158,520	158520	0
34	Rakh Kotla	3	3	0	118,890	118,890	0
35	7 Gagh	1	1	0	39,630	39630	0
36	487/ JB Interchange	0		0			0
37	Rakh Kotla Interchange	1	1	0	39,630	39630	0
	<b>TOTAL</b>	<b>43</b>	<b>31</b> 72.1%	<b>12</b> 27.9%	<b>2,072,610</b>	<b>1,517,790</b>	<b>554,820</b>



**e) Vulnerable Allowances**

Sr. No	Village	No of Displaced Household			Total Amount (Rs.)	Amount Disbursed (Rs.)	Balanced Amount (Rs.)
		Total	Paid	Un Paid			
<b>A</b>	<b>District TobaTek Singh</b>						
1	304/ JB	5	1	4	198,150	39,630	158,520
2	305/ JB	1	1	-	39,630	39,630	-
3	307/ JB	1	1	-	39,630	39,630	-
4	310/ JB	-	-	-	-	-	-
5	311/ JB	1	1	-	39,630	39,630	-
6	317/ JB	1	0	1	39,630		39,630
7	360/ JB	-	-	-	-	-	-
8	378/ JB	1	1	-	39,630	39,630	-
9	383/ JB	-	-	-	-	-	-
10	384/ JB	-	-	-	-	-	-
11	385/ JB	-	-	-	-	-	-
12	390/ JB	-	-	-	-	-	-
13	396/ JB	3	3	-	118,890	118,890	-
14	398/ JB	-	-	-	-	-	-
15	400/ JB	-	-	-	-	-	-
16	401/ JB	1	1	-	39,630	39,630	-
17	438/ JB	-	-	-	-	-	-
18	469/ JB	2	0	2	79,260	79,260	-
19	383/ JB Interchange	-	-	-	-	-	-
20	388/ JB Interchange	-	-	-	-	-	-
21	401/ JB Interchange	-	-	-	-	-	-
<b>B</b>	<b>District Jhang</b>						
22	487/ JB	-	-	-	-	-	-
23	488/ JB	-	-	-	-	-	-
24	489/ JB	-	-	-	-	-	-
25	490/ JB	-	-	-	-	-	-
26	406/ JB	-	-	-	-	-	-
27	505/ JB	-	-	-	-	-	-
28	494/ JB	-	-	-	-	-	-
29	496/ JB	-	-	-	-	-	-
30	Kalo Wala	2	2	-	79,260	79,260	-
31	500/ JB	-	-	-	-	-	-
32	504/ JB	-	-	-	-	-	-
33	501/ JB	1	1	-	39,630	39,630	-
34	Rakh Kotla	-	-	-	-	-	-
35	7 Gagh	3	1	2	118,890	39,630	79,260
36	487/ JB Interchange	-	-	-	-	-	-
37	Rakh Kotla Interchange	-	-	-	-	-	-
	<b>TOTAL</b>	<b>22</b>	<b>13</b> <b>59.1%</b>	<b>9</b> <b>40.9%</b>	<b>871,860</b>	<b>594,450</b>	<b>277,410</b>

**f) Employment Losses Allowances**

Sr. No.	Village	No of DPs			Total Amount (Rs.)	Amount Disbursed (Rs.)	Balanced Amount (Rs.)	Amount Disbursed (%age)
		Total	Paid	Un Paid				
A	District Toba Tek	Singh						
1	304/ JB	-	-	-	-	-	-	-
2	305/ JB	-	-	-	-	-	-	-
3	307/ JB	-	-	-	-	-	-	-
4	310/ JB	5	-	5	198,150	-	198150	0%
5	311/ JB	-	-	-	-	-	-	-
6	317/ JB	-	-	-	-	-	-	-
8	360/ JB	-	-	-	-	-	-	-
7	378/ JB	-	-	-	-	-	-	-
9	383/ JB	-	-	-	-	-	-	-
10	384/ JB	-	-	-	-	-	-	-
11	385/ JB	-	-	-	-	-	-	-
12	390/ JB	-	-	-	-	-	-	-
13	396/ JB	-	-	-	-	-	-	-
14	398/ JB	-	-	-	-	-	-	-
15	400/ JB	-	-	-	-	-	-	-
16	401/ JB	-	-	-	-	-	-	-
17	438/ JB	-	-	-	-	-	-	-
18	469/ JB	-	-	-	-	-	-	-
19	388/ JB Interchange	-	-	-	-	-	-	-
	401/ JB Interchange	-	-	-	-	-	-	-
B	District Jhang							
20	487/ JB	1	-	1	39,630	-	39,630	0%
21	488/ JB	-	-	-	-	-	-	-
22	489/ JB	-	-	-	-	-	-	-
23	490/ JB	-	-	-	-	-	-	-
24	406/ JB	-	-	-	-	-	-	-
25	505/ JB	-	-	-	-	-	-	-
25	494/ JB	-	-	-	-	-	-	-
27	496/ JB	-	-	-	-	-	-	-
28	Kalo Wala	-	-	-	-	-	-	-
29	500/ JB	-	-	-	-	-	-	-
30	504/ JB	-	-	-	-	-	-	-
31	501/ JB	-	-	-	-	-	-	-
32	Rakh Kotla	-	-	-	-	-	-	-
33	7 Gagh	-	-	-	-	-	-	-
	487/ JB Interchange	-	-	-	-	-	-	-
	Rakh Kotla Interchange	-	-	-	-	-	-	-
	<b>Total</b>	<b>6</b>	<b>- (0%)</b>	<b>6 (100%)</b>	<b>237,780</b>		<b>237780</b>	<b>0%</b>

**g) Replacement Cost**

Sr. No	Village	No of Displaced Household			Total Amount (Rs.)	Amount Disbursed (Rs.)	Balanced Amount (Rs.)
		Total	Paid	Un Paid			
<b>A District TobaTek Singh</b>							
1	304/ JB	74		74	2,211,867		2,211,867
2	305/ JB	135	82	53	2,024,868	1,645,890	378,978
3	307/ JB	186	128	58	1,874,472	1,721,999	152,473
4	310/ JB	163	0	163	2,332,598		2,332,598
5	311/ JB	411	0	411	2,247,485		2,247,485
6	317/ JB	8	8	0	95,228	95,224	4
7	360/ JB	-	-	-	-	-	-
8	378/ JB	-	-	-	-	-	-
9	383/ JB	-	-	-	-	-	-
10	384/ JB	-	-	-	-	-	-
11	385/ JB	-	-	-	-	-	-
12	390/ JB	-	-	-	-	-	-
13	396/ JB	36	0	36	2,211,867		2,211,867
14	398/ JB	95	29	66	194,215	109,847	84,368
15	400/ JB	25	0	25	393,979		393,979
16	401/ JB	-	-	-	-	-	-
17	438/ JB	-	-	-	-	-	-
18	469/ JB	83	0	83	48,330		48,330
19	388/ JB Interchange	-	-	-	-	-	-
20	401/ JB Interchange	-	-	-	-	-	-
<b>B District Jhang</b>							
22	487/ JB	31	20	11	1,150,640	727686	422954
23	488/ JB	-	-	-	-	-	-
24	489/ JB	-	-	-	-	-	-
25	490/ JB	-	-	-	-	-	-
26	406/ JB	-	-	-	-	-	-
27	505/ JB	-	-	-	-	-	-
28	494/ JB	-	-	-	-	-	-
29	496/ JB	-	-	-	-	-	-
30	Kalo Wala	-	-	-	-	-	-
31	500/ JB	-	-	-	-	-	-
32	504/ JB	-	-	-	-	-	-
33	501/ JB	-	-	-	-	-	-
34	Rakh Kotla	-	-	-	-	-	-
35	7 Gagh	-	-	-	-	-	-
36	487/ JB Interchange	-	-	-	-	-	-
37	Rakh Kotla Interchange	-	-	-	-	-	-
	<b>TOTAL</b>	<b>1247</b>	<b>267</b> <b>21.4%</b>	<b>980</b> <b>78.6%</b>	<b>14,785,549</b>	<b>4,300,646</b>	<b>10,484,903</b>

**h) Electricity Allowances**

Sr. No	Village	No of Displaced Household			Total Amount (Rs.)	Amount Disbursed (Rs.)	Balanced Amount (Rs.)
		Total	Paid	Un Paid			
<b>A District TobaTek Singh</b>							
1	304/ JB	5	1	4	200,000	40,000	160,000
2	305/ JB	0	0	0	0		0
3	307/ JB	0	0	0	0		0
4	310/ JB	1	0	1	40,000		40,000
5	311/ JB	0	0	0	0		0
6	317/ JB	1	0	1	40,000		40,000
7	360/ JB	0	0	0	0		0
8	378/ JB	0	0	0	0		0
9	383/ JB	0	0	0	0		0
10	384/ JB	0	0	0	0		0
11	385/ JB	0	0	0	0		0
12	390/ JB	0	0	0	0		0
13	396/ JB	4	2	2	160,000	80,000	80,000
14	398/ JB	0	0	0	0		0
15	400/ JB	0	0	0	0		0
16	401/ JB	0	0	0	0		0
17	438/ JB	0	0	0	0		0
18	469/ JB	0	0	0	0		0
19	388/ JB Interchange	0	0	0	0		0
20	401/ JB Interchange		0	0			0
<b>B District Jhang</b>							
22	487/ JB	1	1	0	40,000	40000	0
23	488/ JB	0		0	0		0
24	489/ JB	0		0	0		0
25	490/ JB	1	1	0	40,000	40000	0
26	406/ JB	0		0	0		0
27	505/ JB	0		0	0		0
28	494/ JB	1		1	40,000		40000
29	496/ JB	2		2	80,000		80000
30	Kalo Wala	2	2	0	80,000	80000	0
31	500/ JB	1		1	40,000		40000
32	504/ JB	1	1	0	40,000	40000	0
33	501/ JB	4	1	3	160,000	40000	120000
34	Rakh Kotla	0		0	0		0
35	7 Gagh	3	3	0	120,000	120000	0
36	487/ JB Interchange			0			0
37	Rakh Kotla Interchange			0			0
	<b>TOTAL</b>	<b>27</b>	<b>12</b> <b>44.4%</b>	<b>15</b> <b>55.6%</b>	<b>1,080,000</b>	<b>480,000</b>	<b>600,000</b>

**i) House Rent Allowances**

Sr. No	Village	No of Displaced Household			Total Amount (Rs.)	Amount Disbursed (Rs.)	Balanced Amount (Rs.)
		Total	Paid	Un Paid			
<b>A District TobaTek Singh</b>							
1	304/ JB	4	1	3	144,000	36,000	108,000
2	305/ JB	-	-	-	-	-	-
3	307/ JB	-	-	-	-	-	-
4	310/ JB	-	-	-	-	-	-
5	311/ JB	-	-	-	-	-	-
6	317/ JB	1	-	1	36,000	-	36,000
7	360/ JB	-	-	-	-	-	-
8	378/ JB	-	-	-	-	-	-
9	383/ JB	-	-	-	-	-	-
10	384/ JB	-	-	-	-	-	-
11	385/ JB	-	-	-	-	-	-
12	390/ JB	-	-	-	-	-	-
13	396/ JB	4	4	0	144,000	144,000	0
14	398/ JB	-	-	-	-	-	-
15	400/ JB	-	-	-	-	-	-
16	401/ JB	-	-	-	-	-	-
17	438/ JB	-	-	-	-	-	-
18	469/ JB	-	-	-	-	-	-
19	388/ JB Interchange	-	-	-	-	-	-
20	401/ JB Interchange	-	-	-	-	-	-
<b>B District Jhang</b>							
22	487/ JB	-	-	-	-	-	-
23	488/ JB	-	-	-	-	-	-
24	489/ JB	-	-	-	-	-	-
25	490/ JB	-	-	-	-	-	-
26	406/ JB	-	-	-	-	-	-
27	505/ JB	-	-	-	-	-	-
28	494/ JB	-	-	-	-	-	-
29	496/ JB	1	-	1	40,000	-	40000
30	Kalo Wala	3	2	1	120,000	72000	48000
31	500/ JB	1	1	0	40,000	36000	4000
32	504/ JB	1	1	0	40,000	36000	4000
33	501/ JB	4	4	0	160,000	123000	37000
34	Rakh Kotla	3	3	0	108,000	108000	0
35	7 Gagh	3	3	0	120,000	108000	12000
36	487/ JB Interchange	-	-	-	-	-	-
37	Rakh Kotla Interchange	-	-	-	-	-	-
	<b>TOTAL</b>	<b>25</b>	<b>19</b> <b>76.0%</b>	<b>6</b> <b>24.0%</b>	<b>952,000</b>	<b>663,000</b>	<b>289,000</b>

**Annex6: Schedule Visits of LAC M-4 Section-II Toba Tek Singh**

شیدول دورہ پروگرام ہارون الرشید درانی لینڈ ایکویزیشن گلبرائیم-4 سیکشن-II NHA کی پیس آفس ٹوبہ ٹیک سنگھ  
بلسلسلہ ملاقات Unpaid Aps پابست تقسیم کیے جانے معاوضہ زمین فصلات درختاں سٹرکچر مکان وغیرہ سیکشن-II ایم-4

نمبر شمار	تاریخ	ہم پیک	تفصیل وطن	نوعیت کام	کیلیت
1	1-01-2016	304	گوہڑوہ پیک سنگھ	ملاقات Unpaid Aps دینے جانے معاوضہ	
2	4-01-2016	305	گوہڑوہ پیک سنگھ	ملاقات Unpaid Aps دینے جانے معاوضہ	
3	4-01-2016	307	گوہڑوہ پیک سنگھ	ملاقات Unpaid Aps دینے جانے معاوضہ	
4	5-01-2016	310	گوہڑوہ پیک سنگھ	ملاقات Unpaid Aps دینے جانے معاوضہ	
5	6-01-2016	438	گوہڑوہ پیک سنگھ	ملاقات Unpaid Aps دینے جانے معاوضہ	
6	7-01-2016	378	ٹوبہ ٹیک سنگھ	ملاقات Unpaid Aps دینے جانے معاوضہ	
7	8-01-2016	385	ٹوبہ ٹیک سنگھ	ملاقات Unpaid Aps دینے جانے معاوضہ	
8	11-01-2016	384	ٹوبہ ٹیک سنگھ	ملاقات Unpaid Aps دینے جانے معاوضہ	
9	12-01-2016	390,363	ٹوبہ ٹیک سنگھ	ملاقات Unpaid Aps دینے جانے معاوضہ	
10	13-01-2016	396,469	ٹوبہ ٹیک سنگھ	ملاقات Unpaid Aps دینے جانے معاوضہ	
11	14-01-2016	400,398	ٹوبہ ٹیک سنگھ	ملاقات Unpaid Aps دینے جانے معاوضہ	
12	15-01-2016	401	ٹوبہ ٹیک سنگھ	ملاقات Unpaid Aps دینے جانے معاوضہ	
13	18-01-2016	487	شورکوٹ جنگ	ملاقات Unpaid Aps دینے جانے معاوضہ	
14	19-01-2016	488	شورکوٹ جنگ	ملاقات Unpaid Aps دینے جانے معاوضہ	
15	20-01-2016	490	شورکوٹ جنگ	ملاقات Unpaid Aps دینے جانے معاوضہ	
16	21-01-2016	505,406	شورکوٹ جنگ	ملاقات Unpaid Aps دینے جانے معاوضہ	
17	22-01-2016	494	شورکوٹ جنگ	ملاقات Unpaid Aps دینے جانے معاوضہ	
18	25-01-2016	496	شورکوٹ جنگ	ملاقات Unpaid Aps دینے جانے معاوضہ	
19	26-01-2016	کاوال پیک	شورکوٹ جنگ	ملاقات Unpaid Aps دینے جانے معاوضہ	
20	27-01-2016	500	شورکوٹ جنگ	ملاقات Unpaid Aps دینے جانے معاوضہ	
21	28-01-2016	504	شورکوٹ جنگ	ملاقات Unpaid Aps دینے جانے معاوضہ	
22	28-01-2016	501	شورکوٹ جنگ	ملاقات Unpaid Aps دینے جانے معاوضہ	
23	29-01-2016	7 کلاں کنگھ	شورکوٹ جنگ	ملاقات Unpaid Aps دینے جانے معاوضہ	

Land Acquisition Collector  
لینڈ ایکویزیشن گلبرائیم-4  
سیکشن-II NHA ٹوبہ ٹیک سنگھ

دورہ پروگرام برائے اطلاع پیش نمونہ ہے۔

کاپی برائے اطلاع / تقسیم  
ڈائریکٹر لینڈ ایم-4 NHA فیصل آباد  
اسسٹنٹ ڈائریکٹر لینڈ ایم-4 NHA فیصل آباد

شیڈول / دورہ پورسکرام اور انٹریڈر ڈرائی لینڈ اینڈ پورسکرام پلاٹ 4 ایم 4 سیکشن 11/11/15 میں اسٹریٹ لائٹس کی انسٹالیشن کے لیے سلسلہ مددات Un Paid APS باقی بقیہ کے لیے صارفین سے وصول شدہ روٹان سٹریٹ لائٹس کی انسٹالیشن کے لیے 4 ایم 4

میزانہ	تاریخ	نام حکومت	نوعیت تمام	کیفیت
1	1-12-15	7-304	مددات APS	
2	2-12-15	7-305		
3	3-12-15	7-307		
4	4-12-15	2-366-316		
5	7-12-15	2-317-430		
6	8-12-15	2-378		
7	9-12-15	7-385		
8	10-12-15	2-384		
9	11-12-15	370-383		
10	14-12-15	2376-469		
11	15-12-15	400-398		
12	16-12-15	2-401		
13	17-12-15	2-487		
14	18-12-15	2-488		
15	21-12-15	490		
16	22-12-15	$\frac{505}{2} - \frac{405}{2}$		
17	23-12-15	494		
18	24-12-15	496		
19	25-12-15	کانوولر		
20	28-12-15	2-500		
21	29-12-15	2-504		
22	30-12-15	501		
23	31-12-15	2-502		

Created by M4 Section II 2015 No. 11/11/15

11/11/15  
 11-11-15  
 11-11-15

11/11/15  
 11-11-15  
 11-11-15

شیڈول دورہ پروگرام ہارون الرشید درانی لینڈ ایکویزیشن گلنگرا ایم-4 سیکشن-II NHA کیسپس آفس ٹوپیک سٹھ  
بلسلسلہ ملاقات Unpaid Aps باہت تقسیم کیے جانے معاوضہ میں فصلات درختاں سڑکچر مکان وغیرہ سیکشن-II ایم-4

نمبر شمار	تاریخ	نام پیک	تحصیل وطن	نوعیت کام	کیلیت
1	2-11-2015	304 ٹا ب	گوڑو ٹوپیک سٹھ	ملاقات Unpaid Aps دینے جانے معاوضہ	
2	3-11-2015	305 ٹا ب	گوڑو ٹوپیک سٹھ	ملاقات Unpaid Aps دینے جانے معاوضہ	
3	4-11-2015	307 ٹا ب	گوڑو ٹوپیک سٹھ	ملاقات Unpaid Aps دینے جانے معاوضہ	
4	5-11-2015	310 ٹا ب	گوڑو ٹوپیک سٹھ	ملاقات Unpaid Aps دینے جانے معاوضہ	
5	6-11-2015	438 ٹا ب	گوڑو ٹوپیک سٹھ	ملاقات Unpaid Aps دینے جانے معاوضہ	
6	9-11-2015	378 ٹا ب	ٹوپیک سٹھ	ملاقات Unpaid Aps دینے جانے معاوضہ	
7	10-11-2015	385 ٹا ب	ٹوپیک سٹھ	ملاقات Unpaid Aps دینے جانے معاوضہ	
8	11-11-2015	384 ٹا ب	ٹوپیک سٹھ	ملاقات Unpaid Aps دینے جانے معاوضہ	
9	12-11-2015	390,383 ٹا ب	ٹوپیک سٹھ	ملاقات Unpaid Aps دینے جانے معاوضہ	
10	13-11-2015	396,469 ٹا ب	ٹوپیک سٹھ	ملاقات Unpaid Aps دینے جانے معاوضہ	
11	16-11-2015	400,398 ٹا ب	ٹوپیک سٹھ	ملاقات Unpaid Aps دینے جانے معاوضہ	
12	17-11-2015	401 ٹا ب	ٹوپیک سٹھ	ملاقات Unpaid Aps دینے جانے معاوضہ	
13	18-11-2015	487 ٹا ب	شورکوٹ جنگ	ملاقات Unpaid Aps دینے جانے معاوضہ	
14	19-11-2015	488 ٹا ب	شورکوٹ جنگ	ملاقات Unpaid Aps دینے جانے معاوضہ	
15	20-11-2015	490 ٹا ب	شورکوٹ جنگ	ملاقات Unpaid Aps دینے جانے معاوضہ	
16	23-11-2015	505,406 ٹا ب	شورکوٹ جنگ	ملاقات Unpaid Aps دینے جانے معاوضہ	
17	24-11-2015	494 ٹا ب	شورکوٹ جنگ	ملاقات Unpaid Aps دینے جانے معاوضہ	
18	25-11-2015	496 ٹا ب	شورکوٹ جنگ	ملاقات Unpaid Aps دینے جانے معاوضہ	
19	26-11-2015	کاوال ٹا ب	شورکوٹ جنگ	ملاقات Unpaid Aps دینے جانے معاوضہ	
20	26-11-2015	500 ٹا ب	شورکوٹ جنگ	ملاقات Unpaid Aps دینے جانے معاوضہ	
21	27-11-2015	504 ٹا ب	شورکوٹ جنگ	ملاقات Unpaid Aps دینے جانے معاوضہ	
22	30-11-2015	501 ٹا ب	شورکوٹ جنگ	ملاقات Unpaid Aps دینے جانے معاوضہ	
23	30-11-2015	72 کلا کٹھ	شورکوٹ جنگ	ملاقات Unpaid Aps دینے جانے معاوضہ	

Collector  
Land Acquisition Authority  
لینڈ ایکویزیشن گلنگرا ایم-4  
سیکشن-II NHA ٹوپیک سٹھ

دورہ پروگرام برائے اطلاع پیش فرمت ہے۔

کانیا برائے اطلاع / تقسیم  
ڈائریکٹر لینڈ ایم-4 NHA فیصل آباد  
اسسٹنٹ ڈائریکٹر لینڈ ایم-4 NHA فیصل آباد



Annex7: Sample Site Visit Report of LAC M-4 Section-II Toba Tek Singh

انجمن صنفی 20/11/2016 کو 406 نمبر کے شہریوں کے ساتھ گفتگو کی گئی۔  
 وزیر صحت کے دفتر میں صنفی نمبر 406 کے شہریوں کے ساتھ گفتگو کی گئی۔  
 ان کے پاس زمین کی سند ہے اور ان کے پاس زمین کی سند ہے۔  
 ان کے پاس زمین کی سند ہے اور ان کے پاس زمین کی سند ہے۔  
 ان کے پاس زمین کی سند ہے اور ان کے پاس زمین کی سند ہے۔  
 ان کے پاس زمین کی سند ہے اور ان کے پاس زمین کی سند ہے۔

Land Acquisition Collector  
 National Highway Authority  
 M-4 Section II  
 20/11/2016

نوٹ: ان کے پاس زمین کی سند ہے اور ان کے پاس زمین کی سند ہے۔

Land Acquisition Collector  
 National Highway Authority  
 M-4 Section II  
 20/11/2016

نائب  
 اہل کار اور شہریوں کے

نائب  
 اہل کار اور شہریوں کے

امان اللہ خان

نائب

نمبر دار  
 امان اللہ خان پلاٹ نمبر 406  
 0346-5035406

انجمن صوفیہ 22/12/2005 کو جنرل انسٹی ٹیوشن اور اعلیٰ ثانوی اسکول  
 لاہور سٹیٹس ایف ایم 4 واقعہ حکیم 406 تحصیل شوروٹ ضلع حیدرآباد  
 موہن پور ضلع موہن پور APC اور GRE کی کمیٹی جبران کی موجودگی میں  
 لاہور اسکول میں منعقد ہونے والے جلسہ کو اہتمام و نوٹس لینے کے لئے جسے  
 کروہ اپنے اپنے مقامات پر اجلاس منعقد کروائے گئے۔  
 انجلس سے وصول کر لیں اور اپنے وقت کے پتوں سامنے  
 لائیں اور کمیٹی جبران سے دستخط کروائے گئے۔

محمد رفیق اور محمد جبران نے اس بات کی تصدیق کی کہ  
 Land Acquisition Collector  
 National Highway Authority  
 M4 Sec-II  
 محمد اسحاق احمد مولوی ایم 4  
 22/12/2005  
 محمد اسحاق احمد مولوی ایم 4

محمد اسحاق احمد مولوی صدر کمیٹی	محمد اسحاق احمد مولوی	محمد اسحاق احمد مولوی
محمد اسحاق احمد مولوی	محمد اسحاق احمد مولوی	محمد اسحاق احمد مولوی
محمد اسحاق احمد مولوی	محمد اسحاق احمد مولوی	محمد اسحاق احمد مولوی
محمد اسحاق احمد مولوی	محمد اسحاق احمد مولوی	محمد اسحاق احمد مولوی

محمد اسحاق احمد مولوی  
 محمد اسحاق احمد مولوی  
 محمد اسحاق احمد مولوی  
 محمد اسحاق احمد مولوی

انٹرنل منیٹرنگ رپورٹ نمبر 406  
 2015  
 تقسیم شدہ زمین کے بارے میں  
 تفصیلات فراہم کرنے کے لیے  
 تمام متعلقہ اداروں کو مطلع کیا گیا ہے  
 اور ان کے ذریعے زمین کی تفصیلات  
 فراہم کی جائیں گی۔



محمد شعیب  
 نخلہ، رسول  
 محمد عرفان، محمد شعیب، محمد رسول، دلا احمد، سید ابرار، دلا احمد، محمد شعیب، محمد شعیب، محمد شعیب

محمد شعیب  
 محمد شعیب

محمد شعیب

## Annex8: Sample Notices for Payment of Compensation for unpaid DPs

بعدالت جناب کلکٹر حصول اراضی (ایم-4 سکیشن-II)

مجلس ہائی وے اتھارٹی ٹیپ آفس مکان نمبر 19، پنجواں منڈی، لاہور، پنجاب، پاکستان

﴿نوٹس﴾

بنام: خود سر اجودہ بی نورز - عبد الغفور وار لکھو - مرزا کاؤ دیا لہر - سر فرزانہ - محمد عامر - عابد حسین - محمد صالح

محمد ارون، محمد ارون، محمد ارون، حضرت ذفر حسن علی، نایب محمد احمد صلیب، خمدار بلال، محمد سلیم، محمد

چک نمبر: 906 تحصیل: مشرقی ضلع: حیدرآباد

آپ کو بذریعہ نوٹس ہذا مطلع کیا جاتا ہے۔ کہ آپ اپنا معاوضہ زمین، فصلات، درختان، سڑک پتھر (مکانات) وغیرہ زبردستی کے آفس سے 15 یوم کے اندر وصول کر لیں۔ ورنہ بصورت دیگر جملہ واجب الادا رقم متاثرین اراضی زبردستہ 31 حصول ایکٹ اراضی 1894 کے تحت بعدالت جناب سیکرٹری ہولڈنگ صاحب ہینڈل جمع کروادی جائے گی اور بعد میں کوئی نقد رقم قابل قبول نہ ہوگا۔

کلکٹر حصول اراضی (ایم-4 سکیشن-II)

مکان نمبر 19، پنجواں منڈی، لاہور، پنجاب، پاکستان

محمد ارون، محمد ارون، محمد ارون، حضرت ذفر حسن علی، نایب محمد احمد صلیب، خمدار بلال، محمد سلیم، محمد

چک نمبر: 906 تحصیل: مشرقی ضلع: حیدرآباد

محمد صالح

M. H. Sial

**نوٹیشن برائے اطلاع یابی**  
**نیشنل ہائی وے اتھارٹی**  
**فیصل آباد۔ ملتان موٹروے پراجیکٹ (M-4)**  
**سیکشن - II**

کمری و بھڑی : **محمد سعید**  
 موش / پنک / اکاؤنٹ : **406**  
 تحصیل : **سکرپٹ**  
 ضلع : **جھنگ**

عنوان : **نوٹیشن بابت ادائیگی معاوضہ زمین، فصلات، درخت، سڑک کچر وغیرہ**

آپ کو بذریعہ نوٹیشن مطلع کیا جاتا ہے کہ آپ کی زمین فیصل آباد۔ ملتان موٹروے پراجیکٹ (M-4) میں آگئی ہے۔ لہذا اس سلسلے میں آپ سے گزارش ہے کہ مندرجہ ذیل معاوضہ جات کی وصولی کیلئے اپنے تمام کاغذات متعلقہ لینڈ ایکویزیشن کلکٹر صاحب، سیکشن - II موٹروے پراجیکٹ (M-4)، نیشنل ہائی وے اتھارٹی، مکان نمبر 11/11 انور سٹریٹ، ہائی وے سیکشن میں جمع کرائیں۔ آپ کو اس سے پہلے کسی نوٹیشن دیے جاتے ہیں۔ تاکہ آپ اپنا معاوضہ 15 گھنٹے تک وصول کر لیں۔ بصورت دیگر زیر دفعہ LAA-31، 1894 کے تحت بعد اہل جناب سٹیٹ سول جج صاحب جمع کروایا جائے گا۔

زمین : \_\_\_\_\_  
 فصلات : \_\_\_\_\_  
 درخت : \_\_\_\_\_  
 سڑک کچر : \_\_\_\_\_  
 میزان : \_\_\_\_\_

دستخط وصول کنندہ : \_\_\_\_\_  
 موبائل نمبر : \_\_\_\_\_  
 دستخط نمبر دار / پتی دار : \_\_\_\_\_

مطلوبہ کو آف جمن میں فراہم کیا گیا۔ شناختی کارڈ سائل، شناختی کارڈ آئڈنٹیفیکیشن (فونو کاپی)، بیان حلفی جمع کرنا۔

**Collection Collector**  
**M-4**  
**سیکشن - II نیشنل ہائی وے اتھارٹی**

**Annex9: Deposit of Fund in Treasury**  
District Treasury Toba Tek Singh

لیڈنگ اسٹیٹمنٹ (پیشین 05) (پیشین 05) (پیشین 05) کے مطابق  
 کمیٹی آف انسپکٹرز جنرل  
 ڈسٹرکٹ اکاؤنٹس آفیس ٹوبا ٹیک سنگھ

08/03/16  
 LAC / NHA / MA / Sec 8(5) / 2015 / 689

فریڈمی آرڈر کی دائرہ میں جیت منیفل: پورٹا ٹیک سنگھ اور ٹوبا ٹیک سنگھ ایم ایس ڈی

مندرجہ ذیل کے تحت قریب لاکھ پندرہ سو روپے کے لیے پورٹا ٹیک سنگھ اور ٹوبا ٹیک سنگھ  
 اور ٹوبا ٹیک سنگھ کے مختلف سرکاری پروژوں کے لیے ایک سو تیس لاکھ روپے  
 مندرجہ ذیل ہے۔

نوٹیفکیشن (پورٹا ٹیک سنگھ)	کل رقم (پورٹا ٹیک سنگھ)	نوٹیفکیشن (ٹوبا ٹیک سنگھ)	رقم (ٹوبا ٹیک سنگھ)
- NIL -	21067296 -	15-7-10	16
- NIL -	308074375 -	8-7-10	09
- NIL -	110106389 -	7-12-11	177
15905781 -	31081716 -	29-7-13	07
151987 -	30679924 -	18-6-15	255
5837302 -			

یہ اے ایس ڈی کے تحت قریب لاکھ پندرہ سو روپے کے لیے پورٹا ٹیک سنگھ اور ٹوبا ٹیک سنگھ  
 کے مختلف سرکاری پروژوں کے لیے ایک سو تیس لاکھ روپے

7/3/16  
 لیڈنگ اسٹیٹمنٹ  
 ایم ایس ڈی

verified and noted Balani  
 07/3/16

District Accounts Officer  
 District Accounts Office  
 Toba Tek Singh

B) District Treasury Toba Tek Singh

لینڈ اینڈ میٹریل ڈسٹریکشن ایف ایم ایس ایف ڈی -  
 ڈسٹریکٹ اکاؤنٹس اینڈ ٹریزوری

سرکار پاکستان  
 وفاقی اور ریاستہائے متحدہ عرب امارات میں موجود پاکستانی اداروں کے لیے  
 08/16/2016

موضوع: مقررہ رقم / M4 / Sec II & E / 2010 / 690

مقررہ رقم: 150

مقررہ رقم کے تحت قریب 10 کروڑ روپے کے لیے لینڈ اینڈ میٹریل ڈسٹریکشن ایف ایم ایس ایف ڈی کے ذریعے فراہم کیا گیا ہے۔

مقررہ رقم	مقررہ رقم	مقررہ رقم	مقررہ رقم
10,000,000 --	10,000,000 --	15-6-05	489
96885 --	62,158,813 --	13-7-10	100 - 1
578347 --	1,39,90,600 --	13-7-06	18 - 2
8001319 --	180,000,000 --	25-9-02	05 - 3
3542813 --	3542813 --	24-7-03	402/4 - 4
40000000 --	40000000 --	29-8-05	56 - 5
21365670 --	21365670 --	10-12-09	189 - 6
10000000 --	10000000 --	12-11-05	121 - 7

Verified by the Dist. Head office Dist. Treas.

لینڈ اینڈ میٹریل ڈسٹریکشن ایف ایم ایس ایف ڈی کے ذریعے فراہم کیا گیا ہے۔

2/3/16

لینڈ اینڈ میٹریل ڈسٹریکشن ایف ایم ایس ایف ڈی

**Annex10: List of Consultations with Unpaid DPs**

<b>Sr. No.</b>	<b>Date</b>	<b>Location/ Village</b>	<b>Category of Participant</b>	<b>Name of Main Participant</b>
1	February 16, 2016	Chak 311 /JB	DPCs/DPs/ Local Communities	<ul style="list-style-type: none"> <li>- Mr. Muhammad Khalid</li> <li>- Mr. Adeel Liaqat</li> <li>- Mr. Zahid</li> <li>- Mr. Muhammad Afzal</li> <li>- Mr. Akhtar Ali</li> <li>- Mr. Allah Wasaya</li> <li>- Mr. Ghaffar Ahmad</li> <li>- Mr. Ali Raza</li> <li>- Mr. Faizurrehman</li> <li>- Mr. Nadeem Gill</li> <li>- Mr. Aqeel Ahmad</li> </ul>
2	February 16, 2016	Chak385/JB	DPCs/DPs/ Local Communities	<ul style="list-style-type: none"> <li>- Mr. Muhammad Awais</li> <li>- Mr. Abdur Rauf</li> <li>- Mr. Muhammad Maqbool</li> <li>- Mr. Muhammad Amjad</li> <li>- Mr. Muhammad Usman</li> <li>- Mr. Muhammad Asim</li> <li>- Mr. Muhammad Maqsood</li> <li>- Mr. Naseer Akhtar</li> <li>- Mr. Muhammad Hussain</li> <li>- Mr. Abdul Ghaffar</li> <li>- Mr. Aqeel</li> </ul>
3	February 16, 2016	Chak304/JB	DPCs/DPs/ Local Communities	<ul style="list-style-type: none"> <li>- Mr. Shaukat Warraich</li> <li>- Mr. Muhammad Fazle Rasool</li> <li>- Mr. Muhammad Mustafa</li> <li>- Mr. Muhammad Suleman</li> <li>- Mr. Muhammad Ilyas</li> <li>- Mr. Zeeshan</li> <li>- Mr. Asif</li> <li>- Mr. Ali Sher</li> <li>- Mr. Imran</li> <li>- Mr. Arif Hussain</li> <li>- Mr. Abdul Khaliq</li> <li>- Mr. Muhammad Anwar</li> </ul>
4	February 16, 2016	Chak 378/JB	DPCs/DPs/ Local Communities	<ul style="list-style-type: none"> <li>- Mr. Abdul Ghaffar</li> <li>- Mr. Mubeen</li> <li>- Mr. Zain</li> <li>- Mr. Naveed</li> <li>- Mr. Muhammd Asif</li> <li>- Mr. Muhammad Farooq</li> <li>- Mr. Sabir Ali</li> <li>- Mr. Muhammad Sohail</li> <li>- Mr. Safdar</li> <li>- Mr. Temoor Ali</li> <li>- Mr. Siraj Din</li> </ul>
5	February 16, 2016	Chak307/JB	DPCs/DPs/ Local Communities	<ul style="list-style-type: none"> <li>- Mr. Asghar Ali</li> <li>- Mr. Samiullah</li> <li>- Mr. Adeel Cheemqa</li> <li>- Mr. Khairullah</li> <li>- Mr. Amanullah</li> <li>- Mr. Ghulam Qadir</li> <li>- Mr. Waqar</li> <li>- Mr. Muhammad Sadiq</li> <li>- Mr. Riasat Ali</li> <li>- Mr. Muhammad Muneer</li> </ul>



Sr. No.	Date	Location/ Village	Category of Participant	Name of Main Participant
6	February 16, 2016	Chak500/JB	DPCs/DPs/ Local Communities	- Mr. Muhammad Ramzan - Mr. Muhammad Asif - Mr. Qaisar Abbas - Mr. Muhammad Nawaz - Mr. Bilal - Mr. Fakhar Ijaz - Mr. Rizwan - Mr. Naeem Sharif - Mr. Nazar Abbas - Mr. Ali Abbas
7	February 16, 2016	Chak 310/JB	DPCs/DPs/ Local Communities	- Mr. Zulfiqar Ali - Mr. Gul Nawaz - Mr. Muhammad Ameen - Mr. Muhammad Sharif - Mr. Muhammad Shafiq - Mr. Majid - Mr. Muhammad Waqas - Mr. Muhammad Iqbal - Mr. Muhammad Rashid - Mr. Dilawar Hussain
8	February 16, 2016	Chak360 /JB	DPCs/DPs/ Local Communities	- Mr. Muhammad Shafiq - Mr. Shehzad Rasool - Mr. Nazeer Ahmad - Mr. Zulfiqar - Mr. Muhammad Ilyas - Dr. Shahid - Mr. Munir Ahmad - Mr. Mudasser Hussain - Mr. Sajjad
9	February 16, 2016	Chak305/JB	DPCs/DPs/ Local Communities	- Mr. Waqas Ahmad - Mr. Asif Mehmood - Mr. Muhammad Akram - Mr. Muhammad Ashraf - Mr. Usman Ali Cheema - Mr. Allah Ditta - Mr. Saifullah - Mr. Ghulam Mustafa - Mr. Muhammad Mushtaq - Mr. Hassan Murtaza - Mr. Muhammads Ashraf
10	February 16, 2016	Moza Kalowala	DPCs/DPs/ Local Communities	- Mr. Muhammad Afzal - Mr. Muhammad Aslam - Mr. Muhammad Ashraf - Mr. Manzoor Ahmad - Mr. Amir Sajjad - Mr. Muhammad Usman Zafar - Mr. Mumtaz - Mr. Haq Nawaz - Mr. Sabir Abbas - Mr. Jawadul Hassan
11	February 16, 2016	Chsk398/JB	DPCs/DPs/ Local Communities	- Mr. Ghulam Mustafa - Mr. Muhammad Nawaz - Mr. Nazir Ahmad - Mr. Muhammad Sadiq - Mr. Muhammad Bashir - Mr. Faqeer Muhammad - Mr. Muhammad Amjad

Sr. No.	Date	Location/ Village	Category of Participant	Name of Main Participant
12	February 16, 2016	Chak400/JB	DPCs/DPs/ Local Communities	- Mr. Abdur Rauf - Mr. Muhammad Siddiq - Mr. Muhammad Riaz - Mr. Zahid - Mr. Qudrat Ali - Mr. Noor Muhammad - Mr. Sakhawat Ali - Mr. Muhammad Hussain - Mr. Sabir Hussain - Mr. Nasrullah Khan - Mr. Muhammd Khan - Mr. Ata Muhammad
13	February 16, 2016	Chak487/JB	DPCs/DPs/ Local Communities	- Mr. Khuda Bukhsh - Mr. Rehman Ali - Mr. Muhammad Ashraf - Mr. Muhammad Afzal - Mr. Mukhtar Ali - Mr. Abdul Latif - Mr. Azhar ali
14	February 17, 2016	Chak384/JB	DPCs/DPs/ Local Communities	- Mr. Muhammad Rafiq - Mr. Shahid Nadeem - Mr. Muhammad Rafiq - Mr. Muddasser Usman - Mr. Muhammad Ijaz - Mr. Muhammad Asad - Mr. Muhammad Naeem - Mr. Muhammad Zaheer - Mr. Kashif Riaz - Mr. Muhammad Sharif
15	February 17, 2016	Chak469/JB	DPCs/DPs/ Local Communities	- Mr. Nazar Abbas - Mr. Muhammad Amin - Mr. Asim Shezan - Mr. Muhammad Ijaz - Mr. Dera Khan - Mr. Talib Hussain - Mr. Faiz Ahmad - Mr. Muhammad Riaz
16	February 17, 2016	Chak501/JB	DPCs/DPs/ Local Communities	- Mr. Ghulam Ali - Mr. Abid Shah - Mr. Mazhar Shah - Mr. Muhammad Ijaz - Mr. Asif Shah - Mr. Muhammad Qasim - Mr. Mohsin Raza - Mr. Ali Akbar - Mr. Aqeel Abbas
17	February 17, 2016	Chak396/JB	DPCs/DPs/ Local Communities	- Mr. Muhammad Mubbashir - Mr. Muhammad Aslam - Mr. Asghar - Mr. Raja Saddam - Mr. Nazir Asi - Mr. Haq Nawaz - Mr. Ali Muhammad
18	February 17, 2016	Chak390/JB	DPCs/DPs/ Local Communities	- Mr. Shehzad Alam - Mr. Abdur Rasheed - Mr. Mohsin Rashid - Mr. Zulfigar

<b>Sr. No.</b>	<b>Date</b>	<b>Location/ Village</b>	<b>Category of Participant</b>	<b>Name of Main Participant</b>
				- Mr. Abdul Haq - Mr. Umar Hayat - Mr. Fayyaz - Mr. Aftab Ahmad
<b>19</b>	February 17, 2016	Chak383/JB	DPCs/DPs/ Local Communities	- Mr. Muhammad Yaqoob - Mr. Muhammad Asif - Mr. Muhammad Shahid - Mr. Zeeshan Shokat - Mr. Muhammad Ashraf - Mr. Muhammad Altaf - Mr. Sarfaraz - Mr. Abdul Sattar - Mr. Muhammad Nadeem
<b>20</b>	February 17, 2016	Chak490/JB	DPCs/DPs/ Local Communities	- Mr. Shahbaz Ahmad - Mr. Ansar Abbas - Mr. Muhamamd Hayat - Mr. Ehsanullah - Mr. Qaiser Iqbal - Mr. Muhammad Farooq - Mr. Qasim Ali
			Total DPs	189 Nos.



**Annex12: Notification of DPC/ GRC Constituted at village level****NATIONAL HIGHWAY AUTHORITY****Office of the Director (LM&IS) M-4**Kamalpur Interchange, Sargodha Road, FaisalabadPh:041-8879154-55, Fax:8879153No: ( )Dir/(Land)/M-4/NHA/2015/365<sup>B</sup>20<sup>th</sup> March, 2015Subject: - **CIRCULAR**

It is hereby circulated that APC's & GRC's have been constituted at all villages (32) falling in Section-II (Gojra-Shorkot) M-4 project.

2. The list is attached.

*Linsan kat* 20/3/15  
**(Shoukat Hussain Balouch)**  
Director (Land) M-4

**Copy to:-**

- Member (Central Zone) NHA, Lahore
- Member (Coordination) NHA, Islamabad
- G.M (EALS) NHA, Islamabad
- G.M (M-4) NHA, Faisalabad
- C.C.A.P, NHA, Faisalabad
- Director (L&S) HQ, NHA, Islamabad
- A.D (Land) M-4 NHA, Faisalabad
- L.A.O (M-4) NHA, Faisalabad

**List of Affected Persons Committee (DPC)**

<b>Chak No.</b>	<b>Name</b>	<b>Designation</b>
<b>304-JB</b>	Muhammad Mustafa S/o Muhammad Hasham	President
	Muhammad Akram S/o Muhammad Hussain	General Secretary
	Muhammad Mansha S/o Nazar Muhammad	Member
	Muhammad Arif S/o Nazar Muhammad	Member
	Muhammad Zaman S/o Nazar Muhammad	Member
<b>305-JB</b>	Asmat Abbas S/o Ghulam Abbas	President
	Faryad Hussain s/o Muhammad Aslam	General Secretary
	Muhammad Afzal S/o Sardar Khan	Member
	Basharat Ali S/o Ghulam Mohi-ul Din	Member
<b>307-JB</b>	Haji Asghar Ali S/o Ghulam Nabi	President
	Muhammad Asif Naeem S/o Ghulam Rasool	General Secretary
	Qasim Ali S/o Ghulam Haider	Member
	Muhammad Akram S/o Allah Ditta	Member
	Farzand Ali S/o Muhammad Sadiq	Member
<b>360-JB</b>	Munir Ahmad S/o Ghulam Muhammad	President
	Muhammad Aslam S/o Sardar Muhammad	General Secretary
	Muhammad Aslam S/o Ghulam Muhammad	Member
	Muhammad Akram S/o Muhammad yousaf	Member
<b>310-JB</b>	Zafar Iqbal S/o Muhammad Iqbal	President
	Nazar Hayat S/o Muhammad Khan	General Secretary
	Naveed Raza S/o Fateh Muhammad	Member
	Muhammad Ijaz S/o Muhammad Sarwar	Member
<b>311-JB</b>	Ahsan Ullah S/o Muhammad Ishaq	President
	Saif Ullah S/o Naazar Hussain	General Secretary
	Zafar Hussain S/o Naazar Hussain	Member
	Muhammad Azam S/o Muhammad Siddique	Member
	Qamar Abbas S/o Allah Ditta	Member
<b>438-JB</b>	Zafar Ullah Khan S/o Ghulam Rasool	President
	Umar Hayat S/o Ghulam Ali	General Secretary
	Ghulam Ali S/o Muhammad Ali	Member
	Talib Hussain S/o Muhammad Ali	Member
	Muhammad Arif S/o talib Hussain	Member
<b>317-JB</b>	Muhammad Afzal S/o Muhammad Siddique	President
	Muhammad Ashraf S/o Ghulam Rasool	General Secretary
	Muhammad Asif S/o Muhammad Maghzan	Member
	Shahid Iqbal S/o Muhammad Maghzan	Member
<b>378-JB</b>	Farooq Azam S/o Muhammad Irshad	President
	Muhammad Mohsin S/o Muhammad Arshad	General Secretary

Chak No.	Name	Designation
	Muhammad Tariq S/o Abdul Ghafoor	Member
	Zafar Iqbal S/o Muhammad Irshad	Member
	Master Dildar S/o Muhammad Tofail	Member
<b>385-JB</b>	Abdul Sattar S/o Wali Muhammad	President
	Muhammad Akhtar S/o Abdul Karim	General Secretary
	Muhammad Akram S/o Ghulam Ghous	Member
	Abdullah S/o Muhammad Tofail	Member
	Mehmood Khalid S/o Muhammad Yaseen	Member
<b>384/JB</b>	Sultan Baksh S/o Muhammad Mushtaq	President
	Muhammad Javaid S/o Abdul Aziz	General Secretary
	Parwaiz Hussain S/o Muhammad Yousaf	Member
	Imran Nadeem S/o Muhammad Fazil	Member
	Muhammad Nawaz S/o Muhammad Ashraf	Member
<b>383/JB</b>	Saeed Ahmad S/o Allah Ditta	President
	Muhammad Ijaz S/o Qasim Ali	General Secretary
	Muhammad Yaqoob S/o Muhammad Ismail	Member
	Liaqat Ali S/o Muhammad Khalil	Member
	Waheed Akhtar S/o Manzoor Ahmad	Member
<b>390/JB</b>	Shahzad Aalam S/o Munawar Hussain	President
	Muhammad Ragique S/o Ghulam Qadir	General Secretary
	Khawar Javaid S/o Allah Ditta	Member
	Munawar Hussain S/o Noor Muhammad	Member
	Usman Sajid S/o Sajid Javaid	Member
<b>469/JB</b>	Mazhar Abbas S/o Muhammad Nawaz	President
	Noor Ahmad S/o Allah Baksh	General Secretary
	Safdar Ali S/o Ghulam Muhammad	Member
	Sajjad Hussain S/o Ghulam Muhammad	Member
<b>396/JB</b>	Muhammad Riaz S/o Raheem Dad	President
	Liaqat Ali S/o Muhammad Aslam	General Secretary
	Nazir Aasi S/o Muhammad Waryam	Member
	Muhammad Ayaz S/o Kalay Khan	Member
<b>398/JB</b>	Faqeer Muhammad S/o Ameer Din	President
	Muhammad Zafar S/o Peeran Ditta	General Secretary
	Khalid Mehmood S/o Ahmad Ali	Member
	Muhammad Azeem S/o Muhammad Yaqoob	Member
<b>400/JB</b>	Muhammad Sadiq S/o Charagh Din	President
	Zahid Ali S/o Muhammad Sadiq	General Secretary
	Muhammad Javaid S/o Muhammad Ismail	Member
	Liaqat Ali S/o Ashiq Ali	Member
	Noor Muhammad S/o Charagh Din	Member

Chak No.	Name	Designation
401/JB	Muhammad Tariq S/o Muhammad Aslam	President
	Muhammad Amir Shahzad S/o Taj Muhammad	General Secretary
	Abdul Razzaq S/o Jalal Din	Member
	Moosa Rehman S/o Muhammad Zafar Yaseen	Member
	Waqas Sharif S/o Muhammad Sharif	Member
487/JB	Muhammad Ashraf S/o Talib Hussain	President
	Ghulam Mustafa S/o Jalal Din	General Secretary
	Muhammad Asghar S/o Mukhtar Ali	Member
	Abdul Rasheed S/o Kamal Din	Member
	Muhammad Jameel S/o Talib Hussain	Member
488/JB	Tasawar Abbas S/o Ghulam Fareed	President
	Babar Ali S/o Ashiq Ali	General Secretary
	Kazim Ali S/o Faiz Khan	Member
	Rajab Ali S/o Ghulam Khan	Member
489/JB	Iftikhar Ahmad S/o Abdullah Khan	President
	Muhammad Asif S/o Muhammad Afzal	General Secretary
	Ghulam Mustafa S/o Muhammad Hussain	Member
	Muhammad Aslam S/o Muhammad Boota	Member
490/JB	Shahbaz Ahmad S/o Niaz Ahmad	President
	Akhtar Ali S/o Zafar Ali	General Secretary
	Zafar Ullah S/o Muhammad Khan	Member
	Ijaz Ahmad S/o Sultan Ahmad	Member
406/JB	Muhammad Ishaq S/o Muhammad Haneef	President
	Ghulam Rasool S/o Ahmad	General Secretary
	Sajjad Akbar S/o Muhammad Akbar	Member
	Muhammad Ishtiaq S/o Muhammad Haneef	Member
	Muhammad Farooq S/o Muhammad Iqbal	Member
505/JB	Mehmood S/o Manak	President
	Lal Din S/o Manak	General Secretary
	Ghulam Abbas S/o Muhammad Iqbal	Member
	Muhammad Nawaz S/o Muhammad Khan	Member
	Mukhtar Ahmad S/o Muhammad Khan	Member
494/JB	Mehmood S/o Manak	President
	Zahoor Ahmad S/o Muhammad Shafi	General Secretary
	Lal Din S/o Manak	Member
	Muhammad Jameel S/o Muhammad Sadiq	Member
	Lal Kabeer S/o Muhammad Fazil	Member
496/JB	Liaqat Ali S/o Muhammad Sarwar	President
	Khursheed Ahmad S/o Khan Muhammad	General Secretary
	Bashir Ahmad S/o Nawab	Member



Chak No.	Name	Designation
	Manzoor Ahmad S/o Baig	Member
	Muhammad Ishaq S/o Muhammad Nawaz	Member
<b>Kalo Wala</b>	Muhammad Jameel S/o Muhammad Sadiq	President
	Azhar Parwaiz S/o Muhammad Arif	General Secretary
	Muhammad Waqas Khalil S/o Khalil Ahmad	Member
	Zahoor Ahmad S/o Mian Anayait	Member
<b>500/JB</b>	Muhammad Hibib S/o Pehalwan	President
	Muhammad Ramzan S/o Asghar Ali	General Secretary
	Munir Ahmad S/o Noor Muhammad	Member
	Bashir Ahmad S/o Noor Muhammad	Member
<b>504/JB</b>	Akhtar Ali S/o Muhammad Azam	President
	Zafar Iqbal S/o Muhammad Azam	General Secretary
	Ghulam Haider S/o Muhammad Sharif	Member
	Mazhar Ali S/o Muhammad Azam	Member
	Muhammad Nawaz S/o Fateh Muhammad	Member
<b>501/JB</b>	Shoukat Maqsood S/o Muhammad Akram	President
	Faiz Ahmad S/o Ferooz Din	General Secretary
	Naseer Ahmad S/o Saeed Muhammad	Member
	Allah Wasaaya S/o Khuda Baksh	Member
	Niaz Ahmad S/o Ferooz Din	Member
<b>Rakh Kotla</b>	Ijaz Hussain S/o Talib Husain	President
	Tanveer Hussain S/o Muhammad Jafar	General Secretary
	Muhammad Afzal S/o Lal Muhammad	Member
	Abid Khan S/o Pehalwan Khan	Member
<b>07 Ghagh</b>	Abdul Kareem S/o Muhammad Fazil	President
	Muhammad Ramzan S/o Nadir Khan	General Secretary
	Doost Muhammad S/o Bahadar Khan	Member
	Muhammad Afzal S/o Adil Khan	Member

### List of Grievance Redressal Committee (GRC)

Chak. #	Name	Designation
<b>304-JB</b>	Muhammad Mustafa S/o Muhammad Hasham	President
	Muhammad Akram S/o Muhammad Hussain	General Secretary
	Muhammad Mansha S/o Nazar Muhammad	Member
	Ghulam Murtaza S/o Muhammad Hasham	Member
<b>305-JB</b>	Nasrullah S/o Ghulam Mohi-ul Din	President
	Asmat Abbas S/o Ghulam Abbas	General Secretary
	Nasir Hussain s/o Muhammad Aslam	Member
	Muhammad Nawaz s/o Ghulam Ahmad	Member

Chak. #	Name	Designation
307-JB	Haji Asghar Ali S/o Ghulam Nabi	President
	Muhammad Asif Naeem S/o Ghulam Rasool	General Secretary
	Muhammad Yousaf S/o Ghulam Rasool	Member
	Muhammad Qaisar S/o Ghulam Mustafa	Member
360-JB	Muhammad Aslam S/o Sardar Muhammad	President
	Munir Ahmad S/o Ghulam Muhammad	General Secretary
	Muhammad Akram S/o Muhammad yousaf	Member
	Muhammad Ashraf S/o Aalam Din	Member
	Muhammad Saleem S/o Muhammad Din	Member
310-JB	Zafar Iqbal S/o Muhammad Iqbal	President
	Nazar Hayat S/o Muhammad Khan	General Secretary
	Mazhar Iqbal S/o Muhammad Khan	Member
311-JB	Ahsan Ullah S/o Muhammad Ishaq	President
	Saif Ullah S/o Naazar Hussain	General Secretary
	Khan Muhammad S/o Muhammad Ishaq	Member
438-JB	Zafar Ullah Khan S/o Ghulam Rasool	President
	Umar Hayat S/o Ghulam Ali	General Secretary
	Abbas Ali S/o Talib Hussain	Member
317-JB	Muhammad Ashraf S/o Ghulam Rasool	President
	Muhammad Afzal S/o Muhammad Siddique	General Secretary
	Muhammad Asif S/o Muhammad Maghzan	Member
378-JB	Muhammad Yousaf S/o Muhammad Maghzan	Member
	Muhammad Mohsin S/o Muhammad Arshad	President
	Farooq Azam S/o Muhammad Irshad	General Secretary
385-JB	Muhammad Aqeel S/o Muhammad Arshad	Member
	Muhammad Ashraf S/o Abdul Aziz	Member
	Abdul Sattar S/o Wali Muhammad	President
384/JB	Muhammad Akhtar S/o Abdul Karim	General Secretary
	Muhammad Farooq S/o Abdul Rasheed	Member
	Muhammad Javaid S/o Muhammad Din	Member
383/JB	Sultan Baksh S/o Muhammad Mushtaq	President
	Nasir Mehmood S/o Talib Hussain	General Secretary
	Muhammad Riaz S/o Talib Hussain	Member
390/JB	Muhammad Hafeez S/o Abdul	Member
	Liaqat Ali S/o Muhammad Saleem	President
	Muhammad Rasheed S/o Allah Ditta	General Secretary
390/JB	Waheed Akhtar S/o Manzoor Ahmad	Member
	Muhammad Ijaz S/o Qasim Ali	Member
	Munawar Hussain S/o Noor Muhammad	President

Chak. #	Name	Designation
	Shahzad Aalam S/o Munawar Hussain	General Secretary
	Muhammad Imran Sajid S/o Sajid Javaid	Member
	Muhammad Riaz S/o Rustam Ali	Member
<b>469/JB</b>	Mazhar Abbas S/o Muhammad Nawaz	President
	Noor Ahmad S/o Allah Baksh	General Secretary
	Muhammad Riaz S/o Dildar	Member
	Sultan S/o Sher Muhammad	Member
<b>396/JB</b>	Muhammad Ayaz S/o Kalay Khan	President
	Muhammad Riaz S/o Raheem Daad	General Secretary
	Muhammad Anwar S/o Ghulam Hussain	Member
<b>398/JB</b>	Faqeer Muhammad S/o Ameer Din	President
	Muhammad Ali S/o Lal Din	General Secretary
	Muhammad Tahir S/o Abdul Majeed	Member
	Muhammad Nawaz S/o Shameer	Member
<b>400/JB</b>	Zahid Ali S/o Muhammad Sadiq	President
	Muhammad Sadiq S/o Charagh Din	General Secretary
	Zafar Ali S/o Ashiq Ali	Member
	Nasir Ali S/o Ashiq Ali	Member
<b>401/JB</b>	Moosa Rehman S/o Muhammad Zafar Yaseen	President
	Waqar Sharif S/o Muhammad Sharif	General Secretary
	Muhammad Amir Shahzad S/o Taj Muhammad	Member
	Muhammad Akram S/o Ghulam Nabi	Member
<b>487/JB</b>	Muhammad Ashraf S/o Talib Hussain	President
	Ghulam Shabbir S/o Faqeer Muhammad	General Secretary
	Ghulam Mustafa S/o Jalal Din	Member
	Abdul Sattar S/o Kamal Din	Member
<b>488/JB</b>	Babar Ali S/o Ashiq Ali	President
	Tasawar Abbas S/o Ghulam Fareed	General Secretary
	Ghulam Shabbir S/o Faqeer Khan	Member
	Muhammad Khursheed S/o Allah Ditta	Member
<b>489/JB</b>	Muhammad Asif S/o Muhammad Afzal	President
	Iftikhar Ahmad S/o Abdullah Khan	General Secretary
	Muhammad arif S/o Muhammad Boota	Member
	Ghulam Murtaza S/o Ghulam Rasool	Member
<b>490/JB</b>	Shahbaz Ahmad S/o Niaz Ahmad	President
	Safdar S/o Zafar Ullah	General Secretary
	Ijaz Ahmad S/o Sultan Ahmad	Member
	Allah Ditta S/o Muhammad Shafi	Member
<b>406/JB</b>	Muhammad Farooq S/o Muhammad Iqbal	President
	Muhammad Ishaq S/o Muhammad Haneef	General Secretary

Chak. #	Name	Designation
	Muhammad Ishaq S/o Ahmad	Member
	Amir Hussain S/o Muhammad Haneef	Member
<b>505/JB</b>	Lal Din S/o Manak	President
	Lal Kabeer S/o Muhammad Fazil	General Secretary
	Muhammad Nawaz S/o Muhammad Khan	Member
	Raees Abbas S/o Muhammad Khan	Member
<b>494/JB</b>	Mehmood S/o Manak	President
	Muhammad Jameel S/o Muhammad Sadiq	General Secretary
	Zahoor Ahmad S/o Muhammad Shafi	Member
	Abdul Sattar S/o Muhammad Fazil	Member
	Muhammad Rafique S/o Sultan Mehmood	Member
<b>496/JB</b>	Arif Farooqi S/o Muhammad Siddique	President
	Liaqat Ali S/o Muhammad Sarwar	General Secretary
	Muhammad Iqbal S/o Baig	Member
	Muhammad Saeed S/o Mehtab	Member
<b>Kalo Wala</b>	Muhammad Jameel S/o Muhammad Sadiq	President
	Azhar Parwaiz S/o Muhammad Arif	General Secretary
	Muhammad Waqas Khalil S/o Khalil Ahmad	Member
	Zahoor Ahmad S/o Mian Anayait	Member
<b>500/JB</b>	Muhammad Ramzan S/o Asghar Ali	President
	Munir Ahmad S/o Noor Muhammad	General Secretary
	Ghulam Murtaza S/o Fateh Muhammad	Member
	Muhammad Irshaad S/o Muhammad Habib	Member
<b>504/JB</b>	Khadim Hussain S/o Abdul Rasheed	President
	Ghulam Haider S/o Muhammad Sharif	General Secretary
	Akhtar Ali S/o Muhammad Azam	Member
	Muhammad Sajjad S/o Muhammad Azam	Member
<b>501/JB</b>	Shoukat Maqsood S/o Muhammad Ikraam	President
	Aman Ullah S/o Muhammad Ramzan	General Secretary
	Faiz Ahmad S/o Ferooz Din	Member
	Raz Nawaz S/o Mian Fazil	Member
<b>Rakh Kotla</b>	Akhtar Raza Yaseen S/o Muhammad Zafar	President
	Muhammad Ramzan S/o Muhammad Fazil	General Secretary
	Tanveer Hussain S/o Muhammad Jafar	Member
	Ayyub Hussain S/o Adil Khan	Member
<b>07/Ghagh</b>	Muhammad Ramzan S/o Nadir Khan	President
	Abdul Kareem S/o Muhammad Fazil	General Secretary
	Abdul Rehman S/o Doost Muhammad	Member
	Umar Hayat S/o Muhammad Nawaz	Member
