

PMR Public Report

Operation Number	AR-L1136	Chief of Operations Validation Date	04/13/21
Year- PMR Cycle	Second period Jan-Dec 2020	Division Chief Validation Date	04/15/21
Last Update	03/29/21	Country Representative Validation Date	04/28/21
PMR Validation Stage	Validated by Representative		

Basic Data

Operation Profile

Operation Name	Development Programme's Norte Grande provinces: W&S Infrastructure	Loan Number	2776/OC-AR
Executing Agency	MINISTERIO DE PLANIFICACION FEDERAL, INVERSION PUBLICA Y SERVICIOS, MINISTERIO DE OBRAS PUBLICAS	Sector/Subsector	WATER AND SANITATION-WATER SUPPLY URBAN
Team Leader	MORENO MORENO, HENRY ALBERTO	Overall Stage	Disbursing (From eligibility until all the Operations are closed)
Operation Type	Loan Operation	Country	Argentina
Lending Instrument	Investment Loan	Convergence related Operation(s)	
Borrower	NACION ARGENTINA		


Environmental and Social Safeguards

Impacts Category	B	Was/Were the objective(s) of this operation reformulated?	YES
Safeguard Performance Rating	Satisfactory	Date of approval	08/05/20
Safeguard Performance Rating - Rationale	La agencia ejecutora tiene capacidad para gestionar los aspectos ambientales y sociales, del Programa. Las obras en ejecución cumplen con las políticas del Banco en lo referente al relacionamiento comunitario, la gestión de residuos y de materiales peligrosos, etc. El proyecto en preparación, Agua Segura para comunidades indígenas, implicará un desafío en términos de articulación de actores institucionales.		

Financial Data

Item	Total Cost and Source				Available Funds (US\$)				
	Original IDB	Current IDB	Local Counterpart	Co-Financing / Country	Total Original Cost	Current IDB	Disb. Amount to Date	% Disb	Undisbursed Amount
AR-L1136	500,000,000	364,000,000		0	500,000,000	364,000,000	249,253,166.44	68.48%	114,746,833.56
Aggregated	500,000,000	364,000,000		0	500,000,000	364,000,000	249,253,166.44	68.48%	114,746,833.56

Expense Categories by Loan Contract (cumulative values)

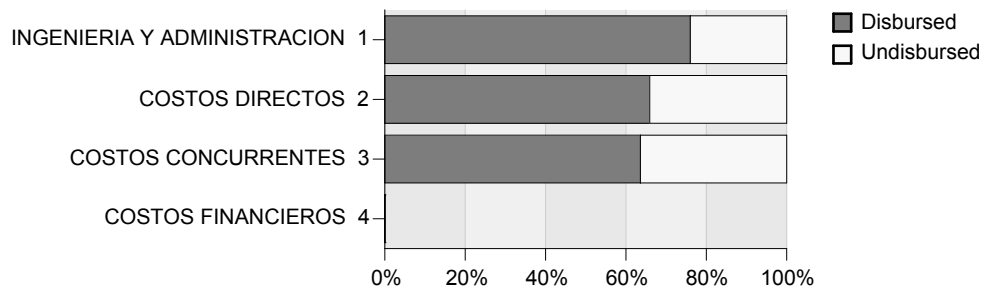

Please note that inactive indicators and outputs are not displayed; totals in the actual cost table may not match the sum of the cost of the outputs displayed, due to the cost of inactive outputs.

PMR Public Report

RESULTS MATRIX

General Development Objectives

No information available for this section

PMR Public Report

RESULTS MATRIX

Specific Development Objectives

Specific Development Objectives Nbr. 0: Objetivo específico 1. Incrementar la cobertura y mejorar el servicio de agua potable y alcantarillado sanitario y pluvial en áreas sin servicio o con servicio deficiente

Observation:

Indicator	Unit of Measure	Baseline	Baseline Year		2013	2014	2015	2016	2017	2018	2019	2020	2021	2022	EOP 2022
0.0	1.1 Hogares con nueva conexión a sistemas de saneamiento por red construidos y/o rehabilitados	# of households	0.00	2014	P	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	9,353.00	9,353.00
					A	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00

Details

Means of verification: Informes de la Unidad Ejecutora basado en reportes de los Entes Operadores.

Observations: El indicador considera el total de hogares con conexión efectiva (conexión intradomiciliaria).

Pro-Gender No **Pro-Ethnicity** No

Indicator	Unit of Measure	Baseline	Baseline Year		2013	2014	2015	2016	2017	2018	2019	2020	2021	2022	EOP 2022
0.1	1.2 Nuevos hogares cuyas aguas residuales son tratadas	Households (#)	0.00	2014	P	0.00	0.00	0.00	0.00	0.00	0.00	0.00	160,000.00	160,000.00	
					A	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	

Details

Means of verification: Informes de la Unidad Ejecutora basado en reportes de los Entes Operadores.

Observations: Se considera tratado cuando cumple con los parámetros de vuelco (según normas vigentes y aplicables)

Pro-Gender No **Pro-Ethnicity** No

Indicator	Unit of Measure	Baseline	Baseline Year		2013	2014	2015	2016	2017	2018	2019	2020	2021	2022	EOP 2022
0.2	1.3 Caudal de Aguas Residuales Tratado	l/s	0.00	2014	P	0.00	0.00	0.00	0.00	0.00	0.00	0.00	2,128.00	2,128.00	
					A	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	

Details

Means of verification: Informes de la Unidad Ejecutora basado en reportes de los Entes Operadores

Observations: Se considera tratado cuando cumple con los parámetros de vuelco (según normas vigentes y aplicables)

Pro-Gender No **Pro-Ethnicity** No

Indicator	Unit of Measure	Baseline	Baseline Year		2013	2014	2015	2016	2017	2018	2019	2020	2021	2022	EOP 2022
0.3	1.4 Hogares con nueva conexión a servicio de agua potable por red construida y/o rehabilitada	# of households	0.00	2014	P	0.00	0.00	0.00	0.00	0.00	0.00	0.00	31,000.00	31,000.00	
					A	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	

Details

Means of verification: Informes de la Unidad Ejecutora basado en reportes de los Entes Operadores.

PMR Public Report

RESULTS MATRIX

Specific Development Objectives

Observations: El indicador considera el total de hogares con conexión potencial al sistema de tratamiento construido y/o rehabilitado.

Pro-Gender No **Pro-Ethnicity** No

Specific Development Objectives Nbr. 1: Objetivo específico 2. Gestión Operativa de los Entes Beneficiarios Fortalecida

Observation:

Indicator		Unit of Measure	Baseline	Baseline Year		2013	2014	2015	2016	2017	2018	2019	2020	2021	2022	EOP 2022
1.0	2.1 Prestadores de servicio beneficiarios cuyos ingresos cubren los costos de operación, mantenimiento y administración del servicio.	N°	0.00	2014	P	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	1.00		1.00
					A	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00			0.00

Details

Means of verification: Informes de la Unidad Ejecutora basado en reportes de los Entes Operadores

Observations: Los entes beneficiarios reportan sus ingresos a través de los informes financieros.

Pro-Gender No **Pro-Ethnicity** No

Indicator		Unit of Measure	Baseline	Baseline Year		2013	2014	2015	2016	2017	2018	2019	2020	2021	2022	EOP 2022
1.1	2.2. Entidades del sector a nivel provincial con personal capacitado en gestión del sector de agua y saneamiento.	Numero	0.00	2020	P	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	2.00		2.00
					A	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00			0.00

Details

Means of verification: Acta de talleres de capacitación

Observations: ninguna

Pro-Gender No **Pro-Ethnicity** No

RESULTS MATRIX

OUTPUTS: ANNUAL PHYSICAL AND FINANCIAL PROGRESS

Component Nbr. 1 Sistemas de Agua Potable y Saneamiento Construidos

Output	Unit of Measure		PHYSICAL PROGRESS		FINANCIAL PROGRESS	
			2020	EOP 2022	2020	EOP 2022
1.1 Sistemas de Saneamiento Construidos	Nº	P	0	5	8,727,407	52,514,431.5
		P(a)	0	5	8,727,407	62,962,913.87
		A	0	1	19,175,889.37	53,450,345.87
1.2 Sistemas de Agua Potable Construidos	Nº	P	0	4	0	131,567,593.08
		P(a)	0	4	0	125,311,309.08
		A	0	3	0	119,055,025.08
1.3 Plantas de tratamiento de aguas residuales construidas	Planta	P	0	4	0	53,391,199.55
		P(a)	0	4	0	64,382,262.23
		A	0	1	4,734,778.68	58,125,978.23
1.4 Planta de tratamiento agua potable	Planta	P	0	1		6,296,775.87
		P(a)	0	1		6,296,775.87
		A	0	1	0	6,296,775.87

Component Nbr. 2 Mejoramiento de la Gestión Operativa

Output	Unit of Measure		PHYSICAL PROGRESS		FINANCIAL PROGRESS	
			2020	EOP 2022	2020	EOP 2022
2.1 Macromedidores instalados	Macromedidores	P	0	80	0	2,581,176
		P(a)	0	80	0	2,581,176
		A	0	80	0	2,581,176
2.2 Micromedidores instalados	Micromedidores	P	0	29,000	0	10,628,824
		P(a)	0	29,000	0	10,628,824
		A	0	29,000	0	10,628,824
2.3 Talleres de capacitación a entes provinciales realizados	Talleres	P	0	2	0	50,000
		P(a)	0	2	0	50,000
		A	0	0	0	0

Other Cost

Ingeniería y Administración	P			185,727	20,120,000
	P(a)			185,727	21,046,945.11
	A			1,112,672.11	13,151,255.11
Auditoría, Evaluación y Seguimiento	P			0	340,000
	P(a)			0	340,000
	A			0	0
Costos Financieros y Auditoría	P			0	12,800,000
	P(a)			0	12,815,815.48
	A			15,815.48	2,220,908.48
Escalamiento	P			0	128,710,000
	P(a)			0	112,583,978.36
	A			0	0

Total Cost

Total Cost	P			8,913,134	419,000,000
	P(a)			8,913,134	419,000,000
	A			25,039,155.64	265,510,288.64

PMR Public Report

CHANGES TO THE MATRIX

Section	Name	Type of Change	Subtype	Modified By	Entered in the System
Output	Plantas de tratamiento de aguas residuales construidas	Modify Output	Modify Financial EOP P(a) value - caused by a change in the Financial P(a).	SOFIAG	03/26/2021
	Sistemas de Saneamiento Construidos	Modify Output	Modify Financial EOP P(a) value - caused by a change in the Financial P(a).	SOFIAG	03/26/2021
			Modify Physical Historical Actual	SOFIAG	03/26/2021

PMR Public Report

IMPLEMENTATION STATUS AND LEARNING

Lesson Learned - Categories

Intra/Inter Coordination
