



Integrated Growth Poles and Corridor Project 2 (P113971)

AFRICA | Madagascar | Competitive Industries Practice Global Practice |
IBRD/IDA | Investment Project Financing | FY 2015 | Seq No: 1 | ARCHIVED on 24-Jun-2015 | ISR19532 |

Implementing Agencies: National Project Secretariat

Key Dates

Key Project Dates

Board Approval date:18-Dec-2014

Effectiveness Date:09-Mar-2015

Planned Mid Term Review Date:03-Apr-2017

Actual Mid-Term Review Date:--

Original Closing Date:30-Sep-2019

Revised Closing Date:30-Sep-2019

Project Development Objectives

Project Development Objective (from Project Appraisal Document)

The Project Development Objective is to contribute to increased economic opportunities and access to enabling infrastructure services, as measured by an increase in jobs and formal firms, in Targeted Regions. The Program objective of the Series of Projects (SOP) is the same as the PDO of this Project.

Has the Project Development Objective been changed since Board Approval of the Project Objective?

No

Components

Name

COMPONENT 1: STRENGTHENING THE ENABLING ENVIRONMENT FOR ENTREPRENEURSHIP AND INVESTMENT:(Cost \$11.00 M)

COMPONENT 2:SECTOR BASED GROWTH IN THE ATSIMO-ANDREFANA, ANOSY AND DIANA REGIONS:(Cost \$35.50 M)

COMPONENT 3:PROJECT IMPLEMENTATION, M&E, SAFEGUARDS, IMPACT EVALUATION:(Cost \$3.50 M)

Overall Ratings

Name	Previous Rating	Current Rating
Progress towards achievement of PDO	--	● Satisfactory
Overall Implementation Progress (IP)	--	● Satisfactory
Overall Risk Rating	--	● Moderate



Implementation Status and Key Decisions

The Project became effective according to plan (ten weeks following Board approval) and disbursement conditions are either fulfilled or on track to be fulfilled within the stated time line.

The first Project Steering Committee will be organized on May 23rd.

It was agreed that the Project would finance urgent technical assistance, upon request, to the Ministry of Finance if it were to assess the economic and financial implications of a prospective PPP for the airports of Nosy Be and Ivato.

The Project launch will be held on June 18-19, 2015, and be launch will be split into: (i) a visit to Diego to visit areas of particular interest; and (ii) a breakfast meeting at the Presidency in Antananarivo.

Risks

Systematic Operations Risk-rating Tool

Risk Category	Rating at Approval	Previous Rating	Current Rating
Political and Governance	--	--	● Substantial
Macroeconomic	--	--	● Low
Sector Strategies and Policies	--	--	● Moderate
Technical Design of Project or Program	--	--	● Moderate
Institutional Capacity for Implementation and Sustainability	--	--	● Low
Fiduciary	--	--	● Moderate
Environment and Social	--	--	● Moderate
Stakeholders	--	--	● Low
Other	--	--	--
Overall	--	--	● Moderate

Results

Project Development Objective Indicators



▶ Number of formal jobs created in the targeted poles (Number, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	3257.00	--	--	8000.00
Date	31-Dec-2013	--	--	31-Dec-2018

▲ Of which in the Diana region (Number, Custom Breakdown)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	1528.00	--	--	4000.00
Date	31-Dec-2013	--	--	31-Dec-2018

▷ Of which in tourism (Number, Custom Breakdown)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	492.00	--	--	600.00
Date	31-Dec-2013	--	--	31-Dec-2018

▲ Of which in Atsimo-Andrefana region (Number, Custom Breakdown)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	335.00	--	--	2500.00
Date	31-Dec-2013	--	--	31-Dec-2018

▷ In which in tourism (Number, Custom Breakdown)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	79.00	--	--	500.00



Date	31-Dec-2013	--	--	31-Dec-2018
------	-------------	----	----	-------------

▲ Of which in Anosy region (Number, Custom Breakdown)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	1394.00	--	--	1500.00
Date	31-Dec-2013	--	--	31-Dec-2018

▶ Number of formal businesses newly registered in the target poles (Number, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	1542.00	--	--	2080.00
Date	31-Dec-2013	--	--	31-Dec-2018

▲ Of which in Atsimo-Andrefana region (Number, Custom Breakdown)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	130.00	--	--	230.00
Date	31-Dec-2013	--	--	31-Dec-2018

▲ Of which in Anosy region (Number, Custom Breakdown)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	383.00	--	--	550.00
Date	31-Dec-2013	--	--	31-Dec-2018



▲ Of which in Diana region (Number, Custom Breakdown)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	1029.00	--	--	1300.00
Date	31-Dec-2013	--	--	31-Dec-2018

▶ Direct project beneficiaries (Number, Core)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	--	--	172000.00
Date	31-Dec-2014	--	--	31-Dec-2018

▲ Of which people provided with improved water sources under the project (Number, Custom Breakdown)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	--	--	65000.00
Date	31-Dec-2014	--	--	31-Dec-2018

▲ Of which people provided with access to regular solid waste collection under the project (Number, Custom Breakdown)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	--	--	80000.00
Date	31-Dec-2014	--	--	31-Dec-2018

▲ Female beneficiaries (Percentage, Core Supplement)



	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	--	--	50.00

Overall Comments

Intermediate Results Indicators

▶ Number of reforms (Number, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	--	--	8.00
Date	31-Dec-2014	--	--	31-Dec-2018

▲ Of which reforms related to tax simplification (Number, Custom Breakdown)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	--	--	2.00
Date	31-Dec-2014	--	--	31-Dec-2018

▲ Of which reforms related to commercial disputes (Number, Custom Breakdown)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	--	--	2.00
Date	31-Dec-2014	--	--	31-Dec-2018



▲ Of which IC reforms (Number, Custom Breakdown)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	--	--	4.00
Date	31-Dec-2014	--	--	31-Dec-2018

▶ Increase in the number of wage jobs in the target corridors in the target poles (Percentage, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	--	--	10.00
Date	31-Dec-2014	--	--	31-Dec-2018

▲ Of which in Atsimo-Andrefana region (Percentage, Custom Breakdown)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	--	--	10.00
Date	31-Dec-2014	--	--	31-Dec-2018

▲ Of which in the Diana region (Percentage, Custom Breakdown)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	--	--	10.00
Date	31-Dec-2014	--	--	31-Dec-2018



▶ Annual municipal revenues collected in the target poles (Amount(USD), Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	3074.00	--	--	4050.00
Date	31-Dec-2014	--	--	31-Dec-2018

▲ Of which in Anosy region (Amount(USD), Custom Breakdown)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	681.00	--	--	850.00
Date	31-Dec-2013	--	--	31-Dec-2018

▲ Of which in Atsimo-Andrefana region (Amount(USD), Custom Breakdown)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	929.00	--	--	1350.00
Date	31-Dec-2013	--	--	31-Dec-2018

▲ Of which in the Diana region (Amount(USD), Custom Breakdown)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	1464.00	--	--	1850.00
Date	31-Dec-2013	--	--	31-Dec-2018



► Roads Rehabilitated (Kilometers, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	--	--	12.00
Date	31-Dec-2014	--	--	31-Dec-2018

▲ Of which non rural (Kilometers, Custom Breakdown)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	--	--	12.00
Date	31-Dec-2014	--	--	31-Dec-2018

► Passengers traffic, including tourists by air or sea per annum in target poles (Number, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	262653.00	--	--	325000.00
Date	31-Dec-2013	--	--	31-Dec-2018

▲ Of which in Atsimo-Andrefana region (Number, Custom Breakdown)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	58477.00	--	--	75000.00
Date	31-Dec-2013	--	--	31-Dec-2018



▲ Of which in the Diana region (Number, Custom Breakdown)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	204176.00	--	--	250000.00
Date	31-Dec-2013	--	--	31-Dec-2018

▶ Hotel rooms for establishments in the target poles (Number, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	4694.00	--	--	5150.00
Date	31-Dec-2013	--	--	31-Dec-2018

▲ Of which in Atsimo-Andrefana region (Number, Custom Breakdown)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	1465.00	--	--	1700.00
Date	31-Dec-2013	--	--	31-Dec-2018

▲ Of which in the Diana region (Number, Custom Breakdown)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	3229.00	--	--	3450.00
Date	31-Dec-2013	--	--	31-Dec-2018



▶ Export value for the selected crops in the target poles (Amount(USD), Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	30600000.00	--	--	46000000.00
Date	31-Dec-2013	--	--	31-Dec-2018

▲ Of which in Atsimo-Andrefana region (cotton and sea cucumber) (Amount(USD), Custom Breakdown)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	9000000.00	--	--	18000000.00
Date	31-Dec-2013	--	--	31-Dec-2018

▲ Of which in the Diana region (cocoa, cashew, ylang ylang) (Amount(USD), Custom Breakdown)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	21600000.00	--	--	28000000.00
Date	31-Dec-2013	--	--	31-Dec-2018

▶ Increase in revenues from target cash crop production for smallholders in the target corridors in the target poles (Percentage, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	--	--	7.00
Date	31-Dec-2013	--	--	31-Dec-2018



▶ Local Governance Index in the targeted municipalities (Percentage, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	--	--	8.00
Date	31-Dec-2013	--	--	31-Dec-2018

▲ Of which in Anosy region (Percentage, Custom Breakdown)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	--	--	8.00
Date	31-Dec-2013	--	--	31-Dec-2018

▲ Of which in Atsimo-Andrefana region (Percentage, Custom Breakdown)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	--	--	8.00
Date	31-Dec-2013	--	--	31-Dec-2018

▲ Of which in the Diana region (Percentage, Custom Breakdown)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	--	--	8.00
Date	31-Dec-2013	--	--	31-Dec-2018



► Enterprises directly benefiting from the project (Number, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	--	--	60.00
Date	31-Dec-2014	--	--	31-Dec-2018

► Annual additional sales value of firms supported by the MBIF (Amount(USD), Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	--	--	150000.00
Date	31-Dec-2014	--	--	31-Dec-2018

► People provided with Business Development Services and training programs (Number, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	--	--	3000.00
Date	31-Dec-2014	--	--	31-Dec-2018

► Farmers provided with improved inputs and equipment (Number, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	--	--	4000.00
Date	31-Dec-2014	--	--	31-Dec-2018

Overall Comments

Data on Financial Performance




Disbursements (by loan)

Project	Loan/Credit/TF	Status	Currency	Original	Revised	Cancelled	Disbursed	Undisbursed	Disbursed
P113971	IDA-55640	Effective	XDR	33.80	33.80	0.00	3.36	30.44	10%

Key Dates (by loan)

Project	Loan/Credit/TF	Status	Approval Date	Signing Date	Effectiveness Date	Orig. Closing Date	Rev. Closing Date
P113971	IDA-55640	Effective	18-Dec-2014	18-Dec-2014	09-Mar-2015	30-Sep-2019	30-Sep-2019

Cumulative Disbursements

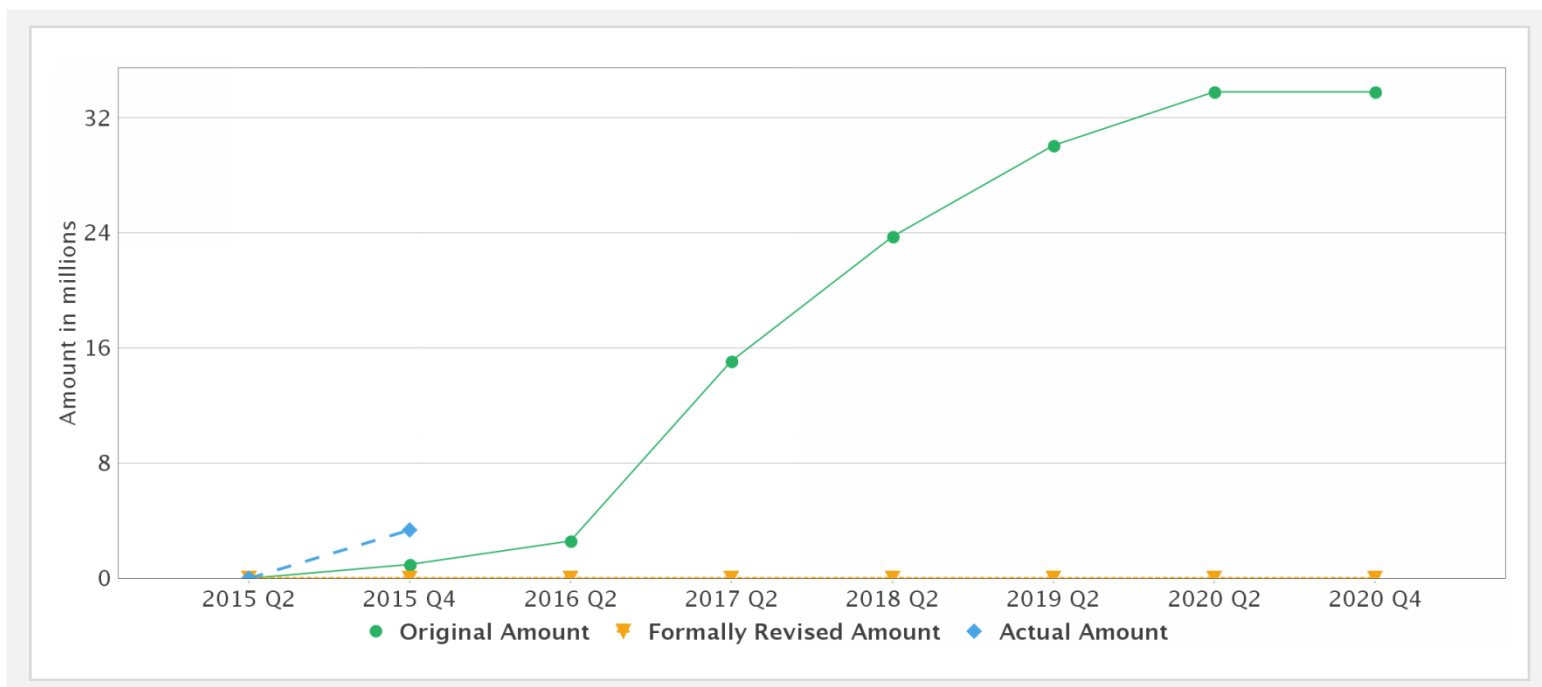

Restructuring History

There has been no restructuring to date.

Related Project(s)

There are no related projects.

