

Updated Initial Environmental Examination

Project number: 35173-013
July 2015

NEP: Third Small Towns Water Supply and Sanitation Sector Project —Itahari (Sunsari District)

Prepared by ITECO Nepal (P) Ltd., SILT Consultants (P) Ltd., and Unique Engineering Consultancy (P) Ltd. for the Government of Nepal and the Asian Development Bank.

This revised initial environmental examination report is a document of the borrower. The views expressed herein do not necessarily represent those of ADB's Board of Directors, Management, or staff, and may be preliminary in nature.

In preparing any country program or strategy, financing any project, or by making any designation of or reference to a particular territory or geographic area in this document, the Asian Development Bank does not intend to make any judgments as to the legal or other status of any territory or area.



Government of Nepal
Ministry of Urban Development
Department of Water Supply and Sewerage
Small Towns Water Supply and Sanitation Sector Project (STWSSSP)
Project Management Office (PMO)
Panipokhari, Maharajgunj, Kathmandu, Nepal



**Enhance Functionality in Small Towns Water Supply and Sanitation
Sector Project (STWSSSP)**

UPDATED INITIAL ENVIRONMENTAL EXAMINATION REPORT (IEE)

for
Itahari Small Towns Water Supply and Sanitation Sector Project
Sunsari District



Kathmandu, July 2015

Submitted by:

Joint Venture in Between



ITECO Nepal (P) Ltd.

P. O. Box 2147
Min Bhawan, Kathmandu, Nepal
Tel: ++977-1- 46 21 764 (Hunting Line),
Fax : ++ 977-1- 46 22 298
E-mail: iteco@mos.com.np
Website: www.iteconepal.com



SILT Consultants (P) Ltd.

P.O. Box 2724
Ratopul, Gaushala, Kathmandu, Nepal
Tel: ++977-1-44 87 598, 44 75139
Fax: ++977-1-44 73 573
E-mail: silt@mos.com.np, info@silt.com.np
Website: www.silt.com.np



**Unique Engineering
Consultancy (P) Ltd.**

P. O. Box 3522, Jwagal-10, Lalitpur, Nepal
Tel: ++977-1-55 49 332, 55 29 896
Fax: ++977-1-55 49 332
E-mail: unecnepal@gmail.com
Website: www.unecnepal.com.np

Table of Contents

EXECUTIVE SUMMARY	VII
1. INTRODUCTION	1
1.1 Background.....	1
1.2 Objectives of IEE	1
1.3 Rational of IEE Requirement	1
1.4 Methodology Used in Preparing IEE	1
2. POLICY, LEGAL & ADMINISTRATIVE FRAMEWORK	2
2.1 ADB Policy.....	2
2.2 ADB Safeguards policy.....	2
2.3 Nepal’s Environmental Policy and Legal Framework.....	4
3. ANALYSIS OF ALTERNATIVES	10
3.1 Alternatives considered in the approved IEE report 2006.....	10
3.1.1 Design Standards.....	11
3.1.2 Project Site	13
3.1.3 Time Schedule.....	13
3.2 Alternatives for the Updated IEE.....	13
4. DESCRIPTION OF SUBPROJECT	14
4.1 The Study Area.....	14
4.2 Existing Condition and Need for the Subproject	16
4.2.1 General Information	16
4.2.2 Technical Information	16
4.2.3 Socio- economic Information	17
4.2.4 Financial Information	17
4.3 Sub Project Construction schedule.....	17
5. DESCRIPTION OF THE ENVIRONMENT	19
5.1 PHYSICAL PROFILE	19
5.1.1 Topography	19
5.1.2 Climate	19
5.1.3 Surface and Groundwater.....	19
5.1.4 Water Quality Analysis.....	19
5.2 ECOLOGICAL PROFILE	20
5.2.1 Flora	20
5.2.2 Fauna	20
5.2.3 Protected Areas.....	20
5.3 Socio economic condition	20
5.3.1 Population, Communities and Occupation.....	20
5.3.2 Health and Sanitation	20
5.3.3 Economic Characteristics	21
5.3.4 Infrastructure Facilities.....	21
5.3.5 Land Use Planning	21
5.3.6 Quality of Life Values.....	21
5.4 Resettlement, Relocation and Compensation Issue	21
6. DESCRIPTION OF IMPACT ASSESSMENT.....	23

6.1	Physical Environment	23
6.1.1	Impact on land use pattern	23
6.1.2	Flooding and Stagnant Water Problem.....	23
6.1.3	Impact on water/land quality	23
6.1.4	Impacts of sediments and Disinfecting Chemicals.....	23
6.1.5	Impacts on Air Quality.....	23
6.1.6	Impacts on Acoustic Environment	23
6.1.7	Impacts on Traffic and Temporary disturbance	23
6.1.8	Water Volume/Quality.....	24
6.2	Biological Environment	24
6.2.1	Impact on natural vegetation and ecology	24
6.2.2	Impact on aquatic life.....	24
6.2.3	Loss of habitat	24
6.3	Socio-Economic and Cultural Environment.....	24
6.3.1	Land acquisition.....	24
6.3.2	Outside workforce conflict/health/pollution/culture.....	24
6.3.3	Workers' Health and Safety Hazards.....	24
6.3.4	Water right Conflict	24
6.4	Beneficial impacts.....	24
7.	DESCRIPTION OF MITIGATION MEASURES.....	25
7.1	Physical Environment	25
7.1.1	Impact on land use pattern	25
7.1.2	Flooding and Stagnant Water Problem.....	25
7.1.3	Water/land quality.....	25
7.1.4	Impacts of sediments and Disinfecting Chemicals.....	25
7.1.5	Water volume	25
7.1.6	Impacts on Air Quality.....	25
7.1.7	Impacts on Acoustic Environment	25
7.1.8	Traffic and Temporary disturbance.....	26
7.2	Biological Environment	26
7.2.1	Impact on natural vegetation and habitat.....	26
7.3	Socio-economic and cultural environment	26
7.3.1	Land acquisition.....	26
7.3.2	Outside workforce conflict/health/pollution/culture.....	26
7.3.3	Workers' Health and Safety Hazards.....	26
7.3.4	Water right Conflict	26
7.4	Enhancement of Beneficial Impacts.....	26
7.5	Activities for Rehabilitation Work and its Mitigation Measures.....	27
8.	INFORMATION DISCLOSURE, CONSULTATION AND PARTICIPATION.....	30
8.1	Consultation.....	30
8.2	Initial consultation: the existing project	30
8.3	The consultation during IEE update	30
8.3.1	Phase I	30
8.3.2	Phase II	31
8.4	Costs.....	31
9.	GRIEVANCE REDRESS MECHANISM.....	32
9.1	Purpose of the Grievance Redress Mechanism.....	32
9.1.1	First Level of GRM (WUSC-level).....	32
9.1.2	Second Level of GRM (VDC/Municipality level).....	33
9.1.3	Third Level of GRM (PMO Level)	33

10. ENVIRONMENT MANAGEMENT PLAN	35
10.1 Institutional Arrangement	35
10.1.1 Executing and implementing agencies	35
10.2 Safeguard Implementation Arrangement	35
10.3 Institutional Capacity Development Program	37
10.4 Staffing Requirement and Budget	38
10.5 Monitoring and Reporting	38
10.6 Environmental Monitoring Mechanism	38
10.7 Monitoring Reporting Mechanism	39
10.8 Monitoring Cost, Parameters, Location and Schedule	39
10.9 Contractors Compliance on EMP	39
10.10 Institutional Capacity Development Program	39
10.11 Environmental Mitigation Cost	39
11. CONCLUSIONS AND RECOMMENDATIONS	47
12. COMMENTS INCORPORATION MATRIX	48

List of Tables

Table 2-1: ADB SPS, 2009 Safeguard Requirements 1: Environment	2
Table 2-2: Other Relevant Environmental and Core Labor Policies, Laws and Guidelines of Nepal Applicable to the Subproject	6
Table 3-1: Comparison of the Options	11
Table 3-2: Adopted Population Growth Trend	11
Table 3-3: Water Consumption Pattern	12
Table 4-1: Technical Details	16
Table 7-1: Activities for Rehabilitation Work	28
Table 8-1: Lists of People and Institutions Consulted	30
Table 10-1: Mitigation measures and corresponding Monitoring plan	40
Table 10-2: Mitigation Measures and Monitoring Plan for Rehabilitation Activities	45

List of Figures

Figure 4-1: Location of the Project Area	15
--	----

Annexes

- Annex 1:** Project Location Map and Water Supply Plan
- Annex 2:** Water Tested Laboratory Analysis Report
- Annex 3:** Rapid Environment Assessment (REA) Checklist
- Annex 4:** Minute of Meeting

Abbreviations

°C	: Degree Centigrade
ADB	: Asian Development Bank
CBD	: Convention of Biological Diversity
CITES	: Convention on International Trade in Endangered Species of wild Fauna and Flora
cum	: Cubic Meter
DSC	: Design and Supervision Consultant
DWSO	: District Water Supply Office
DWSS	: Department of water Supply and Sewerage
EA	: Environmental Assessment
EARF	: Environmental Assessment Regional Office
EIA	: Environmental Impact Assessment
EMP	: Environmental Management Plan
EPA	: Environmental Protection Act
EPR	: Environment Protection Regulations
GoN	: Government of Nepal
HHE	: Health and Hygiene Education Programs
HRF	: Horizontal Roughing Filter
IEE	: Initial Environmental Examination
JICA	: Japanese International Cooperation Agency
km	: Kilometer
IWSSSP	: Itahari Water Supply and Sanitation Sub-Project
LGs	: Local Governments
lpd	: Liter per day
lps	: Liter per second
m	: Meter
MDG	: Millennium Development Goals
MOWR	: Ministry of Water Resources
MPPH	: Ministry of Physical Planning and Housing
MPPW	: Ministry of Physical Planning and Works
MoSTE	: Ministry of Science, Technology and Environment
NGO	: Non-Government Organization
NDWQS	: National Drinking Water Quality Standard
NPC	: National Planning Commission
NRs.	: Nepalese Rupees
O&M	: Operation and Maintenance
PAC	: Public Awareness Campaign
PCO	: Public Call Office
PF	: Pressure Filter
Pop.	: Population
PRA	: Participatory Rural Appraisal
PMO	: Project Management Office
RRA	: Rapid Rural Appraisal
RPMO	: Regional Project Management Office
SPSO	: Sub-Project Site Office
SSF	: Slow Sand Filter
SPS	: Safeguard Policy Statement

STWSSSP : Small Town Water Supply and Sanitation Sector Project
TDF : Town Development Fund
VDC : Village Development Committee
WHO : World Health Organization
WSUC : Water Supply Users' Committee
WUSC : Water Users and Sanitation Committee

EXECUTIVE SUMMARY

General

The Enhance Functionality in Small Towns Water Supply and Sanitation Sector Project (STWSSSP) will support the government of Nepal (the Government) in improving water supply and sanitation facilities and services to 24 small towns in Nepal. Out of the 265 small towns in Nepal, Asian Development Bank (ADB) has already supported the Government, through successful implementation of earlier two projects in 50 towns. These include the 24 project for enhancement.

The outcome will be inclusive and sustainable water supply and sanitation service delivery in this Itahari small town of Nepal. The project will implement improvements/ rehabilitation works within the service area of already completed project. There will be minor civil works necessary for the enhancement of the components without changing the original technical and social concepts.

The Project will be implemented in 6 months period starting around first week of November, 2015.

The project will be funded by a loan using a sector lending approach of ADB. The Executing Agency is the Ministry of Urban Development and the implementing agency is the Department of Water Supply and Sanitation (DWSS).

The sub project IEE report was approved by government of Nepal in 2005. Now the sub project is envisaged to undergo for rehabilitation of project components such as, intake treatment plant, transmission main and distribution line etc. The proposed updated IEE is prepared as an integral part of bid document. However consultant has updated the contents of IEE report already approved from government of Nepal.

This updated IEE Report summarizes anticipated impacts and corresponding mitigation measures, monitoring and also includes cost and time frame for implementation.

In this report, all the policy, legal and administrative framework requirements of ADB including ADB Safeguard Policy and the prevailing GoN Acts/rules & regulations have been considered.

Categorization

Itahari town subproject is classified as Environmental Category B as per the SPS as no significant impacts are envisioned. Accordingly this updated Initial Environmental Examination (IEE) has been prepared and assesses the environmental impacts and provides mitigation and monitoring measures to ensure no significant impacts as a result of the subproject.

Subproject Scope

The subproject is formulated under the 3STWSSSP to improve water supply and sanitation service delivery in the existing Itahari water supply and sanitation project constructed during STWSSP 1. Investments under this subproject includes; (i) rehabilitation of a piped water supply system including intake, water treatment plant, transmission main, and distribution main.

Implementation Arrangements

The Ministry of Urban Development is the executing agency. The Department of Water Supply and Sewerage (DWSS) is the implementing agency. Implementation activities will be overseen by a separate Project Management Office (PMO) which will be established in DWSS head office in Kathmandu and two Regional Project Management Offices (RPMOs) in the eastern and western region. A team of technical, administrative and financial officials, including safeguards specialists, will be provided at the PMO to implement, manage and monitor project implementation activities. The RPMOs will be staffed by qualified and experienced officers and will be responsible for the day-to-day activities of project implementation in the field, and will be under the direct administrative control of the PMO. Consultant teams are responsible for subproject planning and management and assuring technical quality of design and construction; and designing the infrastructure and supervising construction; and safeguards preparation.

Description of the Environment

Subproject components are located in Itahari town area and in its immediate surroundings. There is no presence of natural habitat in this project area. The project components will be located in WUSC sites, public road rights-of-way (ROW) and outside the community managed forest and the protected areas. There are no protected areas, wetlands, mangroves, or estuaries in or near the subproject locations.

Environmental Management

An environmental management plan (EMP) is included as part of this IEE, which includes (i) mitigation measures for environmental impacts during implementation; (ii) an environmental monitoring program, and the responsible entities for mitigating, monitoring, and reporting; (iii) public consultation and information disclosure; and (iv) a grievance redress mechanism. A number of impacts and their significance have already been reduced by amending the designs. The EMP will be included in civil work bidding and contract documents.

Locations and sitting of the infrastructures were considered in the existing sub-project to further reduce impacts. The concepts considered in design of the subproject are: (i) demand for new piped water supply; (ii) maximum population coverage with pipe layout mostly in residential areas and areas of high growth rate; (iii) avoidance of water-use conflicts; (iv) locating pipelines within ROWs to reduce acquisition of land; (v) locating pipelines at least 10 meters from latrines, septic tanks and any main drains to avoid contamination; (vi) locating Intake point 30 m upstream from sanitation facilities; (vii) locating household and public latrines and septic tanks at least 30 meters downstream from the nearest drinking water source; (viii) piloting controlled disposal of septage in accordance to WHO and US EPA standards to reduce the likelihood of uncontrolled disposal as currently practiced; and (ix) ensuring all planning and design interventions and decisions were made in consultation with local communities and reflecting inputs from public consultation and disclosure for site selection.

During the construction phase, impacts mainly arise from the need to dispose of moderate quantities of waste soil; and from the disturbance of residents, businesses, and traffic. These are common impacts of construction in urban areas, and there are well developed methods for their mitigation. Measures such as conducting work in lean season and minimizing inconvenience by best construction methods will be employed. Traffic management will be necessary during pipe-laying on busy roads. In the operational phase, all facilities and infrastructure will operate with routine maintenance, which should not affect the environment. Facilities will need to be repaired from time to time, but environmental impacts will be much less than those of the construction period as the work will be infrequent, affecting small areas only.

Mitigation Measures

Mitigation measures have been developed to reduce all negative impacts to acceptable levels. Mitigation will be assured by a program of environmental monitoring to be conducted during construction. The environmental monitoring program will ensure that all measures are implemented, and will determine whether the environment is protected as intended. It will include observations on- and off-site, document checks, and interviews with workers and beneficiaries. Any requirements for corrective action will be reported to the ADB.

The stakeholders were involved in developing the IEE through discussions on-site and public consultation, after which views expressed were incorporated into the IEE and in the planning and development of the subproject. The IEE will be made available at public locations in the town and will be disclosed to a wider audience via the ADB and DWSS websites. The consultation process will be continued and expanded during project implementation to ensure that stakeholders are fully engaged in the project and have the opportunity to participate in its development and implementation.

The service area of the project covers ward no. 1 to 9 of Itahari Municipality, ward no 1 of Hansposa VDC and Ward no 4 of Ekamba VDC. The core area of the project is market area situated along both sides of the East-West Highway and Biratnagar-Dharan road. The main market area of the municipality is located in the central part. This area is densely populated market area where main economic activities are carried out. The service areas in Ekamba and Hansposa VDCs have semi-

urban settlements with less dense population compared to core area.

The sub-project under construction is a rehabilitation project and the mitigation measures recommended in the approved IEE in 2006 have already been successfully implemented. During the updated IEE preparation process, all of the process mentioned above have been checked and followed. The design report has incorporated the recommended mitigation measures.

During construction phase, there are no major environmental impacts in the enhancement project. However there are minor impacts like decrease in water table, water logging, air and noise pollution during construction, traffic disturbances and some disturbances in household water supply distribution. In order to minimize the impacts, specific arrangements have been made in the design and incorporated in the specification of work. The contractor is responsible to follow all the instruction given by the DSC and agreed specifications.

During operational phase also, there will be no significant impacts. However there may be minor impact on water right conflict (tap distribution) and occupational health and safety of workers. These issues will be addressed by and will be the responsibility of WUSC.

Consultation, Disclosure and Grievance Redress

Public consultations were done in the preparation of the project and IEE and throughout the project implementation period of the completed project.

During the preparation of this enhancement project and updated IEE, Public consultations were done at different phases. The first consultation was done during survey and design period. Further consultation was made with the stakeholders at project site after the project design report was approved.

The consultation was focused on environmental impacts, resettlement, social issues, relocation and compensation issues.

Monitoring and Reporting

The PMO, RPMO and DSMC will be responsible for environmental monitoring. The RPMO with support from the DSMC will submit monthly monitoring reports to the PMO. The PMO will consolidate the monthly reports and will send semi-annual monitoring reports to ADB. ADB will post the environmental monitoring reports on its website.

Conclusions and Recommendations

The proposed subproject is unlikely to cause significant adverse impacts. The potential impacts that are associated with design, construction and operation can be mitigated to standard levels without difficulty through proper engineering design and the incorporation or application of recommended mitigation measures and procedures. Based on the findings of the IEE, there are no significant impacts and the classification of the subproject as Category "B" is confirmed. No further special study or detailed environmental impact assessment (EIA) needs to be undertaken to comply with ADB SPS (2009).

1. INTRODUCTION

1.1 Background

1. The Enhance Functionality in Small Towns Water Supply and Sanitation Sector Project (STWSSSP) will support the government of Nepal (the Government) in improving water supply and sanitation facilities and services to 24 small towns in Nepal. Out of the 265 small towns in Nepal, Asian Development Bank (ADB) has already supported the Government, through successful implementation of earlier two projects in 50 towns. These include the 24 project for enhancement.
2. The Enhance Functionality in Small Towns Water Supply and Sanitation Sector Project (STWSSSP) will be implemented in 9-12 months period starting around first week of November, 2015 and will be funded by a loan using a sector lending approach of ADB. The Executing Agency is the Ministry of Urban Development and the implementing agency is the Department of Water Supply and Sanitation (DWSS).
3. The outcome will be inclusive and sustainable water supply and sanitation service delivery in selected small towns in Nepal. The project will implement improvements/rehabilitation works within the service area of already completed 24 projects. There will be minor civil works necessary for the enhancement of the components without changing the original technical and social concepts.

1.2 Objectives of IEE

4. The Updated IEE summarizes anticipated impacts and corresponding mitigation measures, monitoring and also includes cost and time frame for implementation.

1.3 Rational of IEE Requirement

5. The sub project IEE report was approved by government of Nepal in 2005. Now the sub project is envisaged to undergo for rehabilitation of project components such as, treatment plant (specific area) of transmission and distribution line. The proposed IEE is prepared as an integral part of bid document. However consultant has updated the contents of IEE report already approved from government of Nepal.

1.4 Methodology Used in Preparing IEE

- In the process of preparation of EMP, an extensive review of approved IEE and feasibility reports reviewed with some field based information
- Public consultations were held in the entire process of IEE study and during the disclosure of the draft IEE report to the local people. These processes have taken place and the results were documented. The involvement of the local people in EMP implementation activities have been recommended in EMP, 2000. Accordingly, in the process of EMP implementation, the following mechanism has been adopted to involve the local people in EMP activity:
 - Public Consultation and Involvement have been given highest priority in the implementation of Mitigation measures carried out by EMP; initially prior to the implementation, public consultation usually takes place and on the basis of decision of the consultation meeting, implementation of mitigation measures are being prioritized and carried out with the involvement of local people.
 - Monitoring is another component of EMP. Monitoring of Physical, Biological and Socio-economic components of Environment of the project is being carried out. In the process of compliance monitoring of the project construction, local people and construction workers are being involved and consulted

2. POLICY, LEGAL & ADMINISTRATIVE FRAMEWORK

2.1 ADB Policy

6. All projects funded by the ADB must comply with the Safeguard Policy Statement (SPS) 2009 to ensure that projects undertaken as part of programs funded under ADB loans are environmentally sound, are designed to operate in compliance with applicable regulatory requirements, and are not likely to cause significant environmental, health, or safety hazards. With respect to the environment, the SPS 2009 is underpinned by the ADB Operations Manual, Bank Policy (OM Section F1/OP, 2010). The policy promotes international good practice as reflected in internationally recognized standards such as the World Bank Group's Environmental, Health and Safety Guidelines.¹

2.2 ADB Safeguards policy

7. ADB's environmental safeguards policy principles are defined in SPS, 2009, Safeguard Requirements¹ and the IEE is intended to meet these requirements, Table 2-1.

Table 2-1: ADB SPS, 2009 Safeguard Requirements 1: Environment

SPS 2009 - Safeguard Requirements	Remarks
Use a screening process for each proposed project, as early as possible, to determine the appropriate extent and type of environmental assessment (EA) so that appropriate studies are undertaken commensurate with the significance of potential impacts and risks.	REA has been undertaken (Annex A), indicating that subproject is NOT: (i) environmentally critical; and (ii) adjacent to or within environmentally sensitive/critical area. The extent of adverse impacts is expected to be local, site-specific, confined within main and
SPS 2009 - Safeguard Requirements	Secondary influence areas. Significant adverse impacts during construction will be temporary and short-term, can be mitigated without difficulty. There is no adverse impact during operation. Hence, IEE is sufficient. The IEE including specific description of the environment and corridor of impact will be updated as necessary based on the final design and alignments.
Conduct EA to identify potential direct, indirect, cumulative, & induced impacts and risks to physical, biological, socioeconomic (including impacts on livelihood through environmental media, health and safety, vulnerable groups, and gender issues), and physical cultural resources in the context of the project's area of influence. Assess potential transboundary global impacts, including climate change.	IEE has been undertaken to meet this requirement. (Section VI). No transboundary & global impacts, including climate change.
Examine alternatives to the project's location, design, technology, and components and their potential environmental and social impacts and document the rationale for selecting the particular alternative proposed. Also consider the no project alternative.	Analysis of "with-subproject" or "without subproject" is presented in Section III.
Avoid, and where avoidance is not possible, minimize, mitigate, &/or offset adverse impacts and enhance positive impacts by means of environmental planning & management. Prepare an EMP that includes the proposed mitigation	An EMP has been prepared to address this requirement. Section IX

¹New Version of the "World Bank Group Environmental, Health, and Safety Guidelines", April 30 2007, Washington, USA. <http://www.ifc.org/ifcext/enviro.nsf/Content/EnvironmentalGuidelines>

SPS 2009 - Safeguard Requirements	Remarks
<p>measures, environmental monitoring and reporting requirements, related institutional or organizational arrangements, capacity development and training measures, implementation schedule, cost estimates, and performance indicators.</p>	
<p>Carry out meaningful consultation with affected people & facilitate their informed participation. Ensure women's participation. Involve stakeholders, including affected people & concerned NGOs, early in the project preparation process & ensure that their views & concerns are made known to & understood by decision makers and taken into account. Continue consultations with stakeholders throughout project implementation as necessary to address issues related to EA. Establish a GRM to receive & facilitate resolution of affected people's concerns & grievances on project's environmental performance.</p>	<p>Key informant and random interviews have been conducted (Annex C). A grievance redress mechanism for the resolution of valid project-related social and environmental issues/concerns is presented in Section VIII.</p>
<p>Disclose a draft IEE (including the EMP) in a timely manner, before project appraisal, in an accessible place & in a form & language(s) understandable to affected people & other stakeholders. Disclose the final EA, & its updates if any, to affected people & other stakeholders.</p>	<p>The draft IEE will be disclosed on ADB's website prior to project appraisal. Copies of both SPS-compliant IEE and Government of Nepal-approved IEE will be made available at the offices of the PMO, Project Implementation Support Unit (PISU) and Water Users' and Sanitation Committee (WUSC) for public consultation. For the benefit of the community, the summary of the IEE will be translated in the local language and made available at (i) offices of executing and implementing agencies, (ii) area offices, (iii) consultant teams' offices; and (iv) contractor's campsites. It will be ensured that the hard copies of IEE are kept at places which are conveniently accessible to people, as a means to disclose the document and at the same time creating wider public awareness. An electronic version of the IEE will be placed in the official website of executing and implementing agencies and the ADB website after approval of the IEE by ADB</p>
<p>Implement the EMP and monitor its effectiveness. Document monitoring results, including the development and implementation of corrective actions, and disclose monitoring reports.</p>	<p>EMP implementation, reporting and disclosure of monitoring reports are in this IEE.</p>
<p>Do not implement project activities in areas of critical habitats, unless (i) there are no measurable adverse impacts on the critical habitat that could impair its ability to function, (ii) there is no reduction in the population of any recognized endangered or critically endangered species, and (iii) any lesser impacts are mitigated. If a project is located within a legally protected area, implement additional programs to promote and enhance the conservation aims</p>	<p>The subproject does not encroach into areas of critical habitats.</p>

SPS 2009 - Safeguard Requirements	Remarks
of the protected area. In an area of natural habitats, there must be no significant conversion or degradation, unless (i) alternatives are not available, (ii) the overall benefits from the project substantially outweigh the environmental costs, and (iii) any conversion or degradation is appropriately mitigated. Use a precautionary approach to the use, development, and management of renewable natural resources.	
Apply pollution prevention and control technologies and practices consistent with international good practices as reflected in internationally recognized standards such as the World Bank Group's Environmental, Health and Safety Guidelines. Adopt cleaner production processes and good energy efficiency practices. Avoid pollution, or, when avoidance is not possible, minimize or control the intensity or load of pollutant emissions and discharges, including direct and indirect greenhouse gases emissions, waste generation, and release of hazardous materials from their production, transportation, handling, and storage. Avoid the use of hazardous materials subject to international bans or phase-outs. Purchase, use, and manage pesticides based on integrated pest management approaches and reduce reliance on synthetic chemical pesticides.	This requirement is only minimally applicable to the subproject in the aspect of waste generation, e.g., effluent from septic tanks and generated sludge and sludge disposal from water supply and sanitation structures. The subproject will not involve hazardous materials subject to international bans/phase outs.
Provide workers with safe and healthy working conditions and prevent accidents, injuries, and disease. Establish preventive and emergency preparedness and response measures to avoid, and where avoidance is not possible, to minimize, adverse impacts and risks to the health and safety of local communities	EMP provides measures to mitigate health and safety hazards during construction and operation.
Conserve physical cultural resources and avoid destroying or damaging them by using field-based surveys that employ qualified and experienced experts during environmental assessment. Provide for the use of "chance find" procedures that include a pre-approved management and conservation approach for materials that may be discovered during project implementation	The subproject will not affect any physical cultural resource. The EMP recommends the measure/s to mitigate adverse impact on physical cultural resources (PCRs) in case of chance find.

2.3 Nepal's Environmental Policy and Legal Framework

8. The Interim Constitution of Nepal, 2007 defines the right to live in clean environment as one of the fundamental rights of its citizens (Article 16). It prescribes for the State to give priority to the protection of the environment and prevention of its further damage due to physical development activities (Clause 5 of Article 35). Proceeding from, and conformable to, the Constitution, the Government of Nepal has passed a series of environmental laws, policies and implementing regulations and standards. Among these, the basic legislation that provides the framework within which environmental assessment is carried out in Nepal is the:

- Environmental Protection Act (EPA), 1997. requires a proponent to undertake IEE or EIA of the proposed project and have the IEE or EIA report approved by the concerned sector

agency or Ministry of Science, Technology and Environment (MoSTE), respectively, prior to implementation. The EPA: (i) sets out the review and approval process of IEE and EIA reports, that involve informing and consulting stakeholders; (ii) stipulates that no one is to create pollution that would cause significant adverse impacts on the environment or harm to public life and health, or to generate pollution beyond the prescribed standards; (iii) specifies for the Ministry in charge of environment (currently the MoSTE) to conduct inspection of approved projects to ensure that pollution prevention, control or mitigation is carried out according to the approved IEE or EIA report; (iv) provides for the protection of objects and places of national heritage and places with rare plants, wildlife and biological diversity; and (v) states that any person/party affected by pollution or adverse environmental impact caused by anybody may apply to the prescribed authority for compensation to be recovered from the polluter/pollution generator.

- Environmental Protection Rules (EPR), 1997, and its amendments in 1999 and 2007. Defines the implementing rule and regulations of the IEE/EIA process, elaborating the provisions in the EPA. The preparation, review and approval of IEE and EIA reports are dealt with in Rules 3 to 7 and 10 to 14. Schedules 1 and 2 list down the projects of activities that are required IEE and EIA, respectively, as amended in 2007.
- Other environmental and core labor policies, laws and rules that are relevant to the subproject are presented in Table 2-2.

Table 2-2: Other Relevant Environmental and Core Labor Policies, Laws and Guidelines of Nepal Applicable to the Subproject,

Policy/Law/Guideline	Year	Relevant Provisions	Remarks
Resources Act	1992	Comprehensive law on the development, use and conservation of water resources in Nepal, it aims to minimize damage to water bodies by requiring the conduct of IEE & preparation of IEE Report before granting license to use water resources for any purpose.	Government of Nepal environmental assessment report will be prepared based on this IEE.
		Proponents shall make sure that the beneficial use of water resources does not cause damage to other water uses/users (Article 4).	The source is groundwater to be drawn from the deep aquifer. Prevailing water source is the shallow aquifer and water drawn has Mn, Fe, Al and coliform levels exceeding National Drinking Water Quality Standard (NDWQS). Hence, people are eager to be connected to piped water supply system.
		Article 17 requires proponents to apply for any necessary land acquisition accordingly;	Site for the intake well, treatment unit, overhead tank is government land (Dept. of Forest).
		Article 18 requires the compliance to quality standards in making use of water resources. Article 19 prohibits the pollution of water resources. Under the Act are two regulations for drinking water purposes: (i) Water Resources Regulation, 1993, setting out the implementation procedures for the Act; and (ii) the Drinking Water Regulation, 1998, which specifies compliance with the drinking water quality standards and control of water pollution (or sanitation) as it affects drinking water.	Environmental Management Plan prescribes the compliance with NDWQS and its Directives during operation.
Labor Act	1992	Chapter 5 stipulates health and safety provisions at work places, keeping work premises clean and safe, e.g., (i) with provisions for solid waste, sewage and hazardous substance management; (ii) instituting measures to prevent dust, fumes and other impure materials that would adversely affect health; (iii) with supply of potable water and water for emergency situations; (iv) with arrangements for the use of protective devices and wears; (v) with fire safety arrangements; and (vi) measures for protection from hazardous machines/equipment and from physical injury or harm from lifting of heavy weights.	EMP provides measures to mitigate workers' health and safety hazards.
Forest Act	1993	The Act prohibits the extraction of boulders, rocks,	Subproject will not impact on any forest. EMP stipulates

Policy/Law/Guideline	Year	Relevant Provisions	Remarks
		pebbles, sand or coal from national forests, defined as all forests, excluding private forests, whether marked or unmarked with forest boundary, to include waste or uncultivated lands, or unregistered lands surrounded by the forest or situated near adjacent forests as well as paths, streams rivers, lakes, riverine lands within the forest.	no illegal quarrying of natural aggregate materials.
National Environmental Policy and Action Plan (NEPAP)	1993	Of its five objectives, most relevant to the Project are to: (i) mitigate adverse environmental impacts; and (ii) safeguard national & cultural heritage & preserve biodiversity, within & outside protected areas.	Subproject will not impact on physical cultural heritage & biodiversity. EMP provides measures to mitigate impacts.
National Water Supply and Sanitation Policy	1998	The Policy requires the: (i) monitoring of water quality supplied by completed WSS projects; and (ii) evaluation of their benefits in improving health (e.g., reducing water-borne diseases) and in relieving the sufferings of women and other disadvantaged groups in carrying out their responsibilities over water collection and maintenance of sanitation and hygiene.	Monitoring of the quality of supplied water is prescribed in the EMP following the NDWQS Directives.
Drinking Water Rules	1998	The Rules: (i) gives the procedure for the settlement of dispute on use of water sources; (ii) requires water supplier to maintain the quality of water as prescribed in the Water Resources Act; (iii) prohibits water supplier to construct structures and conduct activities that would pollute the water source and cause significant adverse effect on the environment.	Monitoring of the quality of supplied water is prescribed in the EMP following the NDWQS Directives.
Local Self-Governance Act	1999	The Act gives Local Government the functions, duties & powers to: (i) conserve & protect their local environment & natural resources; (ii) plan, implement &/or operate & maintain local WS projects; (iii) implement or arrange for implementation local sanitation/sewerage & drainage projects; (iv) protect cultural heritage & religious sites; &/or (v) monitor project activities within their respective jurisdictions.	Provides basis for Local Government to monitor the environmental performance of the subprojects. EMP provides the responsibilities of Local Governments (LGs) in EMP implementation.
National Urban Policy	2007	Policy gives importance to environment conservation while carrying out urban development works and natural resource use; thus, supporting the required environmental	Government of Nepal Government of Nepal environmental assessment report, based on this IEE, will be prepared to ensure environmental conservation

Policy/Law/Guideline	Year	Relevant Provisions	Remarks
		conservation and protection in donor-assisted development projects.	and protection.
National Urban Water Supply and Sanitation Sector Policy	2008	The Policy requires the IEE or EIA of proposed WSS projects in accordance with the EPA/EPR to: (i) incorporate consultations with key stakeholders, including end-point users; & (ii) specify measures to mitigate environmental impacts prior to, during construction & operation, as well as corrective measures.	Government of Nepal environmental assessment report will be prepared based on this IEE. This ADB IEE will be submitted to ADB for review and approval.
Implementation Directives for the National Drinking Water Quality Standards	2005	It sets out the water sampling, testing, analysis, monitoring and surveillance procedures to certify that the quality of supplied drinking water conforms to the National drinking Water Quality Standards.	Monitoring of the quality of supplied water is prescribed in the EMP following the NDWQS Directives.
Updated 15-Yr Development Plan for Small Towns Water Supply and Sanitation Sector	2009	The Plan defines the population threshold of “small towns” to be in the range of 5,000 to 40,000. Reference to Schedules 1 and 2 of the EPR, as amended in 2007, places water supply projects in small towns under Schedule 1 or within the threshold of water supply projects requiring only an IEE. The Plan emphasizes monitoring and evaluation as an important component of a project to determine the overall impact of a project.	EMP prescribes environmental effects and performance monitoring.
Solid Waste Management Act	2011	Article 4 provides that the management of hazardous, medical, chemical or industrial waste rests upon the generators of such wastes. Management should be as prescribed in the Act. Article 5 provides that individuals and entities have the duty to reduce the amount of solid waste generated while carrying out work or business.	EMP prescribes eco- friendly management of solid and hazardous wastes.

9. The key Government of Nepal environmental quality standards are: (i) National Ambient Air Quality Standards for Nepal, 2003; (ii) National Noise Standard Guidelines, 2012; and (iii) National Drinking Water Quality Standards, 2006, which would also be applied to surface and ground water quality monitoring since these resources are used for drinking.
10. Nepal is party to the following international environmental agreements that have broad relevance to works and environmental assessment of works under the project: (i) World Heritage Convention, in 1978; (ii) Convention on Wetlands of International Importance Especially as Waterfowl Habitat (Ramsar Convention), in 1987; (iii) Convention on Biodiversity, in 1992, (iv) Vienna Convention for the Protection of the Ozone Layer and its Montreal Protocol and subsequent London Amendment, in 1994, and (v) Basel Convention on the Control of Transboundary Movements of Hazardous Wastes and Their Disposal, in 1996.
11. The relevance of the aforementioned environmental agreements to the subproject are on their emphasis for human activities (such as development projects) to: (i) take on/institute measures to protect the local, as well as global, natural resources and/or environment; (ii) prevent and/or reduce the causes of climate change; and (ii) anticipate and mitigate the adverse impacts of climate change. The country is also committed to the Millennium Development Goals (MDG), the seventh goal of which is to “ensure environmental sustainability” targeting the reverse of loss of forest and environmental resources, reduction of biodiversity loss, and increase in the proportion of population with sustainable access to safe drinking water and basic sanitation.

3. ANALYSIS OF ALTERNATIVES

3.1 Alternatives considered in the approved IEE report 2006

12. Feasibility of the proposed ISTWSSP is done by the survey team and visited all possible water sources around the Project area as per the TOR to assess and study the different alternative scheme designs for the project.. Feasible water sources in the Project area are limited. The team studied the existing boreholes pointed out by the communities. These boreholes are quite old and are still functioning as artesian wells. but with limited discharges as follows:

- Deep boring located within the premises of roads department at ward number - 5 - Discharge 1 1ps
- Deep boring - located at Janata Basti ward no. 5 - Discharge 0.5 1ps.
- Deep boring - located at ward number 7 and presently being used for local irrigation - Discharge 0.3 1ps.

13. The above existing boreholes are technically not viable because of their old age, existing deplorable condition, and very low yield.

Surface Water Sources

14. Surface water sources were also looked into for alternatives. Tyangra and Budhi khola streams were ruled out from the following considerations:

- The bed elevation of the stream is lower than the service area, thereby making it impossible for gravity flow.
- The stream is being used for irrigation purposes.
- iii) The stream is being used as waste disposal sites and the water is polluted.

15. In contrary to above, Taltaliya, a wet land located at the north-eastern corner of the municipality and with the forest area designated as its catchments, was found suitable and could be one of the surface water sources for the project. Keeping this in view, system alternatives have been studied as follows:

Itahari System A

16. There is no alternative other than underground water for this system. This system is an existing water supply system with 2 deep boreholes (20 1ps & 26 1ps) and one overhead reservoir 450 m³ capacity. The system will be rehabilitated for water treatment and for extension of distribution lines.

Itahari System B

17. There is no alternative other than underground water for this system. The system consisting of two deep boreholes at ward # 5, one overhead tank 450 m³ capacity and a loop design distribution network .

Itahari System C

18. The following two options have been studied for this Itahari System C .

Option I

19. Two Deep bore holes at ward 2 at Shantinagar, one OFT 450 m³ capacity, Loop Design Distribution Network .

Option II

20. Sump well (4 meter diameter 10 meter deep with collectors) at Taltaliya and pumping to overhead' tank located at Shantinagar ward no. 2, pumping main and distribution network.

Comparison of the Options

21. Detailed financial and economic analysis was made for both options I & II.. As a summary, a comparative description expressing important criteria for selection is presented in Table 3-1 below:

Table 3-1: Comparison of the Options

S.N	Description	Option I	Option II	Remarks (better
1	Project Cost Rs. (Water Supply	71,915,79	73,774,94	I
2	Cost per Capita Rs.	I		
	Base Year 2008 5971		6125	I
	Design Year 2022	3234	3318	I
3	AIEC Rs./Cu.m.	19.60	20.04	I
	AIFC Rs./ Cu.m.	23.87	24.39	I
	EIRR °A).	60.6	59.4	I
	FIRR %	8.2	8.3	I
4	Water Tariff Rs./Cu.m.			
	0 - 10	14.00	14.50	I
	1,1 - 20	21.00	21.00	I & II
	> 20	23.00	24.00	I
5	Affordability %			
	Low Income	3.30	3.42	I
	Average Income	2.99	3.09	I
	Higia Income	3.99	4.06	I

22. All above financial and economic indices reveal that option I is better than option II

Recommendation on option

23. From technical as well as financial point of consideration option I is better than option II. From EDC side, the option 1 is recommended for detailed engineering study.

3.1.1 Design Standards

Design Period

24. Considering higher growth rates associated with ISTWSSP, economic design period of 15 years has been adopted. Three years period has been adopted for preparation phase and construction phase.

Growth Rate

25. Population forecasting of Project Area has been analyzed by first estimating the size of the existing population. and assessing the different rate of growths by Census 2001, district data, ward wise growth rate, Itahari Municipality past historical data and the growth trend was considered for assessment of the realistic growth rate for the specific area under consideration. The adopted average growth rate is 4.39 percent per annum.

Table 3-2: Adopted Population Growth Trend

S N	Location	Adopted Growth Rate in %	Remarks
1	Itahari	1.57	Saturated Settlement
2		4.06	Rapidly Growing
3		2.56	Rural settlement
4		4.39	Rapidly Growing
5		4.39	Rapidly Growing
6		4.39	Rapidly Growing
7		4.39	Rapidly Growing
8		2.24	Saturated Settlement
9		4.39	Rural settlement
10	Hansposa 1	1.85	Rural settlement
11	Ekamba 4	4.39	Rapidly Growing

Service Level

26. The service level should be in accordance to consumer's needs, desires and willingness to pay. Service level improvement means essentially providing reliable and efficient supply predominantly through house connections and a few communities stand posts for disadvantaged groups. The per capita demand of 55 lpcd, and 75-100 lpcd is employed for community stand posts and private connections, respectively. 122 number of the community stand posts are allocated in Itahari project as per the desire and need of the WUSC and consumers. Majority of the households will obtain water by the private house connection facilities.

Adopted Water Demand Figures

27. The following water demand figures have been adopted for the design of the system. These figures are within the Design Guidelines for STWSSSP. Details on the adopted design values are as follows:

Domestic	Through community taps	55 lpcd
	Through yard connection	75 lpcd
	Through house connection	100 lpcd
Institutional	Academic Institutes	5 lpcd
	Government and non government offices	10 lpcd
	Hotels	80 lpcd
	Restaurants	5 lpcd
Industrial	Actual water consumption figures have been taken for the existing industries. The unidentified industry would have their own system in the future	
Fire fighting		1 lpcd
Leakage and Wastage	10% of domestic demand has been assumed for the system losses as well as leakage, theft and wastage	

Technical Design Parameters

28. The following design parameters have been observed for the design of the water supply system.

System	24 hours supply. Looped networks. It has been designed under Auto Water Program (a computer software package). The details on its program theory, parameters taken, its size / restrictions: Overhead R.C.C. Tank.
Water Quality: Treated Water Quality after filtration	
pH	6.8-7.5
Iron	<0.3 ppm as Fe
Ammonia Turbidity	<1.5 ppm as ammonia
E collies	<5 ITV
Arsenic Consumption Pattern	Traces (nil) Mpn Index/100 ml <0.05 mg/l

29. The distribution system capacity to meet design water demand at the desired rate and time is determined by the service area consumption pattern. This consumption pattern is used to determine balancing storage tank capacity. Therefore, it is essential to establish the type of consumption pattern. The consumption pattern of typical Terai systems recommended by PPTA has been used in detail design also. The recommended consumption pattern is as follows

Table 3-3: Water Consumption Pattern

Hours	% of daily demand
0500 - 0700	20
0700 - 1200	35
1200 - 1700	15

1700 - 1900	20
1900 - 0500	10

30. This consumption pattern provides a peak factor of 2.4 for the distribution system. Hence, peak factor of 2.4 has been used to design distribution pipe sizes.

Pipe Materials

31. DLGI and HDPE are used in the distribution of water in the service area. GI pipe has been used for external exposed pipelines whereas HDPE pipes are used for embedded lines. With economy point of view HDPE pipes have been used in gravel road, dead end section and from pressure consideration. Smaller pipe sizes less than 50 mm are not used.

Pressure and Velocity

32. There must be some residual head or pressure at all the service nodes of water system to account for the unforeseen during operation. As per DWSS guidelines, a minimum residual head of 5 meters has been maintained at all service nodes. However, in the most service nodes an attempt been made to have 8m residual head. Similarly, there must be some minimum cleansing velocity in the pipe sections. An attempt has been made to have at least 0.2m/sec velocity in all pipe sections.

3.1.2 Project Site

33. The project is situated at the intersection of East-West Highway and Biratnager-Dharan Road in Sunsari District of Koshi Zone in Eastern Development Region. The Itahari links far western corner with many parts of the country through the buses. Infrastructures facilities, including roads. Electricity and telephone services available in the project area have been attracting people from different parts of Nepal and, thus, contributing in the growth of marketing and other such economic activities in the area.

3.1.3 Time Schedule

34. An illustrative overall implementation schedule for the project is presented in following table. This schedule has been prepared for the feasibility study, for detail study and design and for the construction phase till the handover of the project to WUSC. A total of 9 months for the planning phase and 24th months for the construction phase have been considered.

3.2 Alternatives for the Updated IEE

35. The water supply system for the town of Itahari was constructed several years before under STWSSP 1, funded by ADB. The project is in operation at present. The WUSC is the operating agency. The project had anticipated a 24 hour service and water quality standards within the NDWQS. After a few years of operation, it was observed that this anticipation was not fulfilled due to some unseen problems. The problems were observed both in technical as well as social and institutional field. Therefore some enhancement measures were necessary. This project is designed to recommend for such enhancement works.

36. IEE had been carried out in accordance with the prevailing rules and regulations of ADB and the GoN incorporating the alternatives like “without –sub project or do nothing” and “with sub-project” was carried out in 2005.

37. As such, alternatives for the water supply project have not been studied in the design report.

4. DESCRIPTION OF SUBPROJECT

4.1 The Study Area

38. The project is situated at the intersection of East-West Highway and Biratnager-Dharan Road in Sunsari District of Koshi Zone in Eastern Development Region. Itahari Municipality was established in 1997 A.D. Total area of Itahari Municipality is 4377 hectares. The location of the project area is 26° 23'-26 55" North Latitude and 87° 5' East Longitude. Itahari is one of the rapid growing planned towns of Sunsari district. It is situated at 22 Km. North of Biratnager and 18 Km South of Dharan. The elevation of the town is about 116-164 meters from sea level.
39. The project area falls in the climatic range of warm, humid and warm sub-tropical plane. Average rain fall is recorded from 9.8 mm to 559.8 mm. Monsoon is usually experienced during warm seasons of mid-June to mid August when temperature ranges from 24° C to 34.30°C. During Winter the temperature ranges from 7.5°C to 13.6° C
40. The service area of the project covers ward no. 1 to 9 of Itahari Municipality; ward no 1 of Hansposa VDC and Ward no 4 of Ekamba VDC. The core area of the project is market area situated along both sides of the East-West Highway and Biratnagar-Dharan road. The main market area of the municipality is located in the central part. This area is densely populated market area where main economic activities are carried out. The service areas in Ekamba and Hansposa VDCs have semi-urban settlements with less dense population compared to core area.

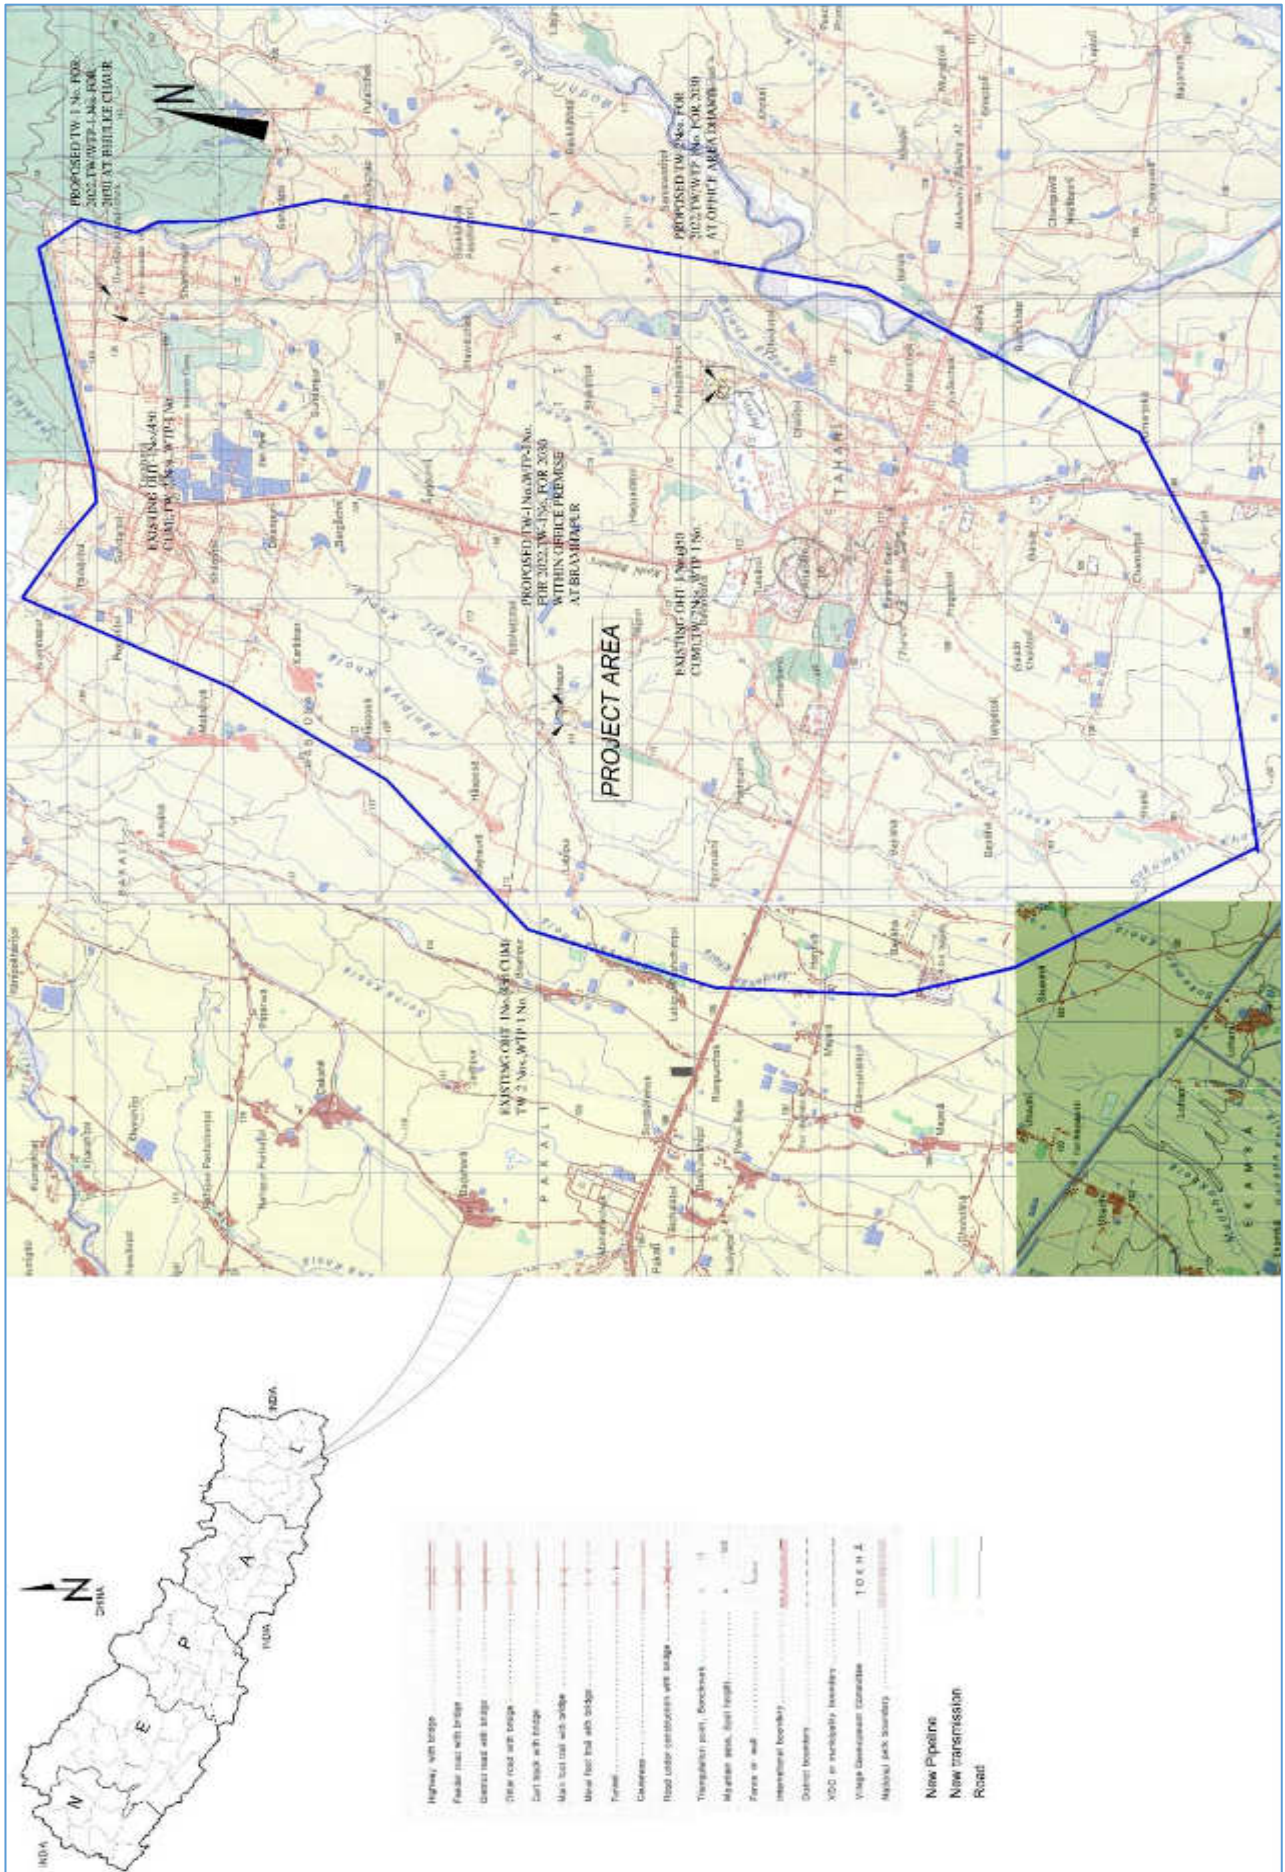


Figure 4-1: Location of the Project Area

4.2 Existing Condition and Need for the Subproject

41. The sub-project includes the following works;

- Maintenance of 1,350 m³ ground reservoir
- Three water treatment plant with PF facility
- 26.4 km of pipe line laying
- Construction of Chlorination unit
- One surface water intake consisting of infiltration gallery at source river

42. The technical details are shown in Table 4-1.

4.2.1 General Information

1. Name of the project: Enhance Functionality in Small Town Water Supply and Sanitation Sector project
2. Name of Sub-project: Itahari Small Town Water Supply & Sanitation Project, Sunsari
3. Service Area of the project: Former Ward no. 1 to 9 of Itahari Municipality, ward no 1 of Hansposa VDC and Ward no 4 of Ekamba VDC. (Now Itahari Municipality)
4. Total Project Cost NRs. 132,834,421

4.2.2 Technical Information

43. Details of technical information are mentioned

Table 4-1: Technical Details

S. No	Name of structure	Existing	Additional	Total
1	No. and capacity of Reservoirs:	3(1,350 cum)	0	3(1,350 cum)
2	Treatment Facilities	3 (PF 3) Chlorination Unit	3 (PF 3) Chlorination Unit (Rehabilitation)	6 number
3	Pipeline Length:			
3.1	Transmission	1 km	0.4 km	1.4 km
3.2	Distribution	165 km	26 km	191 km
3.3	Total	166 km	26.4 km	191.4 km
4	Guard House	1	None	
5	Generator / Operator House	4	None	
6	Chlorination Unit with lab	None	3	3
7	Office Building:	One	None	One
8	Surface Intake/ Borehole Drilling	Bore hole 6	Bore hole 4	Bore hole 10
9	Fire hydrant	5	None	5

S. No	Description	Existing (2014)	Design year (2022)	Design year (2030)
10	Household connection	12,670	16,493	21,467
10.1	Fully plumbed	7,349	12,205	19,320
10.2	Yard connection	5,321	4,288	2,147
10.3	Community		10	13
10.4	Institutional	173	216	264
10.5	Total	12,843	16,719	21,744
11	Total Water Demand			
11.1	MLD	1.60	2.19	2.99
11.2	LPS	82.4	112.9	154.7

4.2.3 Socio- economic Information

Total Household Number and Population (Pop.)

Present year (2014): 12,670/64,363
 Design year (2022) : 16,493/83,776
 Design year(2030) : 21,467/109,045

4.2.4 Financial Information

1. The financial planning for the enhancement project is as follows;
 - Total investment 100%
 - Government: Grant 70%
 - WUSC Contribution: 5 – 10% of total investment as cash (% to be decided later)
 - TDF Loan: 20 – 25% of total investment to be provided to the WUSC (% to be decided later)
2. Weighted Average Tariff NRs 21 per cum
3. **Cost Per Capita and per household**

Description	Base year 2014	Design Year 2022	Design Year 2030
Cost per Capita	2,063.83	1,585.59	1,218.16
Cost per House hold connection	10,484.17	8,053.99	6,187.84

4.3 Sub Project Construction schedule

44. It is expected that the contract will be awarded by the last week of November 2015 and the construction work will be completed by the last week of August 2016. The detail of work is shown in Figure 4-2.

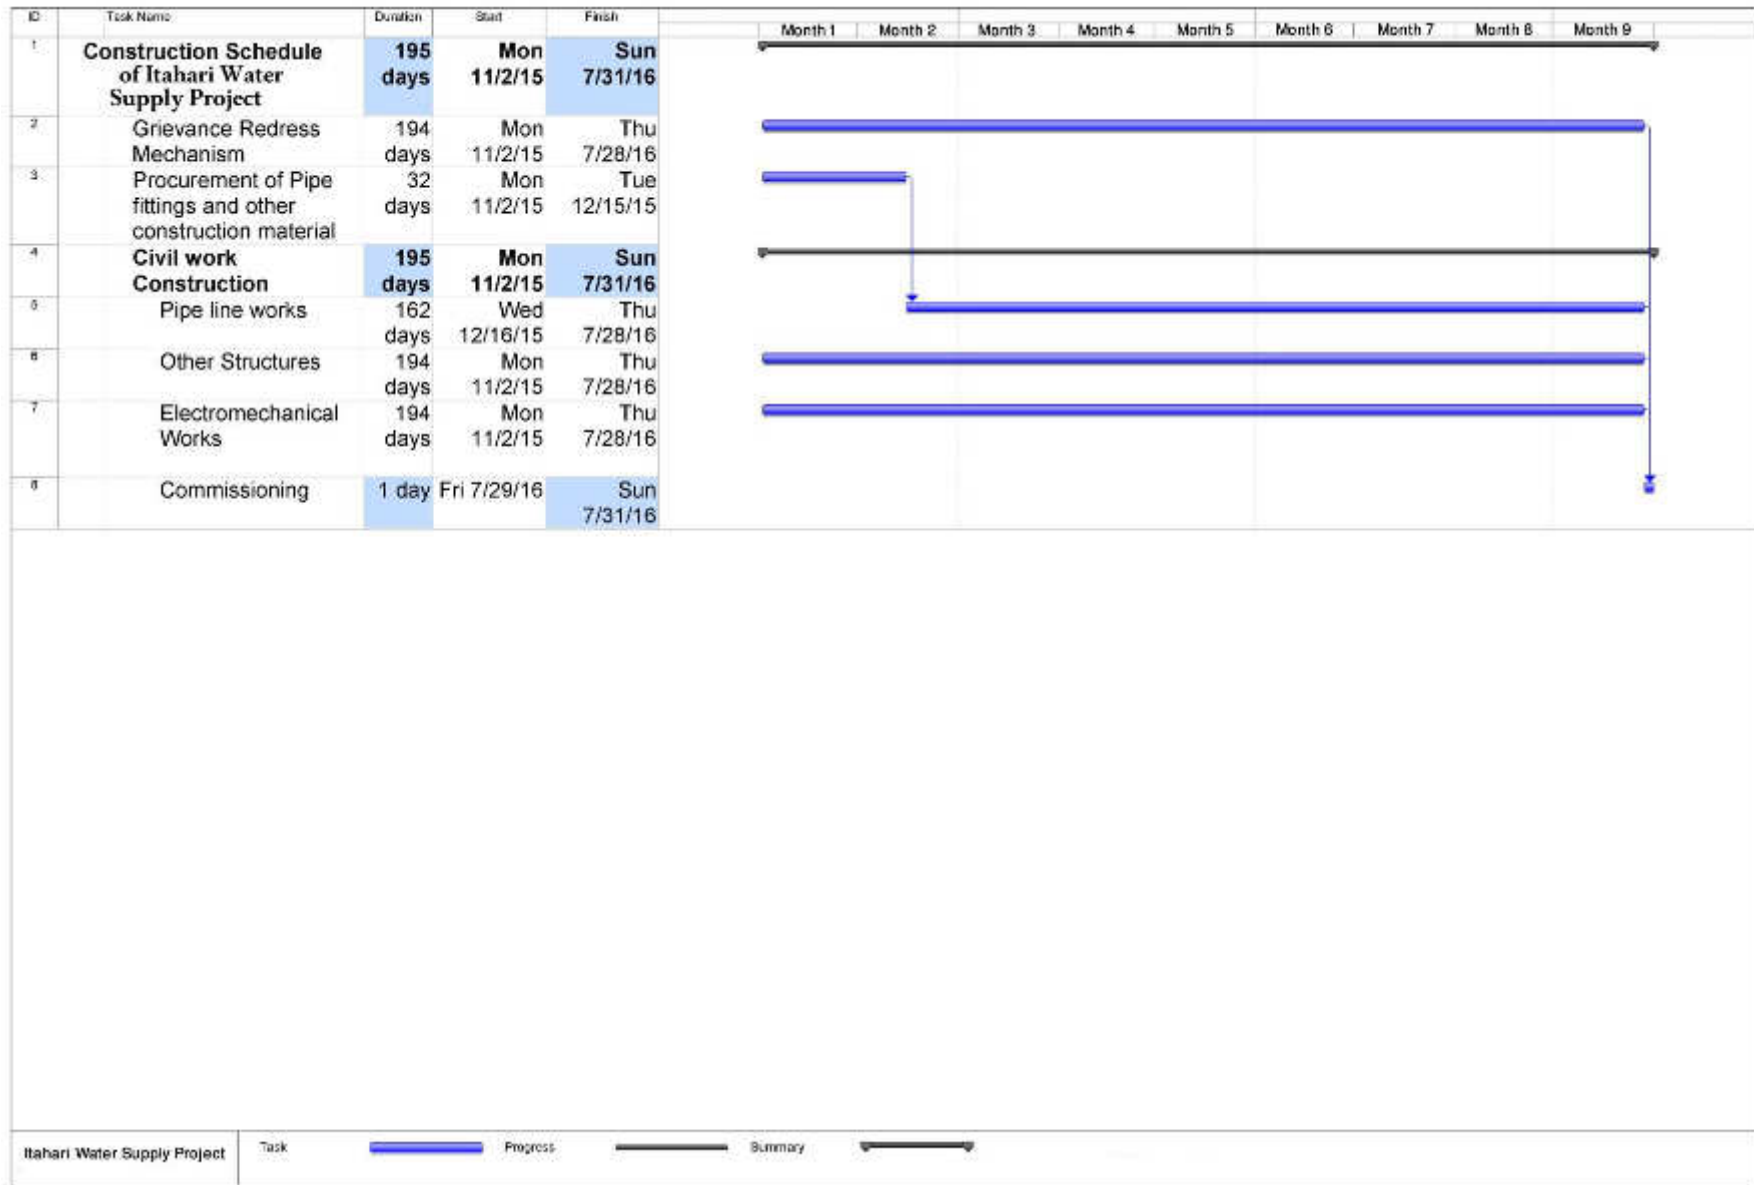


Figure 4-2: Construction Schedule

5. DESCRIPTION OF THE ENVIRONMENT

5.1 PHYSICAL PROFILE

5.1.1 Topography

5.1.1.1 GEOLOGY AND SOILS

45. The service area is situated on upper terai region of the indogangetic plains with the Siwalik Hills to the north. The area is composed mainly of gravel and boulder along with sand, close to the Aduwa khola that runs along the middle of the project area, whereas the rest of the area is composed of silty loamy soil, which is highly fertile.

5.1.2 Climate

46. The climate of the town is tropical with average yearly minimum and maximum temperatures being 2.5°C and 41.200, respectively. The mean monthly minimum and maximum temperatures are 8.5°C and 37.4°C. It receives an average annual rainfall of 1667mm. The highest recorded is 3060 mm.

5.1.3 Surface and Groundwater

47. The Itahari Water Supply Sub-project uses Ground water source.

S .No.	Name of Source	Design discharge	Tapped(Surveyed) discharge	Minimum discharge	Remarks
		lps			
1	TW#1 (Dhanti WN-4) Tank 1	23	19	19	The bulk meter is absent in the TWs
2	TW#2 (Dhanti WN-4) Tank 1	23	15	10	
3	TW#3(Bulke Chaur WN- 2) Tank 2	20	18	18	
4	TW#4 (Bulke Chaur WN- 2) Tank 2	20	18	18	
5	TW#5 (BhramapurWN-5) Tank 3	20	15	15	
6	TW#6 Tank 3(BhramapurWN-5)	20	15	15	
Total		126	100	95	

5.1.4 Water Quality Analysis

48. In the enhancement project additional units of SSF and Chlorination are proposed. The detail analysis of the water quality report is presented in Annex 2 of this report.

49. Water quality analyses were done for all critical sub project components such as intake, water before and after treatment plant. Samplings were also done in the distribution networks as well as randomly selected HHs taps to assure the quality. Mainly Physical component testing was done as pH, Turbidity, Electrical conductivity temperature. Similarly the various chemical components were also tested mostly like Calcium, Iron, Magnesium, Arsenic, Ammonia, Chromium, Nitrate, Sulphate, Chloride, Fluoride and Total Hardness as well.

50. In biological mainly parameter like Total Coliform and Fecal Coliform were tested for. If any contamination is encountered simultaneously the chlorination unit, pressure filter unit, slow sand filter treatment units should be provided. In case of this Water supply sub project due to the presence of Coliform, SSF and Chlorination units are constructed and now functioning.

5.2 ECOLOGICAL PROFILE

5.2.1 Flora

51. It can be expected that three types of forests would be the natural habitat of the area, namely *Shorea robusta* (sal); *Acacia catechu* (khayar)-*Dalbergia sissoo* (sisau), other riverine forests and grasslands. The *Shorea robusta* forest is dominated by the *Shorea robusta* species with common associates of *Terminalia tomentosa* (Asna), *Adina cordifolia* (karma), *Anogeissus latifolia* (bud dhayera), *Lagerstroemia parvifolia* (botdhaiyero), *Dillenia pentagyna* (Tantari), *Syzygium cumini* (jamun) and *Semecarpus anacardium* (bhalayo), etc.
52. The acacia catechu-dalbergia sissoo forest is found on newly deposited alluvium, often gravelly along streams and rivers.
53. The other riverine forest consists of tropical evergreen forest dominated by *syzygium cumini* (black plum) tropical deciduous forest usually dominated by *Bombax ceiba* (simal), *Holoptelia integrifolia* (chepte pagro) and *Trewia nudiflora* (pindar) species.
54. Medicinal plants of significance that would be expected here are *Sikakai* (*Acacia concinna*), *Assuro* (*Adhetoda vasica*), *Tulasi* (*Ocimum sanctum*), *Kureelo* (*Asparagus racemosus*), *Harro* (*Terminalia cheberia*), *Barro* (*Terminalia felerica*) and *Amala* (*Emblica officinalis*), etc.

5.2.2 Fauna

No natural forest to be habitat for wild animals exists in the service area. However, the Charali forest was known to have deer and many other wild animals. It does not have any of the wild animals at present.

55. It is possible that snakes like King Cobra (*Ophiophagus hannah*), Green Pit Viper (*Trimeresurus albolabris*), Common Krait (*Bungarus caeruleus*) and the Indian Python (*Python molurus*) would be present in the fields.

5.2.3 Protected Areas

56. There is no protected area in the project.

5.3 Socio economic condition

5.3.1 Population, Communities and Occupation

57. The Itahari town project intends to provide continuous, adequate and safe water supply to 38913 beneficiaries and 7660 Households in Itahari municipality. Ekamba & Hansposa VDC through predominantly house connections. The quantity of water supply ranges from 55 - 75 lpcd for Community taps & yard connections to 100 lpcd for fully plumbed connection which is sufficient for urban areas to fulfill daily needs. The system shall also supply drinking water to academic, government and private institutions for personal consumption. There will be 5099 tap connection for the base year.
58. Population forecasting of Project Area has been analyzed by first estimating the size of the existing population, and assessing the different rate of growths by Census 2011, VDC data, ward wise and Sunsari district data. Past historic data and the growth trend was considered for assessment of the realistic growth rate for the specific area under consideration. The adopted growth rate is 4.39 percent per annum.
59. The major ethnic castes in the proposed project area are Brahman, Chhetri, Giri Tamang, Limbu, Kami, Damai, Sarki, Newar, Gurung, Rai etc. Similarly, there are also minority ethnic groups such as Rajbansi, Choudhary, Satar, Meche and Muslim etc. residing in the proposed service area.

5.3.2 Health and Sanitation

60. There is a sub Health Post in the VDC with 8 staff, a Village clinic, a vaccination clinic, and number of women Health volunteers and trained midwife. Besides a Mary Stopes Centre and Nepal Family Planning Association Clinic are providing service. There is a good water supply system in the main bazaar area. Of the 3260 households 1181 have connection from the town supply. 1939 HH have only tubewell for drinking water. 140 have dug wells. Even those HH, which have connection to the town supply, have tube well.

61. The prevalent infectious disease is diarrhea. The numbers of children affected in the year 2057/58, 058/059, and 059/060 are 705, 693 and 1392, indicating poor sanitary status. The population without toilets is 771 of the total 3260 HHs. The spread of the infectious disease stem from the defecation at unsafe locations by those without toilets.

5.3.3 Economic Characteristics

5.3.3.1 INDUSTRIES

62. Although not adequate to give full employment to the total population, the project area is economically the most active location in the region. There are a number of industries in the area. Most of them are agro based. Tea appears to be thriving industry.

5.3.3.2 AGRICULTURAL DEVELOPMENT

63. The land is fertile for agriculture and the rate of production is good. The main crops are paddy and maize. Two crops of paddy or one each of paddy and maize are planted in a year. Besides wheat, oilseeds, pulses are grown here. Cultivation of vegetables including off seasonal is conducted commercially.

5.3.3.3 MINERAL DEVELOPMENT

64. Mineral exploitation activities are nonexistent.

5.3.4 Infrastructure Facilities

65. All major infrastructural facilities like water supply, roads, electricity and telephones/communication are available to the consumers in the service area. Such facilities are of course better within the Itahari market area, which lies on the East-West Highway.

5.3.4.1 INSTITUTIONS

66. There are 8 banks, 4 cooperative banks a primary health post, a police office, a post-office, a forestry office, a veterinary centre, irrigation office, VDC office and an agriculture services centre. The educational institutes consist of 5 primary schools (2 government, 3 private), 4 high schools (1 government, 3 private, and a private higher secondary school of commerce. The bazaar area is lies in ward nos. 4, 6 and 7 of Anarmani VDC.

5.3.4.2 TRANSPORTATION

67. Ithari is situated on the East-West Highway (Mahendra Rajmarga) and is 12 km north of the Biratnagar and is easily accessible. Biratnagar airport is the nearest airport. It is accessible form different parts of the district by a number of gravel and black-topped roads. Means of transport are buses, trucks, cars, motorcycles, tractors and bicycles.

5.3.5 Land Use Planning

68. There is no scientific land use planning at the moment and that is why ribbon development is occurring at a fast pace. The most extensive land use in the market area is residential/commercial along the East West Highway. Most of the heavily built area is around the old Ithari Bazar and along the high way. The houses along the other roads are more scattered.

5.3.6 Quality of Life Values

69. The Project is not expected to adversely affect any cultural or recreational resources but will increase the existing quality of life values due to the improvement in personal, household and community hygiene practices and community health.

5.4 Resettlement, Relocation and Compensation Issue

70. The various project components do not require resettlement of households or relocation. The system network has followed public property line and hence the issue of resettlement or relocation is not evident. The minutes of stakeholder consultation meeting also suggests that there is no need of resettlement or relocation.

71. The land required for construction of treatment plant and reservoir has been purchased by

the WUSC and there is no need to provide compensation from the project side.

6. DESCRIPTION OF IMPACT ASSESSMENT

72. No significant impacts of project construction and operation were anticipated (IEE, 2005), but the following impacts were likely to occur. The project is now in operational phase and that all the physical and biological and socio-economic cultural impacts have been mitigated. In the enhancement project as well the same type of impacts are likely to occur.

6.1 Physical Environment

73. Physical Impact covers impacts on physical resources such as air, water, soil, rocks etc. The positions of a water table keep on fluctuating up and down in relation to wet and dry weather. Porous sand and gravel aquifers yield more water than silt or clay deposits. Hence physical testing of soil structure will help understanding the water availability.

6.1.1 Impact on land use pattern

74. Intake structure, reservoir and treatment plant would require some land area in addition to permanent site to facilitate construction activities, which is envisaged to alter the land use during construction period. The implications of such land use may affect on soil, productivity and land use pattern.

6.1.2 Flooding and Stagnant Water Problem

75. During monsoon season the project area will be affected from flooding and may create the condition of stagnant water. Absence of drainage system in the project area will create flooding problems. This might create public health problem due to increase in number of vector species like mosquito, snails and others.

6.1.3 Impact on water/land quality

76. Excavation and construction spoils are the major outcomes of construction activity. Besides, the workforce camps and their sanitary behavior might produce unwanted waste materials. The spoils and waste materials may have adverse implications on adjoining water sources.

6.1.4 Impacts of sediments and Disinfecting Chemicals

77. Issues like release of sediments from treatment plants, and the use of disinfecting chemicals might affect the water quality. Such effects are minor in nature and can be easily mitigated during the operational phase.

6.1.5 Impacts on Air Quality

78. Dust will be generated from inadequately managed or haphazard: (i) earthworks such as clearing, grubbing, excavations and drilling; (ii) demolition works; (iii) stockpiling of natural aggregates, excavated materials and spoils; (iii) transport, loading and unloading of natural aggregates; (iv) movement of construction-associated vehicles; and (v) on-site rock crushing, cement mixing/concrete batching, borrowing. The significance of dust impact will be high in the bazaar area where more population reside and work and where urban socio-economic activities concentrate. Increase in concentration of vehicle- and process related pollutants will arise from the movement and operation of construction vehicles, equipment and hot-mix plants.

6.1.6 Impacts on Acoustic Environment

79. Noise and vibration emitting construction activities include earthworks, rock crushing, concrete mixing, movement and operation of construction vehicles and equipment, and loading and unloading of coarse aggregates. The significance of noise and vibration impacts will be high in areas where noise-sensitive institutions such as health care and educational facilities are situated. These impacts will be temporary and short term.

6.1.7 Impacts on Traffic and Temporary disturbance

80. During construction phase, implementation of distribution network pipeline will create disturbance to local transport system. The significant impact will be seen in market and busy area only. These impacts will be temporary and short term.

6.1.8 Water Volume/Quality

81. Over extraction water may decrease the volume of water and improper treatment of water also decrease the quality of water which may arise issues affecting the ground water sources of water.

6.2 Biological Environment

6.2.1 Impact on natural vegetation and ecology

82. The natural vegetation and ecology of the project area may be disturbed due to construction activities of the different project components. Besides, the activities of workforce on the adjoining forest may affect the habitat of wildlife.

6.2.2 Impact on aquatic life

83. The source being ground water no impact on aquatic life is envisaged due to implementation of the project

6.2.3 Loss of habitat

84. Clearance of vegetation along the bulk distribution pipeline, and trunk transmission pipeline, may result loss of some forested habitat of wild life and consequently affect the endangered species.

6.3 Socio-Economic and Cultural Environment

85. Many of the adverse impacts on socio-economic and cultural aspects will be limited to construction stage. The following socio-economic issues have been considered in IEE.

6.3.1 Land acquisition

86. The land required for the construction of permanent facilities has been managed by WUSC and no disputes are observed. Similarly there is no necessity of relocation or resettlement.

6.3.2 Outside workforce conflict/health/pollution/culture

87. Involvement of outside workforce in the local area may initiate conflict between the locals and outsiders due to cultural reasons. Disease transmission, pollution and competition for the available resources with outsiders might arise.

6.3.3 Workers' Health and Safety Hazards

88. Like communities, workers will also be exposed to the cross-cutting threats of the aforementioned impacts during construction. Inadequate supply of safe/potable water and inadequate sanitation facilities; poor sanitation practices on site; poor housing conditions; the handling and operation of construction equipment; handling of hazardous substances; exposure to extreme weather and nonobservance of health and safety measures, pose additional threats to the health and safety of construction workers. Construction workers may also be potentially exposed to communicable and transmittable diseases in the community and in the workforce.

6.3.4 Water right Conflict

89. Involvement of outside workforce in the local area may initiate conflict between the locals and outsiders due to cultural reasons. Disease transmission, pollution and competition for the available resources with outsiders might arise.

6.4 Beneficial impacts

90. However there are some benefits of the project implementation; particularly on the following:
- Increase in agricultural and livestock products
 - Employment generation
 - Maintaining the health and sanitation activities
 - Increase in quality of life values
 - Change in cropping pattern

7. DESCRIPTION OF MITIGATION MEASURES

7.1 Physical Environment

7.1.1 Impact on land use pattern

91. The STWSSSP is located in Itahari municipality in the private land of about 2 Ropanis owned by WUSC and with boundary wall constructed. It was ensured in design, that the tube wells and other water retaining structures like OHT, WTP etc., are well protected with good drainage to be located on stable ground. Therefore, the project implementation would have less or no effect on soil, productivity and on the land use pattern.

7.1.2 Flooding and Stagnant Water Problem

92. Proper management of drainage system needs to be improved. Contractor should be instructed not to store construction materials along the water ways.

7.1.3 Water/land quality

93. The project uses sub surface water that will be taken from below the water bed of the river by using infiltration gully technique. Therefore the quality of water is expected to be clean. However the pollution in the surface water may have negative effect. The intake point is upstream from the settlement area and hence external pollution is also not foreseen. Therefore there is ground water pumping, there is less or minimum effect on water quality. Proper drainage system should be made to avoid water logging and the quality of water sources should be protected. Urination, defecation and dumping of solid and liquid waste in open areas, and water ways may be the potential cause of the pollution of surface and sub-surface water and such activities should be strictly prohibited.

7.1.4 Impacts of sediments and Disinfecting Chemicals

94. The water quality should be maintained within WHO NDWQS standards. Filtration and chlorination should be provided to bring the water quality to acceptable levels. Similarly, a manual on water testing and chlorine dosing should be prepared and provided to WUSC.

7.1.5 Water volume

95. The water should be equally distributed to all the users in a controlled way. The amount of water that required should only be extracted.

7.1.6 Impacts on Air Quality

96. Some mitigation measures include: (i) confining earthworks according to a staking plan and excavation segmentation plan that should be part of the working documents and/or C-EMP; (ii) watering of dry exposed surfaces and stockpiles of aggregates at least twice daily, as necessary; (iii) if re-surfacing of disturbed roads cannot be done immediately, spreading of crushed gravel over backfilled surfaces; (iv) during demolition, watering of exterior surfaces, unpaved ground in the immediate vicinity and demolition debris; (v) hoarding active work sites in populated areas; (vi) requiring trucks delivering aggregates and cement to have tarpaulin cover and maintain a minimum of 2' freeboard; (vii) limiting speed of construction vehicles in access roads and work sites to maximum of 30 kph; and (viii) providing pollution controls in batching and hot-mix plants.

7.1.7 Impacts on Acoustic Environment

97. Some mitigation measures include: (i) using equipment that emit least noise, well maintained and with efficient mufflers/exhaust silencers; (ii) restricting noisy activities to daytime and overtime work to avoid using noisy equipment; (iii) limit engine idling to a maximum of 5 minutes; (iv) spread out schedule of material, spoil and waste transport (v) minimizing drop heights when loading and unloading coarse aggregates; and (vi) Identify any buildings at risk from vibration damage and avoiding any use of pneumatic drills or heavy vehicles in the vicinity. Complete work in these areas quickly.

7.1.8 Traffic and Temporary disturbance

98. Some mitigation measures include: (i) distribution pipeline work will be done during night time, (ii) diversion need to be made if work is of long duration.

7.2 Biological Environment

7.2.1 Impact on natural vegetation and habitat

99. The loss of vegetation from construction activities of contractors and construction workforce is recommended to be minimized through the enforcement of the following provisions.

- Prohibition on illegal felling of trees and encroachment of the community forest should be made mandatory.
- Progressive rehabilitation and afforestation of the areas not acquired by the project structures after the completion of the construction activities should be carried out. Such afforestation program is recommended to plant saplings of trees, shrubs and herbs by establishing a nursery or pre-arrangements of such saplings from the local or district level nurseries.
- To enhance the conservation of endangered, protected and threatened species, it is recommended to plant the saplings 2 times the number of felled trees.

7.3 Socio-economic and cultural environment

7.3.1 Land acquisition

100. The land required for the construction of permanent facilities has been managed by WUSC and no disputes are observed. Similarly there is no necessity of relocation or resettlement. Vegetation and agricultural products should be compensated through the afforestation and agricultural enhancement programs in the IWSSSP area.

7.3.2 Outside workforce conflict/health/pollution/culture

101. Outside workers should be provided with the facilities of camps and should be instructed to not to; i) indulge with local people ii) involve themselves for hunting of wildlife iii) involve themselves in social disharmony activities.

7.3.3 Workers' Health and Safety Hazards

102. Some of the mitigation measures for community health and safety hazards: (i) strictly enforce on workers the use of protective wears; (ii) provide safe access to and from work sites; (iii) provide adequate housing at the workers' camp with adequate basic services and provide adequate water supply and sanitation facilities at work sites; (iv) arrange with nearest health center and hospital for health care and emergency care of workers. Overall, the contractor should comply with IFS EHS Guidelines on Occupational Health and Safety.

7.3.4 Water right Conflict

103. The temporary settlement for the workers should be provided with temporary water taps. Open defecation should be controlled. Temporary toilets need to be constructed.

7.4 Enhancement of Beneficial Impacts

104. Some of the beneficial impacts from the implementation of the project should be enhanced by;

- Community mobilization and people's participation in health and sanitation programs should be promoted,
- Training an awareness programs in health and uses of water and its importance (water cost, saving, reuse, recycle, water pollution etc.) should be given,
- Technical training to the local people on plumbing, chlorination, water testing, pump maintenance and repair should be conducted.

7.5 Activities for Rehabilitation Work and its Mitigation Measures

105. As this rehabilitation project is for previously implemented and operated in an excellent order with minimal rectification works. Physical, Biological and Social environment are described respectively in Section 7.1, 7.2 and 7.3. Slight changes are in social that is increased population, number of stakeholders for which additional distribution lines with ancillary works are to be done. Major focused were given for the technical rectification which need to be done during enhancement work are summarized in Table 7-1 in details. Most of the recommended mitigation measures will be incorporated in the contractual obligations and constructions works to be completed by the contractors. Facilities like water treatment plant, water testing laboratory etc are also either existing or to be installed is also included in the contract. Mitigation measures and monitoring plan of each rehabilitation activities is mentioned in Table 10-2, in Chapter 10.

Table 7-1: Activities for Rehabilitation Work

S.No	Name of Structure	Type	Existing Capacity(Q=lps, RVT=cum, WTP lps)	Design Capacity	Major problems	Required Intervention
1	Civil Structures					
2	<ul style="list-style-type: none"> • TW 1(Dhanti ward no4) • TW2(Dhanti ward no4) • TW3(Bhulkechaur ward no2) • TW4(Bhulkechaur ward no2) • TW5(Brahmapur ward no5) • TW6(Brahmapur ward no5) 	Ground water	19 10 18 18 15 15	23 23 20 20 20 20	<ul style="list-style-type: none"> • TW 1 pumping silt, • Lower production rate and high demand in each deep tube wells • No spare pumps. 	<ul style="list-style-type: none"> • 4 New TW has to be installed. • Spare pumps to be installed. • Ultrasonic flow meter to be installed.
			Total=98	126		
3	<ul style="list-style-type: none"> • OHT-Ward no 4-Dhanti no 2,Bhulkechaur • OHT-Ward no 5, Brahmapur 	• OHT	450 m3 450m3 450m3	450 m3 450m3 450m3	<ul style="list-style-type: none"> • Mild steel railing of 10m,10 m& 8m broken in OHT-4,2& respectively. • Leakage problem in OHT of ward 2 &5. • Bottom of dome, leakage in OHT of ward not 2 & 5. 	<ul style="list-style-type: none"> • Repair. • Plastering/ Punning to be done. • Bottom dome leakage in ward 2 and 5.
4	• Distibution Line	• HDPE			<ul style="list-style-type: none"> • OHT2getfrequent overflow due to insufficient net work at Bazar areatherefore pumps are forced to shut down • Shortage of water supply at Halgada Chowk, Sangit Chowk (Itahari Chowk)Bazar,Manakamaana height chowt, Army Chowk and Hawaii Chowk and Pashupati Chowk 	<ul style="list-style-type: none"> • Replace1850 m old GI pipe with HDPE pipe from Halgada Chowk to Sangit Chowk • Lay1750 m new HDPE pipe from Manakamana Height Chowk to Jute Bikash Chowk • Replace 800 m old GI pipe from Army gate to East WestHighway • Lay new 1400 HDPE pipe from Hawaii Chowk to Pashupati Chowk
7	Pressure Filter				• Polluted water	• Install 3pressure filters
8	Drainage	open	OHT2(L=50m)		• overflow, wash out, back washand surface water is unmanaged	• Pond to be constructed at each site
7	Chlorination				• Dosing unit and Compressor Block is damaged.	• New chlorination unit to be installed.

S.No	Name of Structure	Type	Existing Capacity(Q=lps, RVT=cum, WTP lps)	Design Capacity	Major problems	Required Intervention
8	Accessories, Valve Chambers etc	Valve chambers, air valve, washout valves, NRV, lasting and durable bulk meters etc			<ul style="list-style-type: none"> • Problem on distribution network due to absence of valve • Due to breakage of spindles of sluice valves there is problem in supply • Difficult to monitor discharge due to frequent breakage of bulk meters 	<ul style="list-style-type: none"> • Construct two new valve chambers at Simarvana Chowk (300 mm dia & 250 mm dia), • one at Manakamana Aroyga (150 mm dia) and the other one at Fulbari road (150 mm dia) • Make available of different sized new sluice valves ranging from 100 mm dia to 300 mm dia to develop district and zoning inside service area. • 150 mm dia bulk meters of durable and lasting required.
9	Pipes & pipe fittings	HDPE, GI	About 300 Km plus		<ul style="list-style-type: none"> • Existing pipes along one side of high way is buried at a depth of more than 5.0 m which is impractical to operate and maintain and the other side without pipe line in high demand area 	<ul style="list-style-type: none"> • New pipes • Replacement pipe • Both sides of East West and North South highway of main Bazar and core areas
10.	Electromechanical					<ul style="list-style-type: none"> • New Tractor mounted Generator to be installed.

8. INFORMATION DISCLOSURE, CONSULTATION AND PARTICIPATION

8.1 Consultation

106. Stakeholder consultation and participation was an essential process in project preparation and this updated IEE. The process in engaging stakeholders and affected people during the conduct of the IEE involved key informant interviews, joint sites reconnaissance and on- site discussions with WUSC, and field random interview of stakeholders.

8.2 Initial consultation: the existing project

107. During the Feasibility Study, consultations were undertaken by the Design and Supervision Consultants. Stakeholder consultations have been continued through subprojects implementation and operation. All stakeholders were invited and encouraged to participate in community consultations. To facilitate the engagement of stakeholders, the PMO and RPMOs maintained good communication and collaboration with the WUSC and VDC. The PMO, RPMOS, Contractors and/or WUSC were opened to contact by the public on matters concerning the progress of the subprojects, adverse impacts, mitigation measures and environmental monitoring and grievances.

- Prior to construction, the PMO and TPO have conducted information, education and communication (IEC) campaign to ensure sufficient level of awareness/information among the affected communities regarding the upcoming construction, its anticipated impacts, the grievance redress mechanism, contact details and location of the PMO and TPO, and status of compliance with Government's environmental safeguard requirements, among others, are attained/provided. Billboards about the subproject, implementation schedule and contact details of the executing agency, PMO, TPO and Contractors have been set up at strategic locations within the subprojects' main areas of influence. The grievance redress procedure and details will have been posted at the offices of the PMO, TPO, WUSC and VDC.
- During construction, regular random interviews were conducted by the TPO every month to monitor environmental concerns of subproject communities.
- During operation, periodic random interviews were conducted by the PMO and
- TPO and WUSC to monitor the environmental concerns of subproject communities.

8.3 The consultation during IEE update

108. The consultation was done in two phases

8.3.1 Phase I

109. During the engineering survey and design phase, the consultations met with the top level management of DWSS, WUSC officials, WS division officials in Kathmandu and concerned municipality offices, WS customers and general public in field. The main persons consulted during this phase are listed below;

Table 8-1: Lists of People and Institutions Consulted

S No.	Name	Designation
1	Mr. Ram Deep Sah	Director General
2	Mr. Tires Prasad Khatrai	Acting Project Director
3	Mr. Dr. Mahesh Bhattra	PMC, Project Co-ordinator
4	Mr. Keshav Raj Bista	Deputy Project Director
6	Mr. Ram Prasad Chaulagain	Chairman
7	Mr. Harish Katuwal	WUSC

8.3.2 Phase II

110. After approval of Detail Design report, second level of public consultation was made to discussion issues regarding the environmental impact, resettlement, relocation and compensation with immediate stakeholders. Meeting was held on 2072/06/05 at site. In this phase overall project outcomes were discussed with all concerned stakeholders. Details of participants are presented in Annex 4.

8.4 Costs

111. All costs involved in resolving the complaints (meetings, consultations, communication and reporting/information dissemination) at local (field/ward/town) level will be borne by the concerned focal organizations at each level: WUSC at town level; PIU at regional level and PMO at central level.

9. GRIEVANCE REDRESS MECHANISM

9.1 Purpose of the Grievance Redress Mechanism

112. A project-specific grievance redress mechanism (GRM) will be established to receive, evaluate, and facilitate the resolution of APs' concerns, complaints, and grievances related to social and environmental issues of the project. The GRM will aim to provide a time-bound and transparent mechanism to voice and resolve social and environmental concerns linked to the project.
113. A common GRM will be in place for social, environmental, or any other grievances related to the project. The GRM will provide an accessible forum for receiving and facilitating resolution of affected persons' grievances related to the project. Every grievance shall be registered and careful documentation of process with regard to each grievance undertaken, as explained below. The environmental and social safeguards officer (ESO/SSO) at project management office (PMO) will have the overall responsibility for timely grievance redress on environmental and social safeguards issues. The Social Development Officer at the Regional Project Management Office (RPMO) will be the focal person for facilitating the grievance redress at VDC/Municipality level.
114. A town-level public awareness campaign will be conducted to ensure that awareness on the project and its grievance redress procedures is generated. The social safeguards expert of the project management consultant (PMC) and DSMC's safeguards specialists will support the WUSC and DSMC community mobilisers with information/collateral/awareness material etc. to conduct the town-wide awareness campaign. The campaign will ensure that the poor, vulnerable and others are made aware of grievance redress procedures and project's entitlements.
115. A Grievance Redress Committee (GRC) will be formed at VDC/Municipality level, comprising District Chief WSS as Chairperson and Member of Secretary of concerned WUSC as the GRC secretary. The GRC members will be comprise of (1) RPMO social development officer, (2) representatives of affected persons, (3) DSMC's safeguards specialist (social/environment as relevant), (4) a representative of reputable CBO/SHG/organization working in the project area, and (5) contractor's representative. The secretary of the GRC, who will be responsible for convening timely meetings and maintaining minutes of meetings. The concerned social safeguards expert of DSMC will support the RPMO SDO and Regional Director DWSS to ensure that grievances, including those of the poor and vulnerable are addressed. All GRCs shall have at least two women committee members. Representatives of APs, civil society and eminent citizens are to be invited as observers in GRC meetings.
116. The functions of the local GRC are as follows: (i) provide support to affected persons on problems arising from environmental or social disruption; asset acquisition (if necessary); and eligibility for entitlements, compensation and assistance; (ii) record grievances of affected persons, categorize and prioritize them and provide solutions within 15 days of receipt of complaint by WUSC; and (iii) ensure feedback to the aggrieved parties about developments regarding their grievances and decisions of the GRC. The grievance redress mechanism and procedure is depicted in Figure 9-1.
117. The GRM for the project is outlined below, with each step having time-bound schedules and responsible persons to address grievances and indicating appropriate persons whose advice is to be sought at each stage, as required:

9.1.1 First Level of GRM (WUSC-level)

118. The first level and most accessible and immediate venue for quick resolution of grievances will be the contractors, DSMC field engineers and PIU supervision personnel, who will immediately inform the WUSC. Any person with a grievance related to the project works can contact the Project to file a complaint. The WUSC will document the complaint within 24 hours of receipt of complaint in the field, and WUSC will immediately address and resolve the issue at field-level with the contractor, supervision personnel of PIU and DSMC

field engineers within 5 days of receipt of a complaint/grievance. The assigned DSMC social mobilizer will be responsible to fully document: (i) name of the person, (ii) date of complaint received, (iii) nature of complaint, (iv) location and (v) how the complaint was resolved. If the complaint remains unresolved at the local level within 5 days, the WUSC will forward the complaint issue to the VDC/Municipality level GRM.

9.1.2 Second Level of GRM (VDC/Municipality level)

119. The complainant will be notified by the WUSC that the grievance is forwarded to the VDC/Municipality –level GRM. The Grievance Redress Committee (GRC) will be called for a meeting. The GRC meeting will be called and chaired by the District chief of WSS. The GRC will recommend corrective measures at the field level and assign clear responsibilities for implementing its decision within 10 days of receipt of complaint by WUSC. If the grievance remains unresolved within 10 days of receipt of complaint by WUSC, the matter will be referred to the third level. The RPMO SDO will be responsible for processing and placing all papers before the GRC, recording decisions, issuing minutes of the meetings and taking follow up action to see that formal orders are issued and the decisions carried out. If the complaints are related with IP/dalits/other vulnerable groups, specific NGO/CBO that actively involved in development of these communities should be involved.

9.1.3 Third Level of GRM (PMO Level)

120. Any unresolved or major issues at Municipality/VDC level will be referred to the PMO for final solution. The PMO's Project Director and WUSC Union representative will have special meeting to find solution. Decision has to be made within 15 days of receipt of complaint by WUSC. The Project Director will sign off on all grievances received by the PMO. The environmental and social safeguards officers (ESO & SSO) will be involved with support from the PMC Social/Environment Safeguards Experts. The Project Director will sign off on all grievances received by the PMO. The PMO Safeguard Officer will be responsible to convey the final decision to the complainant.
121. All paperwork (details of grievances) needs to be completed by the WUSC member secretary and circulated to the WUSC Chairperson and members. At VDC/Municipality level, the VDC/Municipality SDO will be responsible for circulation of grievances to the Regional Director, DWSS and other GRC members, prior to the scheduled meetings. The PIU SDSO will be responsible for follow-through of all escalated grievances. All decisions taken by the GRC and PSC will be communicated to the APs by the PIU social development and safeguards officer.
122. Despite the project GRM, an aggrieved person shall have access to the country's legal system at any stage, and accessing the country's legal system can run parallel to accessing the GRM and is not dependent on the negative outcome of the GRM.
123. In the event that the established GRM is not in a position to resolve the issue, the affected person also can use the ADB Accountability Mechanism (AM) through directly contacting (in writing) the Complaint Receiving Officer (CRO) at ADB headquarters or the ADB Nepal Resident Mission. The complaint can be submitted in any of the official languages of ADB's DMCs. The ADB Accountability Mechanism information will be included in the PID to be distributed to the affected communities, as part of the project GRM.

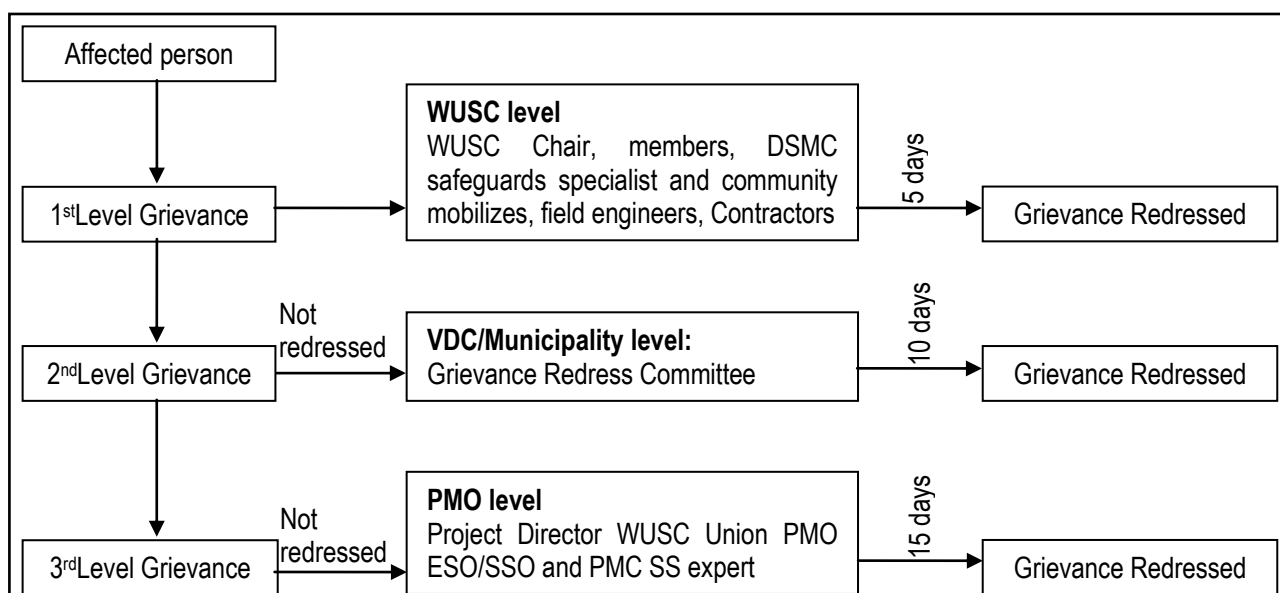


Figure 9-1: Grievance Redress Process

DSMC: Design, supervision and management consultant; ESO: Environmental and social safeguards officer; GRC: Grievance redress committee; PD: Project director; PMC: Project management consultant; PMO: Project management office; WUSC: Water user and sanitation committee.

Record keeping and disclosure

124. Records at the town-level will be kept by the concerned WUSC Member Secretary, of all grievances received, including contact details of complainant, date the complaint was received, nature of grievance, agreed corrective actions and the date of the incident and final outcome. The number of grievances recorded and resolved and the outcomes will be displayed/disclosed in the RPMO office, WUSC/municipal/VDC office, and on the web, as well as reported in the safeguards monitoring reports submitted to ADB on a semi-annual basis. For any grievance escalated to RPMO/VDC/Municipality level, the RPMO SDO will be responsible for record-keeping, calling of GRC meetings and timely sharing of information with WUSC. For grievances escalated to PMO and above, the PMO safeguard officers will be responsible for maintenance of records, sending copies to RPMO and WUSC for timely sharing of information with the person filing complaint.

125. Periodic review and documentation of lessons learned. The PMO social safeguard officer will periodically review the functioning of the GRM at town/WUSC level and PIU level and record information on the effectiveness of the mechanism, especially on the project's ability to prevent and address grievances. Indicators pertaining to grievance redress (no. of grievances received, no. redressed/resolved) to be reported by Member Secretary, WUSC to PIU SDSO, and by PIU SDSO to PMO ESO in monthly progress reports.

Periodic review and documentation of lessons learned

126. The PMO social safeguard officer will periodically review the functioning of the GRM at town/WUSC level and PIU level and record information on the effectiveness of the mechanism, especially on the project's ability to prevent and address grievances. Indicators pertaining to grievance redress (no. of grievances received, no. redressed/resolved) to be reported by Member Secretary, WUSC to PIU SDSO, and by PIU SDSO to PMO ESO in monthly progress reports.

10. ENVIRONMENT MANAGEMENT PLAN

127. The purpose of the environmental management plan (EMP) is to ensure that the activities are undertaken in a responsible, non-detrimental manner with the objectives of: (i) providing a proactive, feasible, and practical working tool to enable the measurement and monitoring of environmental performance on-site; (ii) guiding and controlling the implementation of findings and recommendations of the environmental assessment conducted for the project; (iii) detailing specific actions deemed necessary to assist in mitigating the environmental impact of the project; and (iv) ensuring that safety recommendations are complied with.

128. A copy of the EMP must be kept on work sites at all times. This EMP will be included in the bid documents and will be further reviewed and updated during implementation. The EMP will be made binding on all contractors operating on the site and will be included in the contractual clauses. Non-compliance with, or any deviation from, the conditions set out in this document constitutes a failure in compliance.

10.1 Institutional Arrangement

10.1.1 Executing and implementing agencies.

129. The Ministry of Urban Development (MUD) will be the executing agency with responsibility of subproject execution delegated to the Department of Water Supply and Sewerage (DWSS). The Water Supply and Sanitation Division/Sub-division Office (WSSDOs) are the subproject implementing agencies. Water Users' and Sanitation Committees of participating towns are the implementing agencies.

130. The key responsibilities of the executing and implementing agencies are as follows:

Prior to construction

- The MUD will deputize a qualified staff to act as the Environmental Safeguard Officer of the Project management office (PMO).
- The MUD will establish the grievance redress mechanism, including setting up the Grievance Redress Committee.
- The Water Supply and Environment Division of the MUD will be responsible for reviewing the IEE Report prior to submission to the Ministry of Science, Technology and Environment (MoSTE) for review and approval.
- The DWSS will review the IEE Report prepared by the Design and Supervision Consultants' Team's Environmental Safeguard Expert (DSMC-ESE) prior to forwarding this to MUD.
- The DWSS will prepare the ToRs for the Environmental Safeguard Specialist that will be engaged to support the PMO and for the Environmental Safeguard Specialists of the two Design and Supervision Consultants that will be appointed to prepare the subprojects.

During construction and operation

- The DWSS, through the PMO, will oversee the EARF and EMP implementation of all subprojects.
- The WSSDO, through the RPMOS, will oversee the EARF and EMP implementation at subproject/town level.

10.2 Safeguard Implementation Arrangement

Project Management Office (PMO)

131. The safeguard officers (environmental safeguard officer and social safeguard officer) of the PMO will receive support from the safeguards experts (environmental and social) of the Project Management Consultants (PMC) as specified below:

- i. confirm existing IEEs/EMPs are updated based on detailed designs and that new IEEs/EMPs are prepared in accordance with the EARF and government rules;
- ii. confirm whether EMPs are included in bidding documents and civil works contracts;
- iii. provide oversight on environmental management aspects of subprojects and ensure EMPs are implemented by regional project management offices (Eastern RPMO and Western RPMO) and contractors;

- iv. establish a system to monitor environmental safeguards of the project including monitoring the indicators set out in the monitoring plan of the EMP;
- v. facilitate and confirm overall compliance with all Government rules and regulations regarding site and environmental clearances as well as any other environmental requirements as relevant;
- vi. supervise and provide guidance to the RPMOs to properly carry out the environmental monitoring and assessments as per the EARF;
- vii. review, monitor and evaluate the effectiveness with which the EMPs are implemented, and recommend necessary corrective actions to be taken as necessary;
- viii. consolidate monthly environmental monitoring reports from RPMOs and submit semi-annual monitoring reports to ADB;
- ix. ensure timely disclosure of final IEEs/EMPs in project locations and in a form accessible to the public; and
- x. address any grievances brought about through the Grievance Redress Mechanism in a timely manner as per the IEEs.

Regional Project Management Offices (Eastern and Western RPMOs)

132. The regional DWSS engineers and social development officers of the RPMOs will receive support from; (i) the PMO safeguards officers (environmental and social); and (ii) the safeguards specialists (environmental and social), the social mobilizes and environmental management plan (EMP) monitors of the design, supervision and management consultant (DSMC) teams as specified below:

- i. prepare new IEEs/EMPs in accordance with the EARF and government rules;
- ii. include EMPs in bidding documents and civil works contracts;
- iii. comply with all government rules and regulations;
- iv. take necessary action for obtaining rights of way;
- v. oversee implementation of EMPs including environmental monitoring by contractors;
- vi. take corrective actions when necessary to ensure no environmental impacts;
- vii. submit monthly environmental monitoring reports to PMO, and;
- viii. address any grievances brought about through the Grievance Redress Mechanism in a timely manner as per the IEEs.

Civil Works Contracts and Contractors

133. EMP is to be included in bidding and contract documents and verified by the PMO and RPMOSs. The contractor will be required to designate an environment supervisor to ensure implementation of EMP during civil works. Contractors are to carry out all environmental mitigation and monitoring measures outlined in their contract. The government will ensure that bidding and contract documents include specific provisions requiring contractors to comply with all: (i) applicable labor laws and core labor standards on (a) prohibition of child labor as defined in national legislation for construction and maintenance activities, on (b) equal pay for equal work of equal value regardless of gender, ethnicity or caste, and on (c) elimination of forced labor; and (ii) the requirement to disseminate information on sexually transmitted diseases including HIV/AIDS to employees and local communities surrounding the project sites. Contractors will only starts the civil works activities in the section/subproject sites that has IR/IPP impacts upon the completion of RP/IPP implementation and after receiving clearance from the WUSC and endorsed by RPMO's SDO.

Capacity Building

134. The PMC safeguards experts (environmental and social) will be responsible for training the; (i) PMO's safeguards officers (environmental and social); (ii) RPMOs' engineers and social development officers. Training modules will need to cover safeguards awareness and management in accordance with both ADB and government requirements as specified below:

- i. sensitization;
- ii. introduction to environment and environmental considerations in water supply and wastewater projects;

- iii. review of IEEs and integration into the project detailed design;
- iv. improved coordination within nodal departments; and
- v. Monitoring and reporting system. The contractors will be required to conduct environmental awareness and orientation of workers prior to deployment to work sites.

Water Users and Sanitation Committees (WUSCs)

135. WUSCs are the eventual operators of the completed subprojects. The key tasks and responsibilities of the WUSCs are, but not limited to:

Prior to construction

- Facilitate public consultation and participation, information dissemination and social preparation.
- Provide available data to the DSMC-ESS during the conduct of the IEE.
- Assist in securing the tree-cutting permit and/or registration of water source.
- Participate in the capacity development program.

During construction

- Assist in the observance of the grievance redress mechanism.
- Actively participate in the monitoring of Contractor's compliance with the IEE and its EMP and the conditions set out with Government's approval of the IEE Reports.
- Facilitate public consultations, as necessary.

During operation

- Implement the EMP and the Water Safety Plan.
- Regularly monitor the water quality
- Prepare the environmental monitoring report as per IEE.
- Ensure observance of the grievance redress mechanism

Licensed and accredited laboratory

136. It is recommended that a licensed and accredited laboratory be engaged to conduct water quality monitoring in the first few years of operation and to train the WUSC on the same. The laboratory will ensure that while carrying out the water quality monitoring as prescribed in the National Drinking Water Quality Standard and its Directives, 'hands-on' training is provided to the WUSC.

10.3 Institutional Capacity Development Program

137. Considering the limited capability of the Project's key players in environmental management, technical assistance from environmental specialists and capacity development during loan implementation will be needed. Capacity development will consist of hands-on training in implementing the responsibilities in EMP (as well as in EARF) implementation, complemented with a short-term series of lectures/seminars on relevant topics.

138. WUSC does not have the capacity to monitor the quality of supplied water as prescribed in the NDWQS and its Directives. Albeit monitoring kits and laboratory rooms will be provided, this would not guarantee WUSC can handle monitoring appropriately. DWSS has five regional laboratories; however some are not functioning fully due to lack of manpower. Considering that public health is a critical concern associated with water supply, it is recommended that a licensed and accredited laboratory be engaged to conduct water quality monitoring for at least the first 2-3 years of operation with the WUSC actively participating to develop WUSC capacity. The conduct of water quality monitoring should be carried out in such a way that WUSC will be "learning by doing". After the engagement period, there should be continuing periodic training of new persons to ensure capacity of the WUSC is sustained. The cost for monitoring during operation is based on the assumption that a licensed laboratory will be engaged for both the monitoring requirements and to train the WUSC. A Water Safety Plan is included in subproject design and will oblige the operator to carry out water quality monitoring accordingly. The amount of NPR 500,000 will be provided annually to implement the Plan. There will be sufficient fund to include training by the licensed and accredited lab, while monitoring water quality.

139. The PMO will be responsible for trainings on environmental awareness and management in accordance with both ADB and government requirements. Specific modules customized for the available skill set will be devised after assessing the capabilities of the target participants and the requirements of the project. Typical modules would be as follows: (i) sensitization; (ii) introduction to environment and environmental considerations in water supply and wastewater projects; (iii) review of IEEs and integration into the project detailed design; (iv) improved coordination within nodal departments; and (v) monitoring and reporting system. The contractors will be required to conduct environmental awareness and orientation of workers prior to deployment to work sites.

10.4 Staffing Requirement and Budget

140. Costs required for implementing the EMP will cover the following activities:

- i. Updating IEE, preparing and submitting reports and public consultation and disclosure;
- ii. Application for environmental clearances; and
- iii. Implementation of EMP, environmental monitoring program and long-term surveys.

141. The infrastructure involved in each scheme is generally straightforward to build. Environmental monitoring during construction will also be straightforward and will involve periodic site observations and interviews with workers and others, plus checks of reports and other documents. This will be conducted by PMO assisted by the PMO environmental safeguard officer. Therefore, no separate budget is required for the PMO.

142. The cost of mitigation measures and surveys during construction stage will be incorporated into the contractor's costs, which will be binding on him for implementation. The surveys will be conducted by the contractors.

143. The operation phase mitigation measures are again of good operating practices, which will be the responsibility of the WUSC. All monitoring during the operation and maintenance phase will be conducted by WUSC. The Water Safety Plan, included in each subproject design, will allocate NPR 500,000 annually for operation and maintenance particularly water quality monitoring. If a licensed laboratory will be engaged for the first 2-3 years of operation for training purposes, the cost can be accommodated under the Water Safety Plan.

10.5 Monitoring and Reporting

144. RPMOs will monitor and measure the progress of EMP implementation with assistance from DMSC. The monitoring activities will correspond with the project's risks and impacts, and will be identified in the IEE for the projects. In addition to recording

10.6 Environmental Monitoring Mechanism

145. Under the chairmanship of Itahari municipality, a Monitoring Committee should be formed. The committee should be represented by the chairman of concerned service wards of the VDC, representative from environment related NGOs, local community, Water Users' Committee and local entrepreneur. Secretary of the Itahari municipality should act as member secretary of the Monitoring Committee. This committee should be assigned following duties and responsibilities:

- The committee should meet at least twice a month;
- The committee should collect all complaints from the local people concerning distribution, pipeline etc and should discuss in the meeting for the final decisions;
- The monitoring committee should identify the mistakes and deficiency regarding the project and should discuss in the meeting for the purpose of correction;
- Any negligence regarding the water quality should be considered and take necessary action;
- The committee should also supervise and provide instructions for activities such as:
 - Distribution of qualitative water,
 - Storage of water in the reservoir tanks,
 - Treatment plant,
 - Handling of toxic/chemical matters,
 - Training for the locals, and

- Examine monitoring reports periodically and take necessary actions if required etc.

10.7 Monitoring Reporting Mechanism

146. As proposed by approved EMP, the reporting system should include site supervision and reporting as well and primarily connected with Monitoring plan. The construction contractors are responsible for implementing approved EMP. The supervising consultants are responsible for monitoring to oversee whether or not the contractors have complied with the approved conditions as stated in EMP and also receive the monthly progress report from construction contractors. Based on this information the consulting engineers prepare the front line monitoring report and submit to DWSS for review

10.8 Monitoring Cost, Parameters, Location and Schedule

147. During rehabilitation, the cost for monitoring will be minimum and it should be allocated as and when required from the project contingency.

10.9 Contractors Compliance on EMP

148. The recommended mitigation measures are shown in the Table 10-1. The contractor should comply with the recommended mitigation activities.

10.10 Institutional Capacity Development Program

149. Considering the limited capability of the Project's key players in environmental management, technical assistance from environmental specialists and capacity development during loan implementation will be needed. Capacity development will consist of hands-on training in implementing the responsibilities in EMP (as well as in EARF) implementation, complemented with a short-term series of lectures/seminars on relevant topics.

150. In the Table 10-1 given below, the types of impact as predicted, corresponding mitigation measures, monitoring parameters, monitoring indicators, location and sources, responsibility and frequencies of monitoring have been included. The monitoring protocols given below are based on the Environmental Management Plan (IEE Itahari, 2005) approved by Government of Nepal 2005.

10.11 Environmental Mitigation Cost

151. Most of the recommended mitigation measures are incorporated in the contractual obligations and constructions works to be completed by the contractors. Facilities like water treatment plant, water testing laboratory etc are also either existing or to be installed is also included in the contract. Therefore mitigation cost of the enhancement project will be negligible. However in order to strengthen the existing facilities 2% of total project cost is proposed should be allocated.

Table 10-1: Mitigation measures and corresponding Monitoring plan

Impact and mitigation prescription		Monitoring plan for implementation						Status	
Environmental Impact	Mitigation action	Parameter to be Monitored	Indicators	Location	Sources	Responsibility	Frequency	Previous	Present ²
Physical Environment									
Construction Phase									
Land use pattern	Acquire only required land	Change in cropping pattern	Quality and quantity of yield	Project area	Local people	WUSC	Half yearly	Completed	Not applicable
Flooding and water stagnant	Drainage management	Observation of the project area	Increase in mosquito Increase in vector born diseases	Project area	Field inspection	DSC/Contractor	During and after monsoon	Completed	Recommended
	The excavated material must be safely disposed.	Ensure proper management of excessive spoil materials in place	Evidence of landscape erosion and river turbidity undisturbed	Project area	Field inspection	DSC/Contractor	After monsoon	Completed	Recommended
Impacts of sediments and Disinfecting Chemicals	Safe disposal	Water quality	Chemicals and pathogen exceeding national standards	Project area	Water quality test	DSC/Contractor	Quarterly	Completed	Recommended
Water Volume/ Quality	Limited extraction/ regular testing	Measurement of River flow and underground water table	Change in quantity	Project area	River and ground water	DSC/Contractor	Quarterly	Completed	Recommended

²Recommended for EMP compliance

Impact and mitigation prescription		Monitoring plan for implementation						Status	
Environmental Impact	Mitigation action	Parameter to be Monitored	Indicators	Location	Sources	Responsibility	Frequency	Previous	Present ²
		level							
Air Quality	Confine earthworks according to a staking plan and excavation segmentation plan and a part of the document	Visibility due to presence of dust	Location of stock pile	Project area	Local people and surrounding environment	DSC/Contractor	Twice in a week	Completed	Recommended
		Amount of dust present in surrounding environment	Number of complaint from sensitive receptors	Project area	Local people and surrounding environment	DSC/Contractor	Twice in a week	Completed	Recommended
Acoustic environment	Restrict noisy activities to daytime. Overtime work should avoid using noisy/high noise generating equipment.	Sound intensity during day and night time	Number of complaints from sensitive receptors;	Project area	Local people and surrounding environment	DSC/Contractor	Twice in a week	Completed	Recommended
		Sound intensity at and nearby of source	Use of silencers in noise-producing	Project area	Local people and surrounding environment	DSC/Contractor	Twice in a week	Completed	Recommended

Impact and mitigation prescription		Monitoring plan for implementation						Status	
Environmental Impact	Mitigation action	Parameter to be Monitored	Indicators	Location	Sources	Responsibility	Frequency	Previous	Present ²
			equipment and sound barriers;						
Traffic movement	Pipe line work need to be done during night and during less traffic time	Number of vehicles diverted	Number of vehicles movement	Project area	Local people and surrounding environment	WUSC/DSC/Contractor	During pipeline work	Completed	Recommended
Biological Environment									
Construction Phase									
Impact on natural vegetation and habitat	Construction area should be well demarked and proper instruction to be given for the workers.	Vegetation density, number and types of wild animals	Change in vegetation density and number of wild life	Project area	Project area	DSC/Contractor	Quarterly	Completed	Recommended
Socio-economic and cultural environment									
Construction Phase									
Impairment to Infrastructure	Not applicable								
Land acquisition	Project has to make sure that adequate compensation for the land acquired from	Compensation measures	All affected	Project area	Records and Interview	WUSC/Contractor	Yearly	Completed	Completed

Impact and mitigation prescription		Monitoring plan for implementation						Status	
Environmental Impact	Mitigation action	Parameter to be Monitored	Indicators	Location	Sources	Responsibility	Frequency	Previous	Present ²
	private citizens (if required) is made								
Outside workforce conflict/health/pollution/culture	Disease transmission, pollution and competition for the available resources to outsiders should be thoroughly checked.	Situation of social disharmony Awareness program	Decreased social disharmony Effective awareness program	Project area	Records and Interview	WUSC/Contractor	Yearly	Completed	Recommended
Operation Phase									
Water right Conflict	Public taps should be established in appropriate places.	Number of public taps installed	Adequate water supply to the public	Project area	Field inspection and Interview	WUSC	Quarterly	Completed	Recommended
Workers health and safety	Comply with requirements of Labor Act of GoN and standards on workers' health and safety (H&S).	Health of workers Dress and first-aid facilities stations	Site-specific H&S Plan	Project area	Workers health status and Interview	WUSC	Quarterly	Completed	Recommended
	Arrange for	Health of	Condition	Project	Workers	WUSC	Quarterly	Completed	Recommended

Impact and mitigation prescription		Monitoring plan for implementation						Status	
Environmental Impact	Mitigation action	Parameter to be Monitored	Indicators	Location	Sources	Responsibility	Frequency	Previous	Present ²
	readily available first aid unit including an adequate supply of sterilized dressing materials and appliances	workers Dress and first-aid facilities stations	of sanitation facilities for workers	t area	health status and Interview		y	d	d

Source: IEE Itahari 2005
 2. Recommended for EMP compliance

Table 10-2: Mitigation Measures and Monitoring Plan for Rehabilitation Activities

Overview of Impacts		Required mitigation measures			Monitoring plan for implementation				
Project activities	Possible impacts (on all baseline parameters)	Mitigation associated with project location	Mitigation in project design features	Residual mitigation measures (not addressed by location and design)	Parameter to be Monitored	Indicators	Location	Responsibility	Frequency
Water source									
Maintenance of existing tube well	No significant impact								
Construction of new tube well	Ground water reduction	Construction of ground water recharge pond			Water table level	Reduction in ground water level	site specific	Contractor and WUSC	During operation
Transmission line									
Enhancement not required	No any significant impact								
Treatment plant									
Chlorination unit	No any significant impact								
Maintenance of treatment plant	Noise pollution	Sound muffler installed	Not applicable		Sound level	Noise level emission standard	Site specific	Contractor	During construction
Reservoir									
Maintenance of existing reservoir	No any significant impact								
Distribution line									
Installation of fire hydrant	Minor impact (site specific)	Traffic diversion	Not applicable				Site specific	Contractor	During construction

Overview of Impacts		Required mitigation measures			Monitoring plan for implementation				
Project activities	Possible impacts (on all baseline parameters)	Mitigation associated with project location	Mitigation in project design features	Residual mitigation measures (not addressed by location and design)	Parameter to be Monitored	Indicators	Location	Responsibility	Frequency
Network rehabilitation activities/ Additional distribution network	Traffic disturbance	Arrangement for traffic diversion with traffic	Traffic diversion		Arrangement of vehicular movement during construction	Smooth running of vehicles through diversion	Site specific	Contractor	During construction
	Air pollution	Dust reductions should be controlled	Not applicable		Air quality	Particulate matter in air	Site specific	Contractor, WUSC and Locals	During construction
	HHs water distribution	Intermittent supply	Supply water through other sources		Water supply continued	Adequate amount of water supply in each households	Site specific	Contractor and WUSC	During construction
Electrical and mechanical repairment	Noise pollution and oil spillage	Sound muffler installed and proper management of waste oil	Not applicable		Sound level and amount of oil	Noise level emission standard	Site specific	Contractor	During construction

Note: Table 10-2is prepared according to Table 7-1of Chapter 7.

11. CONCLUSIONS AND RECOMMENDATIONS

152. The proposed subproject is not an environmentally critical undertaking. The IEE indicates that:

- The proposed subproject, its components, are not within or adjacent to environmentally sensitive areas.
- The extent of adverse impacts is expected to be local, confined within the subprojects' main areas of influence, quarry or borrowing sites, waste disposal sites, and the routes to and from these sites. Fine aggregates, sediments and/or wastes would not be transported beyond the aforementioned sites. With mitigation measures in place and ensuring that the bulk of earthworks are completed prior to the onset of the rainy season, the potential adverse impacts during construction would be highly/more site-specific.
- The few adverse impacts of high magnitude during construction will be temporary and short-term (i.e., most likely to occur only during peak construction period). These will not be sufficient to threaten or weaken the surrounding resources. The preparation and implementation of a Contractor's EMP that would address as minimum the requirements of the SPS-compliant subproject EMP will mitigate the impacts and lower their residual significance to acceptable levels. Simple/uncomplicated mitigation measures, basically integral to socially and environmentally responsible construction practices, are commonly used at construction sites and are known to Contractors. Hence, mitigation measures would not be difficult to design and institute.
- During operation, the potential delivery of unsafe water can be mitigated with good operation and maintenance, prompt action on leaks, and complying with the required quality monitoring of supplied water as prescribed in the National Drinking Water Quality Standards Directives.
- The proposed subproject will bring about: (i) the benefits of access to reliable supply of safe and potable water; (ii) promotion of good hygiene and sanitation practices and reduced health and safety risks as positive impacts; and (iii) enhanced public health, improved quality of life and safe communities as outcomes.

153. Based on the above findings, the classification of the 3rdSTWSSSP as Category B is confirmed, and no further special study or detailed EIA needs to be undertaken to comply with the Safeguard Policy Statement of the ADB. The Government of Nepal will incorporate the findings and recommendations of this IEE and prescribed environmental management in the EMP.

12. COMMENTS INCORPORATION MATRIX

Annexes

Annex 1: Project Location Map and Water Supply Plan


Annex 2: Water Tested Laboratory Analysis Report

Annex 3: Rapid Environmental Assessment (REA) Checklist

Annex 4: Minute of Meeting

ITAHARI, SUNSARI

BARMHAPUR TOLE

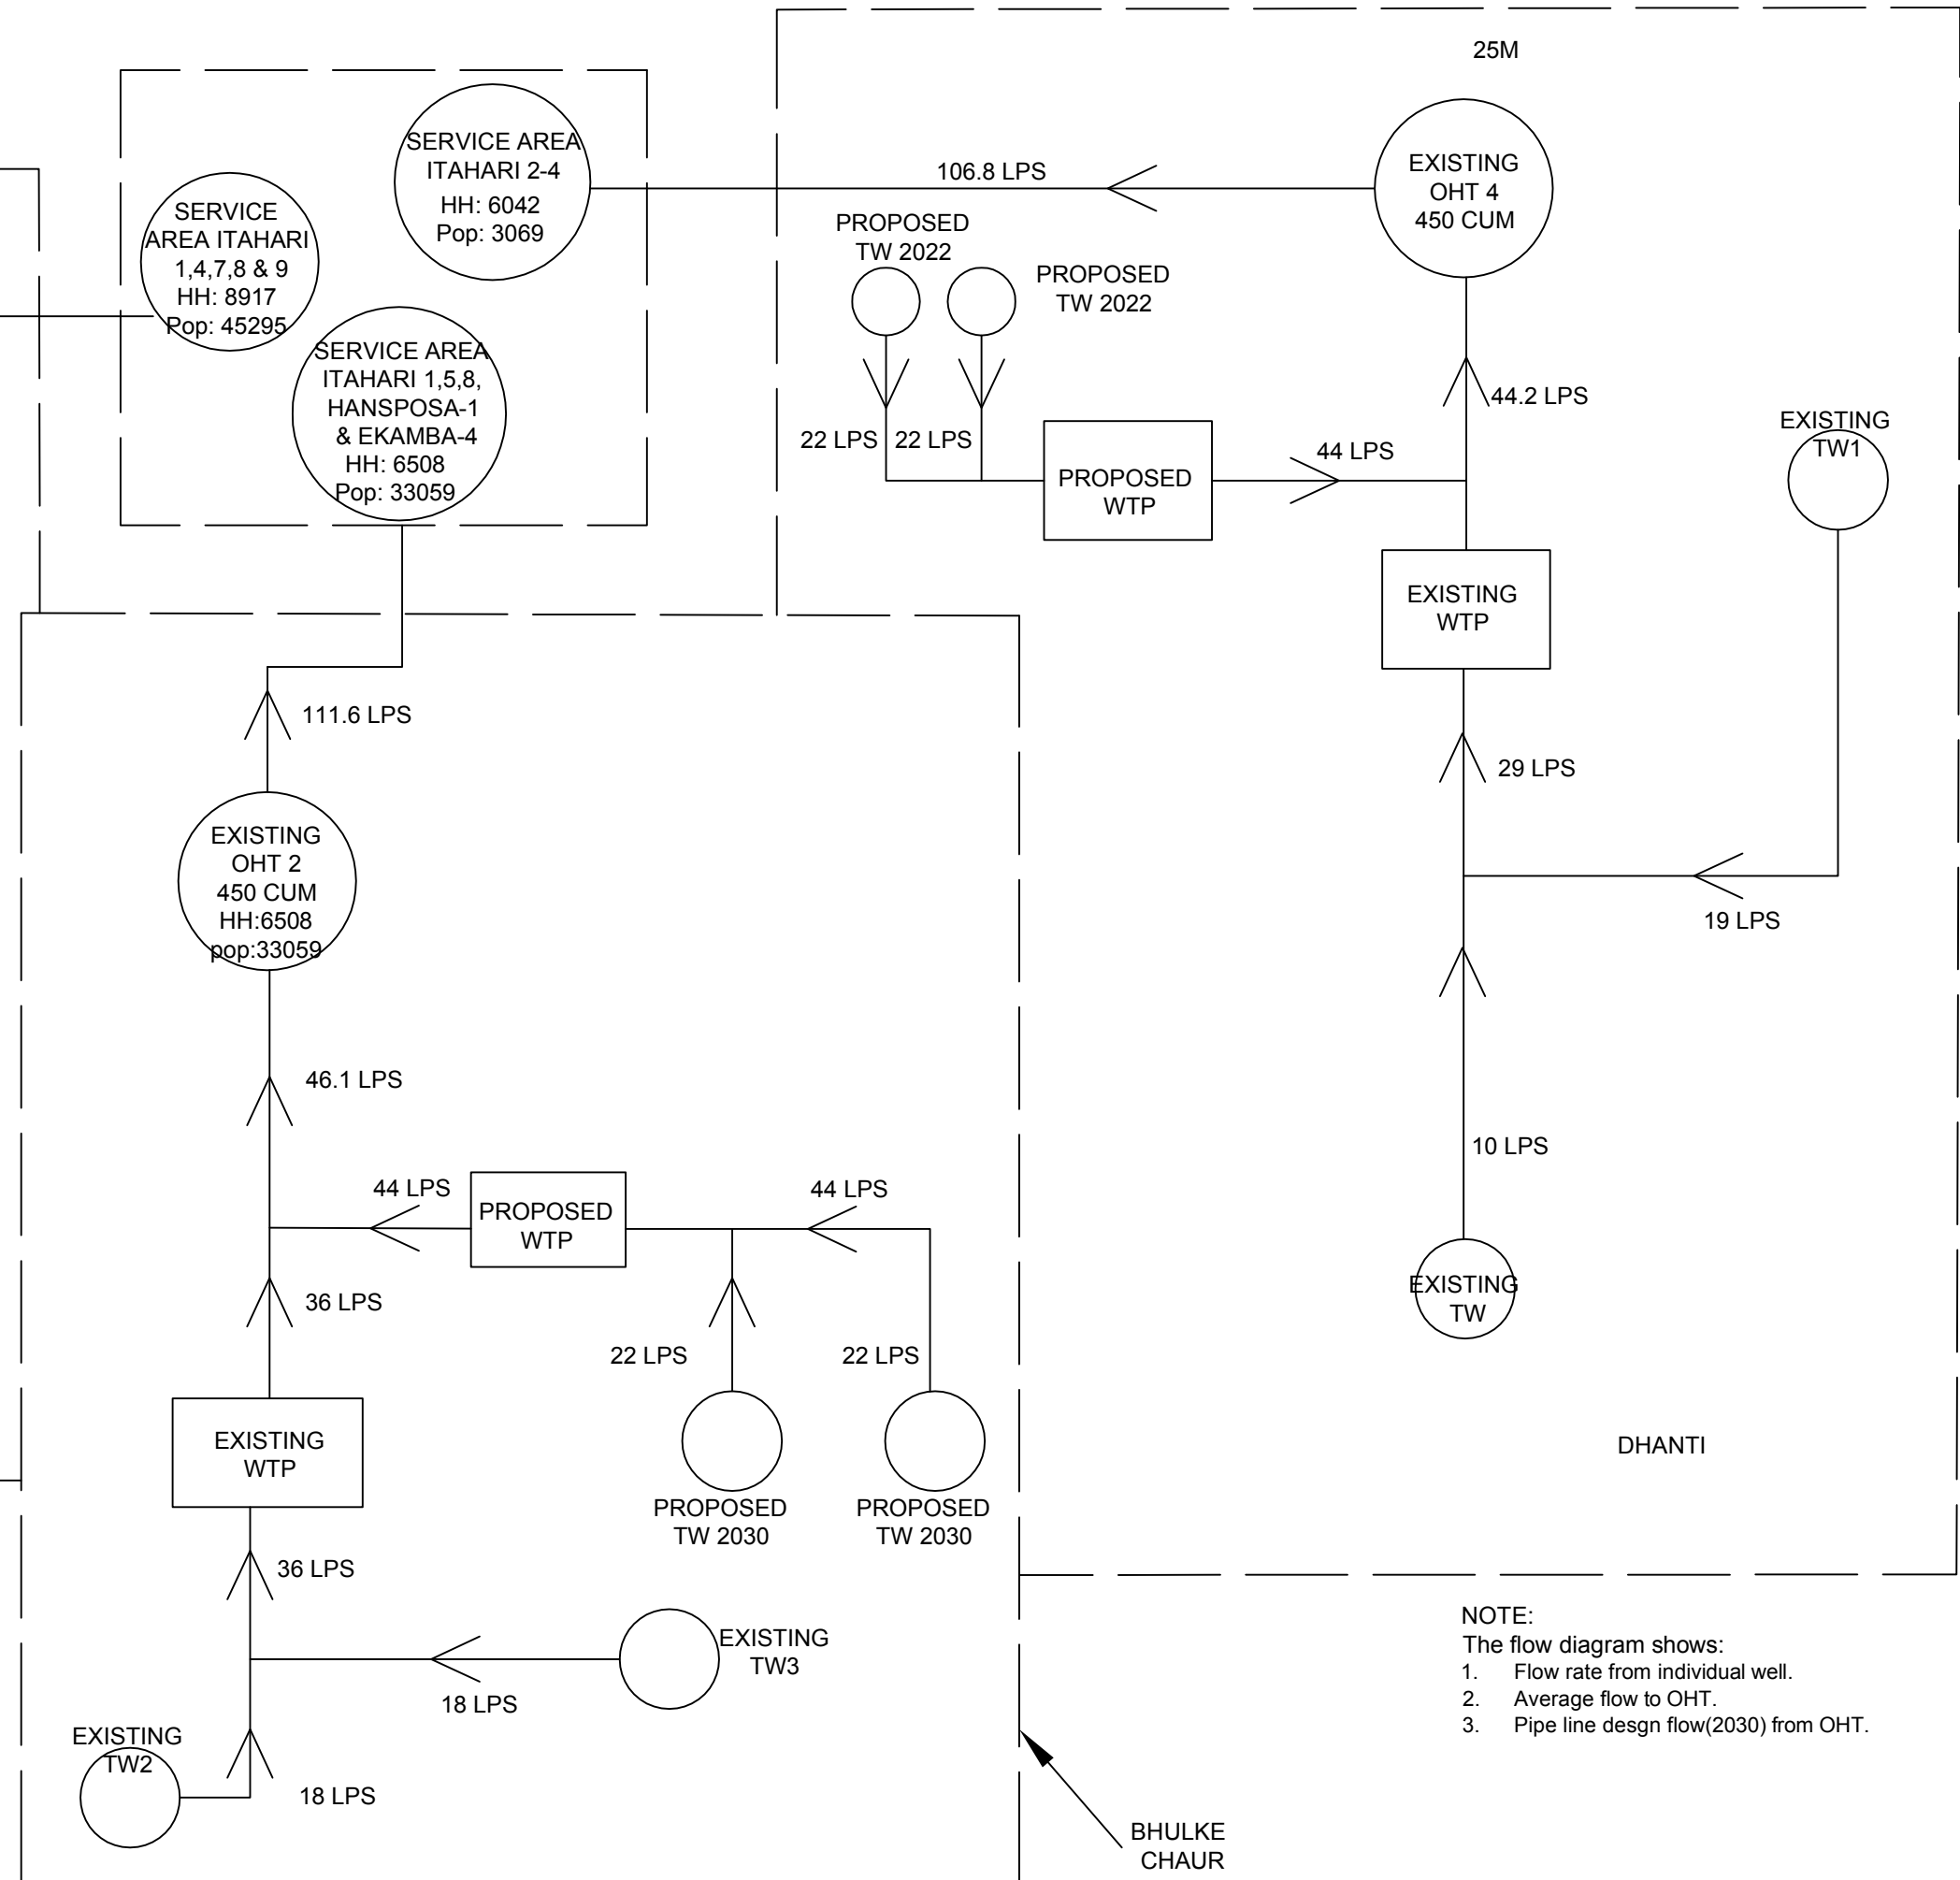

NOTE:
 The flow diagram shows:
 1. Flow rate from individual well.
 2. Average flow to OHT.
 3. Pipe line design flow(2030) from OHT.

Annex - 2: Water Tested Laboratory Analysis Report



Water

Engineering & Training Centre (P.) Ltd.

Laboratory, R & D on Total Water Management, Treatment & Consultancy

LABORATORY ANALYSIS REPORT

Name of Sender: **SILT ITEKO UNICORN JV** Name of the Project: **Ishari STWSSSP1** Date of Collection: **18/9/2014**
 Sample No. **737/071/072** Type of Source: **Boring** No. of Sample: **1**
 Date of Receipt: **21/9/2014** Name of the Source: **Tank 1** Field Temperature: **26.8 °C**
 Analyzed Date: **21-31/9/2014** Sampling Point: **Boring (Tank 1 - South West)** Field pH: **7.4**
 Sampled by: **WETC** Location: **Ishari** Field EC: **442.0 µS/cm**

Parameters	Units	WHO GV	NDWQS	Result	Methods Used
PHYSICAL					
pH	-	6.5-8.5	6.5-8.5*	7.4	4500-H+ B. APHA, 21ST EDITION
Turbidity	NTU	5	5(10)	1.0	2130 B. APHA, 21ST EDITION
Electrical Conductivity	µS/cm	-	1500	463	2510 B. APHA, 21ST EDITION
Lab Temperature	°C	-	-	25.0	2550 B. APHA, 21ST EDITION
CHEMICAL					
Calcium	mg/l as Ca ²⁺	-	200	67.2	3500 - Ca B. APHA, 21ST EDITION
Magnesium	mg/l as Mg ²⁺	-	-	13.6	3500-Mg B. APHA, 21ST EDITION
Iron	mg/l as Fe ²⁺	0.3	0.3(3)	0.41	3111 B. APHA, 21ST EDITION
Manganese	mg/l as Mn ²⁺	0.4	0.2	0.02	3111 B. APHA, 21ST EDITION
Arsenic	mg/l as As ³⁺	0.01	0.05	<0.005	3114 C. APHA, 21ST EDITION
Ammonia	mg/l as NH ₄ ⁺	1.5	1.5	0.10	4500-NH3 C. APHA, 17TH EDITION
Sodium	mg/l as Na ⁺	-	-	8.8	3111 B. APHA, 21ST EDITION
Potassium	mg/l as K ⁺	-	-	1.4	3111 B. APHA, 21ST EDITION
Total Chromium	mg/l as Cr ³⁺	0.05	0.05	<0.01	3111 B. APHA, 21ST EDITION
Bicarbonate	mg/l as CaCO ₃	-	-	226	2320 B. APHA, 21ST EDITION
Carbonate	mg/l as CO ₃ ²⁻	-	-	Nil	2320 B. APHA, 21ST EDITION
Hydroxide Alkalinity	mg/l as OH ⁻	-	-	Nil	2320 B. APHA, 21ST EDITION
Total Alkalinity	mg/l as CaCO ₃	500	-	226	2320 B. APHA, 21ST EDITION
Carbonate Alkalinity	mg/l as CaCO ₃	-	-	Nil	2320 B. APHA, 21ST EDITION
Non-carbonate Alkalinity	mg/l as CaCO ₃	-	-	226	2320 B. APHA, 21ST EDITION
Phosphate	mg/l as P	-	-	0.05	4500-PO ₄ B. APHA, 21ST EDITION
Nitrate	mg/l as NO ₃ ⁻	50	50	0.02	4500-NO ₃ - H. APHA, 21ST EDITION
Nitrite	mg/l as NO ₂ ⁻	3	-	<0.02	4500-NO ₂ - H. APHA, 21ST EDITION
Sulfate	mg/l as SO ₄ ²⁻	250	250	4.0	4500-SO ₄ APHA, 21ST EDITION
Chloride	mg/l as Cl ⁻	250	250	1.9	4500-CL- B. APHA, 21ST EDITION
Silica	mg/l as Si ²⁺	-	-	11.3	4500-SI- D. APHA, 21ST EDITION
Fluoride	mg/l as SiO ₂ ²⁻	1.5	0.5-1.5*	0.21	4500-SIO ₂ D. APHA, 21ST EDITION
Total Hardness	mg/l as CaCO ₃	500	500	224	2340 C. APHA, 21ST EDITION
Non Carbonate Hardness	mg/l as CaCO ₃	-	-	226	Calculation
Total Dissolved Solid	mg/l	1000	-	233	2540 C. APHA, 21ST EDITION
Langelier Saturation Index	-	-	-	-0.49	2330 B. APHA, 21ST EDITION
BIOLOGICAL					
Total Coliform	CFU/100 ml	Nil	Nil	Nil	9222 B. APHA, 21ST EDITION
Fecal Coliform	CFU/100 ml	Nil	Nil	Nil	9222 D. APHA, 21ST EDITION

APHA: American Public Health Association, Standard Methods for the Examination of Water and Wastewater. WHO GV: World Health Organization Guideline Value, 2006 Update. NDWQS: National Drinking Water Quality Standard, 2062 (Nepal). * These values show lower and upper limits. () Values in the parenthesis refers the acceptable values only when alternative is not available. **Not accredited Test Method

Comment: *Within the guideline range.*

Analyzed by

Checked by

Authorized Signature

Note: 1. The results refer only to the parameters tested of the samples provided to our laboratory or collected by us for analysis as specified. Endorsement of the product is not intended or implied.
 2. Any duplication of this report can not be used as evidence in the court of law and should not be used in any advertising media without prior written permission to us.
 3. The total liability of our company for the product is limited to the original contract only.



Water

Engineering & Training Centre (P.) Ltd.

Laboratory, R & D on Total Water Management, Treatment & Consultancy

LABORATORY ANALYSIS REPORT

Name of Sender: **SJ, TITEKO I NICORN JV** Name of the Project: **Itahari STWSSSP** Date of Collection: **18/9/2014**
 Sample No: **738/071/072** Type of Source: **Boring** No of Sample: **1**
 Date of Receipt: **21/9/2014** Name of the Source: **Tank 1** Field Temperature: **25 °C**
 Analyzed Date: **21-31/9/2014** Sampling Point: **Boring (Tank 1 - South East)** Field pH: **7.5**
 Sampled by: **WETC** Location: **Itahari** Field TC: **403.0 µS/cm**

Parameters	Units	WHO GV	NDWQS	Result	Methods Used
PHYSICAL					
pH	-	6.5-8.5	6.5-8.5*	7.5	4500-B- B, APHA, 21ST EDITION
Turbidity	NTU	5	5(10)	<1.0	2130 B, APHA, 21ST EDITION
Electrical Conductivity	µS/cm	-	1500	425	2510 B, APHA, 21ST EDITION
Lab Temperature	°C	-	-	24.6	2550 H, APHA, 21ST EDITION
CHEMICAL					
Calcium	mg/l as Ca ²⁺	-	200	60.8	3500-Ca B, APHA, 21ST EDITION
Magnesium	mg/l as Mg ²⁺	-	-	16.5	3500-Mg B, APHA, 21ST EDITION
Iron	mg/l as Fe ²⁺	0.3	0.3(3)	0.9	3111 B, APHA, 21ST EDITION
Manganese	mg/l as Mn ²⁺	0.4	0.2	<0.01	3111 B, APHA, 21ST EDITION
Arsenic	mg/l as As ³⁺	0.01	0.05	<0.005	3114 C, APHA, 21ST EDITION
Ammonia	mg/l as NH ₄ ⁺	1.5	1.5	0.10	4500-NH3 C, APHA, 17TH EDITION
Sodium	mg/l as Na ⁺	-	-	9.4	3111 B, APHA, 21ST EDITION
Potassium	mg/l as K ⁺	-	-	1.7	3111 B, APHA, 21ST EDITION
Total Chromium	mg/l as Cr ⁶⁺	0.05	0.05	<0.01	3111 B, APHA, 21ST EDITION
Bicarbonate	mg/l as CaCO ₃	-	-	224	2320 B, APHA, 21ST EDITION
Carbonate	mg/l as CO ₃ ²⁻	-	-	Nil	2320 B, APHA, 21ST EDITION
Hydroxide Alkalinity	mg/l as OH ⁻	-	-	Nil	2320 B, APHA, 21ST EDITION
Total Alkalinity	mg/l as CaCO ₃	500	-	224	2320 B, APHA, 21ST EDITION
Carbonate Alkalinity	mg/l as CaCO ₃	-	-	Nil	2320 B, APHA, 21ST EDITION
Non-carbonate Alkalinity	mg/l as CaCO ₃	-	-	224	2320 B, APHA, 21ST EDITION
Phosphate	mg/l as P	-	-	0.13	4500-P C, APHA, 21ST EDITION
Nitrate	mg/l as NO ₃ ⁻	50	50	0.55	4500-NO3- D, APHA, 21ST EDITION
Nitrite	mg/l as NO ₂ ⁻	3	-	<0.02	4500-NO2- B, APHA, 21ST EDITION
Sulfate	mg/l as SO ₄ ²⁻	250	250	12.0	4500-SO4, APHA, 21ST EDITION
Chloride	mg/l as Cl	250	250	2.97	4500-CL- B, APHA, 21ST EDITION
Silica	mg/l as SiO ₂ ²⁻	-	-	9.9	4500F- D, APHA, 21ST EDITION
Fluoride	mg/l as SiO ₂ ²⁻	1.5	0.5-1.5*	0.24	4500-SiO2 D, APHA, 21ST EDITION
Total Hardness	mg/l as CaCO ₃	500	500	220	2340 C, APHA, 21ST EDITION
Non Carbonate Hardness	mg/l as CaCO ₃	-	-	224	Calculation
Total Dissolved Solid	mg/l	1000	-	213	2540 C, APHA, 21ST EDITION
Langher Saturation Index	-	-	-	-0.75	2330 B, APHA, 21ST EDITION
BIOLOGICAL					
Total Coliforms	CFU/100 ml	Nil	Nil	55	9222 B, APHA, 21ST EDITION
Fecal Coliform	CFU/100 ml	Nil	Nil	Nil	9222 D, APHA, 21ST EDITION

APHA: American Public Health Association, Standard Methods for the Examination of Water & Waste Water. WHO GV: World Health Organization Guideline Value. 2006 Update, NDWQS: National Drinking Water Quality Standard, 2062 (Nepal). * These values show lower and upper limits, () Values in the parenthesis refers the acceptable values only when alternative is not available. **Not accredited Test Method

Comment: **Biological contaminated.**

Analyzed by

Checked by

Authorized Signature

Note: 1. The responsibility for the parameters tested of the samples provided to our laboratory or not tested by us for analysis as specified, is the responsibility of the producer. 2. Any duplication of this report can not be used as evidence in the court of law and should not be used in any advertising media without prior written permission to us. 3. The total liability of our company for the product is limited to the amount of amount only.



Water

Engineering & Training Centre (P.) Ltd.

Laboratory, R & D on Total Water Management, Treatment & Consultancy

LABORATORY ANALYSIS REPORT

Name of Sender: **SILTIFEKO UNICORN JV** Name of the Project: **Itahari STWSSSP** Date of Collection: **18/9/2014**
 Sample No: **739/071/072** Type of Source: **Boring** No of Sample: **1**
 Date of Receipt: **21/9/2014** Name of the Source: **Tank 1** Field Temperature: **26.6 °C**
 Analyzed Date: **21-31/9/2014** Sampling Point: **Compound Tap (WTP Outlet)** Field pH: **7.6**
 Sampled by: **WETC** Location: **Itahari** Field EC: **437.0 µS/cm**

Parameters	Units	WHO GV	NDWQS	Result	Methods Used
PHYSICAL					
pH	-	6.5-8.5	6.5-8.5*	7.3	4505-H- B, APHA, 21ST EDITION
Turbidity	NTU	5	5(10)	<1.0	2130 B, APHA, 21ST EDITION
Electrical Conductivity	µS/cm	-	1500	446	2510 B, APHA, 21ST EDITION
Lab Temperature	°C	-	-	24.4	2550 B, APHA, 21ST EDITION
CHEMICAL					
Calcium	mg/l as Ca ²⁺	-	200	67.3	3500-Ca B, APHA, 21ST EDITION
Magnesium	mg/l as Mg ²⁺	-	-	13.6	3500-Mg B, APHA, 21ST EDITION
Iron	mg/l as Fe ²⁺	0.3	0.3(3)	0.11	3111 B, APHA, 21ST EDITION
Manganese	mg/l as Mn ²⁺	0.4	0.2	<0.01	3111 B, APHA, 21ST EDITION
Arsenic	mg/l as As ³⁺	0.01	0.05	<0.005	3114 C, APHA, 21ST EDITION
Ammonia	mg/l as NH ₄ ⁺	1.5	1.5	<0.02	4500-NH3C, APHA, 17TH EDITION
Sodium	mg/l as Na ⁺	-	-	10.4	3111 B, APHA, 21ST EDITION
Potassium	mg/l as K ⁺	-	-	1.8	3111 B, APHA, 21ST EDITION
Total Chromium	mg/l as Cr ⁶⁺	0.05	0.05	<0.01	3111 B, APHA, 21ST EDITION
Bicarbonate	mg/l as CaCO ₃	-	-	222	2320 B, APHA, 21ST EDITION
Carbonate	mg/l as CO ₃ ²⁻	-	-	Nil	2320 B, APHA, 21ST EDITION
Hydroxide Alkalinity	mg/l as OH ⁻	-	-	Nil	2320 B, APHA, 21ST EDITION
Total Alkalinity	mg/l as CaCO ₃	500	-	222	2320 B, APHA, 21ST EDITION
Carbonate Alkalinity	mg/l as CaCO ₃	-	-	Nil	2320 B, APHA, 21ST EDITION
Non-carbonate Alkalinity	mg/l as CaCO ₃	-	-	222	2320 B, APHA, 21ST EDITION
Phosphate	mg/l as P	-	-	0.05	4500-P, APHA, 21ST EDITION
Nitrate	mg/l as NO ₃	50	50	0.56	4500-NO3-B, APHA, 21ST EDITION
Nitrite	mg/l as NO ₂	3	-	<0.02	4500-NO2-B, APHA, 21ST EDITION
Sulfate	mg/l as SO ₄ ²⁻	250	250	18.0	4500-SO4, APHA, 21ST EDITION
Chloride	mg/l as Cl ⁻	250	250	0.99	4500-Cl-B, APHA, 21ST EDITION
Silica	mg/l as F ⁻	-	-	9.6	4500F-D, APHA, 21ST EDITION
Fluoride	mg/l as SiO ₂ ²⁻	1.5	0.5-1.5*	0.35	4500-SiO2 D, APHA, 21ST EDITION
Total Hardness	mg/l as CaCO ₃	500	500	224	2340 C, APHA, 21ST EDITION
Non Carbonate Hardness	mg/l as CaCO ₃	-	-	222	Calculation
Total Dissolved Solid	mg/l	1000	-	223	2540 C, APHA, 21ST EDITION
Langlier Saturation Index	-	-	-	-0.39	2330 H, APHA, 21ST EDITION
BIOLOGICAL					
Total Coliform	CFU/100 ml	Nil	Nil	100	9222 B, APHA, 21ST EDITION
Focal Coliform	CFU/100 ml	Nil	Nil	34	9222 D, APHA, 21ST EDITION

APHA: American Public Health Association, Standard Methods for the Examination of Water & Waste Water, WHO GV: World Health Organization Guideline Value, 2006 Update, NDWQS: National Drinking Water Quality Standard, 2062 (Nepal), * These values show lower and upper limits, () Values in the parenthesis refers the acceptable values only when alternative is not available, **Not accredited Test Method

Comment: *Biological contaminated.*

Analyzed by

Checked by

Authorized Signature

Note: 1. The results refer only to the parameters listed of the samples received to our laboratory or collected by us for analysis as specified. Endorsement of the product is not intended or implied.
 2. Any distribution of this report can not be used as evidence in the court or law and should not be used in any advertisement without prior written permission from us.
 3. The report, any symbols, contents, for the product is limited to the physical analysis only.



Water

Engineering & Training Centre (P.) Ltd.

Laboratory, R & D on Total Water Management, Treatment & Consultancy

LABORATORY ANALYSIS REPORT

Name of Sender: **SILT ITEKO UNICORN JV** Name of the Project: **Itahari STWSSSP** Date of Collection: **18/9/2014**
 Sample No: **740/071/072** Type of Source: **Boring** No of Sample: **1**
 Date of Receipt: **21/9/2014** Name of the Source: **Tank 2** Field Temperature: **29.1 °C**
 Analyzed Date: **21-31/9/2014** Sampling Point: **Private Tap (Ward 2)** Field pH: **7.6**
 Sampled by: **WETC** Location: **Itahari** Field EC: **393.0 µS/cm**

Parameters	Units	WHO GV	NDWQS	Result	Methods Used
PHYSICAL					
pH	-	6.5-8.5	6.5-8.5*	7.1	4500-H+ B, APHA, 21ST EDITION
Turbidity	NTU	5	5(10)	<1.0	2130 B, APHA, 21ST EDITION
Electrical Conductivity	µS/cm	-	1500	403	2510 B, APHA, 21ST EDITION
Lab Temperature	°C	-	-	24.5	2550 B, APHA, 21ST EDITION
CHEMICAL					
Calcium	mg/l as Ca ²⁺	-	200	60.8	4500-Ca B, APHA, 21ST EDITION
Magnesium	mg/l as Mg ²⁺	-	-	10.7	4500-Mg D, APHA, 21ST EDITION
Iron	mg/l as Fe ²⁺	0.3	0.3(3)	0.08	3111 B, APHA, 21ST EDITION
Manganese	mg/l as Mn ²⁺	0.4	0.2	<0.01	3111 B, APHA, 21ST EDITION
Arsenic	mg/l as As ³⁺	0.01	0.05	<0.005	3114 C, APHA, 21ST EDITION
Ammonia	mg/l as NH ₄ ⁺	1.5	1.5	<0.02	4500-NH ₃ C, APHA, 17TH EDITION
Sodium	mg/l as Na ⁺	-	-	9.4	3111 B, APHA, 21ST EDITION
Potassium	mg/l as K ⁺	-	-	2.0	3111 B, APHA, 21ST EDITION
Total Chromium	mg/l as Cr ⁶⁺	0.05	0.05	<0.01	3111 B, APHA, 21ST EDITION
Bicarbonate	mg/l as CaCO ₃	-	-	200	2320 B, APHA, 21ST EDITION
Carbonate	mg/l as CO ₃ ²⁻	-	-	Nil	2320 B, APHA, 21ST EDITION
Hydroxide Alkalinity	mg/l as OH ⁻	-	-	Nil	2320 B, APHA, 21ST EDITION
Total Alkalinity	mg/l as CaCO ₃	500	-	200	2320 B, APHA, 21ST EDITION
Carbonate Alkalinity	mg/l as CaCO ₃	-	-	Nil	2320 B, APHA, 21ST EDITION
Non-carbonate Alkalinity	mg/l as CaCO ₃	-	-	200	2320 B, APHA, 21ST EDITION
Phosphate	mg/l as P	-	-	0.10	4500-P E, APHA, 21ST EDITION
Nitrite	mg/l as NO ₂ ⁻	50	50	2.93	4500-NO ₂ -B, APHA, 21ST EDITION
Nitric	mg/l as NO ₃ ⁻	3	-	<0.02	4500-NO ₃ -B, APHA, 21ST EDITION
Sulfate	mg/l as SO ₄ ²⁻	250	250	54.0	4500-SO ₄ , APHA, 21ST EDITION
Chloride	mg/l as Cl ⁻	250	250	2.97	4500-Cl- B, APHA, 21ST EDITION
Silica	mg/l as SiO ₂ ²⁻	-	-	13.5	4500F-D, APHA, 21ST EDITION
Fluoride	mg/l as SiO ₂ ²⁻	1.5	0.5-1.5*	0.14	4500-SO ₂ D, APHA, 21ST EDITION
Total Hardness	mg/l as CaCO ₃	500	500	196	2310 C, APHA, 21ST EDITION
Non Carbonate Hardness	mg/l as CaCO ₃	-	-	200	Calculation
Total Dissolved Solid	mg/l	1000	-	202	2540 C, APHA, 21ST EDITION
Langelier Saturation Index	-	-	-	-0.65	2330 B, APHA, 21ST EDITION
BIOLOGICAL					
Total Coliform	CFU/100 ml	Nil	Nil	Nil	9222 B, APHA, 21ST EDITION
Fecal Coliform	CFU/100 ml	Nil	Nil	Nil	9222 D, APHA, 21ST EDITION

APHA: American Public Health Association, Standard Methods for the Examination of Water & Wastewater, WHO GV: World Health Organization Guideline Value, 2006 Update, NDWQS: National Drinking Water Quality Standard, 2062 (Nepal), * These values show lower and upper limits, () Values in the parenthesis refers the acceptable values only when alternative is not available. **Not accredited Test Method

Comment: *Biological contaminated.*

Analyzed by

Checked by

Authorized Signature

Note: 1. The results are only for the parameters tested of the samples provided to our laboratory, and of quantity as the analysis as specified. Endorsement of the product or the information supplied.
 2. Any caption or address report can not be used as evidence in the court of law and should not be used in any advertising media without prior written permission.
 3. The total price of water services for the producer is limited to the original amount only.



Water

Engineering & Training Centre (P.) Ltd.

Laboratory, R & D on Total Water Management, Treatment & Consultancy

LABORATORY ANALYSIS REPORT

Name of Sender: **SILT ITEKO UNICORN JV** Name of the Project: **Itahari STWSSSP** Date of Collection: **18/9/2014**
 Sample No: **741/071/072** Type of Source: **Boring** No of Sample: **1**
 Date of Receipt: **21/9/2014** Name of the Source: **Tank 3** Field Temperature: **26.1 °C**
 Analyzed Date: **21-31/9/2014** Sampling Point: **Boring (South East)** Field pH: **7.8**
 Sampled by: **WETC** Location: **Itahari** Field EC: **385.0 µS/cm**

Parameters	Units	WHO GV	NDWQS	Result	Methods Used
PHYSICAL					
pH	-	6.5-8.5	6.5-8.5*	7.8	4500-B, APHA, 21ST EDITION
Turbidity	NTU	5	5(10)	<1.0	2130 B, APHA, 21ST EDITION
Electrical Conductivity	µS/cm	-	1500	387	2540 B, APHA, 21ST EDITION
Lab Temperature	°C	-	-	24.6	2550 B, APHA, 21ST EDITION
CHEMICAL					
Calcium	mg/l as Ca ²⁺	-	200	52.8	3500-Ca B, APHA, 21ST EDITION
Magnesium	mg/l as Mg ²⁺	-	-	14.6	3500-Mg B, APHA, 21ST EDITION
Iron	mg/l as Fe ²⁺	0.3	0.3(3)	0.83	3111 B, APHA, 21ST EDITION
Manganese	mg/l as Mn ²⁺	0.4	0.2	0.01	3111 B, APHA, 21ST EDITION
Arsenic	mg/l as As ³⁺	0.01	0.05	<0.005	3114 C, APHA, 21ST EDITION
Ammonia	mg/l as NH ₄ ⁺	1.5	1.5	0.04	4500-NH ₃ C, APHA, 17TH EDITION
Sodium	mg/l as Na ⁺	-	-	9.6	3111 B, APHA, 21ST EDITION
Potassium	mg/l as K ⁺	-	-	1.4	3111 B, APHA, 21ST EDITION
Total Chromium	mg/l as Cr ³⁺	0.05	0.05	<0.01	3111 B, APHA, 21ST EDITION
Bicarbonate	mg/l as CaCO ₃	-	-	196	2320 B, APHA, 21ST EDITION
Carbonate	mg/l as CO ₃ ²⁻	-	-	Nil	2320 B, APHA, 21ST EDITION
Hydroxide Alkalinity	mg/l as OH ⁻	-	-	Nil	2320 B, APHA, 21ST EDITION
Total Alkalinity	mg/l as CaCO ₃	500	-	196	2320 B, APHA, 21ST EDITION
Carbonate Alkalinity	mg/l as CaCO ₃	-	-	Nil	2320 B, APHA, 21ST EDITION
Non-carbonate Alkalinity	mg/l as CaCO ₃	-	-	196	2320 B, APHA, 21ST EDITION
Phosphate	mg/l as P	-	-	0.06	4500-P E, APHA, 21ST EDITION
Nitrate	mg/l as NO ₃ ⁻	50	50	1.89	4500-NO ₃ -B, APHA, 21ST EDITION
Nitrite	mg/l as NO ₂ ⁻	3	-	<0.02	4500-NO ₂ -B, APHA, 21ST EDITION
Sulfate	mg/l as SO ₄ ²⁻	250	250	32.0	4500-SO ₄ APHA, 21ST EDITION
Chloride	mg/l as Cl ⁻	250	250	3.96	4500-Cl- B, APHA, 21ST EDITION
Silica	mg/l as Si ⁺	-	-	10.7	4500F-D, APHA, 21ST EDITION
Fluoride	mg/l as SiO ₂ ²⁻	1.5	0.5-1.5*	0.16	4500-SiO ₂ D, APHA, 21ST EDITION
Total Hardness	mg/l as CaCO ₃	500	500	192	2340 C, APHA, 21ST EDITION
Non Carbonate Hardness	mg/l as CaCO ₃	-	-	196	Calculation
Total Dissolved Solid	mg/l	1000	-	194	2540 C, APHA, 21ST EDITION
Langlier Saturation Index	-	-	-	-0.33	2330 B, APHA, 21ST EDITION
BIOLOGICAL					
Total Coliform	CFU/100 ml	Nil	Nil	80	9222 B, APHA, 21ST EDITION
Fecal Coliform	CFU/100 ml	Nil	Nil	Nil	9222 D, APHA, 21ST EDITION

APHA: American Public Health Association, Standard Methods for the Examination of Water & Waste Water, WHO GV: World Health Organization Guideline Value, 2006 Update, NDWQS: National Drinking Water Quality Standard, 2062 (Nepal). * These values show lower and upper limits, () Values in the parenthesis refers the acceptable values only when alternative is not available. **Not accredited Test Method

Comment: *Biological contaminated.*

Analyzed by

Checked by

Authorized Signature

Note: 1. The result of the parameters listed of the samples provided to our laboratory or collected by us for analysis as specified. Endorsement of the product is never inferred to be implied.
 2. Any dispute on quality report cannot be used as evidence in the court of law and should not be used in any advertising media without prior written permission to us.
 3. The total liability of our company for the product is limited to the amount shown only.



Water

Engineering & Training Centre (P.) Ltd.

Laboratory, R & D on Total Water Management, Treatment & Consultancy

LABORATORY ANALYSIS REPORT

Name of Sender: **SILT ITEKO UNICORN JV** Name of the Project: **Itahari STWSSSP** Date of Collection: **18/9/2014**
 Sample No: **742/071/072** Type of Source: **Boring** No of Sample: **1**
 Date of Receipt: **21/9/2014** Name of the Source: **Tank** Field Temperature: **27.2 °C**
 Analyzed Date: **21-31/9/2014** Sampling Point: **Compound Tap (Filter Outlet)** Field pH: **7.3**
 Sampled by: **WETC** Location: **Itahari** Field EC: **386.0 µS/cm**

Parameters	Units	WHO GV	NDWQS	Result	Methods Used
PHYSICAL					
pH	-	6.5-8.5	6.5-8.5*	7.1	4500-H- B, APHA, 21ST EDITION
Turbidity	NTU	5	5(10)	<1.0	2130 B, APHA, 21ST EDITION
Electrical Conductivity	µS/cm	-	1500	394	2510 B, APHA, 21ST EDITION
Lab Temperature	°C	-	-	24.5	2550 B, APHA, 21ST EDITION
CHEMICAL					
Calcium	mg/l as Ca ²⁺	-	200	56.8	3500 - Ca B, APHA, 21ST EDITION
Magnesium	mg/l as Mg ²⁺	-	-	12.1	3500-Mg B, APHA, 21ST EDITION
Iron	mg/l as Fe ²⁺	0.3	0.3(3)	0.06	3111 B, APHA, 21ST EDITION
Manganese	mg/l as Mn ²⁺	0.4	0.2	<0.01	3111 B, APHA, 21ST EDITION
Arsenic	mg/l as As ³⁺	0.01	0.05	<0.005	3114 C, APHA, 21ST EDITION
Ammonia	mg/l as NH ₄ ⁺	1.5	1.5	0.15	4500-NH3C, APHA, 17TH EDITION
Sodium	mg/l as Na ⁺	-	-	8.7	3111 B, APHA, 21ST EDITION
Potassium	mg/l as K ⁺	-	-	1.3	3111 B, APHA, 21ST EDITION
Total Chromium	mg/l as Cr ³⁺	0.05	0.05	<0.01	3111 B, APHA, 21ST EDITION
Bicarbonate	mg/l as CaCO ₃	-	-	198	2320 B, APHA, 21ST EDITION
Carbonate	mg/l as CO ₃ ²⁻	-	-	Nil	2320 B, APHA, 21ST EDITION
Hydroxide Alkalinity	mg/l as OH ⁻	-	-	Nil	2320 B, APHA, 21ST EDITION
Total Alkalinity	mg/l as CaCO ₃	500	-	198	2370 B, APHA, 21ST EDITION
Carbonate Alkalinity	mg/l as CaCO ₃	-	-	Nil	2320 B, APHA, 21ST EDITION
Non carbonate Alkalinity	mg/l as CaCO ₃	-	-	198	2320 B, APHA, 21ST EDITION
Phosphate	mg/l as P	-	-	0.07	4500-P, APHA, 21ST EDITION
Nitrate	mg/l as NO ₃	50	50	1.89	4500-NO3- B, APHA, 21ST EDITION
Nitrite	mg/l as NO ₂	3	-	<0.02	4500-NO2- B, APHA, 21ST EDITION
Sulfate	mg/l as SO ₄ ²⁻	250	250	<5.0	4500-SO4, APHA, 21ST EDITION
Chloride	mg/l as Cl ⁻	250	250	3.96	4500-Cl- B, APHA, 21ST EDITION
Silica	mg/l as F	-	-	14.1	4500F- D, APHA, 21ST EDITION
Fluoride	mg/l as SiO ₂ ²⁻	1.5	0.5-1.5*	0.06	4500-SiO2 D, APHA, 21ST EDITION
Total Hardness	mg/l as CaCO ₃	500	500	192	2340 C, APHA, 21ST EDITION
Non Carbonate Hardness	mg/l as CaCO ₃	-	-	198	Calculation
Total Dissolved Solid	mg/l	1000	-	197	2540 C, APHA, 21ST EDITION
Langelier Saturation Index	-	-	-	-0.65	2330 B, APHA, 21ST EDITION
BIOLOGICAL					
Total Coliform	CFU/100 ml	Nil	Nil	Nil	9222 B, APHA, 21ST EDITION
Focal Coliform	CFU/100 ml	Nil	Nil	Nil	9222 D, APHA, 21ST EDITION

APHA: American Public Health Association, Standard Methods for the Examination of Water & Waste Water, WHO GV: World Health Organization Guideline Value, 2006 Update, NDWQS: National Drinking Water Quality Standard, 2062 (Nepal). * These values show lower and upper limits, () Values in the parenthesis refers the acceptable values only when alternative is not available. **Not accredited Test Method

Comment: *Within the guideline range.*

Analysed by

Checked by

Authorized Signature

Note: The responsibility to the parameters listed of the samples provided to our laboratory is undertaken by our analysis as specified. Endorsement of the report is neither affirmed nor implied. Any duplication of this report can not be used as evidence in the court of law and should not be used in any advertising matter without prior written permission to us.

5. The total liability of our company for the product is limited to the measured amount only.



Water

Engineering & Training Centre (P.) Ltd.

Laboratory, R & D on Total Water Management, Treatment & Consultancy

LABORATORY ANALYSIS REPORT

Name of Sender: SILTIFERKO UNICORN JV Name of the Project: Itahari STWSSSP Date of Collection: 18/9/2014
 Sample No: 743/071/072 Type of Source: Boring No of Sample: 1
 Date of Receipt: 21/9/2014 Name of the Source: Tank 3 Field Temperature: 28.6 °C
 Analyzed Date: 21-31/9/2014 Sampling Point: Private Tap (Bimala Rai) Field pH: 7.4
 Sampled by: WETC Location: Itahari Field EC: 396.0 µS/cm

Parameters	Units	WHO GV	NDWQS	Result	Methods Used
PHYSICAL					
pH	-	6.5-8.5	6.5-8.5*	7.2	4500H- B, APHA, 21ST EDITION
Turbidity	NIT	5	5(10)	<1.0	2130 B, APHA, 21ST EDITION
Electrical Conductivity	µS/cm	-	1500	391	2510 B, APHA, 21ST EDITION
Lab Temperature	°C	-	-	24.6	2550 B, APHA, 21ST EDITION
CHEMICAL					
Calcium	mg/l as Ca ²⁺	-	200	56	3500 - Ca B, APHA, 21ST EDITION
Magnesium	mg/l as Mg ²⁺	-	-	12.1	3500-Mg B, APHA, 21ST EDITION
Iron	mg/l as Fe ²⁺	0.3	0.3(3)	0.14	3011 B, APHA, 20ST EDITION
Manganese	mg/l as Mn ²⁺	0.4	0.2	0.01	3111 B, APHA, 21ST EDITION
Arsenic	mg/l as As ³⁺	0.01	0.05	<0.005	3174 C, APHA, 21ST EDITION
Ammonia	mg/l as NH ₄ ⁺	1.5	1.5	0.10	4500-NH3C, APHA, 17TH EDITION
Sodium	mg/l as Na ⁺	-	-	9.3	3111 B, APHA, 21ST EDITION
Potassium	mg/l as K ⁺	-	-	1.6	3111 B, APHA, 21ST EDITION
Total Chromium	mg/l as Cr ³⁺	0.05	0.05	<0.01	4111 B, APHA, 21ST EDITION
Bicarbonate	mg/l as CaCO ₃	-	-	192	2320 B, APHA, 21ST EDITION
Carbonate	mg/l as CO ₃ ²⁻	-	-	Nil	2320 B, APHA, 21ST EDITION
Hydroxide Alkalinity	mg/l as OH ⁻	-	-	Nil	2320 B, APHA, 21ST EDITION
Total Alkalinity	mg/l as CaCO ₃	500	-	192	2320 B, APHA, 21ST EDITION
Carbonate Alkalinity	mg/l as CaCO ₃	-	-	Nil	2320 B, APHA, 21ST EDITION
Non-carbonate Alkalinity	mg/l as CaCO ₃	-	-	192	2320 B, APHA, 21ST EDITION
Phosphate	mg/l as P	-	-	0.06	4500-PO4, APHA, 21ST EDITION
Nitrate	mg/l as NO ₃ ⁻	50	50	1.98	4500-NO3- B, APHA, 21ST EDITION
Nitrite	mg/l as NO ₂ ⁻	3	-	<0.02	4500-NO2- B, APHA, 21ST EDITION
Sulfate	mg/l as SO ₄ ²⁻	250	250	<5.0	4500-SO4, APHA, 21ST EDITION
Chloride	mg/l as Cl ⁻	250	250	2.97	4500-CL- B, APHA, 21ST EDITION
Silica	mg/l as F ⁻	-	-	10.1	4500F- D, APHA, 21ST EDITION
Fluoride	mg/l as SiO ₂ ²⁻	1.5	0.5-1.5*	0.13	4500-SIO2 D, APHA, 21ST EDITION
Total Hardness	mg/l as CaCO ₃	500	500	190	2340 C, APHA, 21ST EDITION
Non Carbonate Hardness	mg/l as CaCO ₃	-	-	192	Calculation
Total Dissolved Solid	mg/l	1000	-	196	2540 C, APHA, 21ST EDITION
Dangher Saturation Index	-	-	-	-0.55	2320 B, APHA, 21ST EDITION
BIOLOGICAL					
Total Coliform	CFU/100 ml	Nil	Nil	Nil	9222 B, APHA, 21ST EDITION
Fecal Coliform	CFU/100 ml	Nil	Nil	Nil	9222 B, APHA, 21ST EDITION

APHA: American Public Health Association, Standard Methods for the Examination of Water & Waste Water, WHO GV: World Health Organization Guideline Value, 2006 Update, NDWQS: National Drinking Water Quality Standard, 2062 (Nepal). * These values show lower and upper limits. @ Values in the parenthesis refers the acceptable values only when alternative is not available. **Not accredited Test Method

Comment: Within the guideline range

Analyzed by

Checked by

Authorized Signature

Note: 1. The result is valid only for the parameters listed of the samples provided to our laboratory or collected by us for analysis as specified. 2. Any duplication of this report can not be used as evidence in the court of law and should not be used in any advertising media without prior written permission of us. 3. The liability of our company for the product is limited to the specified amount only.



Water

Engineering & Training Centre (P.) Ltd.

Laboratory, R & D on Total Water Management, Treatment & Consultancy

LABORATORY ANALYSIS REPORT

Name of Sender: **SILFITTEKO UNICORN JV** Name of the Project: **Itahari STWSSSP** Date of Collection: **18/9/2014**
 Sample No: **744/071/072** Type of Source: **Boring** No of Sample: **1**
 Date of Receipt: **21/9/2014** Name of the Source: **Tank 2** Field Temperature: **28.4 °C**
 Analyzed Date: **21-31/9/2014** Sampling Point: **Boring** Field pH: **39**
 Sampled by: **WETC** Location: **Itahari** Field EC: **75.0 µS/cm**

Parameters	Units	WHO GV	NDWQS	Result	Methods Used
PHYSICAL					
pH	-	6.5-8.5	6.5-8.5*	7.2	4500-H- B, APHA, 21ST EDITION
Turbidity	NTU	5	5(10)	<1.0	2130 B, APHA, 21ST EDITION
Electrical Conductivity	µS/cm	-	1500	403	2510 B, APHA, 21ST EDITION
Lab Temperature	°C	-	-	23.9	2550 B, APHA, 21ST EDITION
CHEMICAL					
Calcium	mg/l as Ca ²⁺	-	200	61.2	3500 - Ca B, APHA, 21ST EDITION
Magnesium	mg/l as Mg ²⁺	-	-	10.9	3500-Mg B, APHA, 21ST EDITION
Iron	mg/l as Fe ²⁺	0.3	0.3(3)	0.70	3111 B, APHA, 21ST EDITION
Manganese	mg/l as Mn ²⁺	0.4	0.2	<0.01	3111 B, APHA, 21ST EDITION
Arsenic	mg/l as As ³⁺	0.01	0.05	<0.005	3114 C, APHA, 21ST EDITION
Ammonia	mg/l as NH ₄ ⁺	1.5	1.5	<0.02	4500-NH ₄ C, APHA, 17TH EDITION
Sodium	mg/l as Na ⁺	-	-	9.0	3111 B, APHA, 21ST EDITION
Potassium	mg/l as K ⁺	-	-	1.6	3111 B, APHA, 21ST EDITION
Total Chromium	mg/l as Cr ³⁺	0.05	0.05	<0.01	3111 B, APHA, 21ST EDITION
Bicarbonate	mg/l as CaCO ₃	-	-	200	2320 B, APHA, 21ST EDITION
Carbonate	mg/l as CO ₃ ²⁻	-	-	Nil	2320 B, APHA, 21ST EDITION
Hydroxide Alkalinity	mg/l as OH ⁻	-	-	Nil	2320 B, APHA, 21ST EDITION
Total Alkalinity	mg/l as CaCO ₃	500	-	200	2320 B, APHA, 21ST EDITION
Carbonate Alkalinity	mg/l as CaCO ₃	-	-	Nil	2320 B, APHA, 21ST EDITION
Non-carbonate Alkalinity	mg/l as CaCO ₃	-	-	200	2320 B, APHA, 21ST EDITION
Phosphate	mg/l as P	-	-	0.03	4500-P E, APHA, 21ST EDITION
Nitrate	mg/l as NO ₃ ⁻	50	50	2.95	4500-NO ₃ - B, APHA, 21ST EDITION
Nitrite	mg/l as NO ₂ ⁻	3	-	<0.02	4500-NO ₂ - B, APHA, 21ST EDITION
Sulfate	mg/l as SO ₄ ²⁻	250	250	65.0	4500-SO ₄ , APHA, 21ST EDITION
Chloride	mg/l as Cl ⁻	250	250	3.01	4500-Cl- B, APHA, 21ST EDITION
Silica	mg/l as SiO ₂	-	-	15.5	4500-SiO ₂ D, APHA, 21ST EDITION
Fluoride	mg/l as F ⁻	1.5	0.5-1.5*	0.14	4500-SiO ₂ D, APHA, 21ST EDITION
Total Hardness	mg/l as CaCO ₃	500	500	192	2340 C, APHA, 21ST EDITION
Non Carbonate Hardness	mg/l as CaCO ₃	-	-	200	Calculation
Total Dissolved Solid	mg/l	1000	-	202	2540 C, APHA, 21ST EDITION
Langelier Saturation Index	-	-	-	-0.07	2330 B, APHA, 21ST EDITION
BIOLOGICAL					
Total Coliform	CFU/100 ml	Nil	Nil	Nil	9222 D, APHA, 21ST EDITION
Fecal Coliform	CFU/100 ml	Nil	Nil	Nil	9222 D, APHA, 21ST EDITION

APHA: American Public Health Association, Standard Methods for the Examination of Water & Waste Water, WHO GV: World Health Organization Guideline Value, 2006 Update, NDWQS: National Drinking Water Quality Standard, 2062 (Nepal). * These values show lower and upper limits. () Values in the parenthesis refers the acceptable values only when alternative is not available. **Not accredited Test Method.

Comment: All the tested parameters are within NDWQS guideline value

Analyzed by

Checked by

Authorized Signature

Note: 1. The result refer only to the parameters tested of the samples provided to our laboratory or collected by us for analysis as specified. Endorsement of the product is not to be implied.
 2. Any duplication of this report can only be used as reference of the main report and should not be used in any advertising media without prior written consent to us.
 3. The total liability of our company for the procedure limited to the highest amount only.



Water

Engineering & Training Centre (P.) Ltd.

Laboratory, R & D on Total Water Management, Treatment & Consultancy

LABORATORY ANALYSIS REPORT

Name of Sender: **SILTI THEKO UNICORN JV** Name of the Project: **Itahari STWSSSP** Date of Collection: **18/9/2014**
 Sample No: **745/071/072** Type of Source: **Boring** No of Sample: **1**
 Date of Receipt: **21/9/2014** Name of the Source: Field Temperature: **28.8 °C**
 Analyzed Date: **21-31/9/2014** Sampling Point: **Itahari Municipality Tap** Field pH: **7.6**
 Sampled by: **WETC** Location: **Itahari** Field EC: **441.0 µS/cm**

Parameters	Units	WHO GV	NDWQS	Result	Methods Used
PHYSICAL					
pH	-	6.5-8.5	6.5-8.5*	7.1	4500-H+ B, APHA, 21ST EDITION
Turbidity	NTU	5	5(10)	1.0	2130 B, APHA, 21ST EDITION
Electrical Conductivity	µS/cm	-	1500	463	2510 B, APHA, 21ST EDITION
Lab Temperature	°C	-	-	24.8	2550 B, APHA, 21ST EDITION
CHEMICAL					
Calcium	mg/l as Ca ⁺⁺	-	200	67.3	3500-Ca B, APHA, 21ST EDITION
Magnesium	mg/l as Mg ⁺⁺	-	-	13.8	3500-Mg B, APHA, 21ST EDITION
Iron	mg/l as Fe ⁺⁺	0.3	0.3(3)	0.14	3111 B, APHA, 21ST EDITION
Manganese	mg/l as Mn ⁺⁺	0.4	0.2	0.01	3111 B, APHA, 21ST EDITION
Arsenic	mg/l as As ⁺⁺⁺	0.01	0.05	<0.005	3114 C, APHA, 21ST EDITION
Ammonia	mg/l as NH ₄ ⁺	1.5	1.5	0.10	4500-NH ₃ C, APHA, 17TH EDITION
Sodium	mg/l as Na ⁺	-	-	8.4	3111 B, APHA, 21ST EDITION
Potassium	mg/l as K ⁺	-	-	1.8	3111 B, APHA, 21ST EDITION
Total Chromium	mg/l as Cr ⁺⁺	0.05	0.05	<0.01	3111 B, APHA, 21ST EDITION
Bicarbonate	mg/l as CaCO ₃	-	-	220	2320 B, APHA, 21ST EDITION
Carbonate	mg/l as CO ₃ ²⁻	-	-	Nil	2370 B, APHA, 21ST EDITION
Hydroxide Alkalinity	mg/l as OH ⁻	-	-	Nil	2320 B, APHA, 21ST EDITION
Total Alkalinity	mg/l as CaCO ₃	500	-	220	2320 B, APHA, 21ST EDITION
Carbonate Alkalinity	mg/l as CaCO ₃	-	-	Nil	2320 B, APHA, 21ST EDITION
Non-carbonate Alkalinity	mg/l as CaCO ₃	-	-	220	2320 B, APHA, 21ST EDITION
Phosphate	mg/l as P	-	-	0.06	4500-P C, APHA, 21ST EDITION
Nitrate	mg/l as NO ₃ ⁻	50	50	0.02	4500-NO ₃ - B, APHA, 21ST EDITION
Nitrite	mg/l as NO ₂ ⁻	3	-	<0.02	4500-NO ₂ - B, APHA, 21ST EDITION
Sulfate	mg/l as SO ₄ ²⁻	250	250	4.0	4500-SO ₄ APHA, 21ST EDITION
Chloride	mg/l as Cl	250	250	1.9	4500-Cl- B, APHA, 21ST EDITION
Silica	mg/l as Si	-	-	10.5	4500F- D, APHA, 21ST EDITION
Fluoride	mg/l as SiO ₂ ²⁻	1.5	0.5-1.5*	0.2	4500-SiO ₂ D, APHA, 21ST EDITION
Total Hardness	mg/l as CaCO ₃	500	500	228	2340 C, APHA, 21ST EDITION
Non Carbonate Hardness	mg/l as CaCO ₃	-	-	220	Calculation
Total Dissolved Solid	mg/l	1000	-	233	2340 C, APHA, 21ST EDITION
Langlier Saturation Index	-	-	-	-0.49	2330 B, APHA, 21ST EDITION
BIOLOGICAL					
Total Coliform	CFU/100 ml	Nil	Nil	Nil	9222 B, APHA, 21ST EDITION
Fecal Coliform	CFU/100 ml	Nil	Nil	Nil	9222 D, APHA, 21ST EDITION

APHA: American Public Health Association, Standard Methods for the Examination of Water Waste Water, WHO GV: World Health Organization Guideline Value, 2006 Update, NDWQS: National Drinking Water Quality Standard, 2062 (Nepal), * These values show lower and upper limits, () Values in the parenthesis refers the acceptable values only when alternative is not available. **Not accredited Test Method

Comment: *All the tested parameters are within NDWQS guideline value*

Analyzed by

Checked by

Authorized Signature

Note: 1. The results apply only to the parameters tested of the samples provided to our laboratory or collected by us for analysis as specified. Enticement of the results is neither inferred nor applied.
 2. Any duplication of the report can not be used as evidence in the court of law and should not be used in any advertising media, without prior written permission from us.
 3. The total liability of our company lies on the problem related to the process of payment only.

**Annex - 3: Rapid Environment Assessment
(REA) Checklist**

ADB'S REA Checklist

Rapid Environmental Assessment (REA) Checklist

WATER SUPPLY

Instructions:

- This checklist is to be prepared to support the environmental classification of a project. It is to be attached to the environmental categorization form that is to be prepared and submitted to the Chief Compliance Officer of the Regional and Sustainable Development Department.
- This checklist is to be completed with the assistance of an Environment Specialist in a Regional Department.
- This checklist focuses on environmental issues and concerns. To ensure that social dimensions are adequately considered, refer also to ADB checklists and handbooks on (i) Involuntary resettlement, (ii) Indigenous peoples planning, (iii) Poverty reduction, (iv) Participation and (v) Gender and development.
- Answer the questions assuming the "without mitigation" case. The purpose is to identify potential impacts. Use the "remarks" section to discuss any anticipated mitigation measures.

Country/Project Title: Itahari Small Town Water Supply Rehabilitation Sub-Project, Sunsari

Sector Division: Water Supply

SCREENING QUESTIONS	Yes	No	REMARKS
A. Project Siting Is the project area...			
• Densely populated?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
• Heavy with development activities?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	Central hub on EW Highway connecting Biratnagar, Dharan, Kakadvittha and Western part of Nepal
• Adjacent to or within any environmentally sensitive areas?			
• Cultural heritage site	<input type="checkbox"/>	<input checked="" type="checkbox"/>	The subproject components are not within locations in or near sensitive and vulnerable ecosystems and protected areas.
• Protected area	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
• Wetland	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
• Mangrove	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
• Estuarine	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
• Buffer zone of protected area	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
• Special area for protecting biodiversity	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
• Bay	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
B. Potential Environmental Impacts Will the Project cause ...			
• Pollution of raw water supply from upstream wastewater discharge from communities, industries, agriculture, and soil erosion runoff?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	Deep boring (Ward no 2 and 5)
• Impairment of historical/cultural monuments/areas and loss/damage to these sites?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	Absence of historical monuments
• Hazard of land subsidence caused by excessive ground water pumping?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	Excessive pumping should be controlled
• Social conflicts arising from displacement of communities?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	Not anticipated. The proposed sites of the deep tube well and new overhead tank will not require acquisition of private land. There are no encroachers/squatters or residential/commercial structures

SCREENING QUESTIONS	Yes	No	REMARKS
			at the proposed sites where infrastructure is to be established.
<ul style="list-style-type: none"> Conflicts in abstraction of raw water for water supply with other beneficial water uses for surface and ground waters? 	<input type="checkbox"/>	<input checked="" type="checkbox"/>	Not anticipated. Water quantity is sufficient.
<ul style="list-style-type: none"> Unsatisfactory raw water supply (e.g. excessive pathogens or mineral constituents)? 	<input checked="" type="checkbox"/>	<input type="checkbox"/>	Arsenic problem occurs in the area, a health hazard
<ul style="list-style-type: none"> Delivery of unsafe water to distribution system? 	<input checked="" type="checkbox"/>	<input type="checkbox"/>	Can be mitigated
<ul style="list-style-type: none"> Inadequate protection of intake works or wells, leading to pollution of water supply? 	<input checked="" type="checkbox"/>	<input type="checkbox"/>	Can be mitigated
<ul style="list-style-type: none"> Over pumping of ground water, leading to salinization and ground subsidence? 	<input type="checkbox"/>	<input checked="" type="checkbox"/>	High cost involved in pumping will constrain over pumping. EMP recommends monitoring pumping & maintaining record to control pumping to design limit.
<ul style="list-style-type: none"> Excessive algal growth in storage reservoir? 	<input checked="" type="checkbox"/>	<input type="checkbox"/>	Treatment will come in existence
<ul style="list-style-type: none"> Increase in production of sewage beyond capabilities of community facilities? 	<input checked="" type="checkbox"/>	<input type="checkbox"/>	Can be mitigated
<ul style="list-style-type: none"> Inadequate disposal of sludge from water treatment plants? 	<input checked="" type="checkbox"/>	<input type="checkbox"/>	Can be mitigated
<ul style="list-style-type: none"> Inadequate buffer zone around pumping and treatment plants to alleviate noise and other possible nuisances and protect facilities? 	<input type="checkbox"/>	<input checked="" type="checkbox"/>	High cost involved in pumping will constrain over pumping. EMP recommends monitoring pumping & maintaining record to control pumping to design limit.
<ul style="list-style-type: none"> Impairments associated with transmission lines and access roads? 	<input checked="" type="checkbox"/>	<input type="checkbox"/>	Minor and temporary impact
<ul style="list-style-type: none"> Health hazards arising from inadequate design of facilities for receiving, storing, and handling of chlorine and other hazardous chemicals. 	<input checked="" type="checkbox"/>	<input type="checkbox"/>	To be consider in design stage
<ul style="list-style-type: none"> Health and safety hazards to workers from the management of chlorine used for disinfection and other contaminants? 	<input checked="" type="checkbox"/>	<input type="checkbox"/>	Training for operator to be provided
<ul style="list-style-type: none"> Dislocation or involuntary resettlement of people 	<input type="checkbox"/>	<input checked="" type="checkbox"/>	Not anticipated
<ul style="list-style-type: none"> Social conflicts between construction workers from other areas and community workers? 	<input checked="" type="checkbox"/>	<input type="checkbox"/>	Minor and temporary impact
<ul style="list-style-type: none"> Noise and dust from construction activities? 	<input checked="" type="checkbox"/>	<input type="checkbox"/>	Minor and temporary impact
<ul style="list-style-type: none"> Increased road traffic due to interference of construction activities? 	<input checked="" type="checkbox"/>	<input type="checkbox"/>	Minor and temporary impact
<ul style="list-style-type: none"> Continuing soil erosion/silt runoff from construction operations? 	<input checked="" type="checkbox"/>	<input type="checkbox"/>	Minor and temporary impact
<ul style="list-style-type: none"> Delivery of unsafe water due to poor O&M treatment processes (especially mud accumulations in filters) and inadequate chlorination due to lack of adequate monitoring of chlorine residuals in distribution systems? 	<input checked="" type="checkbox"/>	<input type="checkbox"/>	Training for operator to be provided
<ul style="list-style-type: none"> Delivery of water to distribution system, which is corrosive due to inadequate attention to feeding of corrective chemicals? 	<input type="checkbox"/>	<input checked="" type="checkbox"/>	Concern for corrosion of G.I. pipes caused by the chlorine content in treated water is low. EMP provides mitigation measures.
<ul style="list-style-type: none"> Accidental leakage of chlorine gas? 	<input type="checkbox"/>	<input checked="" type="checkbox"/>	Bleaching power is used in Nepal
<ul style="list-style-type: none"> Excessive abstraction of water affecting downstream water users? 	<input type="checkbox"/>	<input checked="" type="checkbox"/>	Not applicable

SCREENING QUESTIONS	Yes	No	REMARKS
• Competing uses of water?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	Not applicable
• Increased sewage flow due to increased water supply	<input checked="" type="checkbox"/>	<input type="checkbox"/>	Frequency of septage pumping to be increased; regular testing of ground water for microbiological pollution
• Increased volume of sullage (wastewater from cooking and washing) and sludge from wastewater treatment plant	<input checked="" type="checkbox"/>	<input type="checkbox"/>	Can be mitigated and improved
• Large population influx during project construction and operation that causes increased burden on social infrastructure and services (such as water supply and sanitation systems)?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	Its small project, so limited number of worker will increase, and can be managed
• Social conflicts if workers from other regions or countries are hired?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	Priority in employment will be given to local residents.
• Risks to community health and safety due to the transport, storage, and use and/or disposal of materials such as explosives, fuel and other chemicals during operation and construction?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	Minor and temporary impact
• Community safety risks due to both accidental and natural hazards, especially where the structural elements or components of the project are accessible to members of the affected community or where their failure could result in injury to the community throughout project construction, operation and decommissioning?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	Minor and temporary impact
Sanitation			
C. Potential environmental impacts			
Will the project cause...			
• Impairment of historical/cultural monuments/areas and loss/damage to these sites?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	No such areas near the subproject sites.
• Interference with other utilities and blocking of access to buildings; nuisance to neighboring areas due to noise, smell, and influx of insects, rodents, etc.?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	Minor and temporary impact
• Dislocation or involuntary resettlement of people?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	Not applicable
• Disproportionate impacts on the poor, women and children, indigenous peoples or other vulnerable groups?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	Not applicable
• Impairment of downstream water quality due to inadequate Sewage treatment or release of untreated sewage?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	Toilets will be connected to septic tanks that will be designed to achieve maximum retention.
• Overflows and flooding of neighboring properties with raw sewage?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	Not applicable
• Environmental pollution due to inadequate sludge disposal or industrial waste discharges illegally disposed in sewers?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	Minor and temporary impact
• Noise and vibration due to blasting and other civil works?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	Minor and temporary impact
• Risks and vulnerabilities related to occupational health and safety due to physical, chemical, and biological hazards during project construction and operation?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	Minor and temporary impact
• Discharge of hazardous materials into sewers, resulting in damage to sewer system and danger to workers?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	Minor and temporary impact
• Inadequate buffer zone around pumping and treatment plants to alleviate noise and other possible	<input type="checkbox"/>	<input checked="" type="checkbox"/>	Minor and temporary impact

SCREENING QUESTIONS	Yes	No	REMARKS
nuisances, and protect facilities?			
• Road blocking and temporary flooding due to land excavation during the rainy season?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	Not applicable as construction work will be done during off rainy seasons
• Noise and dust from construction activities?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	Minor and temporary impact
• Traffic disturbances due to construction material transport and wastes?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	Minor and temporary impact
• Temporary silt runoff due to construction?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	Not applicable
• Hazards to public health due to overflow flooding, and groundwater pollution due to failure of sewerage system?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	Minor and temporary impact
• Deterioration of water quality due to inadequate sludge disposal or direct discharge of untreated sewage water?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	Not applicable
• Contamination of surface and ground waters due to sludge disposal on land?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	Not applicable
• Health and safety hazards to workers from toxic gases and hazardous materials which may be contained in confined areas, sewage flow and exposure to pathogens in untreated sewage and unsterilized sludge?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	Not applicable
• Large population increase during project construction and operation that causes increased burden on social infrastructure (such as sanitation system)?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	Not applicable
• Social conflicts between construction workers from other areas and community workers?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	Priority in employment will be given to local residents.
• Risks to community health and safety due to the transport, storage, and use and/or disposal of materials such as explosives, fuel and other chemicals during construction and operation?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	Not applicable.
• Community safety risks due to both accidental and natural hazards, especially where the structural elements or components of the project are accessible to members of the affected community or where their failure could result in injury to the community throughout project construction, operation and decommissioning?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	Minor and temporary impact

English Translation of Minute of Meeting - Phase II

Itahari Small Town Water Supply Sanitation and User's Committee organized a public hearing workshop on 2072/6/5. Participation were made from all concerned stakeholders. After discussion in the public hearing it was observed that there will be no negative impacts on the environment, no necessity of land acquisition and no need of resettlement while implementing the proposed "Enhance Functionality" in Small Town Water Supply and Sanitation Sector Project. As such it was decided to inform this conclusion to the concerned authorities.

Phase 1

आइस आर ०८१/२१२६ को DCO/SIT/काठमाडौं
 UNAC Joint venture को सम्वन्धमा २०१८
 २१११ २१११ २०११११ २०११११ २०११११
 कायानुसार (Enhancement project) को प्रारम्भिक
 पुरवठा (Interim Report) तथा को
 विभिन्न विवरण कायानुसार प्रस्ताव तथा अनुमानित
 पत्राचारको लागि सम्बन्धित विभाग तथा सम्बन्धित
 अधिकारीको माध्यमबाट उपलब्ध गराइने गरिनेछ।

- १) हरि कुमार कोशी Team Leader काठमाडौं
- २) सहाय कुमाल (कृष्ण) Water supply काठमाडौं
- ३) राम कुमार कोशी (कृष्ण) काठमाडौं
- ४) एच.के. कोशी काठमाडौं

सम्बन्धित विवरण :

२०११ २१११ २०११ २०११ २०११ २०११
 कायानुसार कायानुसार विवरण प्रस्ताव तथा अनुमानित पत्राचारको
 लागि प्राप्त तथा प्राप्त गरीने विवरण सम्वन्धित विभाग
 मा उपलब्ध गराइने तथा सम्बन्धित विभागको माध्यमबाट
 उपलब्ध गराइनेछ।

- १) काठमाडौं को नयाँ प्लांट माथिल्लो पत्राचारको लागि
 र DMA Concept अन्तर्गत विवरण प्राप्त गर्ने।
- २) २०११ overhead tank माथिल्लो पत्राचारको लागि
 १/११११ Dip-well boring अन्तर्गत विवरण प्राप्त गर्ने।
 अन्तर्गत विवरण प्राप्त गर्ने।
 (Filtration) अन्तर्गत pressure filter
 विवरण प्राप्त गर्ने।
- ३) Lab-house with instrument अन्तर्गत
 विवरण प्राप्त गर्ने।
- ४) Existing project अन्तर्गत विवरण प्राप्त गर्ने।
 पत्राचारको लागि pipeline अन्तर्गत विवरण प्राप्त गर्ने।

[Handwritten signature]

mobile & sound-less) - 9, 2 2 धान
sound polluted generation (D.G. set) परितंत्र
गण्डे soundless - D.G. set - 2 धान) मरिवा
गण्डे पर.

2 धान 900 K.V.A. (-2 धान) (2 धान) (2 धान)
अवस्था (अवस्था) अवस्था (अवस्था)
O.H.T. पिस्तल गण्डे पर. - 2 धान
flow meter गण्डे पर.

कमरे (कमरे) (कमरे) (कमरे) (कमरे)
प्रदान गण्डे पर (प्रदान) (प्रदान) (प्रदान)

पाइप लाइन्स (पाइप लाइन्स) (पाइप लाइन्स)
कॉन्सिडर (कॉन्सिडर) (कॉन्सिडर) (कॉन्सिडर)

20. धान 9500 (धान) 2000 (धान) (धान) (धान)
WATT (धान) (धान) (धान) (धान)
नया (धान) (धान) (धान) (धान)
राज्य (धान) (धान) (धान) (धान)

कॉन्सिडर (कॉन्सिडर) (कॉन्सिडर) (कॉन्सिडर)
अवस्था (अवस्था) (अवस्था) (अवस्था)
O.H.T. (O.H.T.) (O.H.T.) (O.H.T.)
pressure (pressure) (pressure) (pressure)
Deep Well (Deep Well) (Deep Well) (Deep Well)
N.R.W. (N.R.W.) (N.R.W.) (N.R.W.)
अवस्था (अवस्था) (अवस्था) (अवस्था)
अवस्था (अवस्था) (अवस्था) (अवस्था)

[Handwritten signature]

Phase 2

आज मिति २०७२ साल आश्विन ५ गते मंगलबार दोश्रो साना शहरी खानेपानी तथा सरसफाई आयोजना आयोजना व्यवस्थापन कार्यालयको आयोजना र इटहरी साना शहरी खानेपानी तथा सरसफाई उपभोक्ता संस्थाको व्यवस्थापनमा आयोजना गरिएको इटहरीमा हालै चालु हुन लागेको खानेपानी क्षमता अभिवृद्धि कार्यक्रम (Enhance Functionality in Small Town Water Supply and Sanitation Sector Project) कार्यान्वयन गर्दा वातावरणमा पार्ने प्रभाव मूल्याङ्कनको बारेमा सरोकारवालाहरूसँग सार्वजनिक सुनुवाई कार्यक्रमको उपस्थिति विवरण ।

उपस्थिति

क्र.सं.	नाम, थर	ठेगाना	हस्ताक्षर
१.	दि. दे. मा. बान्नालोक, इटहरी		
२.	राजु चौधरी	इटहरी - ५	
३.	शुभ थापा	इटहरी - १	
(४)	श्याम शर्मा	इटहरी - २	
५.	गंगा शर्मा	इटहरी - ५	
६.	बेसाव बस्नेत	इटहरी - ६	
७.	बमशु लाम	इटहरी - ५	
८.	लाल ब. मरे	इटहरी - ३	
९.	नारायण खत्री	इटहरी - १	
१०.	रवि शर्मा	इटहरी - ४	
११.	कुशी शर्मा	इटहरी - ५	
१२.	सुभा शर्मा	इटहरी - १	
१३.	विद्या कुशी चौधरी	इटहरी - ५	
१४.	विद्या दे. शर्मा	इटहरी - २	
१५.	रा. शर्मा	इटहरी - १५	
१६.	सुमानन्द शर्मा	इटहरी - ४	
१७.	सुभा शर्मा	इटहरी - १	
१८.	सुभा शर्मा	इटहरी - १	
१९.	सुभा शर्मा	इटहरी - १	
२०.	सुभा शर्मा	इटहरी - ५	
२१.	सुभा शर्मा	इटहरी - ५	
२२.	महेश कुमार खिमरे	इटहरी - ८	
२३.	श्री वन्तमाझ	इटहरी - ८	

क्र.सं.	नाम, थर	ठेगाना	हस्ताक्षर
२४	विमला कार्की	इरहरी ८	विमला
२५	लक्ष्मी प्रो शापकोटा	इरहरी ४	लक्ष्मी
२६	विमला कार्की	इरहरी - ६	विमला कार्की
२६	कृष्ण कुमारी कुमारी	इरहरी - ९	कृष्ण
२८	जिज्ञा चौधरी	इरहरी - ६	जिज्ञा चौधरी
२९	कमला निरौला	॥ - १	कमला
३०	शौभा कार्की	॥ - ४	शौभा
३१	अर्पिता थापा मगर		अर्पिता
३२	केल व. थारा	इरहरी - २	केल व. थारा
३३	नेरु कुमारी	इरहरी - २२	नेरु
३४	शान्ति प्रो ओमा	इरहरी - १६	शान्ति
३५	रमेश कुमारी विष्ट	इरहरी - ४	रमेश
३६	सुजाता कार्की	॥ २६	सुजाता
३८	पवन वेहाडा राई	॥ ६	पवन
३९	लक्ष्मी प्रकाश जोष	॥ ९	लक्ष्मी
३९	श्यामला कुमारी	॥ - ९	श्यामला
४०	केल व. मगर	इरहरी ९	केल
४१	पाम व. राई	॥ - ११ - २६	पाम
४२	रमेश थापा	इरहरी शान्ति कार्की	रमेश
४३	अर्पिता कुमारी कार्की	इरहरी शान्ति कार्की	अर्पिता
४४	माला कुमारी	इरहरी - ९	माला
४५	लक्ष्मी कार्की चौधरी	इरहरी शान्ति कार्की	लक्ष्मी
४६	वारा कुमारी थापा	इरहरी - २२	वारा
४६	पुष्पा कुमारी	इरहरी - ४	पुष्पा
४८	हरि व. कटवाल	इ.स.स. कुमारी	हरि
४९	राजु कुमारी	॥	राजु
५०	उमेश चौधरी	॥	उमेश
५१	गुणवती कुमारी चौधरी	॥	गुणवती
५२	विमला कार्की	इरहरी २	विमला

निर्णय पत्र

१) इन्हें भी संचालन के लिए कर्मचारी (मिस्ट्री) की संख्या
 आभाजन/ संयोजन (1950/1) वाले प्रभाग/प्रकार/
 इन्हें सार्वजनिक/स्वयंसेवा/ तथा संचालन/...
 उपभोग/संस्था/संयोजन/...
 तथा...
 पत्र कायम/...
 आवक/...
 दिनांक/...)

२) श्री. सुवर्णानंद सुवर्णानंद (संचालन के लिए) - 1/3/5
 (1950/1) स्वयंसेवा/...
 (Enhance functionality in small town water supply
 and Sanitation sector project) संयोजन/...
 1950/1...
 अनुसंधान/...
 दिनांक/...)

(Handwritten signatures and scribbles)

Signature 1: [Illegible]

Signature 2: [Illegible]

Signature 3: [Illegible]

Signature 4: [Illegible]

Signature 5: [Illegible]

Signature 6: [Illegible]

Signature 7: [Illegible]

Signature 8: [Illegible]

Signature 9: [Illegible]

Signature 10: [Illegible]

Signature 11: [Illegible]

Signature 12: [Illegible]

Signature 13: [Illegible]

Signature 14: [Illegible]

Signature 15: [Illegible]

Signature 16: [Illegible]

Signature 17: [Illegible]

Signature 18: [Illegible]

Signature 19: [Illegible]

Signature 20: [Illegible]

Signature 21: [Illegible]

Signature 22: [Illegible]

Signature 23: [Illegible]

Signature 24: [Illegible]

Signature 25: [Illegible]

Signature 26: [Illegible]

Signature 27: [Illegible]

Signature 28: [Illegible]

Signature 29: [Illegible]

Signature 30: [Illegible]

Signature 31: [Illegible]

Signature 32: [Illegible]

Signature 33: [Illegible]

Signature 34: [Illegible]

Signature 35: [Illegible]

Signature 36: [Illegible]

Signature 37: [Illegible]

Signature 38: [Illegible]

Signature 39: [Illegible]

Signature 40: [Illegible]

Signature 41: [Illegible]

Signature 42: [Illegible]

Signature 43: [Illegible]

Signature 44: [Illegible]

Signature 45: [Illegible]

Signature 46: [Illegible]

Signature 47: [Illegible]

Signature 48: [Illegible]

Signature 49: [Illegible]

Signature 50: [Illegible]

Project Photographs

Photos on Public Gathering Meeting on Environmental and Social Issues

ITAHARI



Photo No. 1



Photo No. 2



Photo No. 3



Photo No. 4
