



## China Contaminated Site Management Project (P145533)

EAST ASIA AND PACIFIC | China | Environment & Natural Resources Global Practice |  
Global Environment Project | Investment Project Financing | FY 2015 | Seq No: 1 | ARCHIVED on 27-Aug-2015 | ISR20480 |

Implementing Agencies: Foreign Economic Cooperation Office of Ministry of Environmental Protection

### Key Dates

#### Key Project Dates

Board Approval date:30-Apr-2015

Effectiveness Date:--

Planned Mid Term Review Date:31-Dec-2018

Actual Mid-Term Review Date:--

Original Closing Date:31-Dec-2021

Revised Closing Date:31-Dec-2021

### Global Environmental Objectives

Global Environmental Objective (from Project Appraisal Document)

The project development objective is to improve the country's capacity for managing site contamination, and demonstrate environmentally sound identification and cleanup of sites contaminated with POPs and other hazardous chemicals.

Has the Global Environmental Objective been changed since Board Approval of the Project Objective?

No

### Components

Name
Component 1: Capacity Development for Prevention and Control of Site Contamination:(Cost \$22.14 M)
Component 2: Cleanup Demonstrations of Sites Contaminated with POPs and Other Hazardous Chemicals:(Cost \$49.70 M)
Component 3: Project Management:(Cost \$3.16 M)

### Overall Ratings

Name	Previous Rating	Current Rating
Progress towards achievement of GEO	--	● Satisfactory
Overall Implementation Progress (IP)	--	● Satisfactory
Overall Risk Rating	--	● Substantial

### Implementation Status and Key Decisions



The project was only recently approved and has not yet become effective. The project launch workshop is scheduled in September 2015.

## Risks

### Systematic Operations Risk-rating Tool

Risk Category	Rating at Approval	Previous Rating	Current Rating
Political and Governance	● Moderate	--	● Moderate
Macroeconomic	● Low	--	● Low
Sector Strategies and Policies	● Moderate	--	● Moderate
Technical Design of Project or Program	● Moderate	--	● Moderate
Institutional Capacity for Implementation and Sustainability	● Substantial	--	● Substantial
Fiduciary	● Moderate	--	● Moderate
Environment and Social	● Substantial	--	● Substantial
Stakeholders	● Substantial	--	● Substantial
Other	--	--	--
Overall	● Substantial	--	● Substantial

## Results

### Global Environmental Objective Indicators



► 1. Selected priority technical guidelines (TG) and policy recommendations (PRs) for prevention and control of site contamination at the national and local levels developed or issued (Text, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	Existing TG for site cleanup (control of site contamination) at the national and local levels (see Annex 2)	--	TORs under preparation.	TG and PRs for prevention and control of site contamination at the national level and in Chongqing and Liaoning developed or issued
Date	01-Jan-2015	--	31-Jul-2015	31-Dec-2021

Comments

TORs for development of technical guidelines and policy recommendations to be prepared and approved during the first year of implementation

► 2. Training materials published and on-line training courses integrated into MEP staff training system (Text, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	No training system for prevention and control of site contamination	--	TORs under preparation.	Training materials published and on-line training courses integrated into the existing staff training system of MEP
Date	01-Jan-2015	--	31-Jul-2015	31-Dec-2021

Comments

TORs for development of training materials to be prepared and approved during the first year of implementation.

► Contaminated land managed or dump sites closed under the project (Hectare (Ha), Core)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	--	0.00	5.20
Date	01-Jan-2015	--	31-Jul-2015	31-Dec-2018



► 4. National database of POPs contaminated sites established (Text, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	No database for contaminated sites	--	TOR under preparation.	The national database is operational
Date	01-Jan-2015	--	31-Jul-2015	31-Dec-2021

Comments

TORs for development of database to be prepared and approved during the first year of implementation

Overall Comments

**Intermediate Results Indicators**

► 5. Number of people trained on prevention and control of site contamination (Text, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0	--	No training conducted yet.	As per annual training plans
Date	31-Dec-2014	--	31-Jul-2015	31-Dec-2021

Comments

The training targets will be government officials and contaminated site cleanup practitioners. This indicator is measured by text (not number) because it was difficult to estimate the number of people to be trained.

► 6. Public Awareness activities implemented (Text, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0	--	No activities carried out yet.	Public awareness campaign successfully implemented
Date	31-Dec-2014	--	31-Jul-2015	31-Dec-2021



► 7. Feasibility Study for Knowledge and Remediation Center in Chongqing prepared (Text, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	No feasibility study	--	TORs under preparation.	Feasibility study completed
Date	01-Jan-2015	--	31-Jul-2015	31-Dec-2021

► 8. Regional Soil and Groundwater Contamination Prevention and Warning System at the Changshou Industrial Park established (Text, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	No warning system	--	TORs under preparation.	Warning system established and functional
Date	01-Jan-2015	--	31-Jul-2015	31-Dec-2021

► POPs&pops waste destroyed,disposed or contained in environmentally sound manner (Metric ton, Core)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	--	0.00	79000.00
Date	01-Jan-2015	--	31-Jul-2015	31-Dec-2021

► 10. Number of people positively affected by site cleanups (Text, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0	--	0	8100
Date	01-Jan-2015	--	31-Jul-2015	31-Dec-2021

Comments

People living near the contaminated sites and at the highest risk of exposure.



## ▲ - Of which female (Text, Custom Breakdown)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0	--	0	To be based on site investigation results
Date	01-Jan-2015	--	31-Jul-2015	31-Dec-2021

Overall Comments


**Data on Financial Performance****Disbursements (by loan)**

Project	Loan/Credit/TF	Status	Currency	Original	Revised	Cancelled	Disbursed	Undisbursed	Disbursed
P145533	TF-A0193	Not Effective	USD	15.00	15.00	0.00	0.00	15.00	0%

**Key Dates (by loan)**

Project	Loan/Credit/TF	Status	Approval Date	Signing Date	Effectiveness Date	Orig. Closing Date	Rev. Closing Date
P145533	TF-A0193	Not Effective	30-Apr-2015	24-Jun-2015	29-Jun-2015	31-Dec-2021	31-Dec-2021

**Cumulative Disbursements**

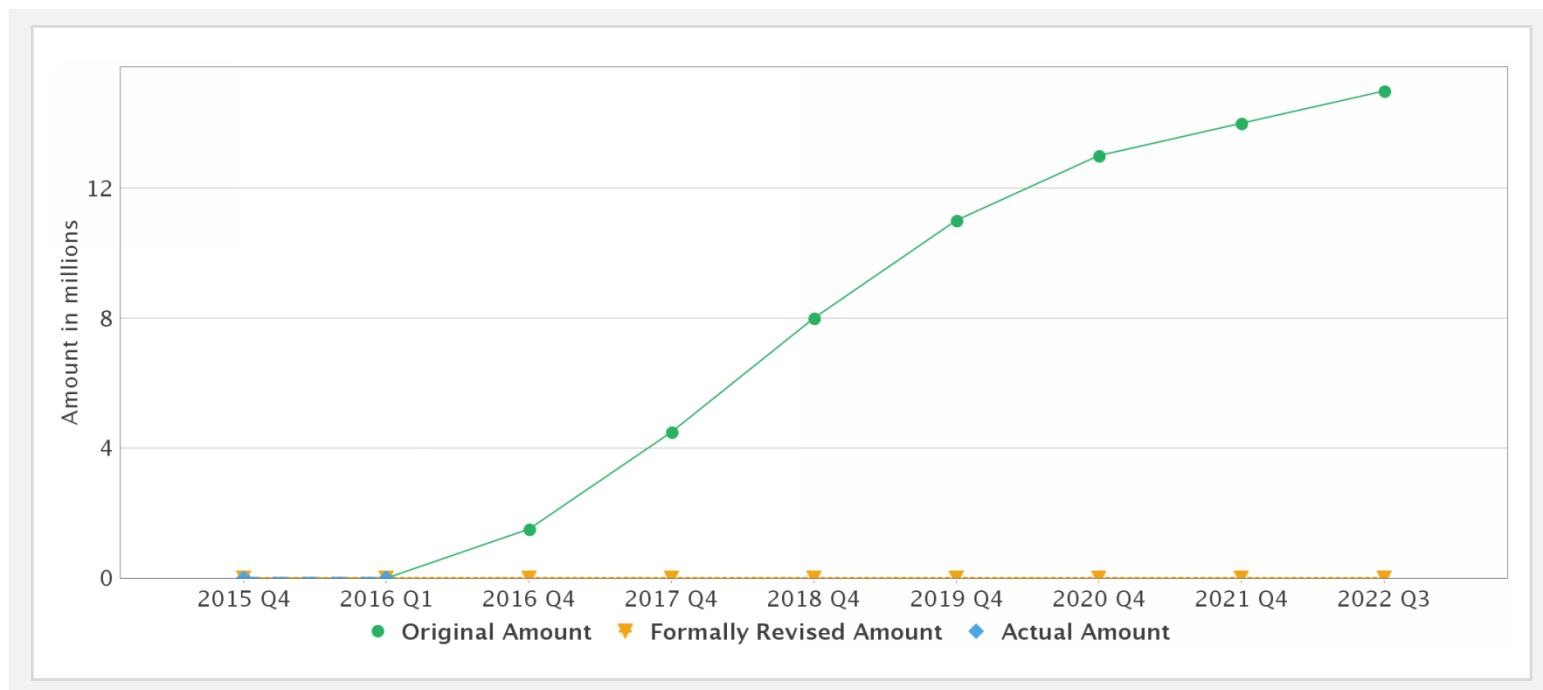

## Restructuring History

There has been no restructuring to date.

## Related Project(s)

There are no related projects.
