






















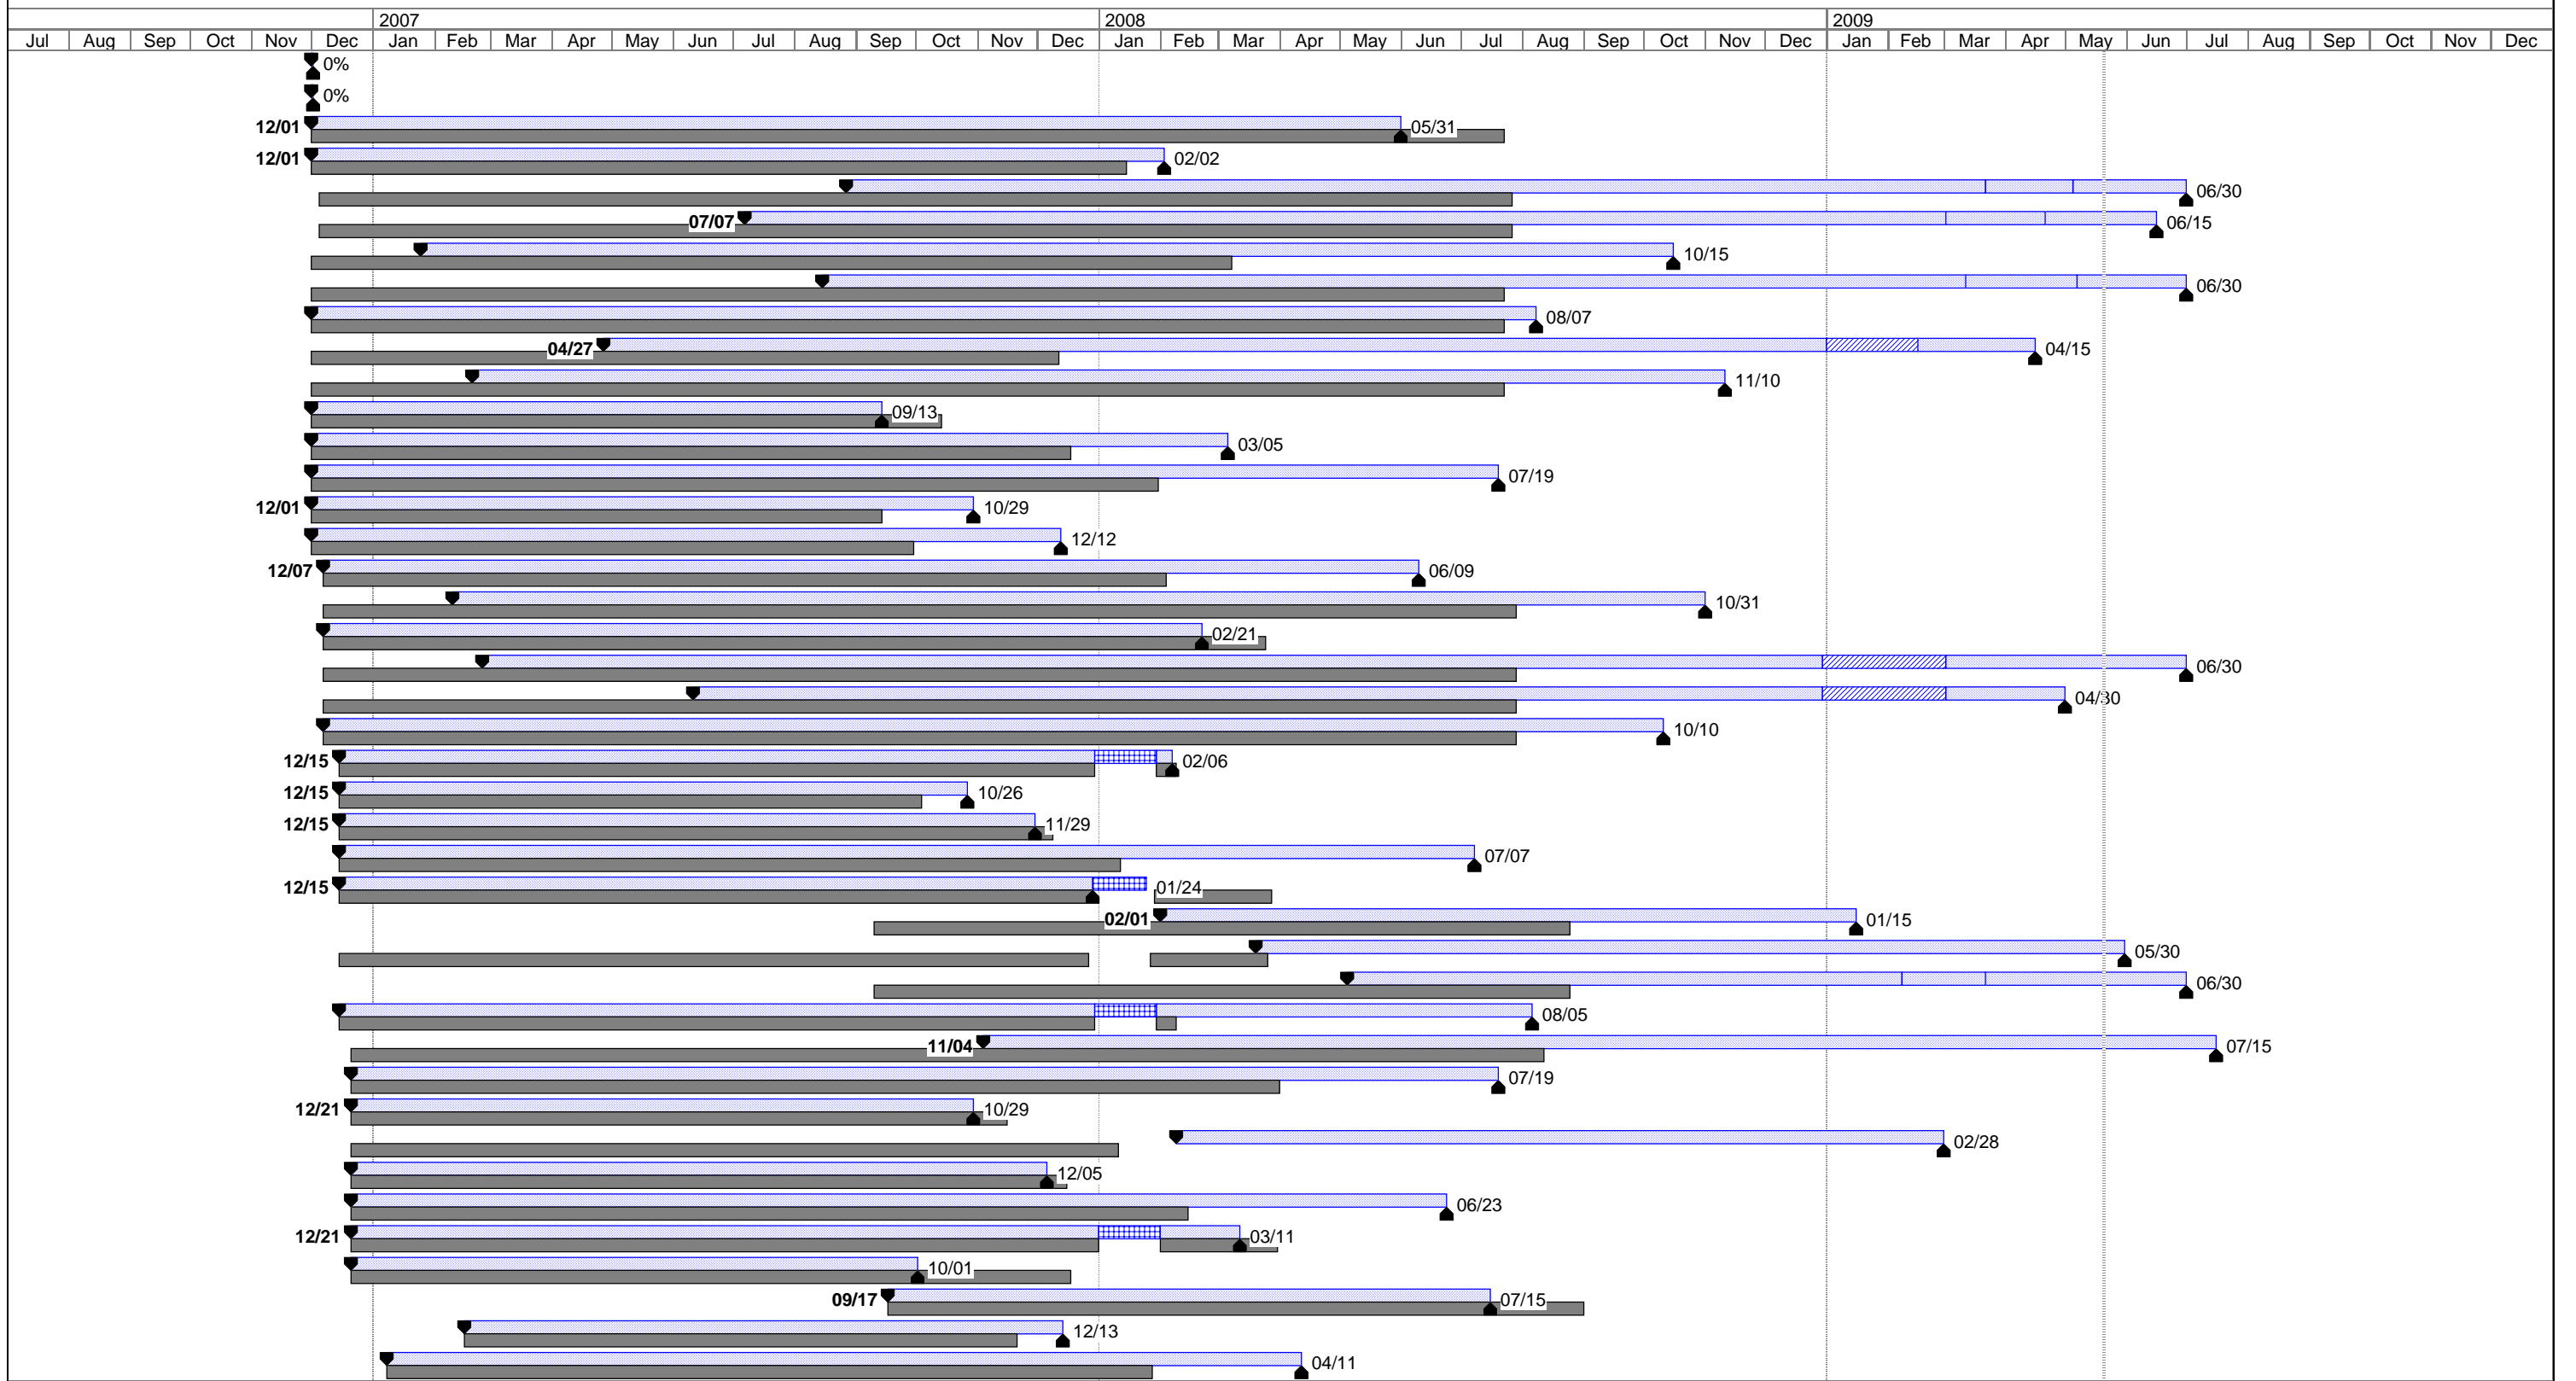
F.M.I.P. ADDITIONAL GRANT

ID	CAZA	ID PROJECT	MUNICIPALITY / VILLAGE	Bid Package Cost Estimate	Original Contract Amount \$	contract after variation order	REMARKS	Proc. Method	WB Review	Forecasted Proc. Duration	Actual Proc. Duration	Project Duration	% Work Complete	Start	Finish	2006					
																Jan	Feb	Mar	Apr	May	Jun
211	SOUR	SL/SO/33-G02	CHAMAA	\$13,926.00	\$0.00	\$0.00		NS	Post	150 days		30 days	0%	Mon 05/25/09	Fri 11/20/09						
212	BINT JBEIL	NA/BJ/17-G02	SAFAD EL BATIKH	\$12,608.00	\$0.00	\$0.00		NS	Post	150 days		30 days	0%	Tue 05/26/09	Sat 11/21/09						
213	MARJOYOUN	NA/MA/11-G02	KLAYAAT	\$38,626.67	\$0.00	\$0.00		NS	Post	150 days		60 days	0%	Tue 05/26/09	Mon 12/21/09						
214	NABATIEH	NA/NA/28-G02	ZAWTAR EL CHARKIEH	\$43,250.67	\$0.00	\$0.00		NS	Post	150 days		60 days	0%	Tue 05/26/09	Mon 12/21/09						
215	JEZZINE	SL/JE/21-G02	RIHAN	\$24,013.33	\$0.00	\$0.00		NS	Post	150 days		30 days	0%	Tue 05/26/09	Sat 11/21/09						
216	BENT JBEIL	NA/BJ/05-G02	BEIT LIF	\$196,696.67	\$0.00	\$0.00		NCB	Post	150 days		90 days	0%	Wed 05/20/09	Wed 12/30/09						
217	BENT JBEIL	NA/BJ/01-G02	AIN EBEL	\$29,704.67	\$0.00	\$0.00		NS	Post	150 days		60 days	0%	Wed 05/27/09	Tue 12/22/09						
218	SOUR	SL/SO/02-G02	AIN BAAL	\$17,524.66	\$0.00	\$0.00		NS	Post	150 days		30 days	0%	Wed 05/27/09	Sun 11/22/09						
219	SOUR	SL/SO/41-G02	BORGHLEH	\$59,533.33	\$0.00	\$0.00		NCB	Post	150 days		60 days	0%	Wed 05/27/09	Tue 12/22/09						
220	<b>TOTAL BATCH 3</b>			<b>\$539,738.66</b>	\$0.00	\$0.00				0 days		0 days	0%	Fri 12/01/06	Fri 12/01/06						

Project: Procurement Plan  
Updated: Wed 05/20/09

Critical		Milestone		External Milestone	
Critical Progress		Exp. Split in proj. exec. due to the winter Season		Deadline	
Task		Summary		Start of Bidding Procedures	
Task Progress		Project Summary		Expected end of Project Execution	
Baseline		External Tasks			


F.M.I.P. ADDITIONAL GRANT



Project: Procurement Plan  
Updated: Wed 05/20/09

Critical		Milestone		External Milestone	
Critical Progress		Exp. Split in proj. exec. due to the winter Season		Deadline	
Task		Summary		Start of Bidding Procedures	
Task Progress		Project Summary		Expected end of Project Execution	
Baseline		External Tasks			

F.M.I.P. ADDITIONAL GRANT

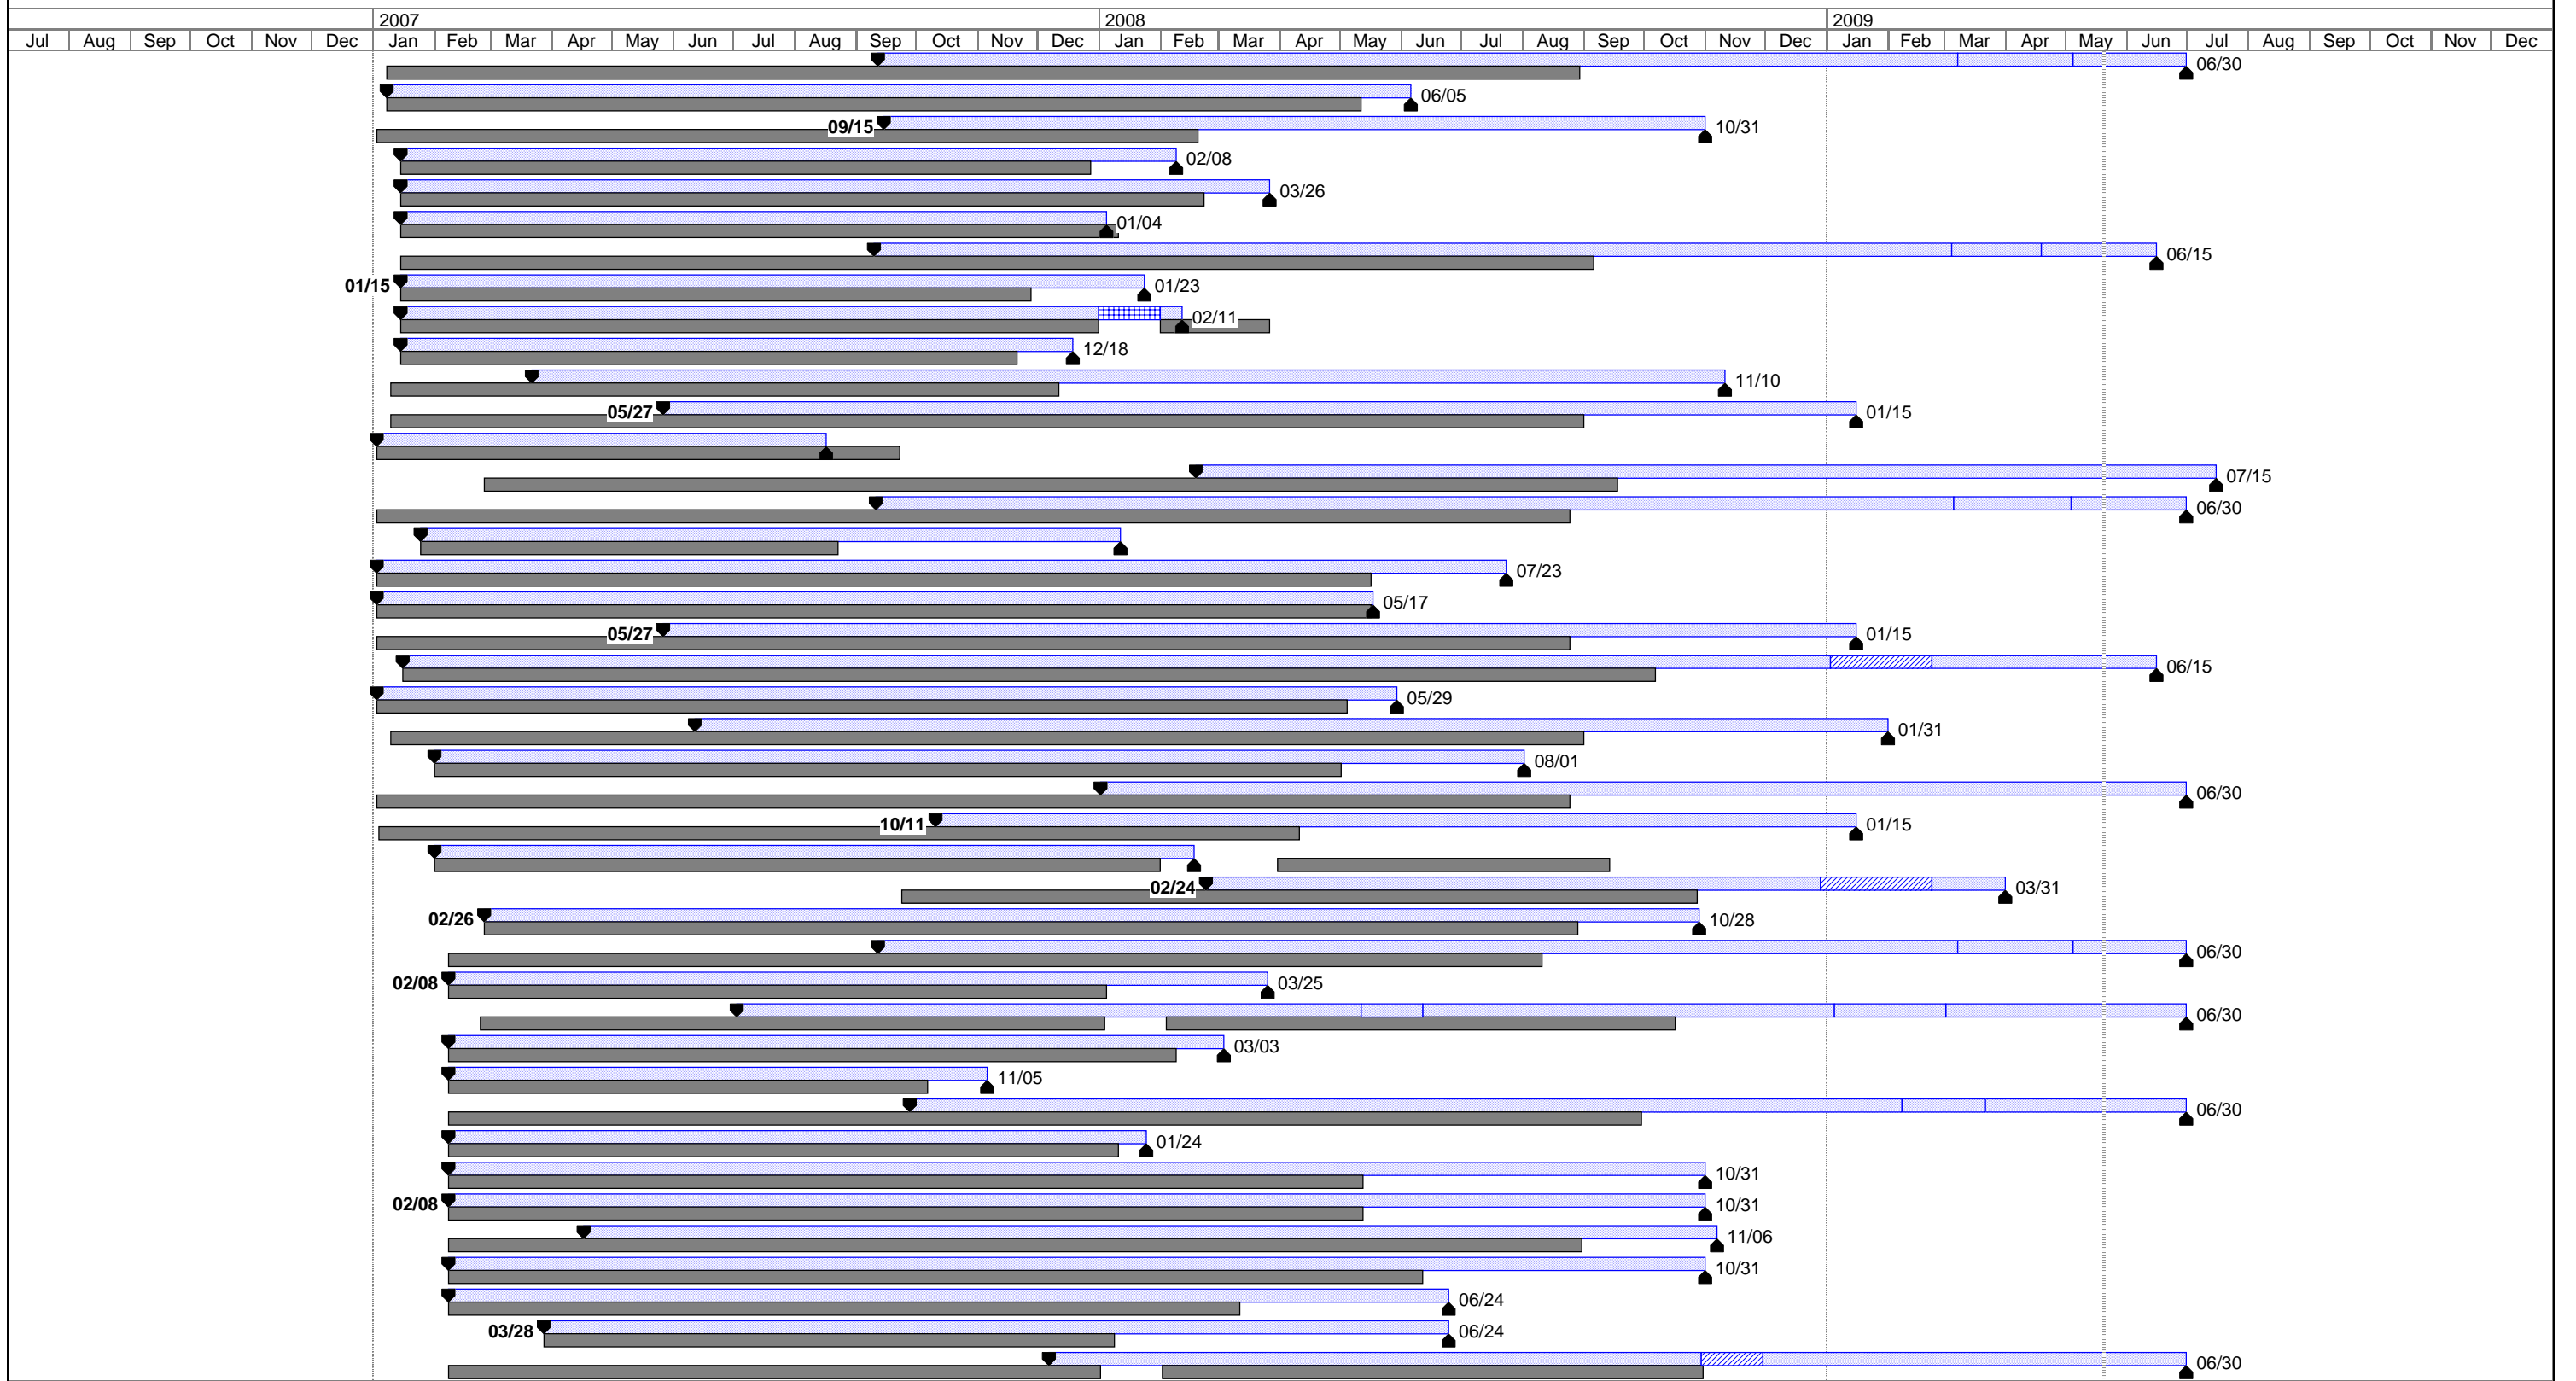


Project: Procurement Plan  
Updated: Wed 05/20/09

Critical		Milestone		External Milestone	
Critical Progress		Exp. Split in proj. exec. due to the winter Season		Deadline	
Task		Summary		Start of Bidding Procedures	
Task Progress		Project Summary		Expected end of Project Execution	
Baseline		External Tasks			




F.M.I.P. ADDITIONAL GRANT

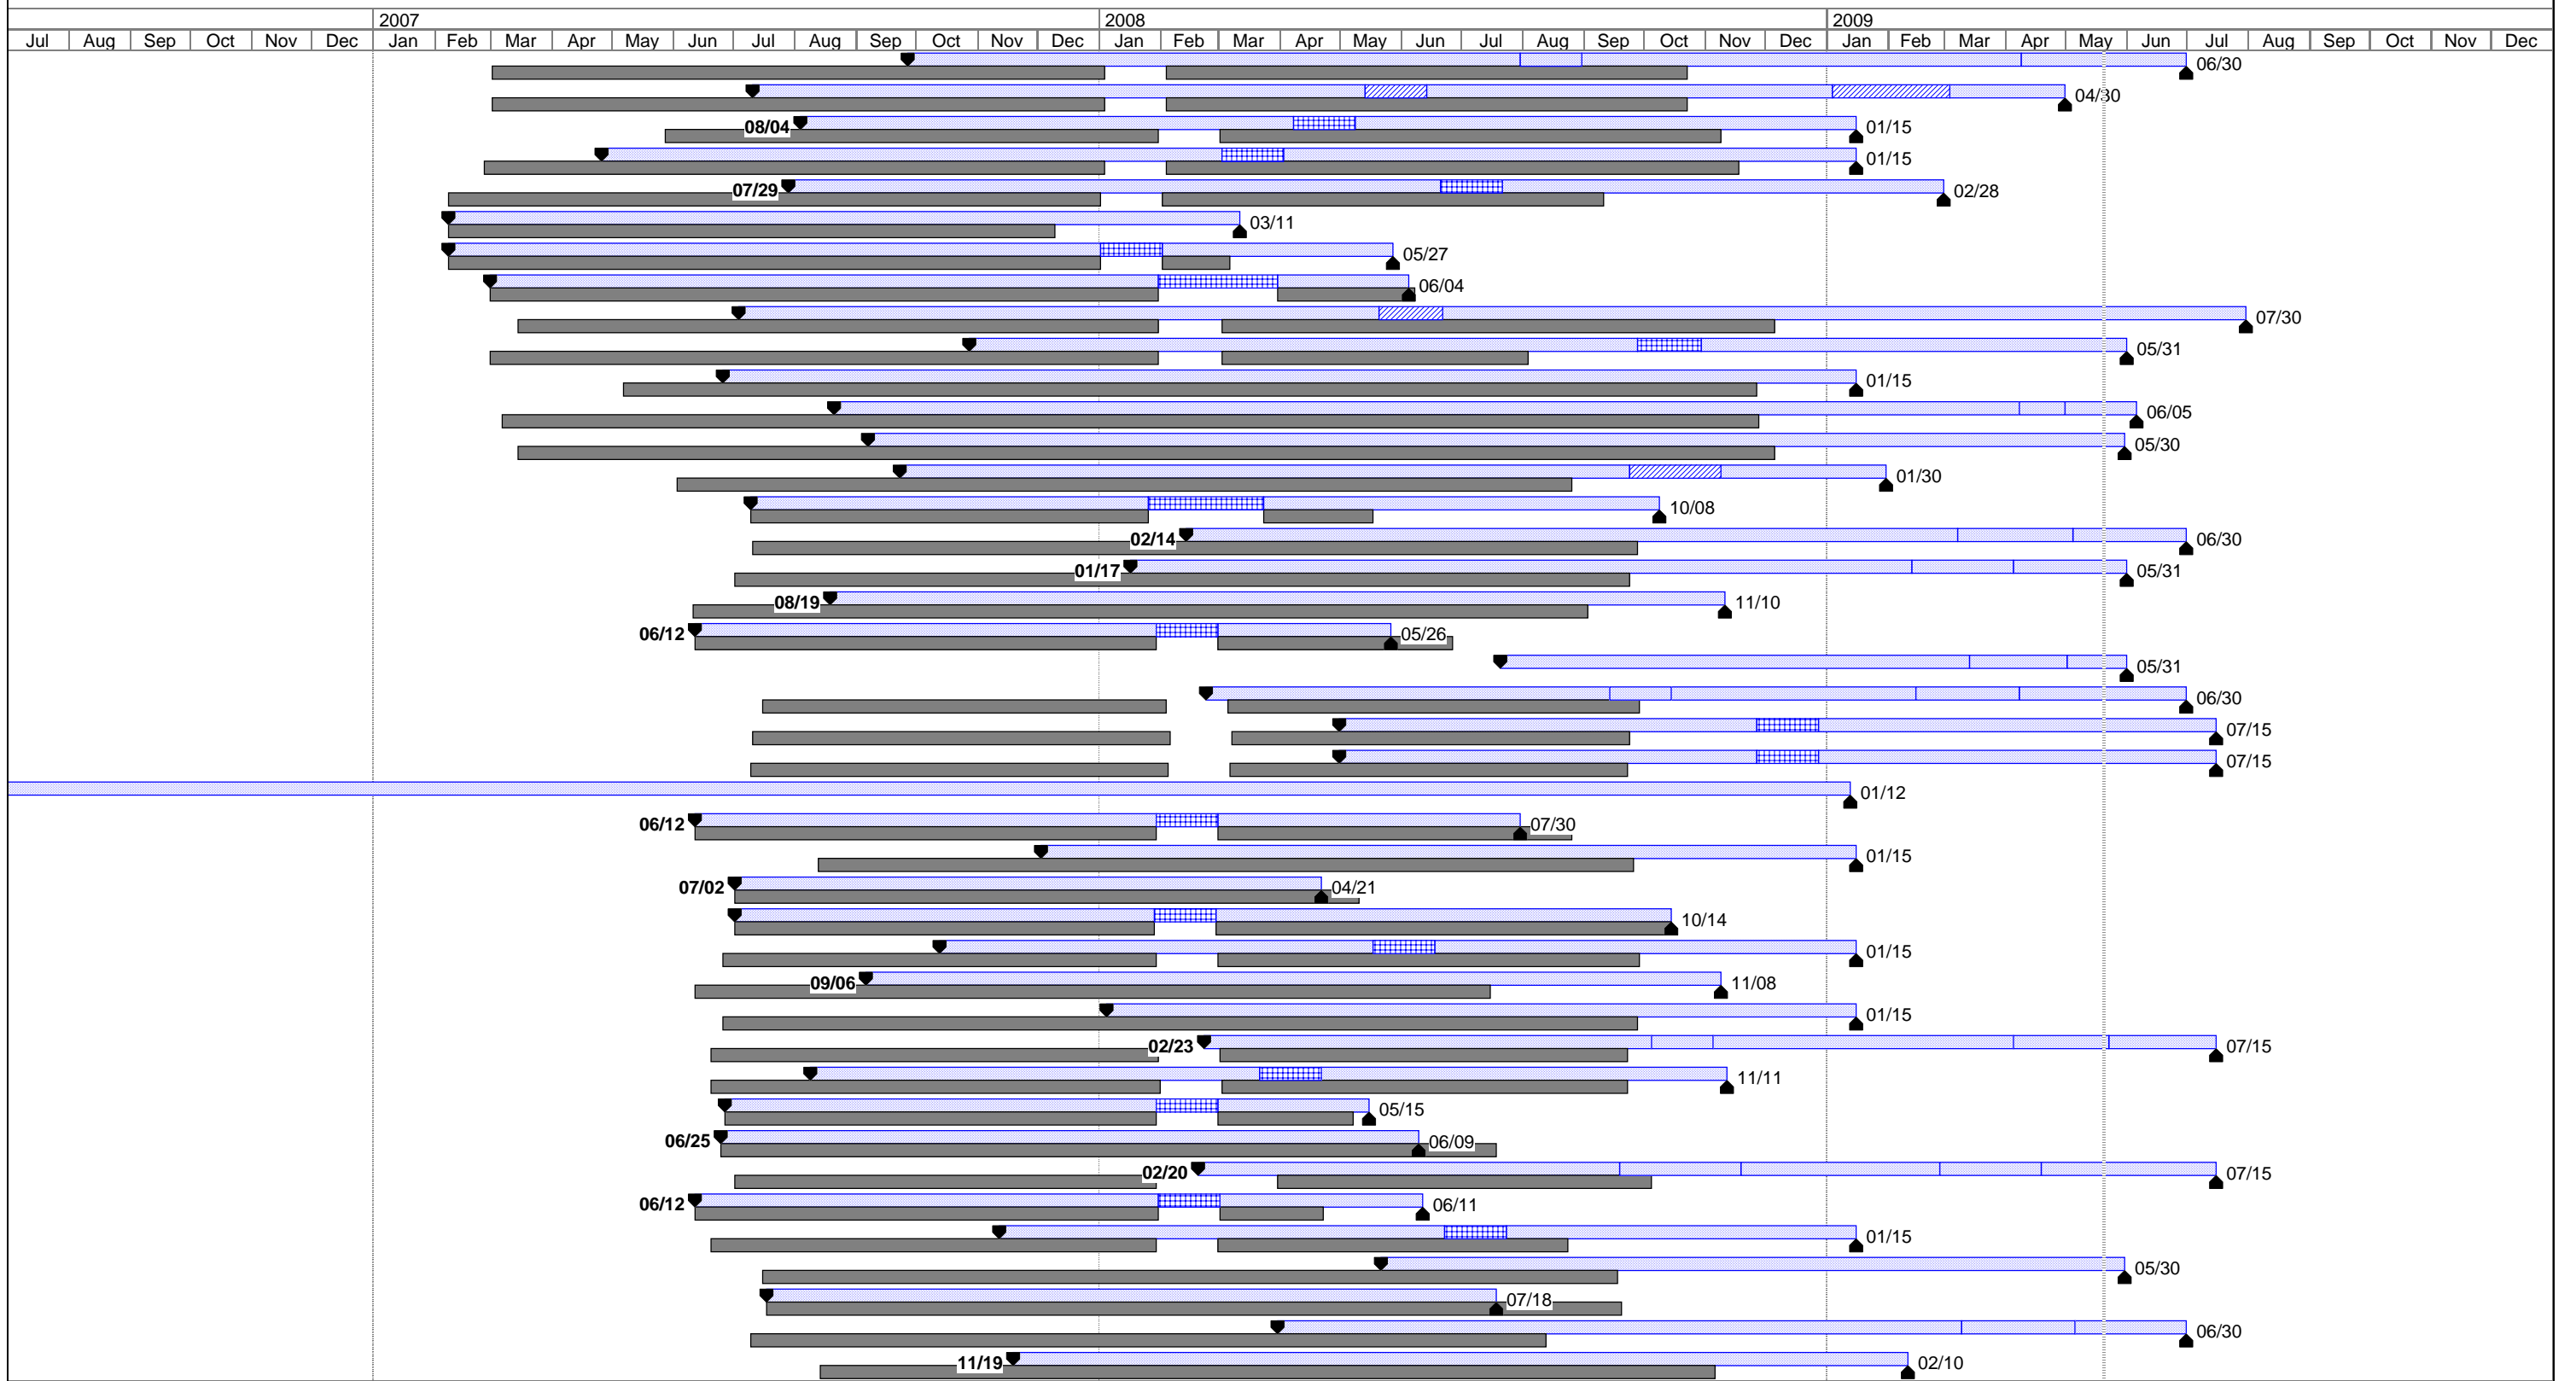

Project: Procurement Plan  
Updated: Wed 05/20/09

Critical		Milestone		External Milestone	
Critical Progress		Exp. Split in proj. exec. due to the winter Season		Deadline	
Task		Summary		Start of Bidding Procedures	
Task Progress		Project Summary		Expected end of Project Execution	
Baseline		External Tasks			


F.M.I.P. ADDITIONAL GRANT

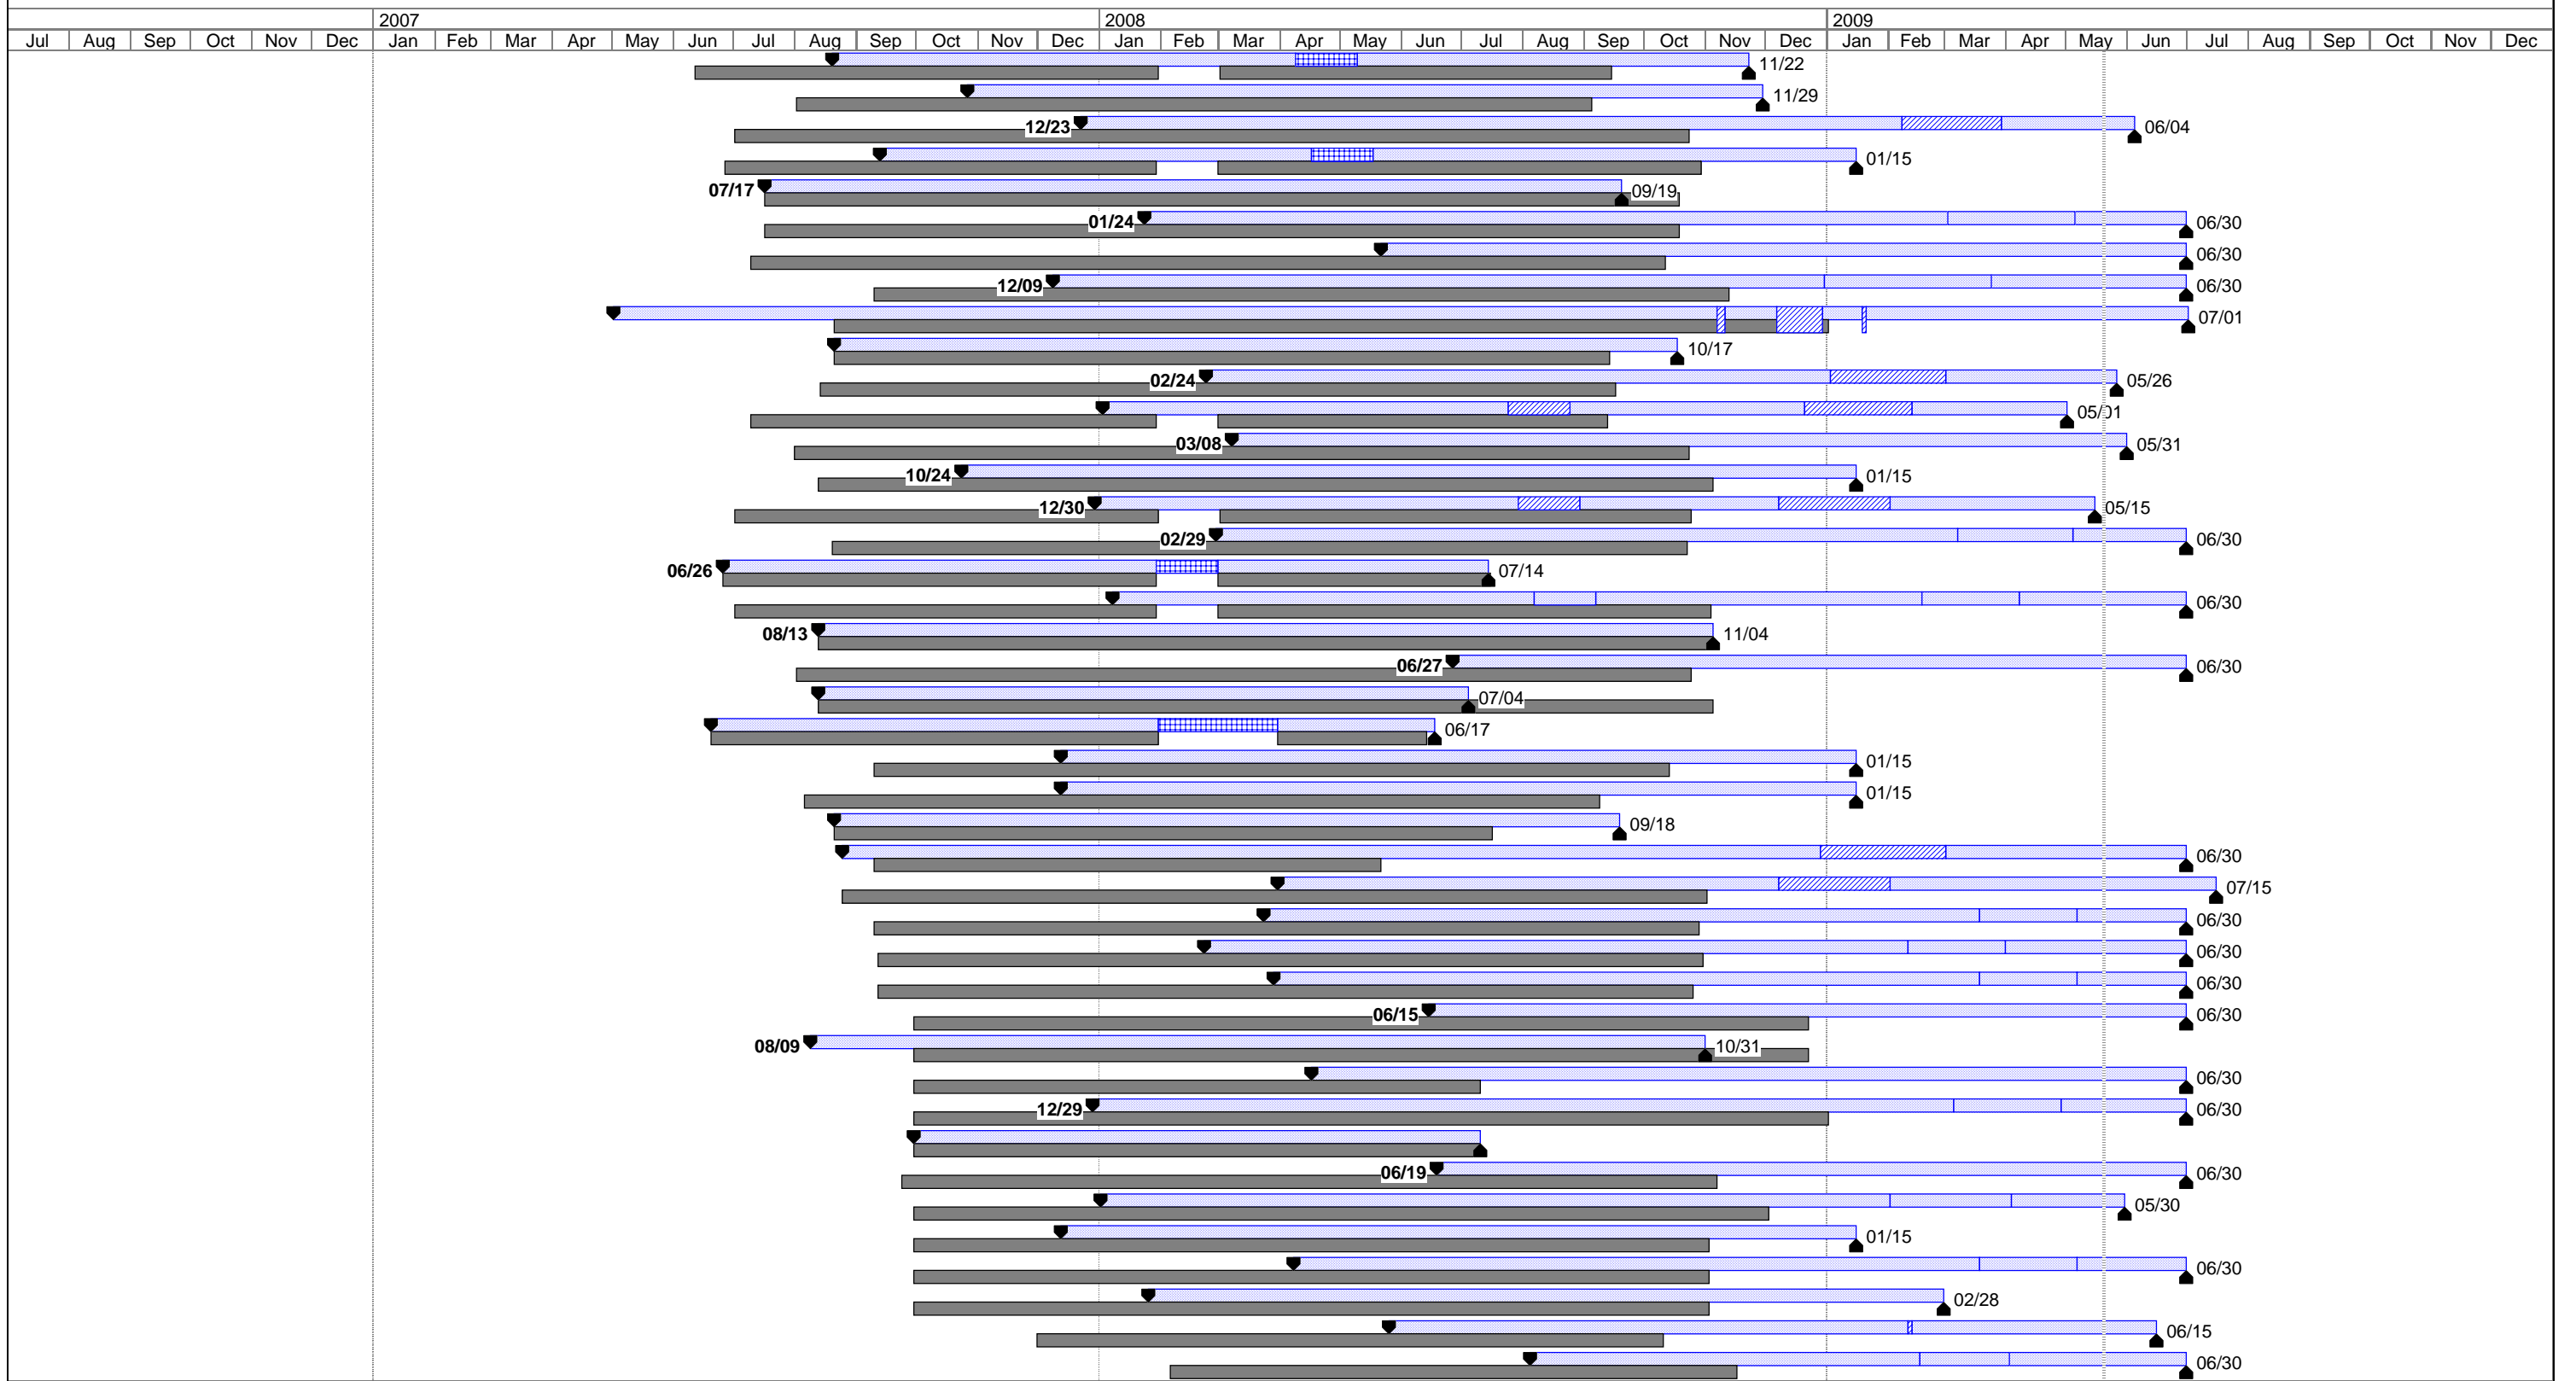

Project: Procurement Plan  
Updated: Wed 05/20/09

Critical		Milestone		External Milestone	
Critical Progress		Exp. Split in proj. exec. due to the winter Season		Deadline	
Task		Summary		Start of Bidding Procedures	
Task Progress		Project Summary		Expected end of Project Execution	
Baseline		External Tasks			


F.M.I.P. ADDITIONAL GRANT

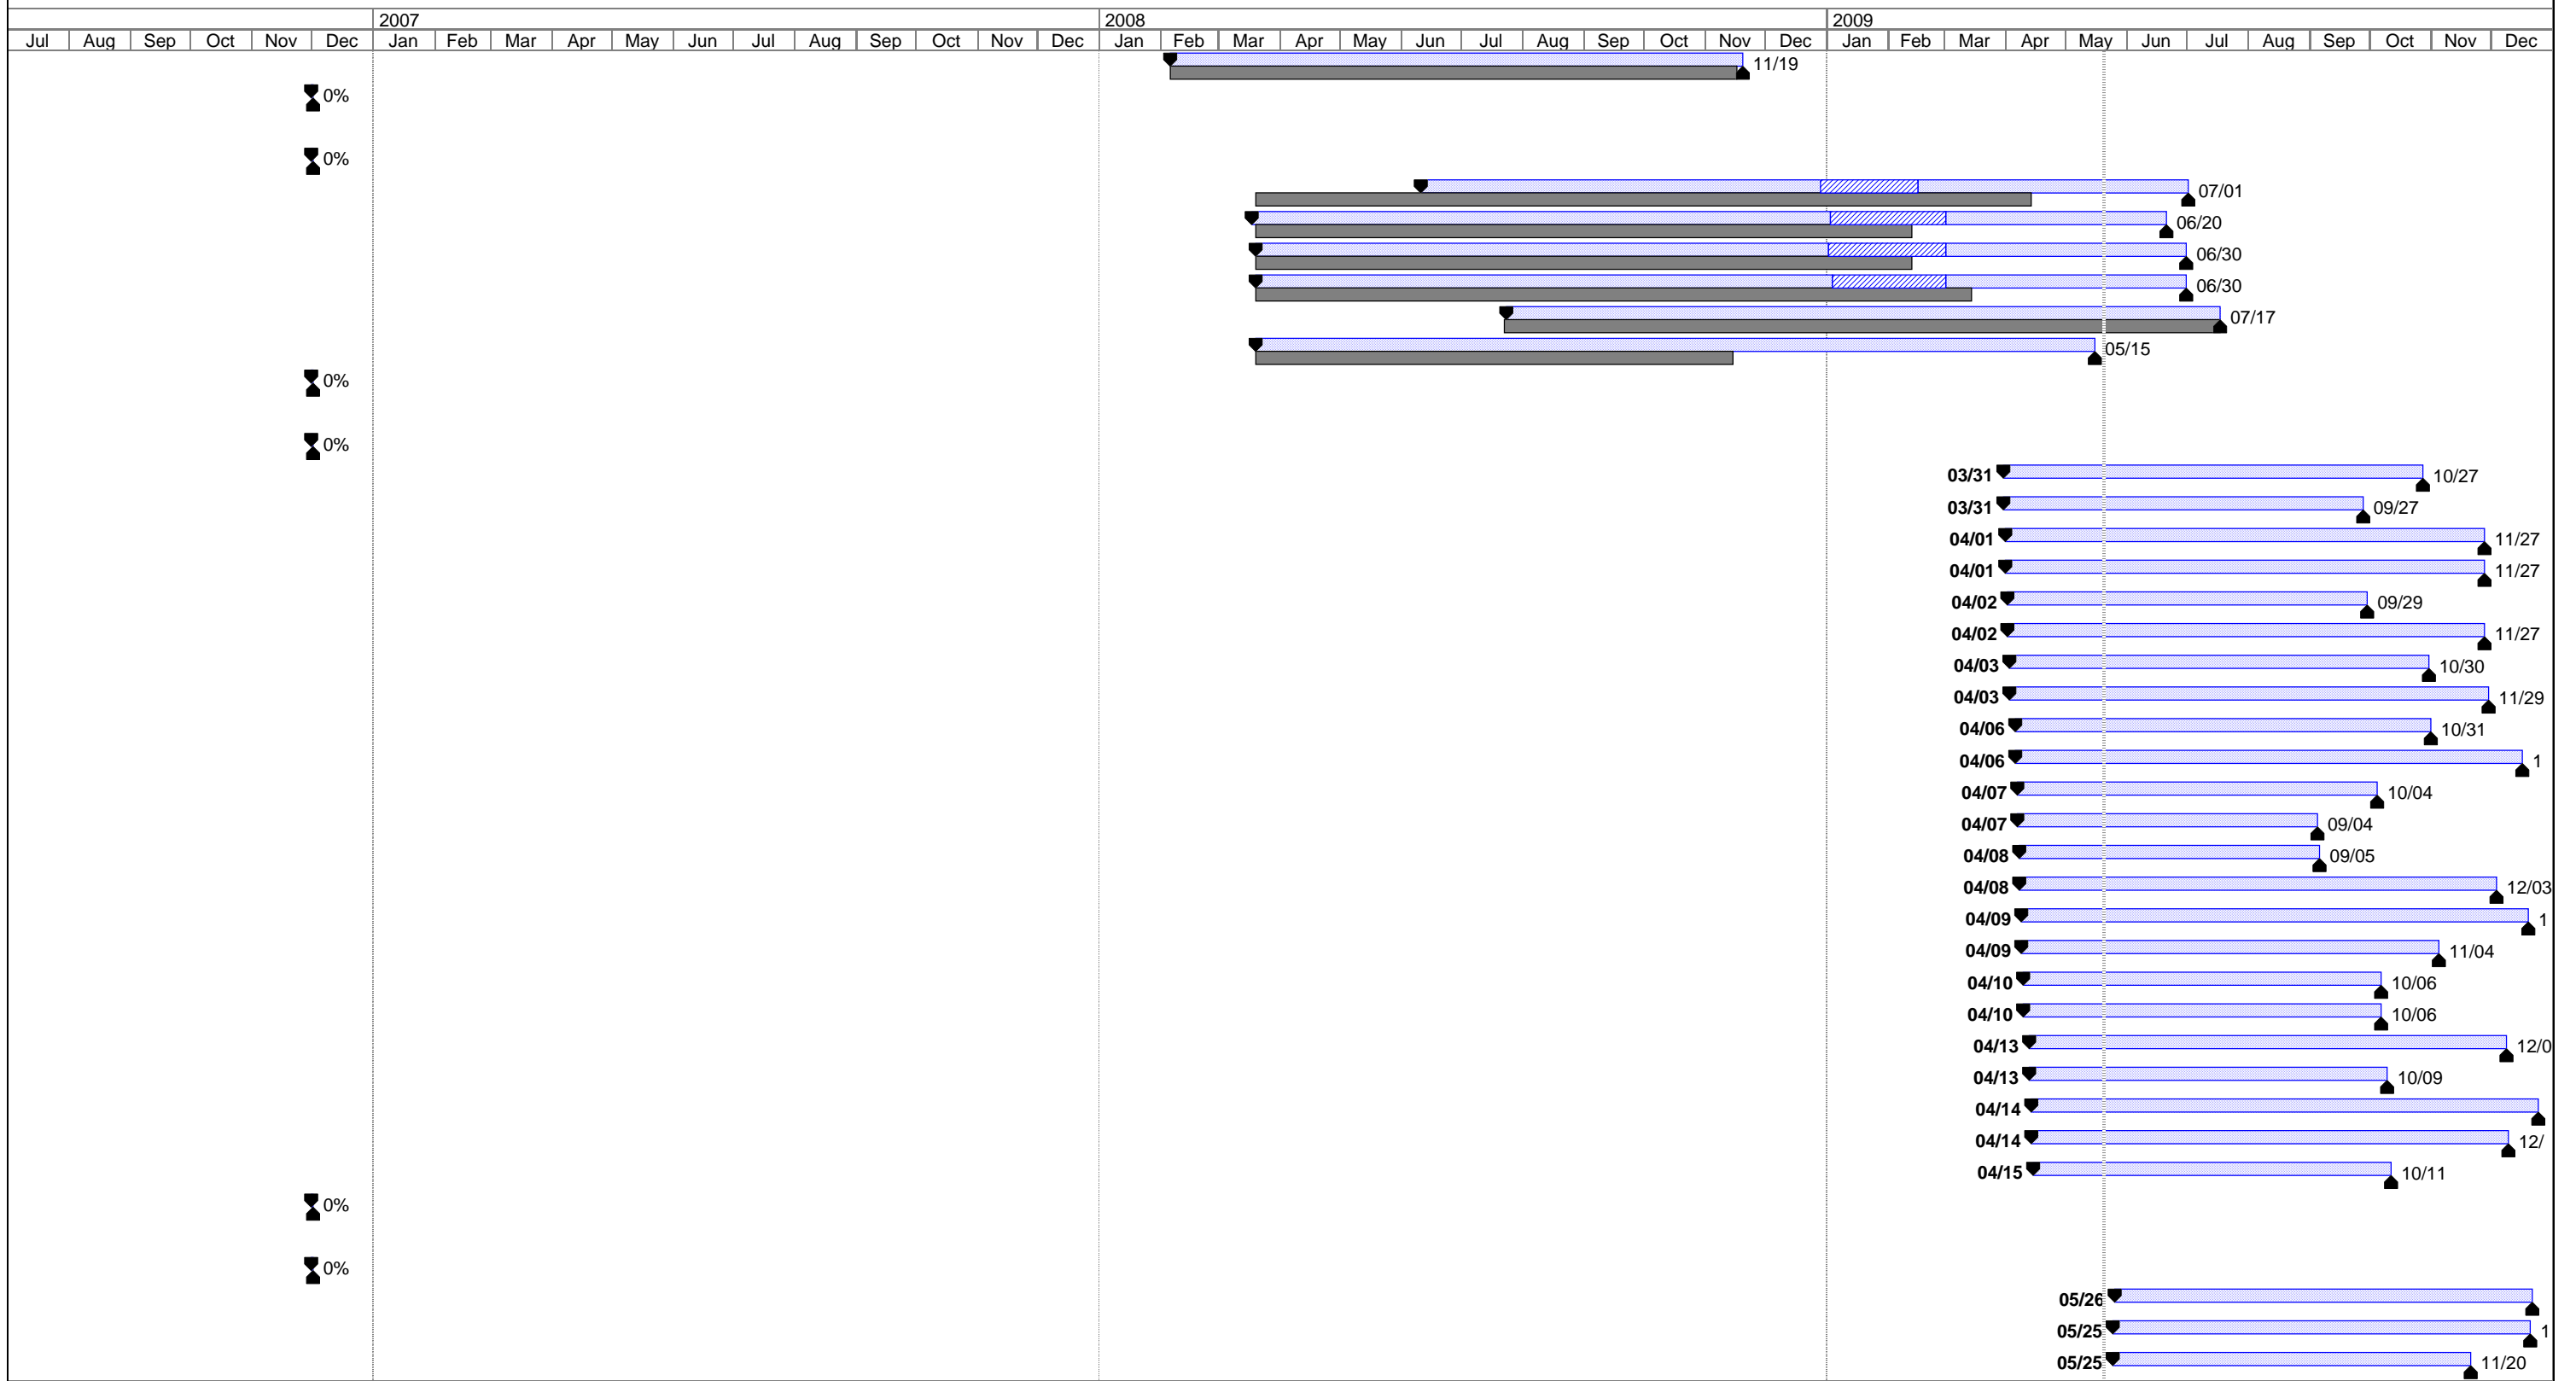

Project: Procurement Plan  
Updated: Wed 05/20/09

Critical		Milestone		External Milestone	
Critical Progress		Exp. Split in proj. exec. due to the winter Season		Deadline	
Task		Summary		Start of Bidding Procedures	
Task Progress		Project Summary		Expected end of Project Execution	
Baseline		External Tasks			

F.M.I.P. ADDITIONAL GRANT

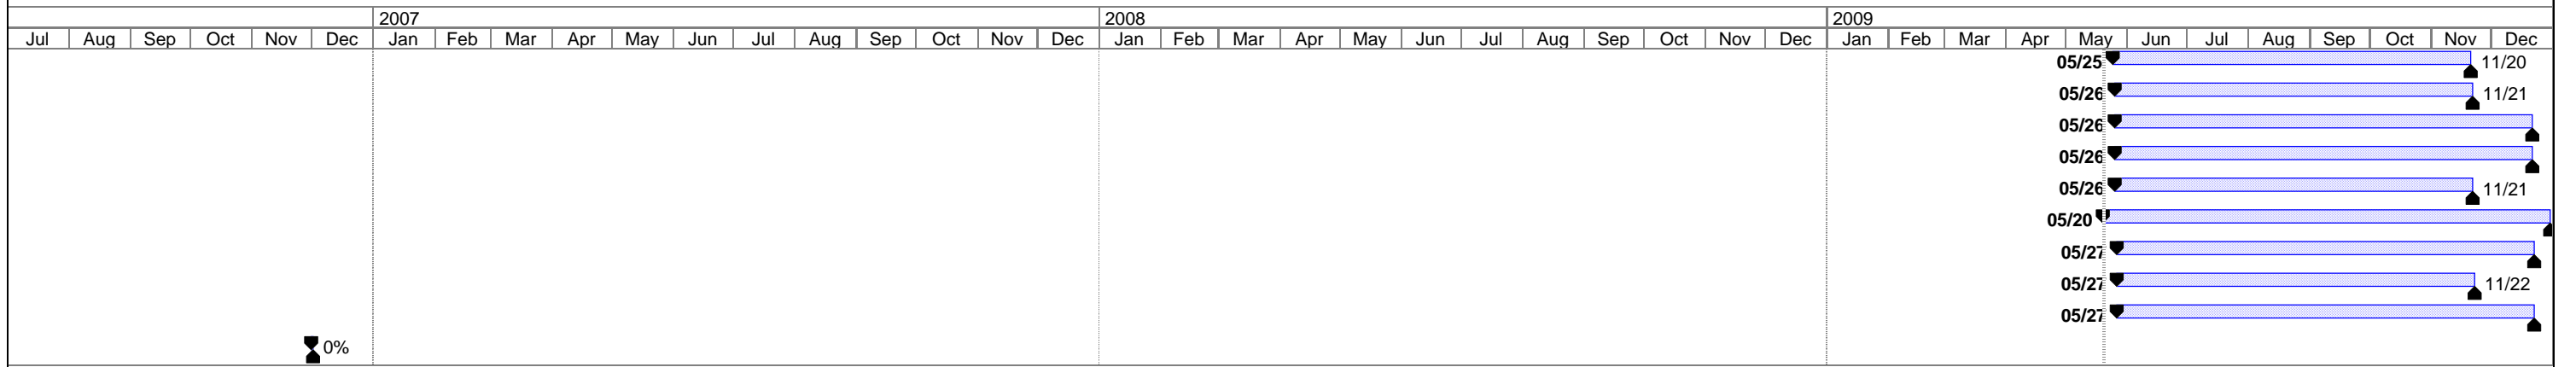

Project: Procurement Plan  
Updated: Wed 05/20/09

Critical		Milestone		External Milestone	
Critical Progress		Exp. Split in proj. exec. due to the winter Season		Deadline	
Task		Summary		Start of Bidding Procedures	
Task Progress		Project Summary		Expected end of Project Execution	
Baseline		External Tasks			
