

REGIONAL PROGRAM TO HARMONIZE AND MODERNIZE LIVING CONDITIONS SURVEYS (P153702)

AFRICA | Western Africa | Poverty and Equity Global Practice |
 IBRD/IDA | Investment Project Financing | FY 2016 | Seq No: 2 | ARCHIVED on 27-Jan-2017 | ISR26797 |

Implementing Agencies:

Key Dates

Key Project Dates

Bank Approval Date:06-Apr-2016

Effectiveness Date:08-Jul-2016

Planned Mid Term Review Date:03-Dec-2018

Actual Mid-Term Review Date:--

Original Closing Date:31-Dec-2021

Revised Closing Date:31-Dec-2021

Project Development Objectives

Project Development Objective (from Project Appraisal Document)

The PDO is to support the WAEMU Commission at strengthening the capacity of its member countries to conduct living conditions surveys that meet harmonized, regional standards and to make the collected micro-data publicly accessible.

Has the Project Development Objective been changed since Board Approval of the Project Objective?

No

Components

Name

Capacity building and survey harmonization and modernization through data collection and dissemination:(Cost \$36.30 M)

Quality control and coordination:(Cost \$4.20 M)

Overall Ratings

Name	Previous Rating	Current Rating
Progress towards achievement of PDO	● Satisfactory	● Satisfactory
Overall Implementation Progress (IP)	● Satisfactory	● Moderately Unsatisfactory
Overall Risk Rating	● Substantial	● Substantial

Implementation Status and Key Decisions

Project has become effective on July 8, 2016. Despite the fact that administrative issues (see above) are preventing implementation to be faster, progress have been made on the technical side with the finalization of the technical documents. That being said the administrative dimension is important and the issues need to be addressed for an effective implementation of the project.

Risks

Systematic Operations Risk-rating Tool

Risk Category	Rating at Approval	Previous Rating	Current Rating
Political and Governance	● Substantial	● Substantial	● High
Macroeconomic	● Low	● Low	● Low
Sector Strategies and Policies	● Substantial	● Substantial	● Substantial
Technical Design of Project or Program	● Moderate	● Moderate	● Moderate
Institutional Capacity for Implementation and Sustainability	● High	● High	● High
Fiduciary	● Substantial	● Substantial	● Substantial
Environment and Social	● Low	● Low	● Low
Stakeholders	● Low	● Low	● Low
Other	--	--	--
Overall	● Substantial	● Substantial	● Substantial

Results

Project Development Objective Indicators

► WAEMU member countries which completed the collection of harmonized living conditions surveys that made the anonymized micro-data available to the public through the WAEMU website (*) (Percentage, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	85.00
Date	14-Apr-2017	11-Jul-2016	31-Dec-2016	15-Apr-2021

► WAEMU member countries that completed a 2nd living conditions survey according to harmonized, regional standards (Number, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	--	0.00	7.00
Date	14-Apr-2017	--	30-Dec-2016	15-Oct-2021

► Adoption by the WAEMU's Council of Minister of a ruling committing all member countries to apply WAEMU living conditions survey standards with respect to methodology, contents and periodicity (Yes/No, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	N	N	N	Y
Date	17-Apr-2016	11-Jul-2016	30-Dec-2016	15-Oct-2021

Overall Comments

Intermediate Results Indicators



► Draft standardized questionnaires, disaggregated by gender are reviewed by data users (Yes/No, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	N	--	--	Y
Date	14-Apr-2017	--	--	15-Apr-2021

► Living conditions surveys that have been subject to review by peers and by independent external parties (Number, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	--	--	12.00
Date	14-Apr-2017	--	--	15-Apr-2021

► Standardized living conditions survey instruments and manuals(**)developed, and jointly adopted by the NSIs of all eight WAEMU member states (Yes/No, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	N	--	--	Y
Date	14-Apr-2017	--	--	15-Apr-2021

► Regional capacity building events (Number, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	--	--	8.00
Date	14-Apr-2017	--	--	15-Apr-2021



► A statistical abstract with selected official welfare statistics for WAEMU countries and the region are published by the WAEMU Commission (Yes/No, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	N	--	--	Y
Date	14-Apr-2017	--	--	15-Apr-2021

► WAEMU member countries that archive their harmonized living conditions surveys (Number, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	--	--	8.00
Date	14-Apr-2017	--	--	15-Apr-2021

Overall Comments

Data on Financial Performance


Disbursements (by loan)

Project	Loan/Credit/TF	Status	Currency	Original	Revised	Cancelled	Disbursed	Undisbursed	Disbursed
P153702	IDA-D1120	Effective	XDR	29.40	29.40	0.00	0.00	29.40	0%

Key Dates (by loan)

Project	Loan/Credit/TF	Status	Approval Date	Signing Date	Effectiveness Date	Orig. Closing Date	Rev. Closing Date
P153702	IDA-D1120	Effective	06-Apr-2016	17-Apr-2016	08-Jul-2016	31-Dec-2021	31-Dec-2021

Cumulative Disbursements

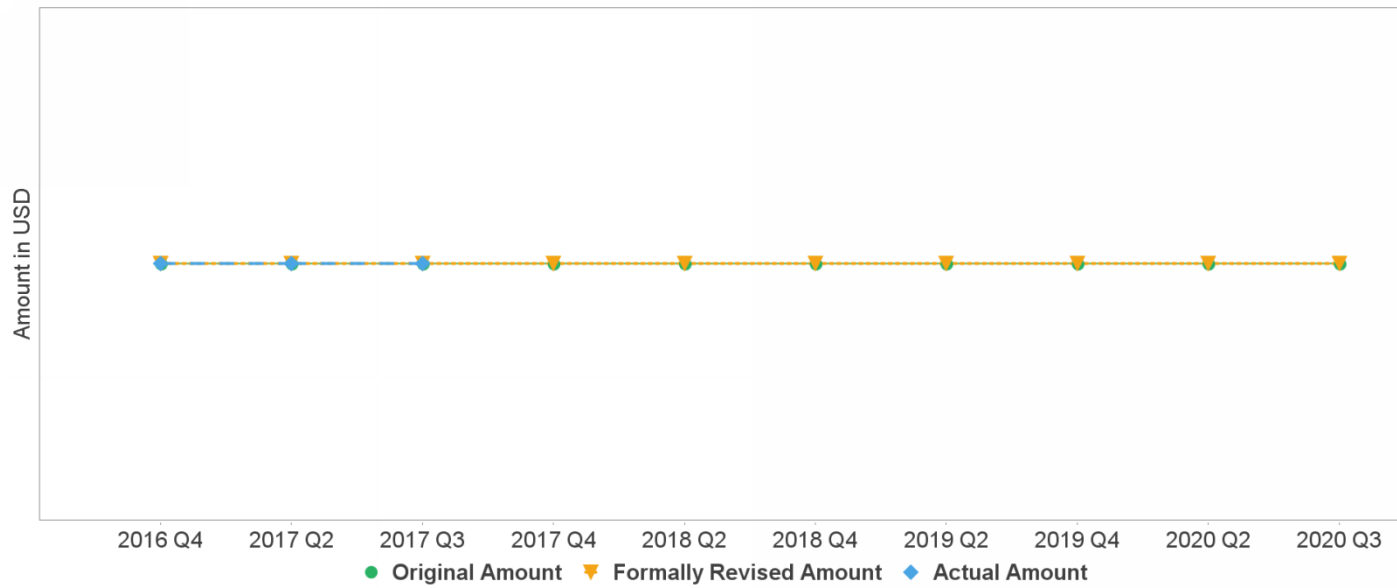

Restructuring History

There has been no restructuring to date.

Related Project(s)

There are no related projects.
