



Enhancement of Poverty Analysis Capacity (P151424)

EAST ASIA AND PACIFIC | Cambodia | Poverty and Equity Global Practice |
Recipient Executed Activities | Investment Project Financing | FY 2016 | Seq No: 2 | ARCHIVED on 21-Dec-2016 | ISR25206 |

Implementing Agencies: Director General of the Ministry of Planning

Key Dates

Key Project Dates

Bank Approval Date:16-Dec-2015

Effectiveness Date:03-Feb-2016

Original Closing Date:31-Dec-2017

Revised Closing Date:31-Dec-2017

Project Development Objectives

Project Development Objective (from Project Appraisal Document)

The project's objectives are to help strengthen Cambodia's national statistical system through the development of a National Strategy for Developing Statistics (NSDS) and to improve the Government's capacity to produce and interpret poverty and inequality indicators.

Has the Project Development Objective been changed since Board Approval of the Project Objective?

No

Components

Name

Overall Ratings

Name	Previous Rating	Current Rating
Progress towards achievement of PDO	● Moderately Satisfactory	● Moderately Unsatisfactory
Overall Implementation Progress (IP)	● Moderately Satisfactory	● Moderately Unsatisfactory

Implementation Status and Key Decisions

Good progress has been made in the last two months with solid and accelerated work plan set for the remaining period, but implementation is behind schedule. The revised work plan, budget and procurement plan, and the first financial interim report are under revision and will be finalized by the end of December 2016. The Project Implementation Unit has committed to expedite the recruitment of all key technical consultant for each component by March 2017. The launch event of the NSDS, which is the high level meeting of stakeholders to introduce the NSDS process and understand the willingness to support of the national stakeholders, will be scheduled on 12 December 2016.



Risks

Overall Risk Rating

Risk Category	Rating at Approval	Previous Rating	Current Rating
Overall	● Moderate	● Moderate	● Substantial

Comments

Due to significant delay in project implementation, including procurement delay which could impact the project's ability to achieve its development outcomes by the closing date in December 2017, the Moderate rating of overall risk has been downgraded to Substantial.

Results

Project Development Objective Indicators



▶Draft of the NSDS developed by the government of Cambodia (Text, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	n/a	n/a	n/a	National Strategy for the Development of Statistics
Date	01-Nov-2015	22-Mar-2016	14-Oct-2016	29-Dec-2017

▶Improved capacity for poverty monitoring and analysis, as evidenced by the publication of two poverty analysis notes authored by the core members of the NWGPM (Text, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	n/a	n/a	n/a	Two notes published and disseminated.
Date	01-Nov-2015	22-Mar-2016	14-Oct-2016	29-Dec-2017

▶Improved price data collection, as evidenced by the preparation and publication of pilot provincial and nationally representative CPIs using the new methodologically sound framework (Text, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	n/a	n/a	n/a	Revised provincial prices index published.
Date	01-Nov-2015	22-Mar-2016	14-Oct-2016	29-Dec-2017

Overall Comments

Intermediate Results Indicators



► Sectoral statistics assessment document (Text, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	n/a	n/a	n/a	Final Draft
Date	01-Nov-2015	22-Mar-2016	14-Oct-2016	30-Jun-2017

► Action Plan for Statistics /identification of costs document (Text, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	n/a	n/a	n/a	Final Draft
Date	01-Nov-2015	22-Mar-2016	14-Oct-2016	29-Dec-2017

► Monitoring and evaluation plan document (Text, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	n/a	n/a	n/a	Final Draft
Date	01-Nov-2015	22-Mar-2016	14-Oct-2016	29-Dec-2017

► Completion of training modules (Percentage, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	100.00
Date	01-Nov-2015	22-Mar-2016	14-Oct-2016	31-Oct-2017



► Attendance to each module of the WGPM members (Percentage, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	80.00
Date	01-Nov-2015	22-Mar-2016	22-Mar-2016	30-Jun-2017

► Identification of the weaknesses of the current methodology, estimation of formula (Percentage, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	100.00
Date	01-Nov-2015	22-Mar-2016	14-Oct-2016	31-May-2017

► Price data collection (Percentage, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	100.00
Date	01-Nov-2015	22-Mar-2016	14-Oct-2016	29-Sep-2017

► Number of provinces where training and the provision of equipment is completed (Number, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	10.00
Date	01-Nov-2015	22-Mar-2016	14-Oct-2016	31-Jul-2017

Overall Comments

Data on Financial Performance




Disbursements (by loan)

Project	Loan/Credit/TF	Status	Currency	Original	Revised	Cancelled	Disbursed	Undisbursed	Disbursed
P151424	TF-A0113	Effective	USD	0.35	0.35	0.00	0.08	0.27	23%

Key Dates (by loan)

Project	Loan/Credit/TF	Status	Approval Date	Signing Date	Effectiveness Date	Orig. Closing Date	Rev. Closing Date
P151424	TF-A0113	Effective	16-Dec-2015	03-Feb-2016	03-Feb-2016	31-Dec-2017	31-Dec-2017

Cumulative Disbursements

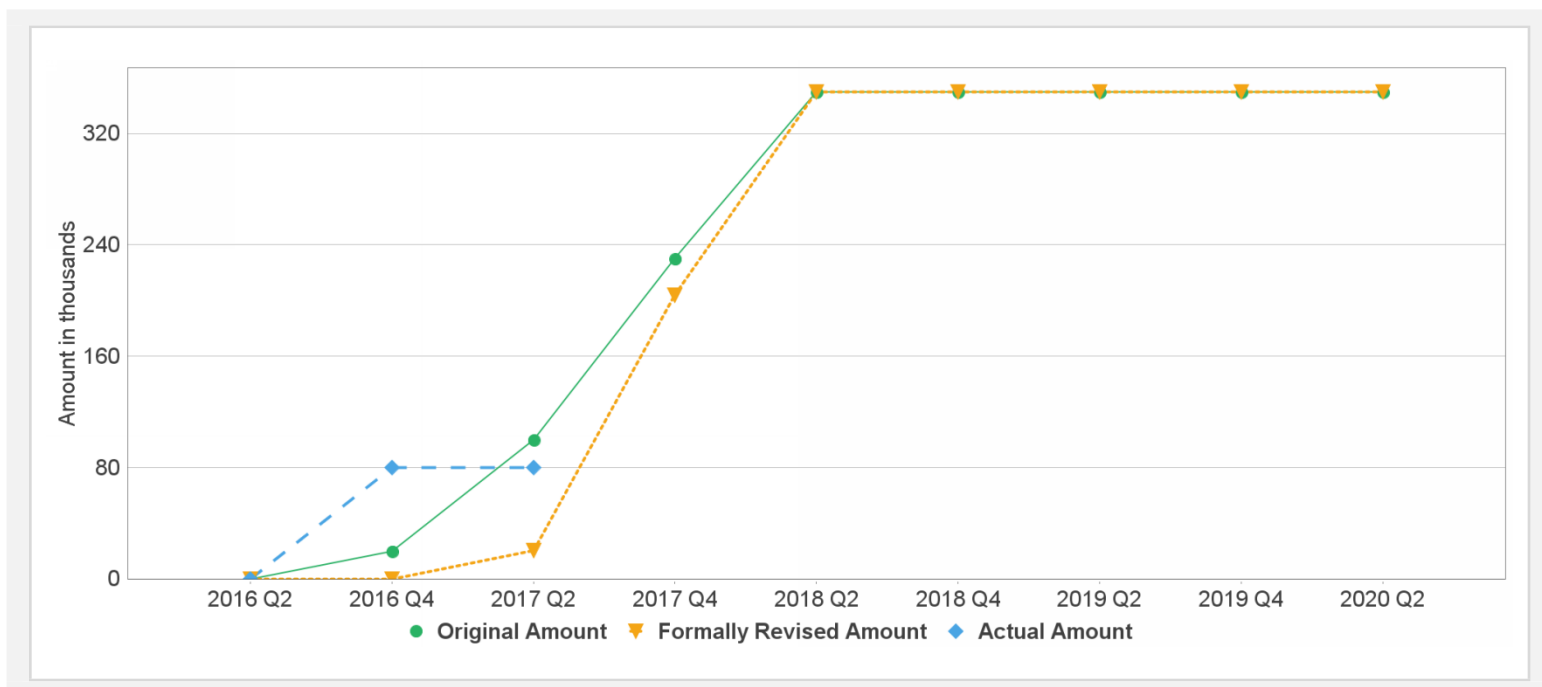

Restructuring History

There has been no restructuring to date.

Related Project(s)

There are no related projects.
