



Corredor Seco Food Security Project (P148737)

LATIN AMERICA AND CARIBBEAN | Honduras | Agriculture Global Practice | Recipient Executed Activities | Investment Project Financing | FY 2016 | Seq No: 2 | ARCHIVED on 20-Jun-2016 | ISR24162 |

Implementing Agencies: Honduran Strategic Investment Office (INVEST-H)

Key Dates

Key Project Dates

Bank Approval Date:25-Sep-2015

Effectiveness Date:--

Planned Mid Term Review Date:20-Dec-2018

Actual Mid-Term Review Date:--

Original Closing Date:30-Jun-2021

Revised Closing Date:30-Jun-2021

Project Development Objectives

Project Development Objective (from Project Appraisal Document)

The objective of the Project is to enhance food and nutritional security of vulnerable households in Selected Areas of the Corredor Seco.

Has the Project Development Objective been changed since Board Approval of the Project Objective?

No

Components

Name

Food production and rural household income generation:(Cost \$28.60 M)

Nutrition education and household hygiene:(Cost \$4.80 M)

Monitoring, evaluation and project management:(Cost \$4.40 M)

Overall Ratings

Name	Previous Rating	Current Rating
Progress towards achievement of PDO	● Satisfactory	● Satisfactory
Overall Implementation Progress (IP)	● Moderately Satisfactory	● Moderately Satisfactory
Overall Risk Rating	● Substantial	● Substantial

Implementation Status and Key Decisions



The Corredor Seco Food Security Project (ACS-GAFSP) is part of the *Alianza para el Corredor Seco* (Alliance for the Dry Corridor, ACS), which is the flagship program of the Government of Honduras for food and nutritional security in a large strip of land characterized by being under severe dry seasons. The ACS aims to lift 50,000 families from extreme poverty and reduce under-nutrition by 20 percent in targeted communities, in order to lay the foundation for continued rural growth. The ACS was initiated by the competitively awarded US \$ 30.0 million from the Global Agriculture and Food Security Program (GAFSP), a multi-donor trust fund created in 2010 to improve food security in the world's poorest countries. In Honduras, the World Bank acts as supervising entity of these GAFSP funds and supported the Government of Honduras to prepare the ACS-GAFSP, which is designed to give attention to 12,000 families in 25 municipalities in the departments of Francisco Morazán, El Paraíso and Choluteca. The investments of this multisector project will include activities for agricultural and non-agricultural production, nutrition education and household hygiene infrastructure. The Honduran Strategic Investment Office INVEST-H, in charge of project implementation, is currently carrying out two competitive bidding processes for the selection of two operators (one NGO and one commercial firm) that will be responsible for project execution in separated geographical areas. It is expected that the award of one of the operators will be concluded by July, 2016.

Risks

Systematic Operations Risk-rating Tool



Risk Category	Rating at Approval	Previous Rating	Current Rating
Political and Governance	● Substantial	● Substantial	● Substantial
Macroeconomic	● Substantial	● Substantial	● Substantial
Sector Strategies and Policies	● Low	● Low	● Low
Technical Design of Project or Program	● Substantial	● Substantial	● Substantial
Institutional Capacity for Implementation and Sustainability	● High	● High	● High
Fiduciary	● Substantial	● Substantial	● Substantial
Environment and Social	● Moderate	● Substantial	● Substantial
Stakeholders	● Moderate	● Moderate	● Moderate
Other	● Low	● Low	● Low
Overall	● Substantial	● Substantial	● Substantial

Results

Project Development Objective Indicators

► Average yield achieved in food crops by participating HH of component 1 (Number, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	--	--	20.00
Date	01-Dec-2015	--	--	31-May-2021

► Average of annual incremental sales of participating HH under Business Plans (Amount(USD), Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	--	--	900.00
Date	01-Dec-2015	--	--	31-May-2021

► Dietary diversity score in participating HHs of component 2 (Percentage, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	--	--	60.00



Date	01-Dec-2015	--	--	31-May-2021
------	-------------	----	----	-------------

► Households benefitting directly from the Project (Number, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	--	--	12000.00
Date	01-Dec-2015	--	--	31-May-2021

Overall Comments

Intermediate Results Indicators

► Client days of training provided (number) (Number, Core)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	--	--	30000.00
Date	01-Dec-2015	--	--	31-May-2021

▲ Client days of training provided - Female (number) (Number, Core Breakdown)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	--	--	4500.00
Date	01-Dec-2015	--	--	31-May-2021



▶ Area provided with irrigation and drainage services (Hectare(Ha), Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	--	--	1000.00
Date	01-Dec-2015	--	--	31-May-2021

▲ Area provided with irrigation and drainage services under Business Plans (Hectare(Ha), Custom Breakdown)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	--	--	700.00
Date	01-Dec-2015	--	--	31-May-2021

▶ Agricultural subprojects implemented under Business Plans (Number, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	--	--	150.00
Date	01-Dec-2015	--	--	31-May-2021

▲ Number of benefiting HH for agricultural subprojects implemented under Business Plans (Number, Custom Supplement)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	--	--	3500.00



▶ Households benefiting of an agricultural subproject implemented under a Food Security Plan (Number, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	--	--	6000.00
Date	01-Dec-2015	--	--	31-May-2021

▶ Business development subprojects implemented (Number, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	--	--	100.00
Date	01-Dec-2015	--	--	31-May-2021

▲ Business development subprojects implemented led by women (Number, Custom Supplement)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	--	--	50.00

▶ Clients who have adopted an improved agr. technology promoted by the project (Number, Core)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	--	--	7000.00
Date	01-Dec-2015	--	--	31-May-2021



▾ Clients who adopted an improved agr. technology promoted by project – female (Number, Core Breakdown)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	--	--	1050.00
Date	01-Dec-2015	--	--	31-May-2021

▶ Increase of links to the market (Percentage, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	--	--	30.00
Date	01-Dec-2015	--	--	31-May-2021

▶ Increase subsistence consumption (Percentage, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	--	--	20.00
Date	01-Dec-2015	--	--	31-May-2021

▶ Client days of nutrition training provided (Days, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	--	--	12000.00
Date	01-Dec-2015	--	--	31-May-2021



► Number of children under age of two attending the growth monitoring program (Number, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	--	--	--	3000.00
Date	01-Dec-2015	--	--	31-May-2021

► Household hygiene investments (Number, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	--	--	4000.00
Date	01-Dec-2015	--	--	31-May-2021

► Evaluations carried out (Number, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	--	--	3.00
Date	01-Dec-2015	--	--	31-May-2021

► Timely semiannual monitoring reports (Number, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	--	--	10.00
Date	01-Dec-2015	--	--	31-May-2021

Overall Comments

Data on Financial Performance




Disbursements (by loan)

Project	Loan/Credit/TF	Status	Currency	Original	Revised	Cancelled	Disbursed	Undisbursed	Disbursed
P148737	TF-17904	Not Effective	USD	30.00	30.00	0.00	0.00	30.00	0%

Key Dates (by loan)

Project	Loan/Credit/TF	Status	Approval Date	Signing Date	Effectiveness Date	Orig. Closing Date	Rev. Closing Date
P148737	TF-17904	Not Effective	24-Sep-2015	--	--	30-Jun-2021	30-Jun-2021

Cumulative Disbursements

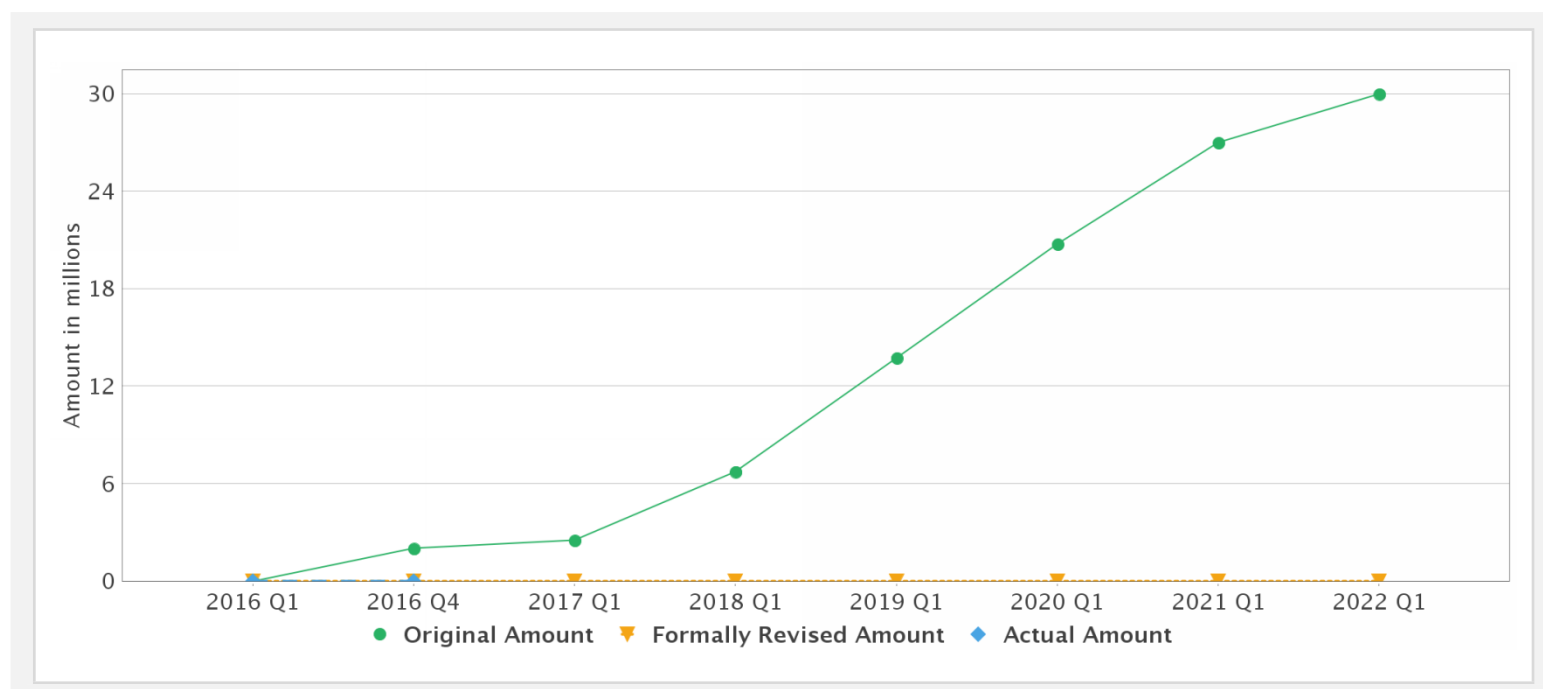

Restructuring History

There has been no restructuring to date.

Related Project(s)

There are no related projects.

