



P4: Pacific Regional ICT Regulatory Development Project (P148238)

EAST ASIA AND PACIFIC | Pacific Islands | Transport & ICT Global Practice |
IBRD/IDA | Investment Project Financing | FY 2015 | Seq No: 3 | ARCHIVED on 05-Feb-2016 | ISR22501 |

Implementing Agencies: University of the South Pacific

Key Dates

Key Project Dates

Bank Approval Date:30-Jul-2014

Effectiveness Date:12-Sep-2014

Planned Mid Term Review Date:01-Mar-2017

Actual Mid-Term Review Date:--

Original Closing Date:31-Jul-2019

Revised Closing Date:31-Jul-2019

Project Development Objectives

Project Development Objective (from Project Appraisal Document)

The development objective of the Project is to strengthen the capacity of ICT Regulatory institutions in participating countries, and enhance regional collaboration on regulatory issues. The primary beneficiaries of the Project are the Pacific island regulatory institutions. Indirect beneficiaries will include consumers, businesses (including telecommunications operators), government agencies, researchers/academia and communities receiving improved ICT services as a result of enhanced regulatory outcomes.

Has the Project Development Objective been changed since Board Approval of the Project Objective?

No

Components

Name

Regional capacity development and knowledge management:(Cost \$2.25 M)

Regional advisory services:(Cost \$1.75 M)

Project administration:(Cost \$0.50 M)

Overall Ratings

| Name | Previous Rating | Current Rating |
|--------------------------------------|---------------------------|---------------------------|
| Progress towards achievement of PDO | ● Moderately Satisfactory | ● Moderately Satisfactory |
| Overall Implementation Progress (IP) | ● Moderately Satisfactory | ● Moderately Satisfactory |
| Overall Risk Rating | ● Low | ● Low |



Implementation Status and Key Decisions

The Project was declared effective on September 12, 2014. Key Project staff positions--Project Director, Researcher and Executive Assistant--have been recruited and mobilized following extended procurement processes. A firm to develop the Project website/ portal will be hired; this will build on the materials developed in the Phase 1 of this program; USP will take responsibility for website hosting. In addition short-term technical, economic and legal consultants are expected to be recruited in the first half of 2016.

The Business Plan and Workplan for 2016 have been completed and approved in principle by the Project Steering Committee. The main objectives of the Business Plan are:

1. Improved quality and reliability of information on the sector in the region: there will be a strong focus in 2016 on establishing an up to date set of sector indicators
2. Improved regulatory and technical capabilities of member countries: through a combination of technical notes and seminars
3. Strengthened interregional cooperation and collaboration among the regulators, the private sector and policy makers of the Pacific Island Countries: this will also include collaboration agreements, for example with ITU, GSMA, APT, the Pacific Islands Telecommunications Association (PITA) and the Council of Regional Organizations in the Pacific agencies.
4. Improved access to knowledge services by Pacific member countries: a series of technical notes will be delivered in 2016, plus regional knowledge events
5. Improved awareness of the project among stakeholders (including economic development ministries and agencies) and the public: through a revamped Project website, and targeted outreach



Risks

Systematic Operations Risk-rating Tool

| Risk Category | Rating at Approval | Previous Rating | Current Rating |
|--|--------------------|-----------------|----------------|
| Political and Governance | -- | ● Low | ● Low |
| Macroeconomic | -- | ● Low | ● Low |
| Sector Strategies and Policies | -- | ● Low | ● Low |
| Technical Design of Project or Program | -- | ● Low | ● Low |
| Institutional Capacity for Implementation and Sustainability | -- | ● Moderate | ● Moderate |
| Fiduciary | -- | ● Moderate | ● Moderate |
| Environment and Social | -- | ● Low | ● Low |
| Stakeholders | -- | ● Low | ● Low |
| Other | -- | -- | -- |
| Overall | -- | ● Low | ● Low |

Results

Project Development Objective Indicators



► Impact on Telecom sector of World Bank Technical Assistance (composite score: 1- low impact to 5-high impact) (Number, Core)

| | Baseline | Actual (Previous) | Actual (Current) | End Target |
|-------|-------------|-------------------|------------------|-------------|
| Value | 0.00 | 1.00 | 1.00 | 4.00 |
| Date | 30-Jul-2014 | 12-Jun-2015 | 15-Jan-2016 | 31-Jul-2019 |

► Impact on IT/ITES Sector of World Bank Technical Assistance (composite score: 1 # low impact to 5 # high impact) (Number, Core)

| | Baseline | Actual (Previous) | Actual (Current) | End Target |
|-------|-------------|-------------------|------------------|-------------|
| Value | 0.00 | 1.00 | 1.00 | 4.00 |
| Date | 30-Jul-2014 | 12-Jun-2015 | 15-Jan-2016 | 31-Jul-2019 |

Overall Comments

Intermediate Results Indicators

► Establishment and Maintenance of Region-wide Data on the State of Competition in ICT Markets Across the Region (Yes/No, Custom)

| | Baseline | Actual (Previous) | Actual (Current) | End Target |
|-------|-------------|-------------------|------------------|-------------|
| Value | N | Y | Y | Y |
| Date | 30-Jul-2014 | 12-Jun-2015 | 15-Jan-2016 | 31-Jul-2019 |

▲ Establishment and Maintenance of Gender-disaggregated Data on ICT Market Penetration Levels Across the Region (Yes/No, Custom Breakdown)

| | Baseline | Actual (Previous) | Actual (Current) | End Target |
|-------|-------------|-------------------|------------------|-------------|
| Value | N | N | N | Y |
| Date | 30-Jul-2014 | 12-Jun-2015 | 12-Jun-2015 | 31-Jul-2019 |



► Collection and Dissemination of Five Working Papers on Priority Regulatory Topics (Number, Custom)

| | Baseline | Actual (Previous) | Actual (Current) | End Target |
|-------|-------------|-------------------|------------------|-------------|
| Value | 0.00 | 1.00 | 2.00 | 5.00 |
| Date | 30-Jul-2014 | -- | 15-Jan-2016 | 31-Jul-2019 |

► Completion of Five or More Training Programs with at Least 15 Regulatory Staff Trained per Program per Year (Number, Custom)

| | Baseline | Actual (Previous) | Actual (Current) | End Target |
|-------|-------------|-------------------|------------------|-------------|
| Value | 0.00 | 0.00 | 0.00 | 20.00 |
| Date | 30-Jul-2014 | 12-Jun-2015 | 15-Jan-2016 | 31-Jul-2019 |

► Three Regional Knowledge Sharing Events Held per Year (Number, Custom)

| | Baseline | Actual (Previous) | Actual (Current) | End Target |
|-------|-------------|-------------------|------------------|-------------|
| Value | 0.00 | 0.00 | 0.00 | 12.00 |
| Date | 30-Jul-2014 | 12-Jun-2015 | 15-Jan-2016 | 31-Jul-2019 |

► Establishment and Maintenance of a Knowledge Portal (Yes/No, Custom)

| | Baseline | Actual (Previous) | Actual (Current) | End Target |
|-------|-------------|-------------------|------------------|-------------|
| Value | Y | N | N | Y |
| Date | 30-Jul-2014 | -- | 15-Jan-2016 | 31-Jul-2019 |



► Establishment and Maintenance of Online Website that Provides Access to an Advisory Services Database that Generates 50 or More Hits per Year (Number, Custom)

| | Baseline | Actual (Previous) | Actual (Current) | End Target |
|-------|-------------|-------------------|------------------|-------------|
| Value | 0.00 | 0.00 | 0.00 | 200.00 |
| Date | 30-Jul-2014 | 12-Jun-2015 | 15-Jan-2016 | 31-Jul-2019 |


► Establishment and Maintenance of Annual Regulatory Lessons Learned Section on Advisory Services Database (Yes/No, Custom)

| | Baseline | Actual (Previous) | Actual (Current) | End Target |
|-------|-------------|-------------------|------------------|-------------|
| Value | N | N | N | Y |
| Date | 30-Jul-2014 | 12-Jun-2015 | 15-Jan-2016 | 31-Jul-2019 |

Overall Comments

Data on Financial Performance


Disbursements (by loan)

| Project | Loan/Credit/TF | Status | Currency | Original | Revised | Cancelled | Disbursed | Undisbursed | Disbursed |
|---------|----------------|-----------|----------|----------|---------|-----------|-----------|-------------|--|
| P148238 | IDA-H9820 | Effective | XDR | 3.00 | 3.00 | 0.00 | 0.19 | 2.81 |  6% |

Key Dates (by loan)

| Project | Loan/Credit/TF | Status | Approval Date | Signing Date | Effectiveness Date | Orig. Closing Date | Rev. Closing Date |
|---------|----------------|-----------|---------------|--------------|--------------------|--------------------|-------------------|
| P148238 | IDA-H9820 | Effective | 30-Jul-2014 | 27-Aug-2014 | 12-Sep-2014 | 31-Jul-2019 | 31-Jul-2019 |

Cumulative Disbursements

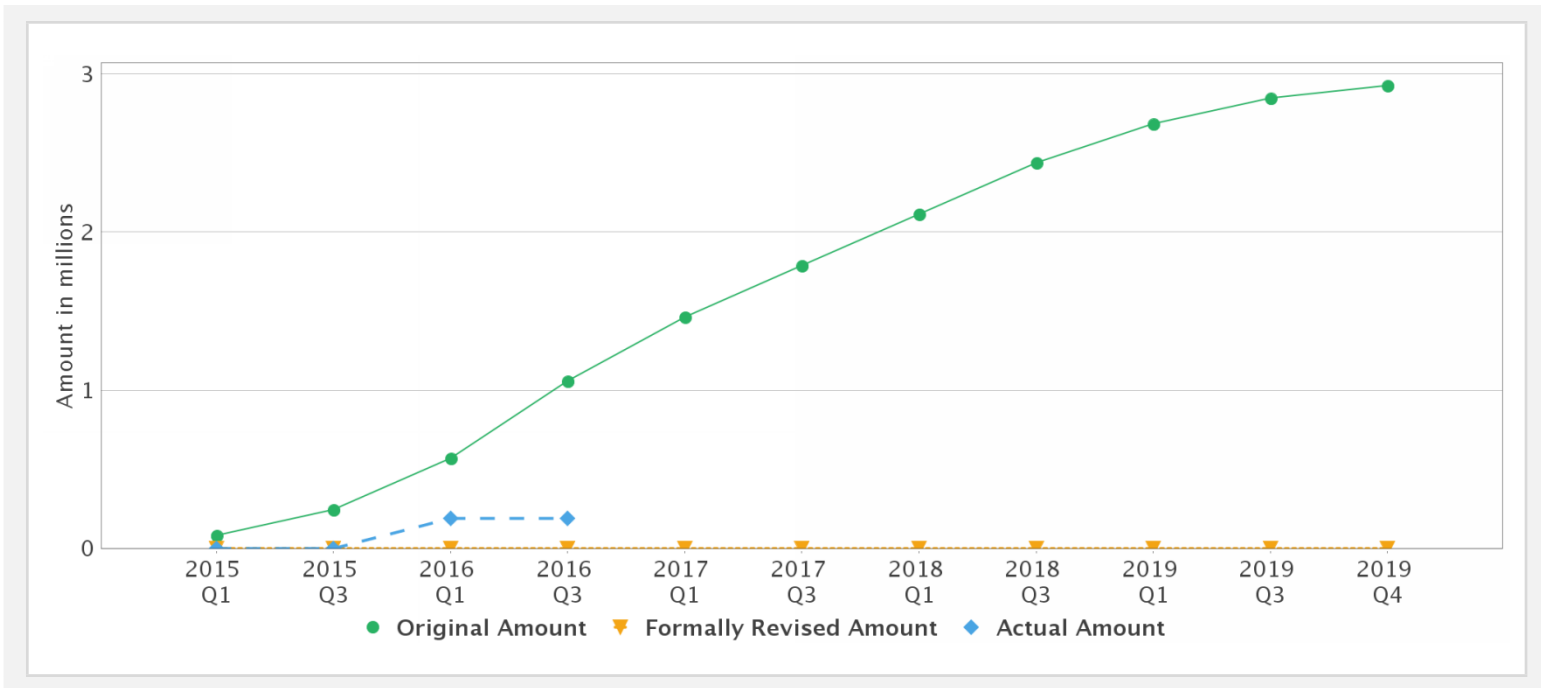

Restructuring History

There has been no restructuring to date.

Related Project(s)

There are no related projects.
