



NIGER Skills Development for Growth Project (P126049)

WESTERN AND CENTRAL AFRICA | Niger | Education Global Practice |
IBRD/IDA | Investment Project Financing | FY 2013 | Seq No: 18 | ARCHIVED on 30-Jun-2023 | ISR56932 |

Implementing Agencies: Government of the Republic of Niger - Ministre du Plan, Ministry of Labor and Professional Training, Ministry of Planning, Ministry of Professional and Technical Education

Key Dates

Key Project Dates

Bank Approval Date: 30-Apr-2013

Effectiveness Date: 28-Oct-2013

Planned Mid Term Review Date: 15-May-2017

Actual Mid-Term Review Date: 03-Apr-2017

Original Closing Date: 30-Nov-2019

Revised Closing Date: 30-Nov-2023

Project Development Objectives

Project Development Objective (from Project Appraisal Document)

The project development objective is to improve the effectiveness of formal technical and vocational training, short term skills development and apprenticeship programs in priority sectors.

Has the Project Development Objective been changed since Board Approval of the Project Objective?

No

Components Table

Name

Improving the Effectiveness of Formal Training:(Cost \$35.40 M)
Strengthening Short Term Skills Development and Apprenticeships Programs:(Cost \$29.50 M)
Institutional Capacity Strengthening and Monitoring and Evaluation:(Cost \$13.10 M)
Contingency:(Cost \$2.00 M)

Overall Ratings

Name	Previous Rating	Current Rating
Progress towards achievement of PDO	<input type="checkbox"/> Satisfactory	<input type="checkbox"/> Satisfactory
Overall Implementation Progress (IP)	<input type="checkbox"/> Moderately Satisfactory	<input type="checkbox"/> Moderately Satisfactory
Overall Risk Rating	<input type="checkbox"/> Moderate	<input type="checkbox"/> Moderate

Implementation Status and Key Decisions

Overview. The *Niger Skills Development for Growth Project* (PRODEC) focuses primarily on improving the effectiveness of formal technical and vocational training, as well as the quality of short-term skills development and apprenticeship programs in key priority sectors. On December 18, 2020, the Project was restructured to include a number of key modifications, including, *inter alia*: a 12-month extension of the Project's closing date; modification to existing activities and inclusion of new activities which further enhanced the Project's ability to achieve the PDO; adjustments to the Project's Results Framework (RF) to ensure full alignment between each indicator's target date and the new closing date (November 30, 2023), the introduction of an additional intermediate results indicator (number of private training institutions supported by the Project); and the inclusion of additional activities linked to the Government's COVID-19 Emergency Response Plan. The restructured design of the PRODEC has significantly improved the Project's chances to fully achieve the PDO.



Progress by Component. Substantial progress under the PRODEC has been achieved to date. The section below provides a comprehensive and current overview of the main outputs and outcomes achieved across the various Components and Sub-components.

Component 1: Improving the Effectiveness of Formal Training focuses on improving: (a) the quality and relevance of TVET institutions; and (b) the school-to-work transition.

Sub-component 1.1—Demand-Driven Approach to Formal Vocational Training

Under sub-component 1.1, the Project supports a number of activities which are expected to have a significant impact on the achievement of the PDO, namely: (i) The construction of the Niger Center for Arts and Leather Crafts (*Centre des Métiers du Cuir et d'Art du Niger* – CMCAN), Doutchi Institute, and Agadez High School for hospitality; (ii) The renovation and upgrading of 20 vocational training centers using a market-driven and employment-focused training approach; (iii) the support to the Mechatronics Department of Niamey Vocational and Professional Training Center; (*Centre de Formation et de Perfectionnement Professionnel* — CFPP Niamey), and (iv) support to the Training Center for Young Farmers (*Centre de Formation des Jeunes Agriculteurs* – CFJA), Kéguel and Bélinde; (v) The provision of institutional grants to all training centers to support the development and implementation of an Institution Improvement Plan at each targeted institution and related training in managing financial resources; and (vi) The support to a selected number of privately-owned training institutions and those owned by women's associations/groups.

- **The renovation and upgrading of the first three targeted TVET Institutions supported under the PRODEC namely the CMCAN, the Doutchi Institute, and the Agadez High School for hospitality.** The Task team noted with satisfaction that the Board of Directors of these structures are functional, and that the new organizational and operational modalities of TVET establishments are being effectively applied. However, the management and accountability tools, such as performance contracts and partnerships with the private sector, have not yet been developed to allow for the implementation of a new mode of governance and leveraging the assets of the economic environment. Training at the three institutions is entirely residential, where as the Project's objective is to develop flexible training schedules. The boarding school built by the PRODEC at CMCAN is still not operational despite the investments made and the need to accommodate learners from the inner regions.
- **Renovation and upgrading of Trade Training Centers (using a market-driven and employment-focused training approach. As defined during the restructuring of PRODEC, it was agreed that part of the project's funds would be used to rehabilitate and upgrade 20 CFMs in Niger.** The work schedule updated at the technical meeting to support implementation of the project in May 2023, provides for provisional acceptance of all rehabilitations by June 2023, except for those already received. To date, (i) 10 sites received provisional acceptance without any objection (Karofane, Abalak, Aderbissinat, Iférouane, Keguel, Dan goulbi, Gabi, Matameye, Droum, Tillabéry), (ii) 8 sites received partial provisional acceptance subject to conditions (Goudoumaria, Chétimari, Sassoumbroum, Mirriah, Baleyara, Makalondi, Kore, Farey), (iii) 1 was technically accepted (Doutchi) with a 96% completion rate, and (iv) the 4 remaining sites works are in progress with more than 85% of completion rate. A total of 72 endogenous and 36 exogenous trainers have been trained in pedagogy, fish farming, gardening, and agri-food processing.
- **The three contracts for technical and pedagogical equipment of the CFMs are completed.** The pedagogical equipment for the Mechatronics Department of CFPP-Niamey has been received with the support of an international consultant who participated in the verification of their compliance and technical specifications.
- **The Project provided grants to the three institutions supported in the first phase and to the CFM/CFJA to support their operations until sustainable funding solutions are identified. Both the Training Center for Young Farmers in Keguel and Belindé** have received grants to implement their Institutional Improvement Plan prepared with the support of the PCU. The transfer of resources was carried out in conjunction with the PCU's financial management and procurement units to ensure rigorous management of the allocated resources and the attendants have been trained in financial management and community procurement procedures.
- **Support to privately or association-owned training institutions.** The selection of centers and women's groups has been completed. A total of 45 beneficiaries received support: (i) 16 private technical and vocational training centers benefited from the private sector support fund in the first cohort, and (ii) 29 women's groups in the second cohort.

Sub-component 1.2: Improvement in the School-to-Work Transition. This sub-component aims to strengthen the transition from formal education and training to the labor market by supporting job counseling and internships for technical secondary and tertiary graduates.

The placement of young graduates in internship programs is continuing to make progress, although lagging project milestones. All the 6,230 trainees placed by the ANPE must complete their placement by October 30, 2023. To date, 5,583 young people have completed their internship, and the last 647 placed in November 2022 are continuing their internship, which will end in October 2023.

The program of training-reconverting of young graduates. To date, 480 young graduates of the Project's 600 target have benefited from retraining in the following trades: (i) hotel trade (130), (ii) construction (190), (iii) cooking assistants (80); and (iv) solar energy (80). To date, all retraining courses have been completed, exception the cooking which will end in July 2023.

Component 2: Strengthening Short Term Skills Development and Apprenticeship Programs focuses on: (a) expanding apprenticeships; (b) developing short-term on-demand training programs; and (c) promoting entrepreneurship training.



Sub-component 2.1: Expanding apprenticeships in priority sectors.

The number of young people completing the dual apprenticeship program is 6,006 out of a total of 6,467, or 93% of the total. Girls completing the FAFPA dual apprenticeship program represent 37% (2,270). FAFPA has contracted an external firm to carry out a final evaluation of the apprenticeship system in order to build a sustainable and renewed system based on the specific experience of PRODEC and lessons learned at the international level. This evaluation will address the financing mechanism and the legal framework as well as the pedagogical approaches.

Sub-component 2.2: Agricultural apprenticeship and On-Demand Training Programs. The objective of this sub-component is to support short-term skills development by developing an on-demand training program. Recent progress has also been made in the implementation of activities aimed at improving the quality of learning, through: (i) the acquisition of pedagogical equipment for the public entities and partners involved in the apprenticeship program; and (ii) the development and adaptation of standard training modules for the apprenticeship training.

Training in the *Agriculture Training Centers "ATC" (Sites d'Apprentissage Agricole -SAA*

To date, 2,283 out-of-school young people have completed apprenticeship programs in the SAA. In addition to these 2,283 young people, there are 1,017 who have taken part in the agricultural apprenticeship program financed by initial funding. This gives a total of 3,300 out-of-school young people who have completed their training out of 4,071 young people in training, representing a rate of 81% to date. The total number of girls who have completed training to date is 1,577, including 1,149 (SAA) and 428 (initial fund agricultural training). This gives a percentage of 48% of girls who have completed training

The Project has benefited from UNICEF's contribution to the construction of latrine blocks for girls and the development of boreholes for the 10 SAA, but to date, only 6 boreholes are completed and no latrine blocks.

Sub-component 2.3: Promotion of Entrepreneurship Training. The objective of this sub-component is to support short-term skills development among Niger's youth by promoting entrepreneurship training.

Regarding the **promotion of youth entrepreneurship**, the process of taking charge of a first group composed of 1,668 dual apprenticeship graduates and 246 from the SAA was implemented by the CCIN. Of this group, 1,506 young people have been trained in entrepreneurship and coached in the development of simplified business plans, and 460 have been selected to benefit from seed funding.

Of the 150 projects selected by the Niger Chamber of Commerce and Industry benefiting from a bonus capped at US\$5,000, 144 requests for disbursement of the second tranche were received. For better sharing of the CPA results, a workshop was organized in September 2022 to exchange on this program and to inform young people about this specific opportunity through an exhibition of some of the innovative actions supported by the Project.

Component 3 - Institutional Capacity Strengthening and Monitoring and Evaluation. It aims to support and finance the following critical activities: (i) overall project management; (ii) development of strategies and policy reforms in the TVET sector (both of which are informed by analytical studies financed under the Project); (iii) strengthening of the operational capacities of the Ministry of Education at the central, regional, and district levels; (iv) beneficiary surveys and activities aimed at improving employment promotion and knowledge of existing employment opportunities; and (v) overall monitoring and evaluation (M&E) of the Project.

Steering and coordination by the PCU: Capacity-building for those involved in implementing the project implementation agendas is continuing. The Niger delegation participated in the regional workshop on strengthening apprenticeship systems in the informal economy in Africa to promote quality, innovation and transitions to formality organized by WB in Benin February 22-24, 2023. A mission to monitor the financial execution of the 20 CFM activities was organized by the Internal Auditor and the Administrative and Financial Manager. In addition, the internal auditor and the administrative and financial manager organized a mission to monitor the financial execution of the 20 CFM activities. Although the financial management of the accounts for 2022 and the first quarter of 2023 was assessed as acceptable, it fell short of the amount expected to be spent by March 30, 2023. It was therefore recommended that the PIU strengthen the monitoring of the project's activities in order to improve the project's overall financial performance. And the recruitment of an external auditor is ongoing.

Institutional and technical audit of the FAFPA. An agreement was reached with the Ministry of Vocational and Technical Training during the previous mission in April 2022 to cancel definitively the recruitment of the firm in charge of this audit after two unsuccessful attempts at a call for expressions of interest. To date this activity was canceled.

Monitoring and evaluation : Monitoring and evaluation of activities focuses more on the short- and medium-term effects of project interventions. An action plan for data collection and integration into the Kobo Collect software has been drawn up. PRODEC data integration is underway in the various regions. The project's results monitoring framework is periodically filled in and updated, and all periodic reports are produced on time.

Studies carried out in Environmental and Social Safeguards aspects: As part of the environmental monitoring carried out by the Bureau National d'Etudes Environnementales (BNEE), a partnership agreement has been signed to monitor compliance with environmental and social standards in the implementation of construction/rehabilitation and equipment projects for target, SAA and CFM facilities. BNEE carried out two monitoring missions at national and regional levels. Training on social and environmental aspects for project partners took place in early December 2022. With regard to the operationalization of PRODEC's complaints management mechanism, (i) dispute settlement committees were set up at



communal level as part of the construction/rehabilitation work on the CFMs, with the exception of the Makonloni CFM due to insecurity, and (ii) the population was made aware of the complaints management mechanism and gender-based violence.

Communication. As part of the implementation of PRODEC's communication strategy, the firm hired for this purpose has implemented the communication strategy for the period covering July 2022 to May 2023. Actions covered include, (i) the communication to reinforce the involvement of young people and communities to the agricultural apprenticeship programs and (ii) have a good impact of the seed funds and the CPA. Seven training centers (Niamey 5, Douchi, Guidan Roumdji, Mirriah, Abalak, CFPP of Niamey 4, and SAA of Say) have been equipped with Poulsat communications equipment, as has the SAA in Say.

Risks

Systematic Operations Risk-rating Tool

Risk Category	Rating at Approval	Previous Rating	Current Rating
Political and Governance	--	<input type="checkbox"/> Moderate	<input type="checkbox"/> Moderate
Macroeconomic	--	<input type="checkbox"/> Moderate	<input type="checkbox"/> Moderate
Sector Strategies and Policies	--	<input type="checkbox"/> Moderate	<input type="checkbox"/> Moderate
Technical Design of Project or Program	--	<input type="checkbox"/> Low	<input type="checkbox"/> Low
Institutional Capacity for Implementation and Sustainability	--	<input type="checkbox"/> Moderate	<input type="checkbox"/> Moderate
Fiduciary	--	<input type="checkbox"/> Moderate	<input type="checkbox"/> Moderate
Environment and Social	--	<input type="checkbox"/> Moderate	<input type="checkbox"/> Moderate
Stakeholders	--	<input type="checkbox"/> Moderate	<input type="checkbox"/> Moderate
Other	--	<input type="checkbox"/> Low	<input type="checkbox"/> Low
Overall	--	<input type="checkbox"/> Moderate	<input type="checkbox"/> Moderate

Results

PDO Indicators by Objectives / Outcomes

Improve the effectiveness of formal technical and vocational training				
▶ Youth graduating in the TVET institutions supported by the Project in the Agriculture Sector (Percentage, Custom)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	77.00	65.00
Date	29-Nov-2013	19-Sep-2022	20-Jun-2023	30-Nov-2023



Comments:	Target exceeded. Out of 602 young people enrolled in the Agro sylvo-pastoralism field, 461 (77%) were admitted, in Target exceeded by 18 percent.			
► Youth graduating in the TVET institutions supported by the Project in priority sectors (%) (Percentage, Custom)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	76.00	84.00	65.00
Date	29-Nov-2013	19-Sep-2022	20-Jun-2023	30-Nov-2023
Comments:	Target exceeded. Total graduates as of November 10, 2022, including CFMs was 3,787 (84%) of which 1,706 are g enrolment of 4,522. Target exceeded by 19 points (29 percent). Female beneficiaries represent 46 percent of the tota targeted.			
□ Percentage of graduating females (Percentage, Custom Supplement)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	46.00	46.00	30.00
► Direct project beneficiaries (Number, Custom)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	29,856.00	31,849.00	31,560.00
Date	29-Nov-2013	19-Sep-2022	20-Jun-2023	30-Nov-2023
Comments:	Target exceeded. From the start of the project to date, PRODEC has reached 31,849 direct beneficiaries approxima target. Girls represent 37% of beneficiaries.			
□ Female beneficiaries (Percentage, Custom Supplement)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	39.00	37.00	50.00

Improve the effectiveness of short-term skills development				
► Youth who completed dual apprenticeship programs in the Agriculture Sector (Percentage, Custom)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	76.00	81.00	70.00
Date	30-Nov-2013	19-Sep-2022	20-Jun-2023	30-Nov-2023
Comments:	Target exceeded. A total of 3,300 out-of-school young people completed their training out of 4,071 in training which represents a rate of 81%. The total number of girls is 1577 (48%). Percentage points exceeded by 11 points (15 percent)			



▶ Short-term vocationally trained youth who are employed or self-employed (overall and by sector) (Percentage, Custom)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	51.00	51.00	50.00
Date	30-Apr-2013	19-Sep-2022	20-Jun-2023	30-Nov-2023
Comments:	Target exceeded. Each of the executing agencies conducted an insertion survey in their area of activity. An average insertion rate of 51 percent s was recorded. Percentage points exceeded by 1 point (two percent)			
▶ Out of school youth who completed dual apprenticeship programs (Percentage, Custom)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	90.00	90.00	80.00
Date	30-Apr-2013	19-Sep-2022	20-Jun-2023	30-Nov-2023
Comments:	Overall target exceeded. The number of young people completing the dual apprenticeship program is 6,006 out of a total of 6,467, or 93% of the total. 2,270 Girls completing the FAFPA dual apprenticeship program , representing 37%. Percentage points exceeded by 10 points (12.5 percent).			
☐ Percentage of youth who completed dual apprenticeship programs in the agriculture sector (Percentage, Custom Supplement)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	76.00	81.00	70.00
☐ Percentage of females (Percentage, Custom Supplement)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	34.00	34.00	40.00
▶ Number of beneficiaries trained in entrepreneurship (Number, Custom)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	6,982.00	7,127.00	5,000.00
Date	30-Apr-2013	19-Sep-2022	20-Jun-2023	30-Nov-2023
Comments:	Target exceeded. A complementary group of 157 youth was added In 2022, and 145 young ANPE returnees trained were added in February 2023. The target exceeded by 2,127 (42.5 percent).			

Intermediate Results Indicators by Components

Improving the effectiveness of formal training



▶ Youth enrolled in the TVET institutions supported by the project in the Agriculture Sector (Percentage, Custom)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	33.00	35.00	60.00
Date	10-Apr-2018	19-Sep-2022	20-Jun-2023	30-Nov-2023
Comments:	Of the total number of students enrolled in the three target establishments and the CFMs, 2,601 are in the agricultural sector (sylvo-pastoral activities and rural mechanics), of which 895 (or 34%) are female. 220 young people enrolled in the CFJA in September 2022, include 128 girls.			
□ Percentage female (Percentage, Custom Supplement)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	32.00	32.00	30.00
▶ Youth enrolled in the TVET institutions supported by the Project in priority sectors (of which in the agriculture sector) (%) (Number, Custom)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	7,252.00	7,427.00	8,300.00
Date	30-Apr-2013	19-Sep-2022	20-Jun-2023	30-Nov-2023
Comments:	220 new students enrolled in the CFJA in September 2022, including 128 girls.			
▶ Trainers trained in the 4 priority sectors as a result of project intervention (Number, Custom)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	45.00	161.00	70.00
Date	30-Apr-2013	19-Sep-2022	20-Jun-2023	30-Nov-2023
Comments:	In addition to 41 trainers within the framework of the initial financing, 4 trainers of the CFPP have been trained in mechatronics in 2021. During the second half of 2022, 116 trainers were trained in the agricultural trades.			
▶ Trained youth unemployed for more than two years requalified as a result of project intervention (Number, Custom)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	440.00	480.00	600.00
Date	30-Nov-2017	19-Sep-2022	20-Jun-2023	30-Nov-2023
Comments:	To date, 480 young graduates have benefited from retraining in: the hotel industry (130), construction (190), kitchen energy (80).			



► Tertiary and secondary technical graduates connected with potential employers as a result of project intervention (Number, Custom)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	5,666.00	6,230.00	6,500.00
Date	30-Apr-2013	19-Sep-2022	20-Jun-2023	30-Nov-2023
Comments:	All the 6230 trainees placed by the ANPE will complete their placement by October 30, 2023.			
► Number of private training institutions supported by the Project (Number, Custom)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	16.00	45.00	15.00
Date	01-Dec-2020	19-Sep-2022	20-Jun-2023	30-Nov-2023
Comments:	Target exceeded. This indicator was added when the Project was restructured in December 2020. In 2021, 16 private-sector projects were selected for the private-sector support fund. For the second cohort, 29 applications from women's groups have been selected in 2022.			
► Students benefiting from direct interventions to enhance learning (Number, Corporate)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	19,007.00	19,227.00	17,300.00
Date	28-Oct-2013	19-Sep-2022	20-Jun-2023	30-Nov-2023
Comments:	Target exceeded. This is a new indicator added in the results framework from the 15th restructuring in December 2020. (Dual, CFM, SAA, registered). The cumulative results of this indicator are 19,227 young people aged between 15 and 25, of whom 7,158 are females or (37%) The female beneficiaries are nearly 38 percent above the target.			
□ Students benefiting from direct interventions to enhance learning - Female (Number, Corporate Supplement)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	7,030.00	7,158.00	5,190.00
Strengthening short-term skills development and apprenticeship programs				
► Out of school youth enrolled in dual apprenticeship programs as a result of project intervention (of which in the agriculture sector) (%) (of which females) (%) (Number, Custom)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	7,863.00	8,660.00	9,000.00
Date	30-Apr-2013	19-Sep-2022	20-Jun-2023	30-Nov-2023
Comments:	797 young people registered with SAA from July to October 31, 2022 and 400 young people enrolled in January 2023 will help reach the end target.			



<input type="checkbox"/> Out of school youth enrolled in the dual apprenticeship programs in the agriculture sector (Percentage, Custom Supplement)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	27.00	33.00	50.00
<input type="checkbox"/> Percentage female (Percentage, Custom Supplement)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	31.00	35.00	40.00
<input checked="" type="checkbox"/> Out of school youth completing on-demand technical training as a result of project intervention (Number, Custom)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	923.00	923.00	1,500.00
Date	30-Apr-2013	19-Sep-2022	20-Jun-2023	30-Nov-2023
Comments:	The on-demand training program conducted by FAFPA was finalized in 2019 with an achievement of 923 out of 1500 (target).			
<input checked="" type="checkbox"/> Number of prizewinner youth in the business plan competition (of which females) (Number, Custom)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	595.00	706.00	300.00
Date	30-May-2018	19-Sep-2022	20-Jun-2023	30-Nov-2023
Comments:	Target exceeded. 144 young laureates are beneficiaries of CPA funds and 562 seed funds, including 220 women among the laureates (31%).			
<input type="checkbox"/> Percentage of females (Percentage, Custom Supplement)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	35.00	31.00	40.00
<input checked="" type="checkbox"/> Number of trainers in entrepreneurship programs trained as a result of project intervention (Number, Custom)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	90.00	90.00	90.00
Date	30-Apr-2013	19-Sep-2022	20-Jun-2023	30-Nov-2023
Comments:	Target achieved.			

Institutional capacity strengthening and monitoring and evaluation



► Beneficiary surveys completed to support on-going training improvement (Yes/No, Custom)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	No	Yes	Yes	Yes
Date	30-Apr-2013	19-Sep-2022	20-Jun-2023	31-May-2023
Comments:	Target achieved. Each of the implementing agencies conducted an insertion survey in their area of activity. An average insertion rate of 51% was recorded for all these surveys.			
► Labor Market Observatory Data Collection (Yes/No, Custom)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	No	Yes	Yes	Yes
Date	30-Apr-2013	19-Sep-2022	20-Jun-2023	31-May-2023
Comments:	Target achieved. The project conducted insertion surveys for the beneficiaries of the programs carried out by the 3 implementing agencies (dual apprenticeship, business immersion, entrepreneurship training).			

Performance-Based Conditions

Data on Financial Performance


Disbursements (by loan)

Project	Loan/Credit/TF	Status	Currency	Original	Revised	Cancelled	Disbursed	Undisbursed	% Disbursed
P126049	IDA-D2960	Effective	USD	50.00	50.00	0.00	46.89	0.29	99%
P126049	IDA-H8400	Closed	USD	30.00	30.00	0.00	28.09	0.00	100%

Key Dates (by loan)

Project	Loan/Credit/TF	Status	Approval Date	Signing Date	Effectiveness Date	Orig. Closing Date	Rev. Closing Date
P126049	IDA-D2960	Effective	10-Apr-2018	28-Jun-2018	26-Oct-2018	30-Nov-2022	30-Nov-2023
P126049	IDA-H8400	Closed	30-Apr-2013	07-Jun-2013	28-Oct-2013	30-Nov-2019	30-Nov-2019

Cumulative Disbursements

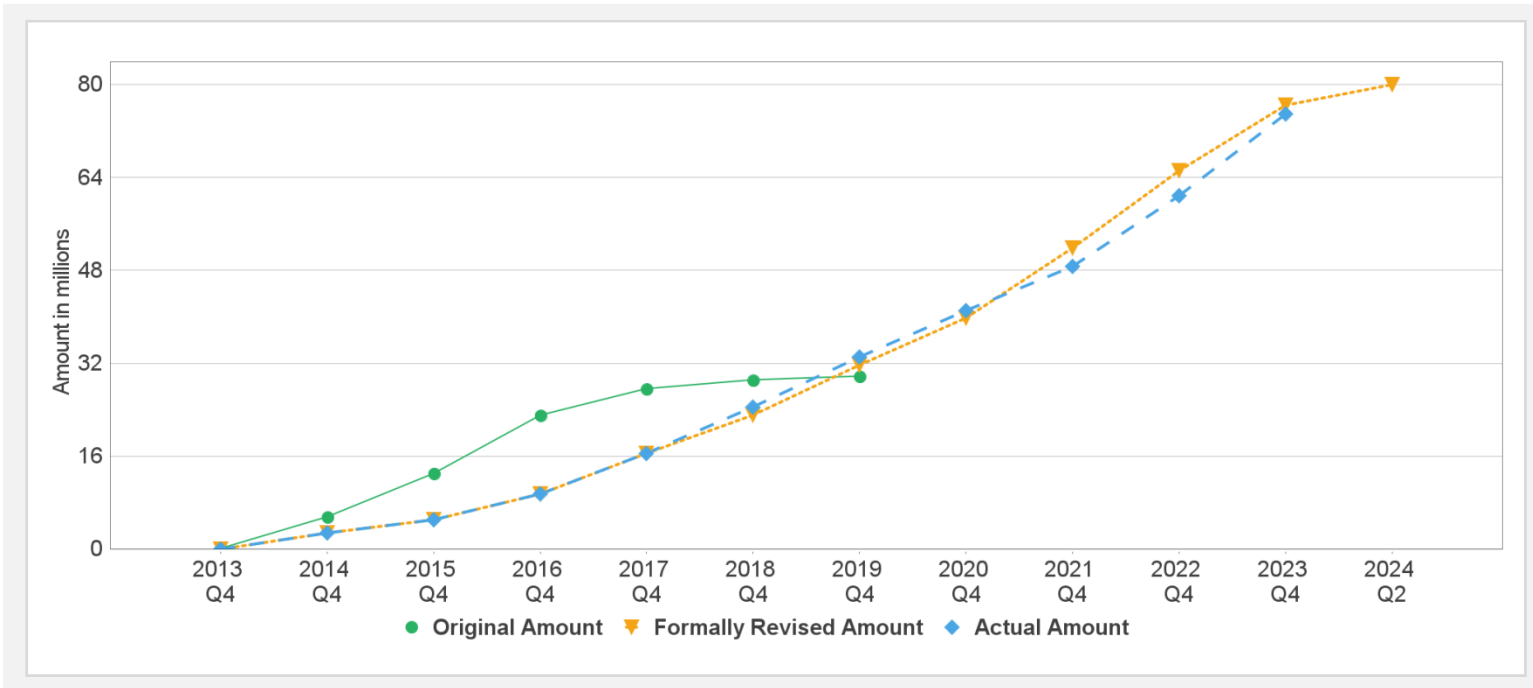

Restructuring History

Level 2 Approved on 18-Dec-2020

Related Project(s)

P163467-Niger Skills Development for Growth Project Additional Financing
