



Citizen-Centric Judicial Modernization and Justice Service Delivery (P155759)

AFRICA | Tanzania | Governance Global Practice |

IBRD/IDA | Investment Project Financing | FY 2016 | Seq No: 1 | ARCHIVED on 01-Nov-2016 | ISR24879 |

Implementing Agencies: Judiciary of Tanzania

Key Dates

Key Project Dates

Bank Approval Date:06-Apr-2016

Effectiveness Date:24-Aug-2016

Planned Mid Term Review Date:--

Actual Mid-Term Review Date:--

Original Closing Date:30-Jun-2021

Revised Closing Date:30-Jun-2021

Project Development Objectives

Project Development Objective (from Project Appraisal Document)

The project development objective is to improve the efficiency and transparency of, and access to, selected citizen-centric justice services.

Has the Project Development Objective been changed since Board Approval of the Project Objective?

No

Components

Name

Component 1: Governance, Organization and Systems Development:(Cost \$18.00 M)

Component 2: Skills Development, Inspection and Performance Management:(Cost \$10.00 M)

Component 3: Access to Justice and Public Trust:(Cost \$37.00 M)

Overall Ratings

Name	Previous Rating	Current Rating
Progress towards achievement of PDO	--	● Moderately Satisfactory
Overall Implementation Progress (IP)	--	● Moderately Satisfactory
Overall Risk Rating	--	● Substantial

Implementation Status and Key Decisions



After project effectiveness in August 2016, the project launch was successfully carried out on September 21, 2016.

The launch event was officiated by the Prime Minister of the United Republic of Tanzania, Honorable Kassim Majaliwa, in the presence of the Chief Justice, Honorable Mohamed Chande Othman, the Minister of Constitution and Legal Affairs, Dr. Mwakyembe, the Deputy Speaker of the Parliament Dr. Tulia Jackson, and other dignitaries including Ambassador Ian Myles of Canada, and Ms. Awa Dabo, Director of UNDP. The launch of the Bank supported Project also involved the launch of the Judiciary Strategic Plan 2016-2020, which forms the basis of the Project. The event also allowed to lay out the foundation stone for the Kibaha Integrated Justice Center.

Agreed Next Steps:

	Actions	Target Achievement Date	Responsibility
1.	Send a draft Project Operational Manual (OM) to the Bank	November 7, 2016	Judiciary
2.	Update the procurement plan	December 31, 2016	Judiciary
3.	Share models of operational manuals from other projects	October 15, 2016	World Bank
4.	Draft a video documentary for comments	November 30, 2016	World Bank
5.	Hire expert for court user survey	December 31, 2016	Judiciary & World Bank

Risks

Systematic Operations Risk-rating Tool

Risk Category	Rating at Approval	Previous Rating	Current Rating
Political and Governance	● Moderate	--	● Moderate
Macroeconomic	● Substantial	--	● Substantial
Sector Strategies and Policies	● Substantial	--	● Substantial
Technical Design of Project or Program	● Moderate	--	● Moderate
Institutional Capacity for Implementation and Sustainability	● Substantial	--	● Substantial
Fiduciary	● Substantial	--	● Substantial
Environment and Social	● Moderate	--	● Moderate
Stakeholders	● High	--	● High
Other	--	--	--
Overall	● Substantial	--	● Substantial

Results

Project Development Objective Indicators

► Citizen Engagement: (Text, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	Court User Survey 2015	--	--	Action taken for achieving and improving trend in citizen-centric justice service delivery



in selected urban and rural areas for poorer and other segments of the society.

Date	10-Nov-2015	--	--	30-Jun-2021
------	-------------	----	----	-------------

► Efficiency: (Number, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	515.00	--	--	350.00
Date	08-Feb-2016	--	--	30-Jun-2021

▲ (i) Percentage reduction in the number of cases older than three years in the court system [Baseline: 5,000 in higher-level courts; EOP: 45 percent reduction] (Number, Custom Breakdown)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	1.00	--	--	0.45
Date	08-Feb-2016	--	--	30-Jun-2021

▲ (ii) Average time it takes from the date of filing to the determination of a case, for (a) Commercial cases [Baseline: 515; EOP: 350]; (b) Family cases [Baseline: 1,650; EOP: 750]; ... (Number, Custom Breakdown)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	515.00	--	--	350.00
Date	08-Feb-2016	--	--	30-Jun-2021

► Transparency/Access: Court decisions published online in courts with requisite infrastructure [Baseline: Less than 1 percent; EOP: More than 10 percent] (Percentage, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	1.00	--	--	10.00
Date	08-Feb-2016	--	--	30-Jun-2021



► Access: (i) Number of beneficiaries of mobile courts and ADR services in selected areas [Baseline: 0; EOP Target 1000 per year, number disaggregated by gender and or type of business and women entrepr (Number, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	--	--	4000.00
Date	08-Feb-2016	--	--	30-Jun-2021

► Access: (ii) Percentage of citizens with closer access to high courts [Baseline: 53; EOP: 65 percent] (Percentage, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	53.00	--	--	65.00
Date	08-Feb-2016	--	--	30-Jun-2021

Overall Comments

Indicators may be updated at mid term review

Intermediate Results Indicators

► E-complaints system established and put to operation (e.g., via Short Message Service (SMS), Whatup, etc.) (Yes/No, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	N	--	--	Y
Date	08-Feb-2016	--	--	30-Jun-2021

Overall Comments



Data on Financial Performance


Disbursements (by loan)

Project	Loan/Credit/TF	Status	Currency	Original	Revised	Cancelled	Disbursed	Undisbursed	Disbursed
P155759	IDA-57780	Effective	XDR	47.10	47.10	0.00	0.36	46.74	1%

Key Dates (by loan)

Project	Loan/Credit/TF	Status	Approval Date	Signing Date	Effectiveness Date	Orig. Closing Date	Rev. Closing Date
P155759	IDA-57780	Effective	06-Apr-2016	28-Jun-2016	24-Aug-2016	30-Jun-2021	30-Jun-2021

Cumulative Disbursements

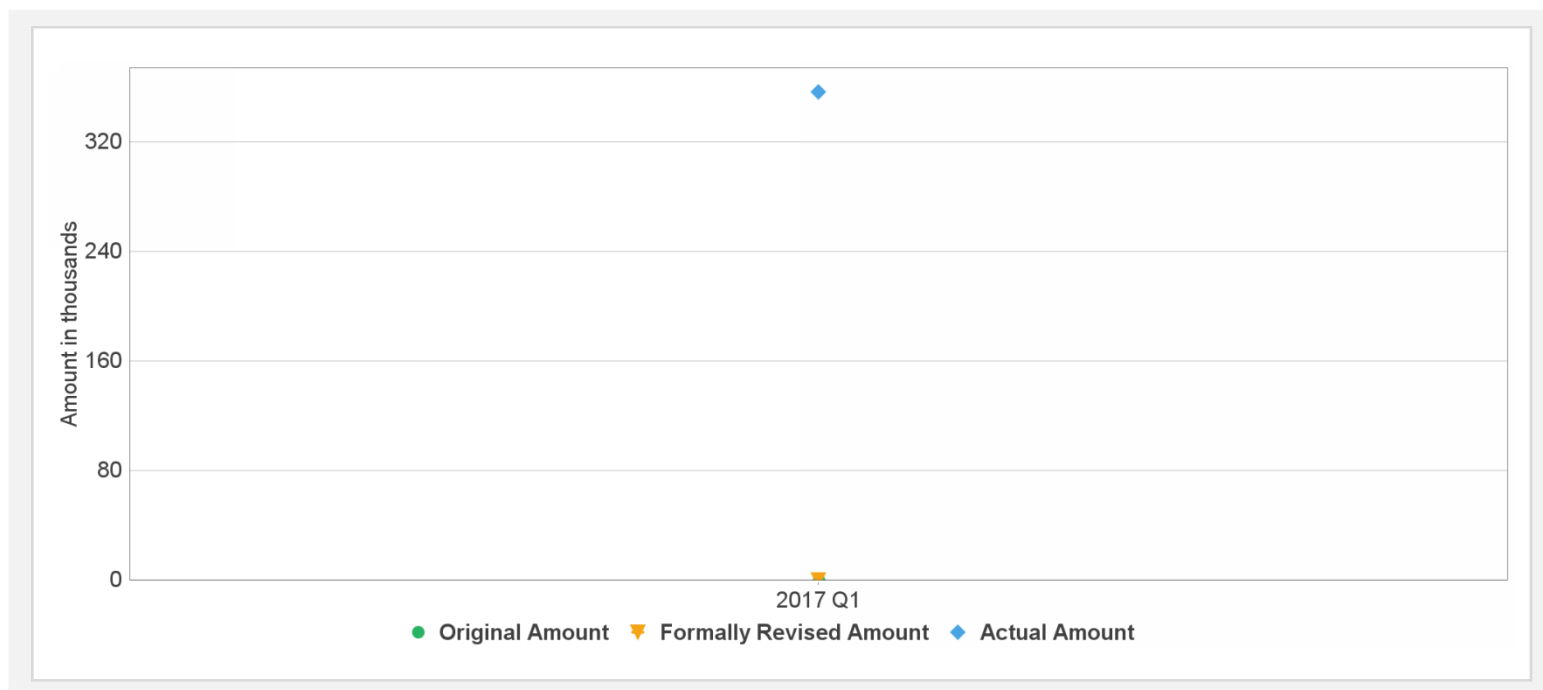

Restructuring History

There has been no restructuring to date.

Related Project(s)



There are no related projects.
