



## Social Protection System Modernization Project (P145171)

EUROPE AND CENTRAL ASIA | Croatia | Social Protection Global Practice |  
IBRD/IDA | Investment Project Financing | FY 2015 | Seq No: 1 | DRAFT | ISR16839 |

Implementing Agencies: Ministry of Social Protection and Youth

### Key Dates

#### Key Project Dates

Board Approval date:19-Sep-2014

Effectiveness Date:24-Dec-2014

Planned Mid Term Review Date:01-Dec-2016

Actual Mid-Term Review Date:--

Original Closing Date:31-Dec-2018

Revised Closing Date:31-Dec-2018

### Project Development Objectives

Project Development Objective (from Project Appraisal Document)

The project aims to improve the efficiency and effectiveness of Croatia's social protection system.

Has the Project Development Objective been changed since Board Approval of the Project Objective?

No

### Components

Name

Improving efficiency and effectiveness of the social protection system:(Cost \$68.00 M)

Investments and TA to support improvements in efficiency and effectiveness of the social protection system:(Cost \$26.00 M)

Project Management Support:(Cost \$0.80 M)

### Overall Ratings

Name	Previous Rating	Current Rating
Progress towards achievement of PDO	--	● Satisfactory
Overall Implementation Progress (IP)	--	● Satisfactory
Overall Risk Rating	--	● Moderate

### Implementation Status and Key Decisions



The project was approved on 19 September, 2014 and signed on 25 September, 2014. Effectiveness is expected by 24 December, 2014.

## Risks

### Systematic Operations Risk-rating Tool

Risk Category	Rating at Approval	Previous Rating	Current Rating
Political and Governance	--	--	● Moderate
Macroeconomic	--	--	● Moderate
Sector Strategies and Policies	--	--	● Moderate
Technical Design of Project or Program	--	--	● Substantial
Institutional Capacity for Implementation and Sustainability	--	--	● Moderate
Fiduciary	--	--	● Moderate
Environment and Social	--	--	● Low
Stakeholders	--	--	● Substantial
Other	--	--	--
Overall	--	--	● Moderate

## Results

### Project Development Objective Indicators



► One Stop Shop: Reduce private costs for social assistance beneficiaries and unemployed by 15% from baseline (of X%,month 2014) (Percentage, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	--	0.00	15.00
Date	01-Jan-2014	--	--	31-Dec-2018

► Central Disability Certification Institute: Percentage of cases certified by IDCPREPD's full-time certifying officers increased from 0% to 90% (Percentage, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	--	0.00	90.00
Date	01-Jan-2014	--	--	31-Dec-2018

► Reduced Error and Fraud: EFC risk-prone programs have strengthened information systems, and oversight and control procedures (Text, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	Piecemeal, partial EFC actions aimed at a limited set of Social Protection Programs	--	Piecemeal, partial EFC actions aimed at a limited set of Social Protection Programs	EFC risk-prone programs have strengthened information systems and oversight and control procedures
Date	01-Jan-2014	--	--	31-Dec-2018

► Deinstitutionalization: Number of vulnerable children and adults moved from institutions to family-type care environments (Number, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	--	174.00	715.00
Date	01-Jan-2014	--	--	31-Dec-2018



► Fiscal Savings realized (Percentage, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	--	0.00	0.50
Date	01-Jan-2014	--	--	31-Dec-2018

Overall Comments

**Intermediate Results Indicators**

► Direct project beneficiaries (Number, Core)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	951690.00	--	951690.00	951690.00
Date	01-Jan-2014	--	--	31-Dec-2018

▲ Female beneficiaries (Percentage, Core Supplement)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	475845.00	--	475845.00	475845.00
Date	01-Jan-2014	--	--	31-Dec-2018

► DLIs 1-4: OSS in place (Text, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	GMB, Child Allowance, non-contributory Mat/Pat allowance and Birth Grants, and Unemployment Benefits administered through different networks	--	GMB, Child Allowance, non-contributory Mat/Pat allowance and Birth Grants, and Unemployment Benefits administered through different networks	GMB, Child Allowance, non-contributory Mat/Pat allowance and Birth Grants, and Unemployment Benefits



				administered through the OSS
Date	01-Jan-2014	--	--	31-Dec-2018

► DLIs 5-6 CDCI operating independently (Text, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	No CDCI	--	CDCI Law adopted by Parliament, confirming establishment of CDCI from 1 January 2015.	CDCI operating independently
Date	01-Jan-2014	--	--	31-Dec-2018

► DLIs 7-10 Reduced Error and Fraud (Text, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	Piecemeal, partial EFC actions aimed at a limited set of Social Protection Programs	--	Piecemeal, partial EFC actions aimed at a limited set of Social Protection Programs	EFC risk-prone programs have strengthened information systems and oversight and control procedures
Date	01-Jan-2014	--	--	31-Dec-2018

► DLIs 11-14: Deinstitutionalization (Number, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	--	174.00	715.00
Date	01-Jan-2014	--	--	31-Dec-2018



► Activation: Statistically assisted profiling introduced (Text, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	No statistically assisted profiling of unemployed	--	No statistically assisted profiling of unemployed	Statistically assisted profiling introduced
Date	01-Jan-2014	--	--	31-Dec-2018

Overall Comments

### Data on Financial Performance


#### Disbursements (by loan)

Project	Loan/Credit/TF	Status	Currency	Original	Revised	Cancelled	Disbursed	Undisbursed	Disbursed
P145171	IBRD-84260	Effective	USD	95.55	95.55	0.00	0.00	95.55	0%

#### Key Dates (by loan)

Project	Loan/Credit/TF	Status	Approval Date	Signing Date	Effectiveness Date	Orig. Closing Date	Rev. Closing Date
P145171	IBRD-84260	Effective	19-Sep-2014	25-Sep-2014	24-Dec-2014	31-Dec-2018	31-Dec-2018

#### Cumulative Disbursements

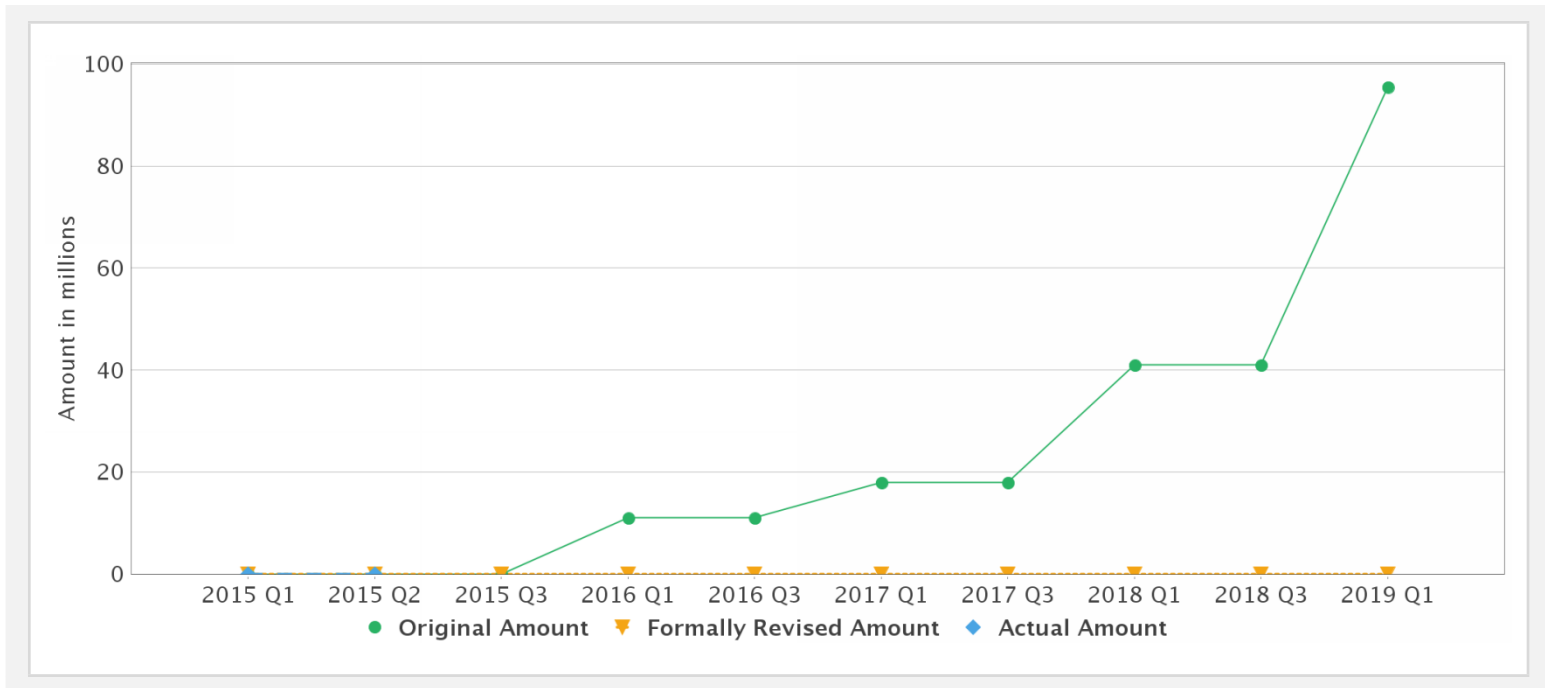

## Restructuring History

There has been no restructuring to date.

## Related Project(s)

There are no related projects.
