



## KYRGYZ REP IMPLEMENTATION OF NSDS (P144874)

EUROPE AND CENTRAL ASIA | Kyrgyz Republic | Governance Global Practice |  
Recipient Executed Activities | Technical Assistance Loan | FY 2015 | Seq No: 2 | ARCHIVED on 22-Dec-2016 | ISR25882 |

Implementing Agencies: National Statistical Committee of the Kyrgyz Republic

### Key Dates

#### Key Project Dates

Bank Approval Date:03-Feb-2015

Effectiveness Date:23-Jun-2015

Original Closing Date:30-Jun-2018

Revised Closing Date:30-Jun-2018

### Project Development Objectives

Project Development Objective (from Project Appraisal Document)

The development objective of the proposed KGSTAT project is to support and facilitate production and dissemination of reliable and timely statistics in a cost-effective manner, in accordance with international standards and in response to user needs, by modernizing and streamlining the processes in the NSC to ensure that it has sufficient resources in terms of human resources, essential tools and infrastructure.

Has the Project Development Objective been changed since Board Approval of the Project Objective?

No

### Components

Name

### Overall Ratings

Name	Previous Rating	Current Rating
Progress towards achievement of PDO	● Satisfactory	● Moderately Satisfactory
Overall Implementation Progress (IP)	● Satisfactory	● Moderately Satisfactory

### Implementation Status and Key Decisions

The **National Statistic Committee of the Kyrgyz Republic (NSC)** continues successfully implementing the project. The Project Management Group has completed several important tasks leading toward contracting the Twinning Partnership (TP) for capacity building and methodological enhancements. The ICT contract was awarded and delivery and installation of equipment in regional statistical offices has been finalized.





## Risks

### Overall Risk Rating

Risk Category	Rating at Approval	Previous Rating	Current Rating
Overall	● Moderate	● Moderate	● Moderate

## Results

### Project Development Objective Indicators

#### ►Statistical Capacity of the state according to the Wolrd Bank Bulletin Board (Amount(USD), Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	84.40	82.20	82.20	86.00
Date	31-Dec-2013	06-May-2016	16-Nov-2016	31-Dec-2019

### Overall Comments

### Intermediate Results Indicators

#### ►Adequate statistical legislation that covers UN fundamental principles of official statistics is in palce and functional. (Text, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	The score of 20 was established based on the U.S. Census Bureau assessment.(Scores range from 0 to 24)	Activities will be conducted under the Twinning partnership. For the current date activities under the component were developed and included in the TOR for twinning partnership.	Activities will be conducted under the Twinning partnership. For the current date activities under the component were developed and included in the TOR for twinning partnership. 3	The score = 22.



			companies have submitted their proposals: JV ICON-Institut Public Sector Consulting Gruppe (Germany), JV Ltd "SoftClub" (Belarus), JV Federal Statistical Office of Germany (Destatis). Expert evaluation process has been started. The tender committee will meet on December 7, 2016 to evaluate applications.	
Date	01-Sep-2015	--	06-Dec-2016	31-Dec-2019

►Mechanisms for effective inter-agency coordination are established and operational. (Text, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	There is no such mechanism.	Initial steps toward establishing such mechanism are being made.	Initial steps toward establishing such mechanism are being made. The Advisory Council (AC) was created to manage the project on January 18, 2016 (the NSC collegium resolution № 6 dated 01.18.2016). Composition and regulation on the AC have been approved. The next meeting of the council is scheduled for December 2016.	The Advisory Council with members of the public and private sectors that advises the NSC, meets regularly and works effectively.
Date	01-Sep-2015	30-Apr-2016	16-Nov-2016	31-Dec-2017

►User satisfaction surveys are conducted regularly, user satisfaction rates have increased by 40% at the end of the project. (Text, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	to be defined.	n/a	NSC improved an official website, in particularly a feedback system has been improved to ensure that users have an option to send their comments and suggestions to the NSC. Survey will be carried	User satisfaction surveys are conducted annually; user satisfaction rates have increased by 40% compared



			out within the terms of reference of twinning partnership.	to the baseline.
Date	01-Oct-2016	30-Apr-2016	07-Dec-2016	31-Dec-2018

►IT capacity for operations is adequate and maintained (Text, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	Practically all IT systems and equipment are outdated.	Contract for ICT equipment is awarded.	Contract for ICT equipment is awarded. Equipment was delivered to the regional statistical offices in September, 2016	IT capacity (hardware and software) for operations is adequate and maintained.
Date	31-Aug-2015	30-Apr-2016	07-Dec-2016	31-Dec-2018

►Printing facility is adequate for production of the NSC publications (Text, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	Printing facility is outdated	RFP was issued, but no satisfactory proposal received. RFP is reissued.	After retendering, a company was selected for the Procurement of printing equipment using International Competitive Bidding. After the contract signed, the company will start delivery of equipment.	Printing facility is adequate for production of NSC publications submitted
Date	01-Sep-2015	30-Apr-2016	07-Dec-2016	29-Dec-2017



► Compliance with internationally accepted standards and classifications (Text, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	Limited compliance with internationally accepted standards and classifications.	n/a	Activities will be conducted under the Twinning partnership. For the current date activities under the component were developed and included in the TOR for twinning partnership. 3 companies have submitted their proposals: JV ICON-Institut Public Sector Consulting Gruppe (Germany), JV Ltd "SoftClub" (Belarus), JV Federal Statistical Office of Germany (Destatis). Expert evaluation process has been started. The tender committee will meet on December 7, 2016 to evaluate applications.	NSC is in full compliance with the internationally accepted standards and classifications
Date	31-Aug-2015	--	06-Dec-2016	31-Dec-2018

► Adoption of the electronic data collection (Text, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	no regular electronic data collection	n/a	NSC has been started to implement CAPI technologies for the Kyrgyz Intergated Households Survey (KIHS), Index of Trust and Tourism Survey. Currently Bishkek (a capital) has been conducting KIHS in CAPI on regular basis, while Chui and Issyk Kul oblasts started implementation in October and November 2016.	Electronic data collection is adopted and used.
Date	31-Aug-2015	--	07-Dec-2016	31-Dec-2018



►Data quality assurance framework and quality assurance is established and functions. (Text, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	there is no state of the art QAF	--	n/a	Data quality assurance framework and quality assurance working group is established and functioning. (Data errors are reduced and regular reviews are conducted).
Date	31-Aug-2015	--	07-Dec-2016	31-Dec-2019

►Establishment and proper updates of statistical registers (Text, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	TBD	n/a	Updates of registers are in ToR of the Twining partnership.	Statistical registers are established and regularly updated.
Date	01-Sep-2016	--	07-Dec-2016	31-Dec-2019

►Improved specialized knowledge of the core staff. (Text, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	there is limited number of staff with sufficient knowledge in areas of census/survey data collection, analysis, evaluation, and dissemination.	n/a	Local trainings on registers and CAPI (in Osh and Issyk-Kul) were delivered according the the local trainings plan	sufficient number of core staff specialized in all areas of census/survey collection data collection, analysis, evaluation, and dissemination
Date	31-Aug-2015	--	07-Dec-2016	31-Dec-2018




►HR management framework established and functions (Text, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	There is no properly functioning HR management framework that includes recruitment, training programs, and performance management.	--	Activities have been developed and included in the TOR for twinning partnership.	Management framework for human resources (including recruitment, training programs, and performance management) is in place and functioning well.
Date	31-Aug-2015	--	07-Dec-2016	31-Dec-2018

## Overall Comments

### Data on Financial Performance

#### Disbursements (by loan)


Project	Loan/Credit/TF	Status	Currency	Original	Revised	Cancelled	Disbursed	Undisbursed	Disbursed
P144874	TF-17862	Effective	USD	2.50	2.50	0.00	1.12	1.38	 45%

#### Key Dates (by loan)

Project	Loan/Credit/TF	Status	Approval Date	Signing Date	Effectiveness Date	Orig. Closing Date	Rev. Closing Date
P144874	TF-17862	Effective	04-Feb-2015	04-Feb-2015	23-Jun-2015	30-Jun-2018	30-Jun-2018

#### Cumulative Disbursements



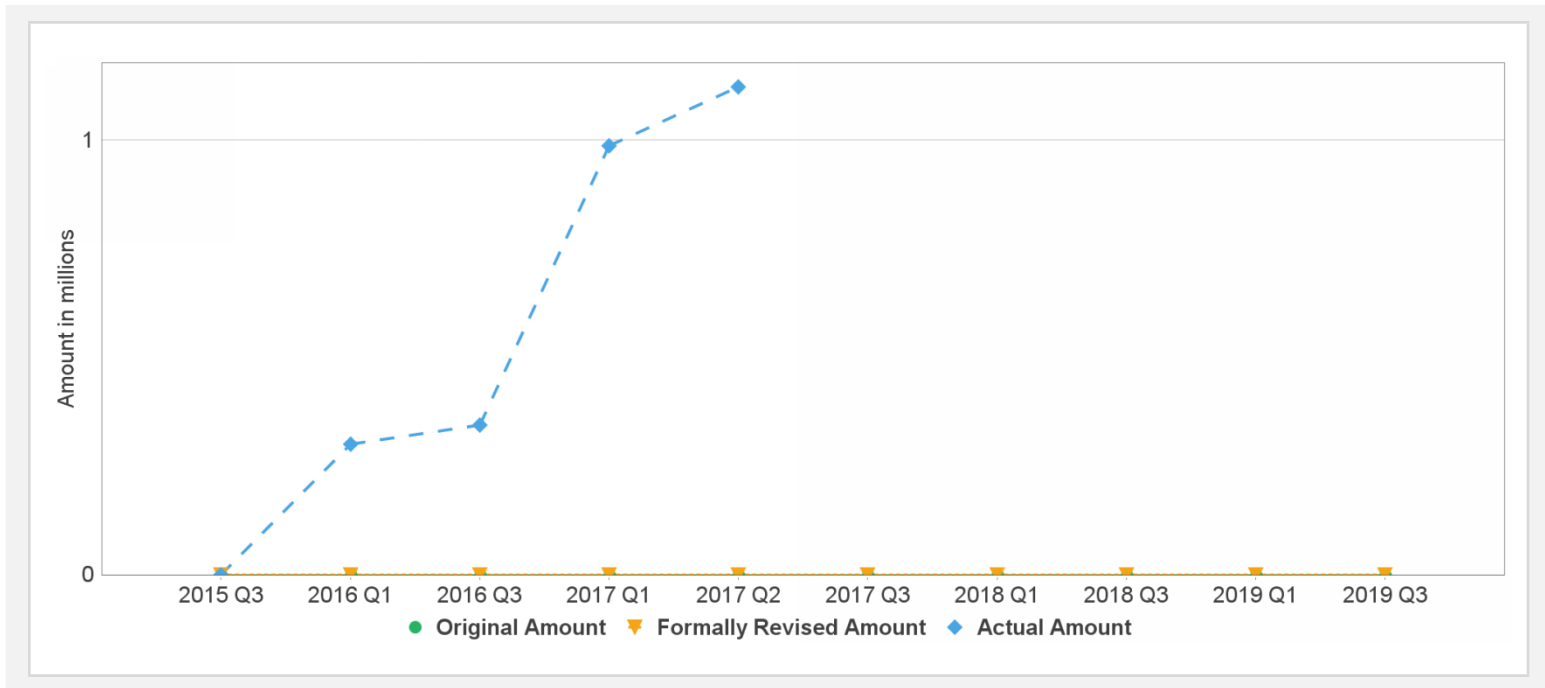

## Restructuring History

There has been no restructuring to date.

## Related Project(s)

There are no related projects.
