



Sahel Women's Empowerment and Demographics Project (P150080)

AFRICA | Western Africa | Health, Nutrition & Population Global Practice |
IBRD/IDA | Investment Project Financing | FY 2015 | Seq No: 2 | ARCHIVED on 14-Sep-2015 | ISR20500 |

Implementing Agencies:

Key Dates

Key Project Dates

Board Approval date:18-Dec-2014

Effectiveness Date:22-May-2015

Planned Mid Term Review Date:14-Jun-2017

Actual Mid-Term Review Date:--

Original Closing Date:30-Jun-2019

Revised Closing Date:31-Dec-2019

Project Development Objectives

Project Development Objective (from Project Appraisal Document)

The development objective is to increase women and adolescent girls' empowerment and their access to quality reproductive, child and maternal health services in selected areas of the participating countries, including the Recipients' territory, and to improve regional knowledge generation and sharing as well as regional capacity and coordination.

Has the Project Development Objective been changed since Board Approval of the Project Objective?

No

Components

Name

Addition of Burkina Faso:(Cost \$16.58 M)

Addition of Burkina Faso:(Cost \$12.52 M)

Addition of Burkina Faso:(Cost \$5.70 M)

Overall Ratings

Name	Previous Rating	Current Rating
Progress towards achievement of PDO	● Satisfactory	● Satisfactory
Overall Implementation Progress (IP)	● Satisfactory	● Satisfactory
Overall Risk Rating	● Substantial	● Substantial



Implementation Status and Key Decisions

The Sahel Women Empowerment and Demographic Dividend regional project (SWEDD) was approved on December 18, 2014, for 5 countries (Chad, Cote d'Ivoire, Mali, Mauritania and Niger) and one regional partner (West African Health Organization or WAHO). Burkina Faso was added through an additional financing, approved on April 23, 2015.

Financing agreements (FAs) with the 7 above-mentioned recipients have been signed. Out of the 7 recipients, 4 have their financing agreement now effective (Chad, Cote d'Ivoire, Mali, and Mauritania). Niger has ratified the FA and should issue a legal opinion. WAHO still has to sign its Subsidiary Agreement with the Economic Community of West African States (ECOWAS) and issue the corresponding legal opinion. It is expected that the financing agreement for Niger and WAHO will be effective by late October 2015. Burkina Faso is the latest recipient included in the project and should be effective by end-September 2015.

Risks

Systematic Operations Risk-rating Tool

Risk Category	Rating at Approval	Previous Rating	Current Rating
Political and Governance	--	● Substantial	● Substantial



Macroeconomic	--	● High	● High
Sector Strategies and Policies	--	● Substantial	● Substantial
Technical Design of Project or Program	--	● High	● High
Institutional Capacity for Implementation and Sustainability	--	● Substantial	● Substantial
Fiduciary	--	● Substantial	● Substantial
Environment and Social	--	● Low	● Low
Stakeholders	--	● Substantial	● Substantial
Other	--	--	--
Overall	--	● Substantial	● Substantial

Results

Project Development Objective Indicators

► 01. Percentage of drop-out in secondary schools among participating adolescent girls (Percentage, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	5.50	5.50	5.50	2.20
Date	22-Oct-2014	--	03-Mar-2015	22-Oct-2018

Comments

Source: Gov education sector reports

► 02. Percentage of participating adolescent girls and women (10-19) with improved knowledge on RMNCHN (Percentage, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	28.50	28.50	28.50	58.50
Date	22-Oct-2014	03-Mar-2015	03-Mar-2015	22-Oct-2018

Comments

Source: DHS-based estimates

► 03. Number of young women (16-19) participating in life-skills or livelihood interventions (Number, Custom)



	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	210000.00
Date	22-Oct-2014	03-Mar-2015	03-Mar-2015	22-Oct-2018

► 04. A regional framework contract for purchasing RMNCHN commodities is in place (Number, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	1.00
Date	22-Oct-2014	03-Mar-2015	03-Mar-2015	22-Oct-2018

► 05. Number of students enrolled in the regional hubs (for retraining as a midwifery faculty) (Number, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	299.00
Date	22-Oct-2014	03-Mar-2015	03-Mar-2015	22-Oct-2018

► 06. Number of countries with a Demographic Dividend observatory which is functional and part of the regional observatory network (Percentage, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	6.00
Date	22-Oct-2014	03-Mar-2015	03-Mar-2015	22-Oct-2018

► 07. Number of completed regional evaluations (related to girls' empowerment and demographic impact) (Number, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	5.00
Date	22-Oct-2014	--	03-Mar-2015	22-Oct-2018



▶ Number of regional-level knowledge sharing events (Number, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	8.00
Date	22-Oct-2014	--	03-Mar-2015	22-Oct-2018

▶ 08. Number of regional-level knowledge sharing events (Number, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	--	--	8.00
Date	10-Dec-2014	--	--	20-Dec-2018

Overall Comments

Intermediate Results Indicators

▶ Percent of test audience who recall seeing or hearing a specific message related to the campaign (Percentage, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	70.00
Date	22-Oct-2014	03-Mar-2015	03-Mar-2015	22-Oct-2018

▶ Percent of test audience who has RMNCHN knowledge (Percentage, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	25.50	25.50	25.50	55.00
Date	22-Oct-2014	--	03-Mar-2015	22-Oct-2018



► Number of girls who benefited from schooling interventions (transportation services, accommodation, food, school supplies, additional courses, UCT or CCT) (Number, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	87900.00
Date	22-Oct-2014	--	03-Mar-2015	22-Oct-2018

► Number of adolescents, women and men who have been reached by SBCC interventions (Number, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	--	--	4400000.00
Date	22-Oct-2014	--	--	22-Oct-2018

► Number of country experiences (component 1.2) that have been peer reviewed by other countries (Number, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	10.00
Date	22-Oct-2014	--	03-Mar-2015	22-Oct-2018

► Number of countries that have adopted a drug regulation consistent with WAHO/WAEMU directives (Number, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	4.00
Date	22-Oct-2014	03-Mar-2015	03-Mar-2015	22-Oct-2018



▶ Number of drug regulation staff that have been trained (Number, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	86.00
Date	22-Oct-2014	03-Mar-2015	03-Mar-2015	22-Oct-2018

▶ Number of labs that have achieved GPCL compliance (Number, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	1.00
Date	22-Oct-2014	03-Mar-2015	03-Mar-2015	22-Oct-2018

▶ Number of countries with a functional logistics management information system (LMIS) (Number, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	6.00
Date	22-Oct-2014	03-Mar-2015	03-Mar-2015	22-Oct-2018

▶ Number of prequalified contraceptive products registered in the 5 countries (Number, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	--	0.00	20.00
Date	22-Oct-2014	--	03-Mar-2015	22-Oct-2018



► Number of individuals who have received training in new midwifery/RMNCH competencies (through new short and longer term training programs) (Number, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	--	0.00	9550.00
Date	22-Oct-2014	--	03-Mar-2015	22-Oct-2018

► Number of regional high-level meetings held for monitoring policies, financial commitment and results linked to demographic dividend (Number, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	8.00
Date	22-Oct-2014	03-Mar-2015	03-Mar-2015	22-Oct-2018

► Number of persons trained on demographic / population analysis at regional level (Number, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	293.00
Date	22-Oct-2014	03-Mar-2015	03-Mar-2015	22-Oct-2018

Overall Comments

Data on Financial Performance

Disbursements (by loan)

Project	Loan/Credit/TF	Status	Currency	Original	Revised	Cancelled	Disbursed	Undisbursed	Disbursed
P150080	IDA-55690	Not Effective	XDR	36.20	36.20	0.00	0.00	36.20	0%
P150080	IDA-55700	Not Effective	XDR	27.10	27.10	0.00	0.00	27.10	0%
P150080	IDA-55710	Not Effective	XDR	13.60	13.60	0.00	0.00	13.60	0%




P150080	IDA-56280	Not Effective	XDR	16.50	16.50	0.00	0.00	16.50	0%
P150080	IDA-D0180	Not Effective	XDR	6.80	6.80	0.00	0.00	6.80	0%
P150080	IDA-D0190	Effective	XDR	10.20	10.20	0.00	0.00	10.20	0%
P150080	IDA-D0200	Effective	XDR	18.10	18.10	0.00	0.00	18.10	0%
P150080	IDA-D0240	Not Effective	XDR	3.40	3.40	0.00	0.00	3.40	0%
P150080	IDA-D0520	Not Effective	XDR	8.30	8.30	0.00	0.00	8.30	0%

Key Dates (by loan)

Project	Loan/Credit/TF	Status	Approval Date	Signing Date	Effectiveness Date	Orig. Closing Date	Rev. Closing Date
P150080	IDA-55690	Not Effective	18-Dec-2014	23-Mar-2015	--	31-Dec-2018	31-Dec-2018
P150080	IDA-55700	Not Effective	18-Dec-2014	03-Apr-2015	--	31-Dec-2018	31-Dec-2018
P150080	IDA-55710	Not Effective	18-Dec-2014	02-Apr-2015	--	30-Jun-2019	30-Jun-2019
P150080	IDA-56280	Not Effective	23-Apr-2015	21-May-2015	--	31-Dec-2019	31-Dec-2019
P150080	IDA-D0180	Not Effective	18-Dec-2014	02-Apr-2015	--	30-Jun-2019	30-Jun-2019
P150080	IDA-D0190	Effective	18-Dec-2014	11-Mar-2015	22-May-2015	31-Dec-2018	31-Dec-2018
P150080	IDA-D0200	Effective	18-Dec-2014	07-Apr-2015	22-May-2015	31-Dec-2018	31-Dec-2018
P150080	IDA-D0240	Not Effective	18-Dec-2014	29-Apr-2015	--	31-Dec-2018	31-Dec-2018
P150080	IDA-D0520	Not Effective	23-Apr-2015	21-May-2015	--	31-Dec-2019	31-Dec-2019

Cumulative Disbursements

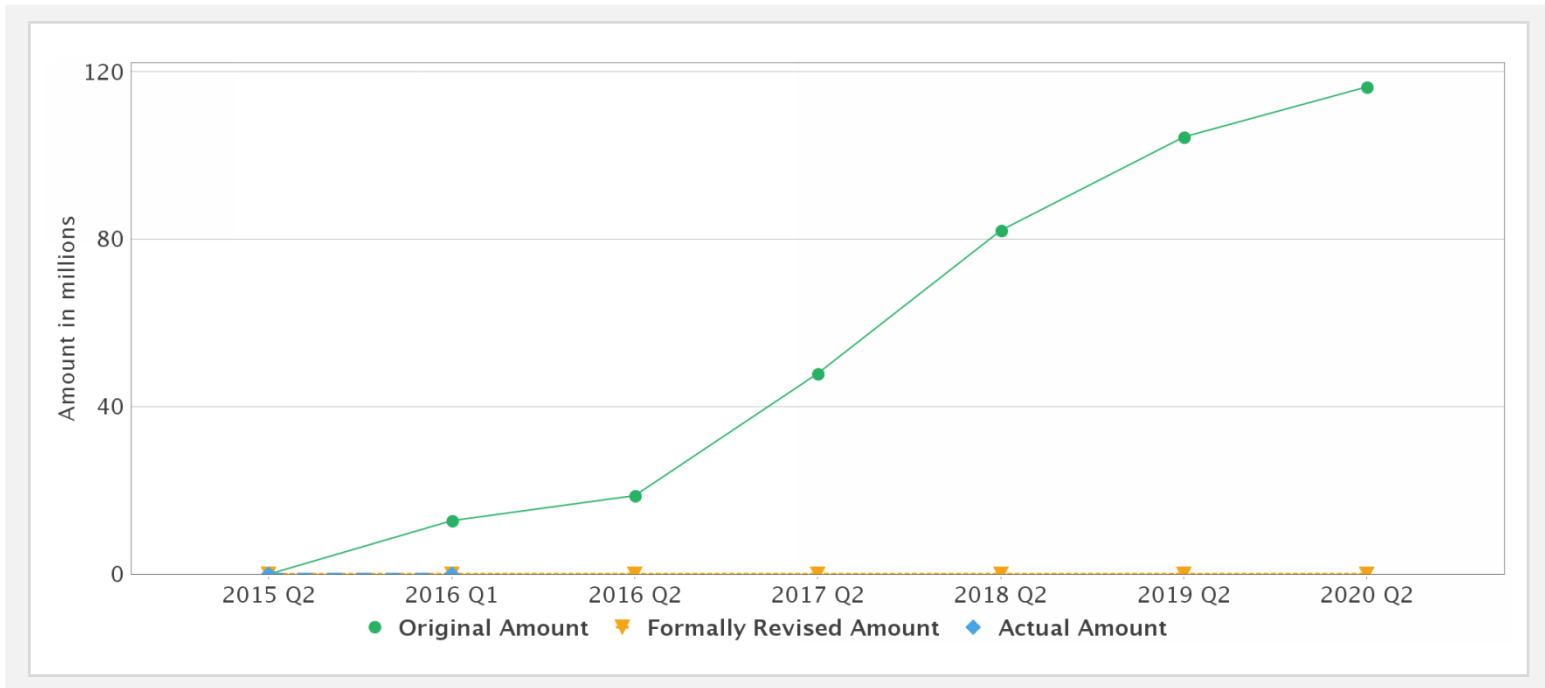

Restructuring History

There has been no restructuring to date.

Related Project(s)

P154549-SWEDD AF for Burkina Faso
