



Republic of Tajikistan - Implementation of the NSDS (P145185)

EUROPE AND CENTRAL ASIA | Tajikistan | Governance Global Practice |
Recipient Executed Activities | Technical Assistance Loan | FY 2015 | Seq No: 2 | ARCHIVED on 27-Sep-2016 | ISR24769 |

Implementing Agencies: Agency on Statistics under the President of the Republic of Tajikistan

Key Dates

Key Project Dates

Bank Approval Date: 26-Sep-2014

Effectiveness Date: 29-May-2015

Original Closing Date: 30-Jun-2018

Revised Closing Date: 30-Jun-2018

Project Development Objectives

Project Development Objective (from Project Appraisal Document)

The overall objective of the proposed project (TAJSTAT-II) is to further improve the capacity of statistical system of Tajikistan to produce and disseminate relevant, reliable and timely statistics in a cost-effective manner that are in line with international standards and will be responsive to user needs. The project will build on the achievements of the previous TAJSTAT project to sustain the progress.

Has the Project Development Objective been changed since Board Approval of the Project Objective?

No

Components

Name

Overall Ratings

Name	Previous Rating	Current Rating
Progress towards achievement of PDO	● Moderately Satisfactory	● Moderately Satisfactory
Overall Implementation Progress (IP)	● Moderately Satisfactory	● Moderately Satisfactory

Implementation Status and Key Decisions

The **Agency for Statistics** continues successfully implementing the project, although progress was somewhat slow at the start of the project but has improved in the past few months. Slow progress was partially a result of the time it took the Agency for Statistics (AS) to form the Project Management Group, i.e. hiring qualified staff.

Resolution of tax issue has also somewhat delayed implementation. The issue is now resolved - the Ministry of Finance has requested the Bank to include relevant taxes into the project budget. It has been decided to restructure the project by amending the Grant Agreement to include these



taxes as eligible expenditures.

The AS invited qualified international consortiums to bid for a Twinning Partnership (TP) contract (to provide capacity building and other consulting services) with the AS. As a result of the bidding process, two international consulting firms, namely GOPA and DevStat passed the technical proposal evaluation stage and their financial proposals were publicly opened. Using the Quality and Cost-Based selection method, DevStat Joint Venture was selected to sign the Twinning Partnership arrangement with. DevStat Joint Venture includes the following entities: Joint Venture DevStat, Serviciosde Consultoria EstadisticaS.Lis (Spain), UDA Consulting (Turkey), Open Data Watching (USA), High School of Economics of Moscow (Russia), CaiCo Consulting (Tajikistan), Statistics Lithuania (Lithuania). On August 18th, 2016 the World Bank issued a "no objection" to contracting the DevStat Joint Venture for the TP contract.

The Bank will continue close cooperation with the Agency for Statistics and supervision of the project implementation.

Risks

Overall Risk Rating

Risk Category	Rating at Approval	Previous Rating	Current Rating
Overall	● Moderate	● Moderate	● Moderate

Results

Project Development Objective Indicators

►Statistical capacity of the state statistical system according to the score published on the World Bank Bulletin Board (Text, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	The overall statistical capacity score is 71 in 2013.	--	--	Score will be 75 at the end of the project.
Date	31-Dec-2013	--	--	30-Jun-2018

Overall Comments

Intermediate Results Indicators



► Strengthened relationships with relevant policy-making bodies through meetings and high-level seminars to improve understanding of the role of official statistics (Text, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	No dedicated seminars or workshops to improve understanding of the role of official statistics	<p>With the view to enhance the role of the state statistics agencies, the interdepartmental working group on the improvement of statistics in various sectors of the economy was created by request of the Prime Minister of the Republic of Tajikistan. In 2015, reportedly five meetings were conducted: high-level seminars with the participation of management staff of key ministries and departments, of which two meetings were held with participation of the Prime Minister of the Republic of Tajikistan. Problems and their solutions were discussed, as well as ways to enhance the role of the state statistics agencies. An "Action Plan for improving the statistics for the period 2016-2021" was prepared and adopted by the Resolution of the Government of Tajikistan from October 29, 2015 (comprised about 80 percent of the NSDS project activities).</p> <p>In addition, during the year there were held various seminars with users and providers of statistical information of various kinds, in particular on methodological explanations of SNA, agriculture, gender statistics, databases, data quality, database</p>	<p>For the 9 months of 2016 one meeting of the interdepartmental working group was held at the level of the heads of key ministries and departments under the leadership of the Prime Minister of RoT. On June 22 of this year, the sixth session of the interdepartmental working group was conducted on the improvement of the statistical accounting, which was attended by representatives of nearly 20 relevant ministries and departments. In addition the meeting of the working group was held in the Agency including two subgroup meetings on the SNA and transition to electronic reporting. On March 29 a donor meeting was conducted with the participation of development partners, ministries and departments of the Republic of Tajikistan in the course of which there were presented the results of the project for 2015, the upcoming labor force survey and improvement of household surveys, improvement the dialogue with the users of statistical information on price statistics, the results of user surveys. Two press conferences with the media were conducted. The conduction of the second donor meeting is scheduled on October 25.</p>	On average 3-5 seminar/meetings to be organized annually



		management, etc.		
Date	30-Jun-2015	--	23-Sep-2016	30-Nov-2018

► Improved implementation of the Law on Statistics. (Text, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	The score 1.5 is established based on the U.S. Census Bureau assessment. (Scores range from 0 to 3)	The project implementation plan for 2016, stipulates amending the Law "On State Statistics" for improving the statistics accounting, taken into account the international standards requirements. The work on the development of a model Law on Statistics is being conducted within the framework for the EECCA countries.	The Model Law on Statistics was discussed on the Conference of European Statisticians which was held in Paris on April 26-29, 2016, with the participation of EECCA and AS, the Agency presented problematic issues on the Model law for discussion, in particular, an explanation of the "official statistics" or "State Statistics". The draft amendments to the Code of Administrative Offences, Articles 515 and 516 (the amount of penal sanctions) was submitted to the Government of RoT.	the score will go up by 1 point over the life of the project.
Date	30-Jun-2015	--	23-Sep-2016	30-Nov-2018

► Optimized data collection programs and redistributed functions between the AS departments with a clear structure (Text, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	The score 1.5 is established based on the U.S. Census Bureau assessment. (Scores range from 0 to 3)	In 2015, the first draft of the Decree of the President of the Republic of Tajikistan on amendments to the Regulation "On the Agency on Statistics under the President of	During this period the updated version of the draft Decree of the President of the Republic of Tajikistan was prepared on amendments to the Regulation "On the	The score will go up by 0.25 on average per year over the life of the project.



		<p>the Republic of Tajikistan” was prepared. This draft was reviewed by the Government of the Republic of Tajikistan and returned for completion. This document considers the issue of redistribution of the workload between the central and regional levels. Similar provisions were also included in the “Action Plan for improving the statistics for the period 2016-2021”</p>	<p>Agency on Statistics under the President of the Republic of Tajikistan”.</p> <p>Currently it is under consideration by the ministries and departments.</p>
--	--	---	---

Date	30-Jun-2015	--	23-Sep-2016	30-Jun-2018
------	-------------	----	-------------	-------------

►Develop professional knowledge and training fro staff to support NSDS objectives. Conduct employee satisfaction survey (Text, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	<p>The score 1.5 is established based on the U.S. Census Bureau assessment. (Scores range from 0 to 3).</p>	<p>In 2015 the training center of AS was restored. Since then trainings for mid-level and junior staff are conducted twice a week. Training seminars also conducted for leaders of the NSDS subcomponents. The topic was devoted to the preparation of terms of reference for each sub-component within the framework of twining partnership. The staff satisfaction questionnaire has been prepared.</p>	<p>In February 2016 the user survey was conducted results of which are published on the AS website and discussed at a donor meeting which was held in the AS on March 29, 2016. The plan of action is prepared on the suggestions presented from the users of statistics, including the Government of Tajikistan on statistical improvement.</p> <p>The employee satisfaction survey is under preparation.</p> <p>The specialists of the AS are learning the English and Russian languages (more than 100 employees) within the framework of the Project. The equipment has been purchased for Training Center of the AS and an electronic library.</p>	<p>The score will go up by 0.25 on average per year over the life of the project.</p>



			The training of the middle and junior staff of the AS is conducted two times a week in the Training Center.	
Date	30-Jun-2015	--	23-Sep-2016	30-Jun-2018

►AS core staff has obtained and uses latest methodological skills in classification, standards, sampling and seasonal adjustments (Text, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	The score 1.5 is established based on the U.S. Census Bureau assessment. (Scores range from 0 to 3).	In 2015, the AS approved the National Classification of Goods and Services based on the International Classification of Goods and Services. In 2015, based on the statistical form PD-1 (RUT) "Operating Report" the data at the level of the city of Dushanbe were collected. The main purpose of data collection under this classifier was for the AS to develop "Resources and Use Table". The work on transition to the 2008 SNA has started. Specialists of the AS compiled a sample for LFS and the seasonal adjustment program which are used by sector departments. The terms of reference for hiring an international consultant on the development of skills for the execution of seasonal adjustment, their use for adjusting data on production prices has been prepared. The Regulation and composition of the Working Group under the Agency for Statistics under the	The training for the regional statistical bodies on the methodology of the new statistical form 1-PD (TRU) "Report on production activity" for the table "Resources Use" of SNA is conducted during period of 2016. Moreover the working group on the transition to the environmental-economic accounts system is created. The draft Model Waste Classifier of the CIS Statistical Committee of the CIS statistics services has been reviewed. The National Classifier of sectors of the economy (SNA 2008) has been also developed.	The score will go up by 0.25 on average per year over the life of the project.



			President of the Republic of Tajikistan has been prepared to review opportunities to reduce data collection program, including reduction of frequency, sample size and questions in order to exclude unnecessary, outdated works.	
Date	30-Jun-2015	--	--	30-May-2018

►Data quality assurance framework and quality assurance working group are established and functioning (Text, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	There is no data quality assurance group.	On the basis of the elaborated Regulation for the Agency on Statistics under the President of the Republic of Tajikistan to review opportunities to reduce data collection program, including reduction of frequency, sample size and questions in order to exclude unnecessary, outdated works, it is planned to create a Working Group to work on the quality of data in 2016.	AS plans to attract the Working Group to work on data quality in 2016	Fully functioning data quality assurance framework or working group
Date	30-Jun-2015	--	23-Sep-2016	30-Jun-2018

►Improved quality, access, and use of poverty and employment data through improvement to and use of the HBS and LFS (Text, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	No poverty rate has been published since 2009 or LFS since 2009.	Starting from 2015, specialists of AS independently evaluate the level of poverty and food poverty based on the HBS data. It is expected that in 2016 (01 July) additional HBS modules (in	The annual and quarterly data on the poverty level have been assessed. The new questionnaire on the labor force survey, taking into account the standards of the 19th "MKCT" (abbreviation is	2016: Poverty rates reported in a quarterly moving average. 2018: Unemployment rates (LFS) reported in a



particular, labor, health, education and social protection) will be launched.

in Russian) is prepared and in July and August, the survey was examined. Currently data is being processed: As part of the HBS the survey was conducted on the tobacco use in the Republic of Tajikistan with the support of the SESTRIC. Currently data is being analyzed including publication of results.

quarterly moving average

Date	30-Jun-2015	--	23-Sep-2016	30-Jun-2018
------	-------------	----	-------------	-------------

► Improve quality, access, and use of gender disaggregated data (Text, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	<p>2013-14:</p> <p>Limited gender-disaggregated statistics, mainly LFS 2009, LSMS 2009, DHS 2012, Child Labor 2013</p>	<p>Within the framework of the project "Support to the statistical capacity to build and analyze disaggregated data on gender" (FAO UN) a round table and a national seminar were conducted, as a result of which the "Guidelines for gender statistics in agriculture for the countries of Central Asia" and "National gender profile of Tajikistan" were developed. It is planned to include into the list the recommended indicators and data on Census of Agriculture (2013).</p>	<p>The materials on the results of the project "Support to statistical potential on formation and analysis of disaggregated data on the gender aspect were prepared in the final workshop", which was held in Istanbul. Disaggregated data on the gender aspects were obtained in the context of the land availability by the regions, type of livestock, etc. based on the agricultural census. The collection on gender indicators dehkan farms has been prepared. It is planned to prepare a new project for the next 2 years on the gender aspect. In the section "Gender statistics" of the AS website the new page "Women Entrepreneurs" is created with the data of 2016 by regions on the newly created, re-registered, liquidated and current private entrepreneurs – women.</p>	<p>2016: The list of gender-disaggregated indicator increased by 10% 2018: The list of gender-disaggregated indicator increased by 10% compared to 2016.</p>



Date	30-Jun-2015	--	23-Sep-2016	30-Jun-2018
------	-------------	----	-------------	-------------

► Improve statistical reporting forms and prepare for "electronic reporting" to reduce burden on respondents (Text, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	Number of current reporting forms in a year:	<p>On the pilot basis there were introduced "electronic reporting" on Labour Statistics (monthly) of statistical form 1-T "Report on labor" and "Labour Movement Report (quarterly)) from July 1, 2015 in Dushanbe. Later the coverage areas was extended and included the districts of Vahdat, Rudaki, Hissar, Tursunzoda. From February 2016 it is expected to introduce the electronic forms on the industry statistics under the Report 1-P (urgent), reports on trade and services, construction and other.</p>	<p>On April 21, 2016 in the Agency on Statistics the presentation on the transition to a monthly electronic reporting for industry decision-makers in Dushanbe industry was conducted.</p> <p>It was attended by managers, accountants and economists of about 50 industry enterprises of Dushanbe. From May 1, 2016, industrial enterprises of Dushanbe are presenting monthly statistical report 1 industry in electronic form.</p> <p>According to the information, 4155 enterprises presented the electronic reporting on the labor for February 2016, which is 77.2% of the total number of reporting companies. In order to accelerate work on the transition to electronic reporting, the fiber-optic line is connected to the Main Department of the Agency on Statistics in Dushanbe, regions and RRS as well as the local statistical authorities are connected to the Internet via ADSL within the framework of the Project.</p>	<p>Reduce the respondent burden by 10 percent by the end of second year of project implementation; Reduce the respondent burden by another 10 percent by end of implementation period.</p>



In addition the tablets which were used for data collection during listing and LFS were purchased and will be used in future for surveys and it was the first step to the transition from manual information collection to the electronic.

Date	30-Jun-2015	--	--	30-Jun-2018
------	-------------	----	----	-------------

►Improved tracking of user feedback and higher user satisfaction (Text, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	User satisfaction surveys are introduced.	The questionnaire has been prepared; a program for conducting surveys of user satisfaction electronically is also prepared. The survey will be held in January 2016.	In February 2016 the user survey was conducted results of which are published on the AS website and discussed at a donor meeting held in the AS on March 29, 2016. The plan of action is prepared on the suggestions from the users of statistics, including from the Government of Tajikistan on statistical improvement.	User satisfaction surveys conducted at least annually. User satisfaction rates have increased by 20% at the end of the project.
Date	30-Jun-2015	--	23-Sep-2016	30-Jun-2018

►Develop integrated and harmonized statistical information sources for NSS and standards for exchange of statistical data (SDMX) (Text, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	Integrated and harmonized statistical information exchange does not exist.	It is planned to start working on the SDMX in 2016.	It is scheduled for the second half of 2016	The SDMX is implemented.
Date	30-Jun-2015	--	30-Jun-2016	30-Jun-2018



►Organize training and workshops for users of statistics and establish feedback mechanism to measure satisfaction with disseminated information (Text, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	User-friendly feedback system does not exist	<p>During the year five meetings were conducted - high-level seminars with the participation of management staff of key ministries and departments. Two meetings were held with the participation of Prime Minister of the Republic of Tajikistan. The problems and their solutions have been discussed, as well as the enhancing role of the state statistics agencies. In addition, during the year there were held various seminars with users and providers of statistical information of various kinds, in particular on methodological explanations of SNA, agriculture, gender statistics, databases, data quality, database management, etc. The feedback mechanism has been created on the AS website as well as the article were issued in the local newspaper about the misinterpretation of statistical data. The press center of the AS has been operating since 2014</p>	<p>For the 9 months of 2016 one meeting of the interdepartmental working group was held at the level of the heads of key ministries and departments under the leadership of the Prime Minister of RoT. On June 22 this year, the sixth session of the interdepartmental working group was conducted on the improvement of the statistical accounting, which was attended by representatives of nearly 20 relevant ministries and departments. In addition the meeting of the working group was held in the Agency including two subgroup meetings on the SNA and the transition to electronic reporting. On March 29 a donor meeting was conducted with the participation of development partners, ministries and departments of the Republic of Tajikistan in the course of which there were presented the results of the project for 2015, the upcoming labour force survey and improvement of household surveys, improving the dialogue with the users of statistical information on price statistics, the results of user surveys. Two press conferences with the media were conducted. The conduction of the second donor meeting is scheduled on October 25.</p>	On average 2-3 trainings/works hops to be held every year.



Date	30-Jun-2015	--	23-Sep-2016	30-Jun-2018
------	-------------	----	-------------	-------------

► Improved dissemination and access to statistics, metadata and quality reports according to the SDDS of IMF standards (Text, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	No reporting and dissemination is done according to IMF SDDS	The terms of reference for the International Monetary Fund was prepared covering the methodological assistance on the transition to the SDDS, as well as the calculation of the quarterly national accounts and price indices. The IMF provided technical assistance to the AS on the translation of Metadata for 2014 into English to be posted on the IMF website.	It is scheduled for the second half of 2016.	2016: Adopt and implement the steps to fully comply with the IMF's SDDS standards. 2018: Fully comply with the IMF's SDDS standards.
Date	30-Jun-2015	--	30-Jun-2016	30-Jun-2018

► HBS DDI produced and NADA server covering all AS's surveys micro- and metadata is available for use by the AS staff (Text, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	ADP trainings held, most surveys documented, however, there is no functional NADA server/system and DDI-standard documentation is not included in the lifecycle of every survey	Training was conducted to the AS specialists on the DDI development under the ADP Program and NADA system. The equipment necessary for the implementation of the system was included into the procurement plan. The	It is scheduled for the second half of 2016	HBS DDI produced and NADA server covering all AS's surveys micro- and metadata is available for use by the AS staff



			corresponding order of the AS management was issued that identified persons responsible for the implementation of the ADP program NADA system.	
Date	30-Jun-2015	--	30-Jun-2016	30-Jun-2018

►IT capacity (soft ware and hardware) for operations, printing facility and other equipment are adequate and maintained (Text, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	Current state of the IT capacity needs improvement	Necessary equipment to upgrade existing servers of the AS was purchased under the Project (hard drives, RAM and CPU). The purchase of computer equipment, printer, small offset printing equipment for the AS and the regional statistical offices is under the final stage.	The project funded equipment for MCC AS printing offices, head departments of statistics in Dushanbe city, GBAO, Khatlon and Sogd regions has been procured. The tenders are conducted and equipment (computers, printers, servers, etc) are procured for the statistical system as well as for the National University (Department of Statistics), Mountain College of the Ministry of Industry and New Technologies, Statistical college of Vahdat town and NIGIM. The GIS (geographical information systems) software for mapping needed for researches and forthcoming population census and housing fund has also been purchased.	Modern and adequate IT environment established, printing and other equipment are up-to-date.
Date	30-Jun-2015	--	23-Sep-2016	30-Jun-2018




▶Automated database processing and reporting are established (Text, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	No automated database processing and reporting.	Electronic data processing program on agricultural statistics (form 29-agr), 1-TV-monthly - for labor, 1-P-urgent - on the industry has been prepared. This work will continue in 2016.	The innovations have been introduced into the form 1-P for electronic data processing. Within the frame of the project the output tables on agricultural census on the basis of newly developed software have been developed and formed. The register of agricultural enterprises and other farms was prepared for receiving the electronic data as well as a new register of dehkan farms on the basis of agriculture census of 2013 was developed.	2016: Prepare automated database processing and reporting. 2018: Implement automated database processing and reporting.
Date	30-Jun-2015	--	--	30-Jun-2018

Overall Comments

Data on Financial Performance


Disbursements (by loan)

Project	Loan/Credit/TF	Status	Currency	Original	Revised	Cancelled	Disbursed	Undisbursed	Disbursed
P145185	TF-17852	Effective	USD	2.50	2.50	0.00	0.61	1.89	 24%

Key Dates (by loan)

Project	Loan/Credit/TF	Status	Approval Date	Signing Date	Effectiveness Date	Orig. Closing Date	Rev. Closing Date
P145185	TF-17852	Effective	26-Sep-2014	23-Oct-2014	29-May-2015	30-Jun-2018	30-Jun-2018

Cumulative Disbursements

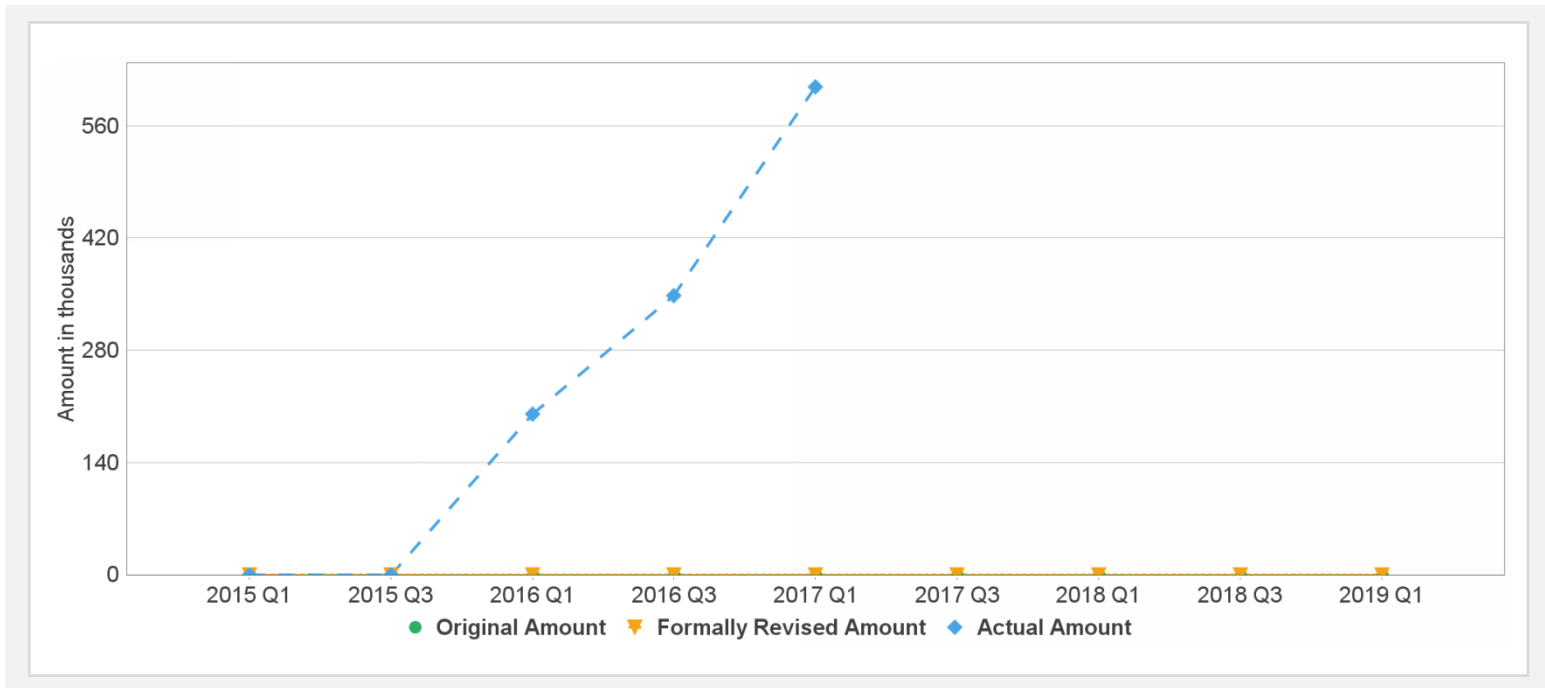

Restructuring History

There has been no restructuring to date.

Related Project(s)

There are no related projects.
