



Jharkhand Opportunities for Harnessing Rural Growth Project (P158798)

SOUTH ASIA | India | Agriculture Global Practice |
IBRD/IDA | Investment Project Financing | FY 2017 | Seq No: 1 | ARCHIVED on 10-Oct-2017 | ISR29603 |

Implementing Agencies: Department of Economic Affairs, Ministry of Finance, Government of India, Department of Rural Development, Government of Jharkhand

Key Dates

Key Project Dates

Bank Approval Date:26-May-2017

Effectiveness Date:04-Sep-2017

Planned Mid Term Review Date:30-Jun-2020

Actual Mid-Term Review Date:--

Original Closing Date:30-Jun-2023

Revised Closing Date:30-Jun-2023

Project Development Objectives

Project Development Objective (from Project Appraisal Document)

The PDO is to enhance and diversify household income in select farm and non-farm sectors for targeted beneficiaries in project areas.

Has the Project Development Objective been changed since Board Approval of the Project Objective?

No

Components

Name

Diversified and Resilient Production and Value Addition:(Cost \$110.72 M)

Promoting Market Access, Skill Development and Pro-Poor Finance Systems:(Cost \$13.46 M)

Project and Knowledge Management:(Cost \$18.82 M)

Overall Ratings

| Name | Previous Rating | Current Rating |
|--------------------------------------|-----------------|----------------|
| Progress towards achievement of PDO | -- | ● Satisfactory |
| Overall Implementation Progress (IP) | -- | ● Satisfactory |
| Overall Risk Rating | -- | ● Moderate |

Implementation Status and Key Decisions



The Project was approved by the World Bank Board on May 26, 2017 and recently became effective on September 4, 2017.

Risks

Systematic Operations Risk-rating Tool

| Risk Category | Rating at Approval | Previous Rating | Current Rating |
|--|--------------------|-----------------|----------------|
| Political and Governance | ● Low | -- | ● Low |
| Macroeconomic | ● Low | -- | ● Low |
| Sector Strategies and Policies | ● Low | -- | ● Low |
| Technical Design of Project or Program | ● Substantial | -- | ● Substantial |
| Institutional Capacity for Implementation and Sustainability | ● Substantial | -- | ● Substantial |
| Fiduciary | ● Moderate | -- | ● Moderate |
| Environment and Social | ● Moderate | -- | ● Moderate |
| Stakeholders | ● Moderate | -- | ● Moderate |
| Other | ● Low | -- | ● Low |
| Overall | ● Moderate | -- | ● Moderate |

Results

Project Development Objective Indicators

► Percent increase in average annual household income (real) of the targeted households (Percentage, Custom)

| | Baseline | Actual (Previous) | Actual (Current) | End Target |
|-------|-------------|-------------------|------------------|-------------|
| Value | 0.00 | -- | 0.00 | 50.00 |
| Date | 02-Oct-2017 | -- | 01-Oct-2017 | 30-Jun-2023 |

► Percent increase in the proportion of income (real) from select livelihoods sources (Percentage, Custom)

| | Baseline | Actual (Previous) | Actual (Current) | End Target |
|-------|-------------|-------------------|------------------|-------------|
| Value | 0.00 | -- | 0.00 | 70.00 |
| Date | 02-Oct-2017 | -- | 01-Oct-2017 | 30-Jun-2023 |



► Number of project beneficiaries that belong to SC/ST categories (Number, Custom)

| | Baseline | Actual (Previous) | Actual (Current) | End Target |
|-------|-------------|-------------------|------------------|-------------|
| Value | 0.00 | -- | 0.00 | 100,000.00 |
| Date | 02-Oct-2017 | -- | 01-Oct-2017 | 30-Jun-2023 |

▲ Number of project beneficiaries that belong to SC/ST categories - female (Number, Custom Breakdown)

| | Baseline | Actual (Previous) | Actual (Current) | End Target |
|-------|-------------|-------------------|------------------|-------------|
| Value | 0.00 | -- | 0.00 | 70,000.00 |
| Date | 02-Oct-2017 | -- | 01-Oct-2017 | 30-Jun-2023 |

► Farmers reached with agricultural assets or services (Number, Custom)

| | Baseline | Actual (Previous) | Actual (Current) | End Target |
|-------|-------------|-------------------|------------------|-------------|
| Value | 0.00 | -- | 0.00 | 200,000.00 |
| Date | 01-Oct-2017 | -- | 01-Oct-2017 | 30-Jun-2023 |

▲ Farmers reached with agricultural assets or services - female (Number, Custom Breakdown)



| | Baseline | Actual (Previous) | Actual (Current) | End Target |
|-------|-------------|-------------------|------------------|-------------|
| Value | 0.00 | -- | 0.00 | 140,000.00 |
| Date | 02-Oct-2017 | -- | 01-Oct-2017 | 30-Jun-2023 |

Overall Comments

Intermediate Results Indicators

► Percent of Producer Groups that have been assessed as grade A (Percentage, Custom)

| | Baseline | Actual (Previous) | Actual (Current) | End Target |
|-------|-------------|-------------------|------------------|-------------|
| Value | 0.00 | -- | -- | 60.00 |
| Date | 02-Oct-2017 | -- | -- | 30-Jun-2023 |

► Percent of project-supported Producer Organizations that are viable and sustainable (Percentage, Custom)

| | Baseline | Actual (Previous) | Actual (Current) | End Target |
|-------|-------------|-------------------|------------------|-------------|
| Value | 0.00 | -- | -- | 50.00 |
| Date | 02-Oct-2017 | -- | -- | 30-Jun-2023 |

► Farmers adopting improved agricultural technology (Number, Corporate)

| | Baseline | Actual (Previous) | Actual (Current) | End Target |
|-------|-------------|-------------------|------------------|-------------|
| Value | 0.00 | -- | -- | 160,000.00 |
| Date | 02-Oct-2017 | -- | -- | 30-Jun-2023 |



▴ Clients who adopted an improved agr. technology promoted by project – female (Number, Custom Breakdown)

| | Baseline | Actual (Previous) | Actual (Current) | End Target |
|-------|-------------|-------------------|------------------|-------------|
| Value | 0.00 | -- | -- | 112,000.00 |
| Date | 02-Oct-2017 | -- | -- | 30-Jun-2023 |

▴ Percent increase in the sale volume of select HVA crops of targeted households (Percentage, Custom)

| | Baseline | Actual (Previous) | Actual (Current) | End Target |
|-------|-------------|-------------------|------------------|-------------|
| Value | 0.00 | -- | -- | 50.00 |
| Date | 02-Oct-2017 | -- | -- | 30-Jun-2023 |

▴ Percent increase in the sale volume of select livestock produce (Percentage, Custom)

| | Baseline | Actual (Previous) | Actual (Current) | End Target |
|-------|-------------|-------------------|------------------|-------------|
| Value | 0.00 | -- | -- | 50.00 |
| Date | 02-Oct-2017 | -- | -- | 30-Jun-2023 |

▴ Percent increase in the sale volume of select fish of the targeted households (Percentage, Custom)

| | Baseline | Actual (Previous) | Actual (Current) | End Target |
|-------|-------------|-------------------|------------------|-------------|
| Value | 0.00 | -- | -- | 50.00 |
| Date | 02-Oct-2017 | -- | -- | 30-Jun-2023 |



► Percent increase in sale volume of select NTFPs of the targeted households (Percentage, Custom)

| | Baseline | Actual (Previous) | Actual (Current) | End Target |
|-------|-------------|-------------------|------------------|-------------|
| Value | 0.00 | -- | -- | 50.00 |
| Date | 02-Oct-2017 | -- | -- | 30-Jun-2023 |

► Area provided with irrigation or drainage services (Hectare(Ha), Custom)

| | Baseline | Actual (Previous) | Actual (Current) | End Target |
|-------|-------------|-------------------|------------------|-------------|
| Value | 0.00 | -- | -- | 18,000.00 |
| Date | 02-Oct-2017 | -- | -- | 30-Jun-2023 |

► Proportion of total production sold by targeted households through producer collectives (Percentage, Custom)

| | Baseline | Actual (Previous) | Actual (Current) | End Target |
|-------|-------------|-------------------|------------------|-------------|
| Value | 0.00 | -- | -- | 50.00 |
| Date | 02-Oct-2017 | -- | -- | 30-Jun-2023 |

► Number of beneficiaries reached with financial services (Number, Custom)

| | Baseline | Actual (Previous) | Actual (Current) | End Target |
|-------|-------------|-------------------|------------------|-------------|
| Value | 0.00 | -- | -- | 150,000.00 |
| Date | 02-Oct-2017 | -- | -- | 30-Jun-2023 |



► Number of community service providers trained and earning at least Rs 3,500 per month through user fees in the last two years (Number, Custom)

| | Baseline | Actual (Previous) | Actual (Current) | End Target |
|-------|-------------|-------------------|------------------|-------------|
| Value | 0.00 | -- | -- | 11,000.00 |
| Date | 02-Oct-2017 | -- | -- | 30-Jun-2023 |

► Number of entrepreneurs trained (Number, Custom)

| | Baseline | Actual (Previous) | Actual (Current) | End Target |
|-------|-------------|-------------------|------------------|-------------|
| Value | 0.00 | -- | -- | 3,000.00 |
| Date | 02-Oct-2017 | -- | -- | 30-Jun-2023 |

► Percent of registered grievances addressed (Percentage, Custom)

| | Baseline | Actual (Previous) | Actual (Current) | End Target |
|-------|-------------|-------------------|------------------|-------------|
| Value | 0.00 | -- | -- | 100.00 |
| Date | 02-Oct-2017 | -- | -- | 30-Jun-2023 |

► Proportion of project investments mobilized through convergence (Percentage, Custom)

| | Baseline | Actual (Previous) | Actual (Current) | End Target |
|-------|-------------|-------------------|------------------|-------------|
| Value | 0.00 | -- | -- | 20.00 |
| Date | 02-Oct-2017 | -- | -- | 30-Jun-2023 |



► Percent increase in average dietary diversity score in target households (Percentage, Custom)

| | Baseline | Actual (Previous) | Actual (Current) | End Target |
|-------|-------------|-------------------|------------------|-------------|
| Value | 0.00 | -- | -- | 10.00 |
| Date | 02-Oct-2017 | -- | -- | 30-Jun-2023 |

► Number of private sector partnerships operationalized (Number, Custom)

| | Baseline | Actual (Previous) | Actual (Current) | End Target |
|-------|-------------|-------------------|------------------|-------------|
| Value | 0.00 | -- | -- | 3.00 |
| Date | 02-Oct-2017 | -- | -- | 30-Jun-2023 |

► Project management has satisfactorily addressed statutory audit findings (cases) according to agreed business standards (Percentage, Custom)

| | Baseline | Actual (Previous) | Actual (Current) | End Target |
|-------|-------------|-------------------|------------------|-------------|
| Value | 0.00 | -- | -- | 100.00 |
| Date | 02-Oct-2017 | -- | -- | 30-Jun-2023 |

Overall Comments

Data on Financial Performance

Disbursements (by loan)


| Project | Loan/Credit/TF | Status | Currency | Original | Revised | Cancelled | Disbursed | Undisbursed | Disbursed |
|---------|----------------|-----------|----------|----------|---------|-----------|-----------|-------------|-----------|
| P158798 | IBRD-87570 | Effective | USD | 100.00 | 100.00 | 0.00 | 0.25 | 99.75 | 0% |

Key Dates (by loan)



| Project | Loan/Credit/TF | Status | Approval Date | Signing Date | Effectiveness Date | Orig. Closing Date | Rev. Closing Date |
|---------|----------------|-----------|---------------|--------------|--------------------|--------------------|-------------------|
| P158798 | IBRD-87570 | Effective | 26-May-2017 | 28-Jul-2017 | 04-Sep-2017 | 30-Jun-2023 | 30-Jun-2023 |

Cumulative Disbursements

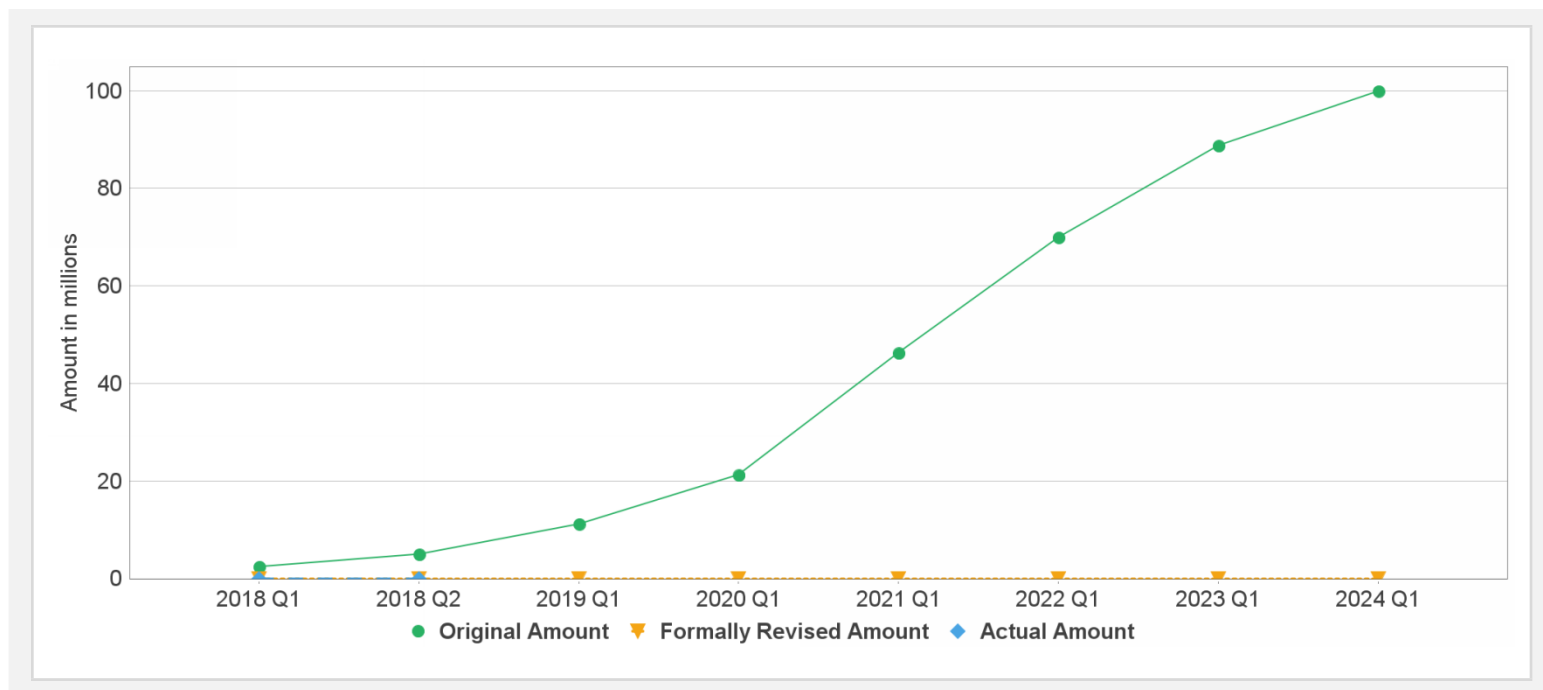

Restructuring History

There has been no restructuring to date.

Related Project(s)

There are no related projects.
